




OIL WELL CEMENTING INC.

Date 9-13-70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6985

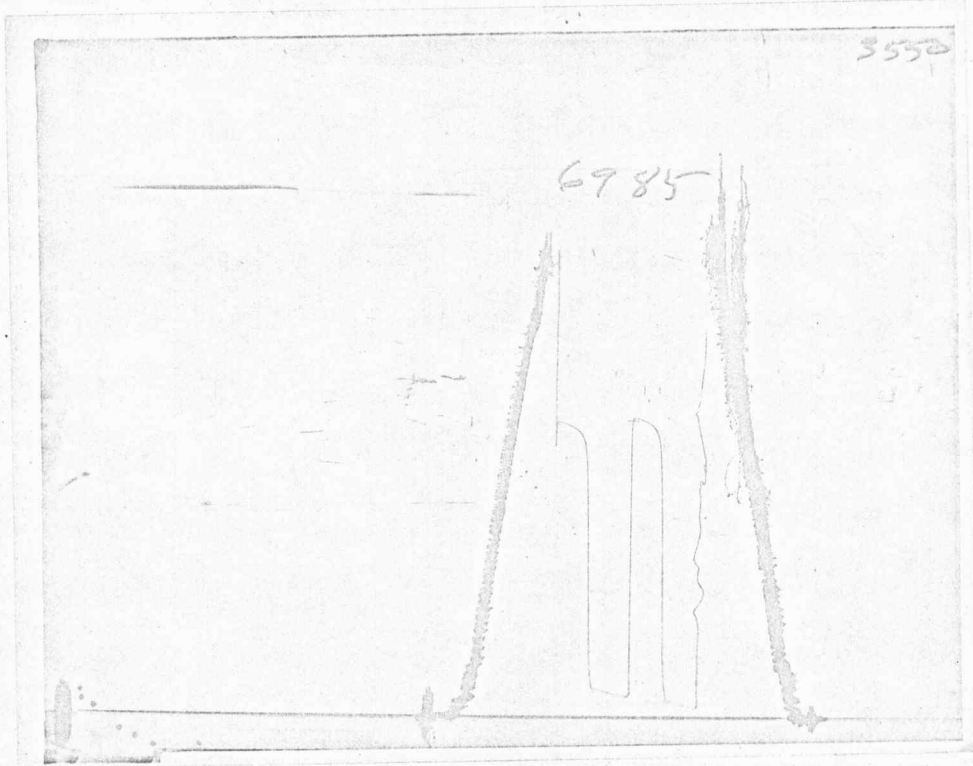

Company Glen Rupe Contractor Red Tiger Drilling Co.

Well No. 1 Lease Ogden County Edwards Sec. 20 Twp 26 Rng 18

Test No. 2 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 E.H.

Interval Tested From 4274 To 4300 Depth of Well 4300 Size Choke 5/8

Fluid Recovered In _____ Temp. 111 Elev. _____

Initial Hyd. 2449 P.S.I. Final Hyd. _____ P.S.I.

First Initial Flow Pressure 44 P.S.I. Opened Tool 5:20 ~~AM~~ P.M.

First Final Flow Pressure 79 P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 1496 P.S.I. Initial Closed-in Pres. 30 Min.

Second Initial Flow Pressure 90 P.S.I. Second Flow Pres. 30 Min.

Second Final Flow Pressure 133 P.S.I. Final Closed-in Pres. 30 Min.

Final Closed-in Pressure 1469 P.S.I.

Blow Weak to Good Thru-Out Test

Recovery 80' Slight Oil & Gas Cut Mud. 60' Thin Mud Slight Oil & Gas Cut Mud.

60' Muddy Water

Remarks _____

Approved By Ray Goodin Tester Bowman #013




OIL WELL CEMENTING INC.

Date 9-15-70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6986

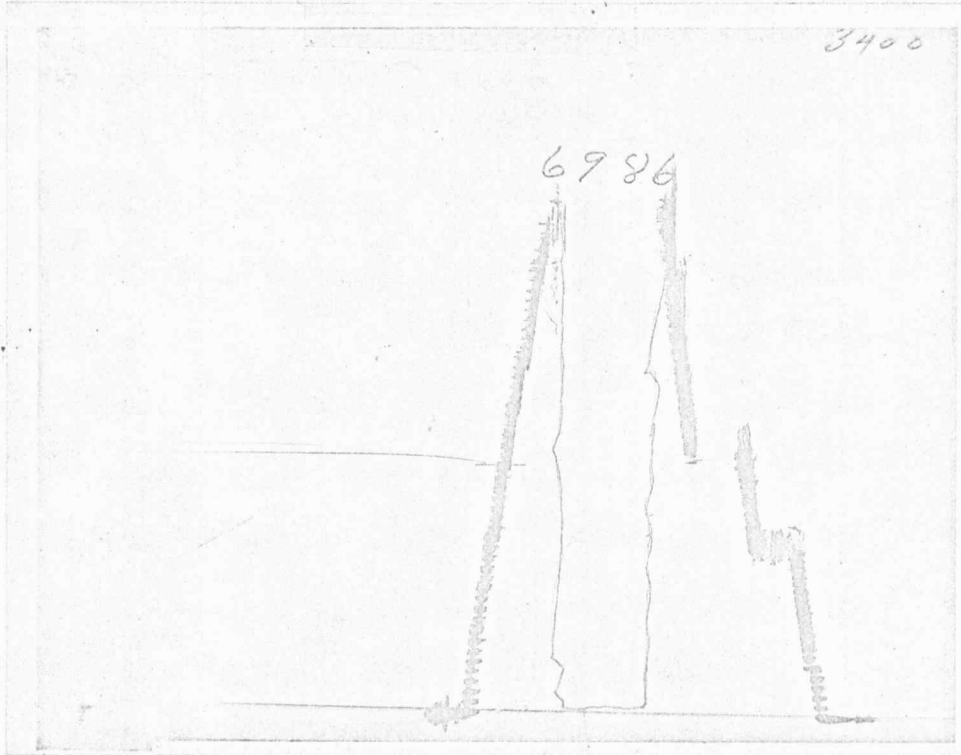

Company Glen Rupe Contractor Red Tiger Drilling Co.

Well No. 1 Lease Ogden County Edwards Sec. 20 Twp 26 Rng 18

Test No. 3 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 E.H.

Interval Tested From 4418 To 4449 Depth of Well 4449 Size Choke 5/8

Fluid Recovered In _____ Temp. 112 Elev. _____

Initial Hyd. 2458 P.S.I. Final Hyd. _____ P.S.I.

First Initial Flow Pressure 17 P.S.I. Opened Tool 9:00 A.M. RMX

First Final Flow Pressure _____ P.S.I. First Flow Pres. 20 Min.

Initial Closed-in Pressure 26 P.S.I. Initial Closed-in Pres. 15 Min.

Second Initial Flow Pressure 17 P.S.I. Second Flow Pres. 15 Min.

Second Final Flow Pressure _____ P.S.I. Final Closed-in Pres. 15 Min.


Final Closed-in Pressure 17 P.S.I.

Blow Very Weak, Dead In 5 Minutes

Recovery 10' of Mud

Remarks _____

Approved By Ray Goodin Tester Bowman




OIL WELL CEMENTING INC.

Date 9-17-70

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6987

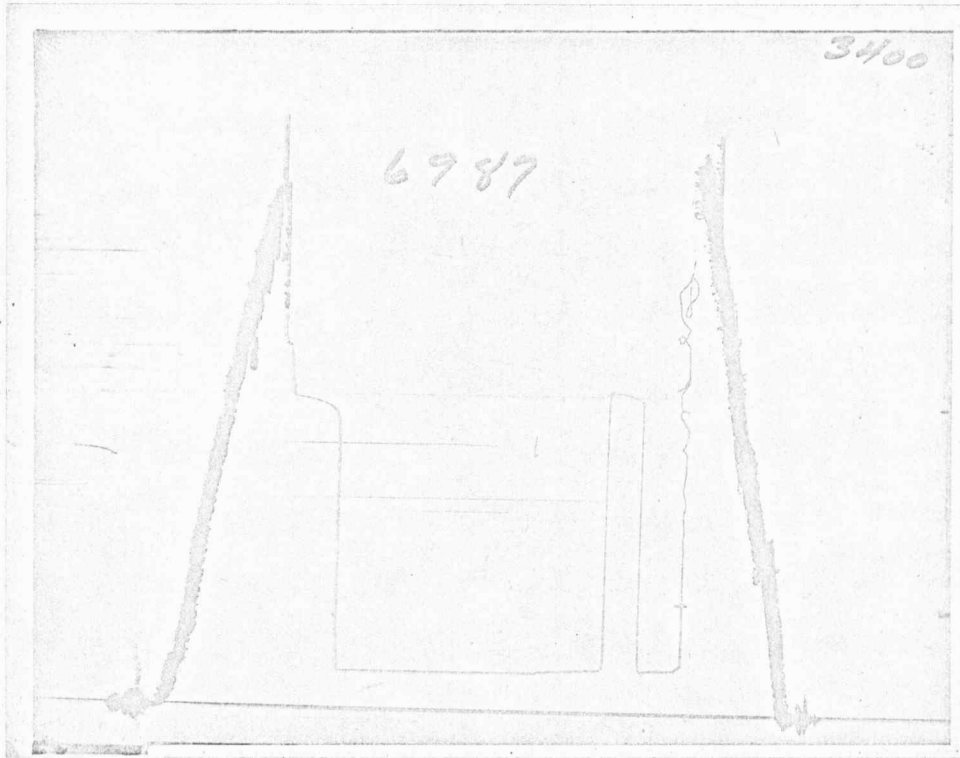

Company Glen Rupe Contractor Red Tiger Drilling Co.

Well No. 1 Lease Ogden County Edwards Sec. 20 Twp 26 Rng 18

Test No. 4 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 EH

Interval Tested From 4678 To 4719 Depth of Well 4719 Size Choke 5/8

Fluid Recovered In _____ Temp. _____ Elev. _____

Initial Hyd. 2650 P.S.I. Final Hyd. _____ P.S.I.

First Initial Flow Pressure 200 P.S.I. Opened Tool 2:25 ~~XXX~~ P.M.

First Final Flow Pressure _____ P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 1517 P.S.I. Initial Closed-in Pres. 30 Min.

Second Initial Flow Pressure 167 P.S.I. Second Flow Pres. 180 Min.

Second Final Flow Pressure _____ P.S.I. Final Closed-in Pres. 30 Min.

Final Closed-in Pressure 1500 P.S.I.

Blow Strong Blow Thru-Out Test

Recovery Gas to Surface in 2 Minutes. Gage 1,020,000 in 10 Minutes. Gaged 1,020,000 Thru-Out Test. No Fluid Recovery.

Remarks _____

Approved By Ray Goodin Tester Smith #013
