

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company OIL PROPERTIES, INC.

Lease and Well No. TAYLOR B-1

County KIOWA

State

KANSAS

Date 4-21-79

Formation Test No. 1 Total Depth 4705 Elev. _____
 Interval Tested 4682 To 4705 Anchor Length 23'
 Size Hole 7 7/8 Size Drill Pipe 4 1/2 F H Size Packer 6 3/4
 Mud Weight 9.2 Viscosity 51 Water Loss 12.2 c.c. Bottom Hole Temp. 110 °F
 Chokes: Top 1/2 Bottom 1/2 Ticket No. 18026
 Length of Drill Collar 366 I. D. 2.76 Length Flexweight _____ I. D. _____

RECOVERY

FIRST FLOW GOOD BLOW DECREASING TO FAIR BLOW.
 SECOND FLOW GOOD BLOW DECREASING TO FAIR BLOW.

90 FEET OF MUD.
 1250 FEET OF GAS IN PIPE.


Lease and Well No. TAYLOR B-1

19-275-17W

Formation Test No. 1

19-275-17W

4332
18026

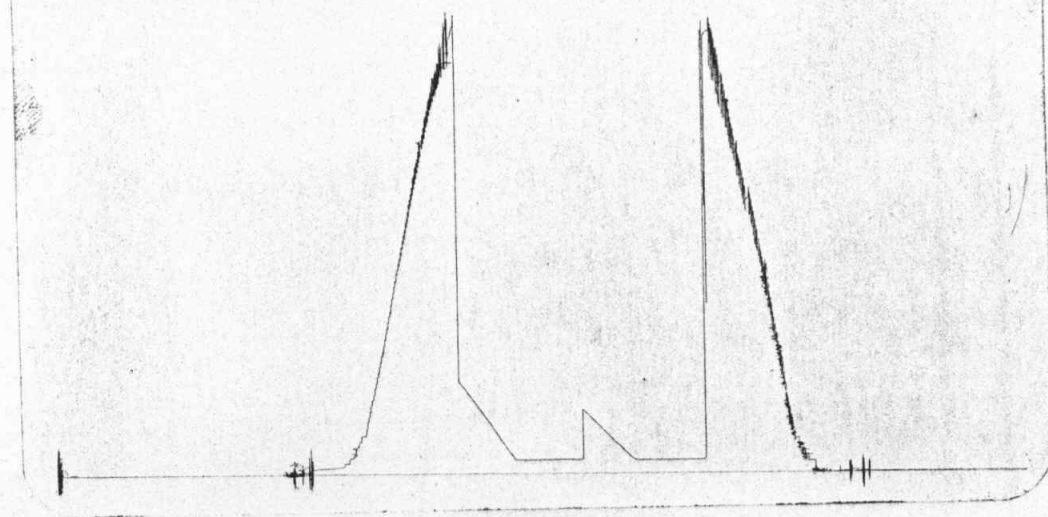

Tool Open: 1st Flow hr. 45 mins: Shut-in Initial hr. 45 min: 2nd Flow hr. 45 min: Shut-in Final hr. 45 min

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>2453</u>	<u>2455</u>
(B) Initial 1st Flow Pressure	<u>64</u>	<u>78</u>
(C) Final 1st Flow Pressure	<u>64</u>	<u>78</u>
(D) Initial Shut-in Pressure	<u>346</u>	<u>361</u>
(E) Initial 2nd Flow Pressure	<u>64</u>	<u>80</u>
(F) Final 2nd Flow Pressure	<u>64</u>	<u>80</u>
(G) Final Shut-in Pressure	<u>519</u>	<u>519</u>
(H) Final Hydrostatic Pressure	<u>2474</u>	<u>2411</u>

18026

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company OIL PROPERTIES

Lease and Well No. TAYLOR B-1

County KIOWA State KANSAS Date 4-22-79

Formation Test No. 2 Total Depth 4730 Elev. _____
Interval Tested 4688 To 4730 Anchor Length 42'
Size Hole 7 7/8 Size Drill Pipe 4 1/2 F H Size Packer 6 3/4
Mud Weight 9.2 Viscosity 41 Water Loss 10.0 c.c. Bottom Hole Temp: _____ °F
Chokes: Top 1/2 Bottom 1/2 Ticket No. 18027
Length of Drill Collar 366 I. D. 2.76 Length Flexweight _____ I. D. _____

RECOVERY

FIRST FLOW FAIR BLOW INCREASING TO GOOD BLOW.
SECOND FLOW FAIR BLOW


65 FEET OF MUD.

Lease and Well No. TAYLOR B-1

19-27S-17W

Formation Test No. 2

4332
6 18027

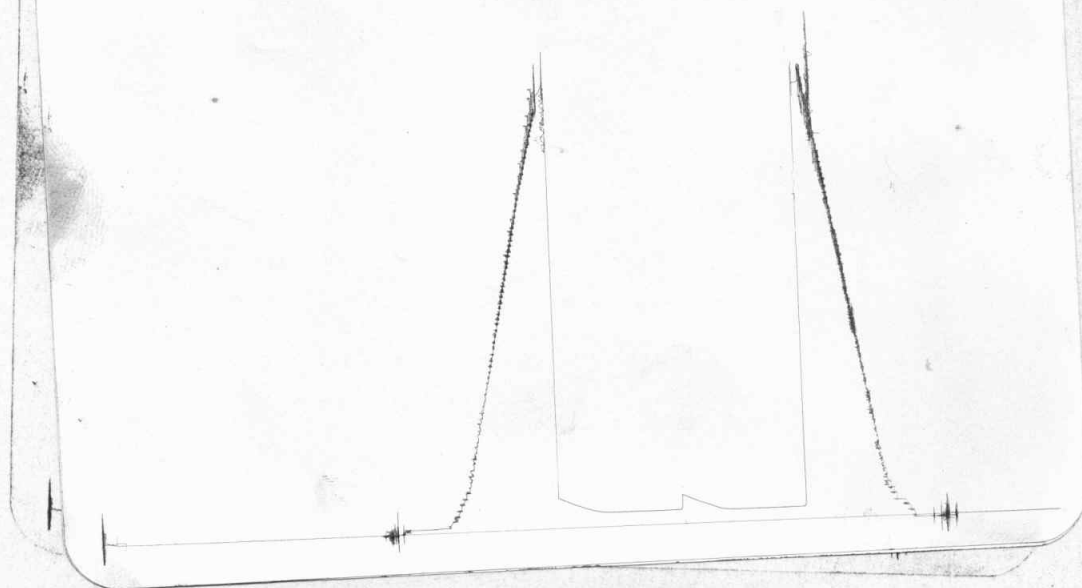

Tool Open: 1st Flow — hr. 45 mins: Shut-in Initial — hr. 45 min: 2nd Flow — hr. 45 min: Shut-in Final — hr. 45 min.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	2495	2423
(B) Initial 1st Flow Pressure	64	72
(C) Final 1st Flow Pressure	64	72
(D) Initial Shut-in Pressure	173	165
(E) Initial 2nd Flow Pressure	64	80
(F) Final 2nd Flow Pressure	64	80
(G) Final Shut-in Pressure	173	165
(H) Final Hydrostatic Pressure	2453	2408

18027
