


KGS

15-057-20625-0000


**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Blueridge Pet. Corp.

Doll #1-9

P.O.Box 1913
Enid Ok. 73702

9-27s-24w Ford Ks.

ATTN: Jim Musgrove

Job Ticket: 33978

DST#: 1

Test Start: 2008.11.12 @ 05:33:55

GENERAL INFORMATION:

Formation: **Pawnee**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 07:58:40

Time Test Ended: 15:22:25

Test Type: Conventional Bottom Hole

Tester: Gary Pevoteaux

Unit No: 39

Interval: **4820.00 ft (KB) To 4860.00 ft (KB) (TVD)**

Total Depth: 4860.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2508.00 ft (KB)

2495.00 ft (CF)

KB to GR/CF: 13.00 ft

Serial #: 8167

Inside

Press@RunDepth: 355.69 psig @ 4821.00 ft (KB)

Start Date: 2008.11.12

End Date:

2008.11.12

Start Time: 05:34:00

End Time:

15:22:25


Capacity: 7000.00 psig

Last Calib.: 2008.11.12

Time On Btm: 2008.11.12 @ 07:57:25

Time Off Btm: 2008.11.12 @ 11:48:39

TEST COMMENT: IF: Strong blow BOB in 4 mins
 IS: Fair blow 1 - 6"
 FF: Strong blow BOB in 3 1/2 mins. GTS in 40 mins TSTM
 FSI: Strong blow BOB

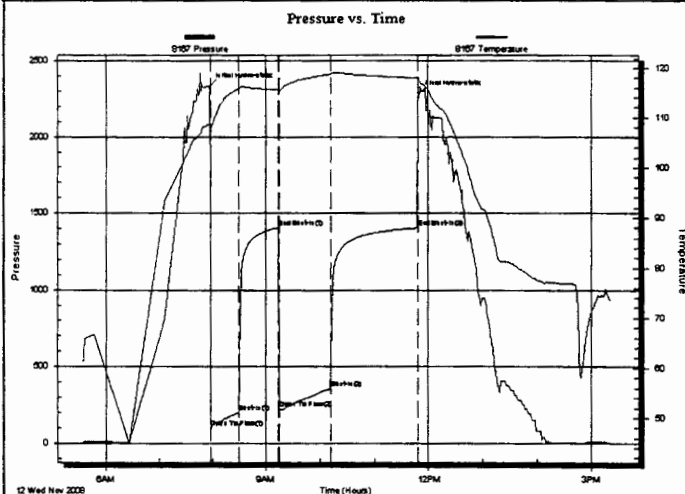

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2330.31	108.57	Initial Hydro-static
2	95.74	107.93	Open To Flow (1)
32	198.84	115.84	Shut-In (1)
76	1405.05	115.69	End Shut-In (1)
77	224.89	115.39	Open To Flow (2)
134	355.69	118.76	Shut-In (2)
231	1404.71	118.06	End Shut-In (2)
232	2281.62	118.28	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
330.00	SW/w o specs /Rw .065 ohms @70 deg	2.37
250.00	GM&WCO 28%g 2% m 14%w 56%o	3.51
250.00	GMO 38%g 11% m 51%o	3.51

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
----------------	-----------------	------------------

RECEIVED

MAR 12 2009

KCO WICHITA



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Blueridge Petl. Corp.

P.O.Box 1913
Enid Ok.73702

ATTN: Jim Musgrove

Doll #1-9

9-27s-24w Ford Ks.

Job Ticket: 33979

DST#: 2

Test Start: 2008.11.13 @ 11:46:21

GENERAL INFORMATION:

Formation: **Miss.**

Deviated: **No** Whipstock: **ft (KB)**

Time Tool Opened: 13:51:51

Time Test Ended: 18:59:21

Test Type: **Conventional Bottom Hole**

Tester: **Gary Pevoteaux**

Unit No: **39**

Interval: **4970.00 ft (KB) To 5020.00 ft (KB) (TVD)**

Total Depth: **5020.00 ft (KB) (TVD)**

Hole Diameter: **7.88 inches** Hole Condition: **Fair**

Reference Elevations: **2508.00 ft (KB)**

2495.00 ft (CF)

KB to GR/CF: **13.00 ft**

Serial #: 8167 **Inside**

Press@RunDepth: **30.46 psig @ 4971.00 ft (KB)**

Start Date: **2008.11.13**

End Date:

2008.11.13

Start Time: **11:46:26**

End Time:

18:59:20

Capacity: **7000.00 psig**

Last Calib.: **2008.11.13**

Time On Btm: **2008.11.13 @ 13:51:06**


Time Off Btm: **2008.11.13 @ 16:12:35**

TEST COMMENT: IF: Weak blow Slow Increase to 3 1/2"

ISI: No blow

FF: Weak blow 1/2 - 2 1/2 "

FSI: No blow

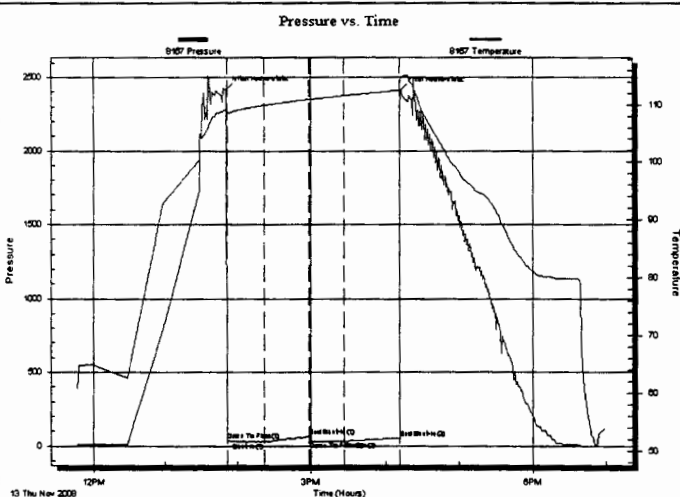

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2413.96	109.15	Initial Hydro-static
1	39.31	108.61	Open To Flow (1)
31	26.32	109.89	Shut-In (1)
68	61.13	110.91	End Shut-In (1)
68	30.14	110.92	Open To Flow (2)
95	30.46	111.55	Shut-In (2)
141	51.58	112.50	End Shut-In (2)
142	2406.12	114.17	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
10.00	Drig.mud	0.05
0.00	185 ft.of GIP	0.00

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



**TRILOBITE
TESTING, INC**

DRILL STEM TEST REPORT

Blueridge Petl. Corp.

P.O.Box 1913
Enid Ok. 73702

ATTN: Jim Musgrove

Doll #1-9

9-27s-24w Ford Ks.

Job Ticket: 33980

DST#: 3

Test Start: 2008.11.14 @ 08:10:39

GENERAL INFORMATION:

Formation: **Miss.**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 10:14:39

Time Test Ended: 16:47:24

Test Type: Conventional Bottom Hole

Tester: Gary Pevoteaux

Unit No: 39

Interval: **5042.00 ft (KB) To 5067.00 ft (KB) (TVD)**

Total Depth: 5067.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2508.00 ft (KB)

2495.00 ft (CF)

KB to GR/CF: 13.00 ft

Serial #: 8167

Inside

Press@RunDepth: 145.45 psig @ 5043.00 ft (KB)

Start Date: 2008.11.14

End Date:

2008.11.14

Capacity: 7000.00 psig

Last Calib.: 2008.11.14

Start Time: 08:10:44

End Time:

16:47:24

Time On Btm: 2008.11.14 @ 10:14:24


Time Off Btm: 2008.11.14 @ 13:33:23

TEST COMMENT: IF: Weak blow. Slow increase to 3 1/2".

ISI: No blow.

FF: Weak blow. Slow increase to 2 1/2".

FSI: No blow.

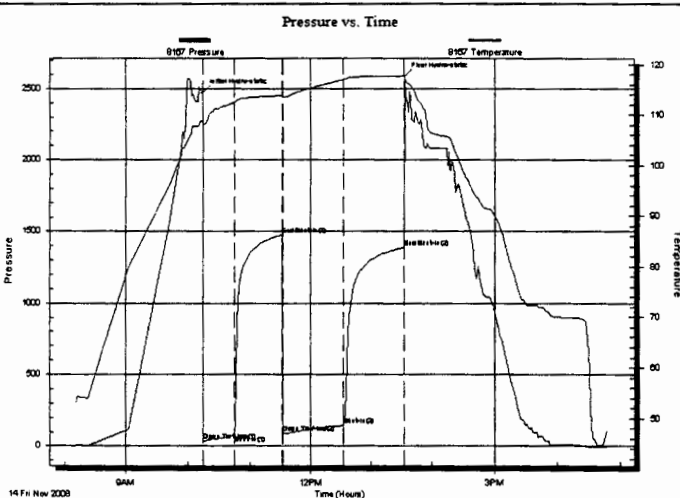

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2471.34	108.59	Initial Hydro-static
1	38.46	107.67	Open To Flow (1)
31	75.76	112.42	Shut-In(1)
78	1477.85	113.82	End Shut-In(1)
78	90.60	113.46	Open To Flow (2)
139	145.45	116.99	Shut-In(2)
199	1389.46	117.59	End Shut-In(2)
199	2586.79	117.67	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
124.00	MW 14% m 86% w / Rw .15 ohms @ 52 deg 0.61	
124.00	WMW o specs .48% w 52% m	0.61
20.00	mud w / o specs.	0.28

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------
