

Company
Address
CSZ
Attn.

Falcon Exploration, Inc.
125 N. Market, Ste. 1252
Wichita, KS 67202
Keith Reavis

Lease Name
Lease #
Legal Desc
Section
Township
County
Drilling Cont

Lanterman
1-8
NE-SE-SE-NE
8
28S
Gray
Val Energy, Inc. Rig #1

Job Ticket
Range
State

2073
30W
KS

Comments

GENERAL INFORMATION

Test # 1
Tester
Test Type

Tim Venters
Conventional Bottom Hole
Mis-run

Test Date 4/1/2009

of Packers
Mud Type
Mud Weight
Filtrate

2.0
Gel Chem
9.5
8.0

Packer Size 6 3/4
Viscosity 51.0
Chlorides 3900

Drill Collar Len
Wght Pipe Len

0
0

Formation
Interval Top
Anchor Len Below
Total Depth
Blow Type

Lower Kansas City
4606.0
45.0
4651.0
Hit a Bridge.

Bottom 4651.0
Between 0

Chokes
Top Recorder #
Mid Recorder #
Bott Recorder #

3/4
W1119

13565

Mileage
Standby Time
Extra Equipmnt
Time on Site
Tool Picked Up
Tool Layed Dwn

232
0
Jars & Safety joint
6:45 PM
8:45 PM
10:40 PM

Approved By
Elevation
Kelley Bushings


2812.00
2822.00

Start Date/Time
End Date/Time

4/1/2009 7:56 PM
4/1/2009 10:36 PM

RECOVERY

Feet	Description	Gas	Oil	Water	Mud
DST Fluids	0				

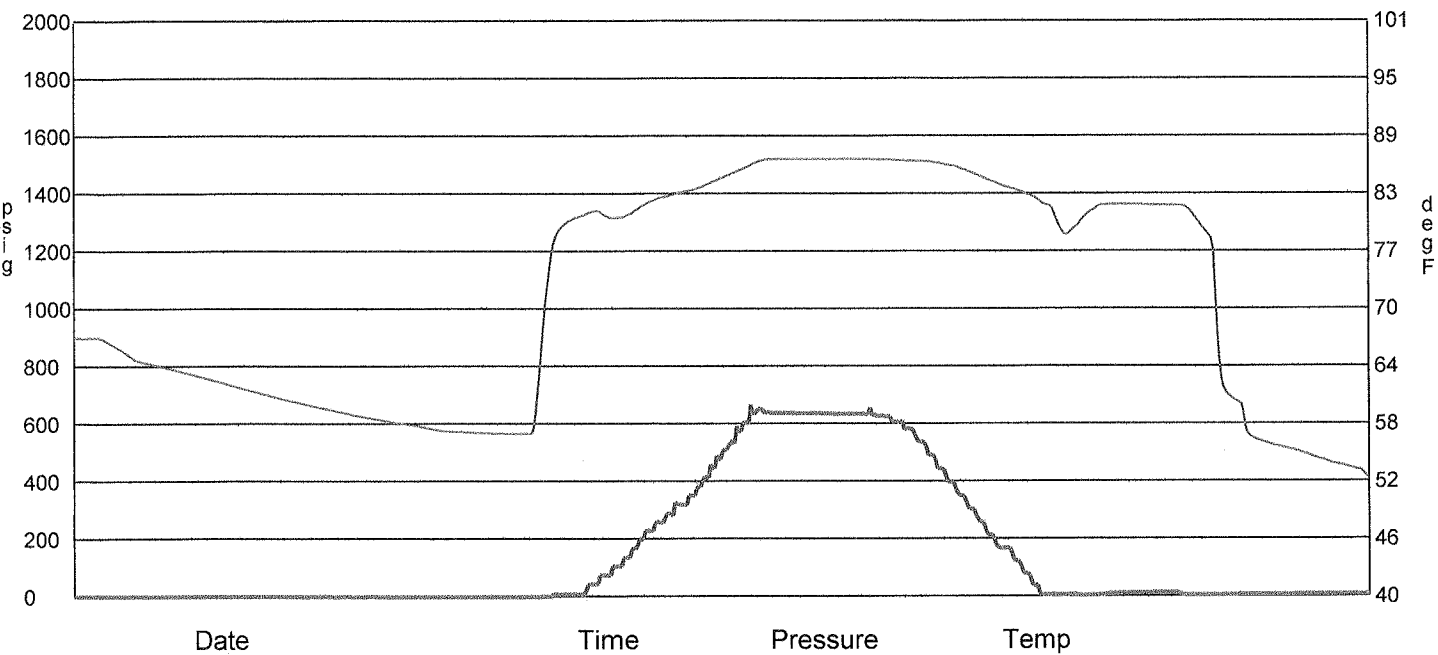

GAS FLOWS

Min Into IFP Min Into FFP Gas Flows Pressure Choke


Lease Name	Lanterman		
Lease #	1-8		
Legal Desc	NE-SE-SE-NE	Job Ticket	2073
Section	8	Range	30W
Township	28S		
County	Gray	State	KS
Drilling Cont	Val Energy, Inc. Rig #1		

Comments

Formation	Lower Kansas City		
Interval Top	4606.0	Bottom	4651.0
Anchor Len Below	45.0	Between	0
Total Depth	4651.0		
Blow Type	We slid about 10 feet. Fairly strong building to 5 inches. Very weak sand building to 10 inches. Times 2		

Feet	Description	Gas		Oil		Water		Mud	
45	Water cut mud	0%	0ft	0%	0ft	28%	12.6ft	72%	32.4ft
60	Very heavy water cut mud	0%	0ft	0%	0ft	43%	25.8ft	57%	34.2ft
120	Mud cut water	0%	0ft	0%	0ft	87%	104.4ft	13%	15.6ft
10	Mud	0%	0ft	0%	0ft	0%	0ft	100%	10ft

DST Fluids 46000

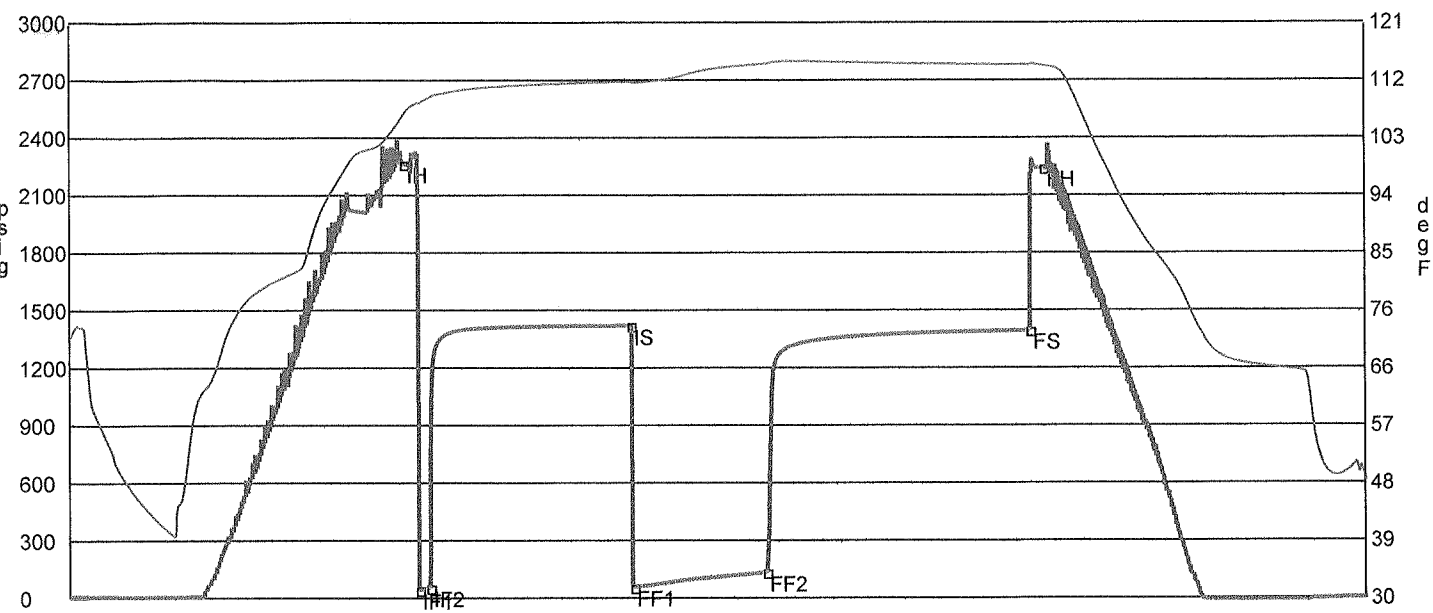

	Date	Time	Pressure	Temp	
IH	4/2/2009 6:55:00 AM	2.5	2264.69	106.522	Initial Hydro-static
IF1	4/2/2009 7:01:45 AM	2.6125	41.898	108.315	Initial Flow (1)
IF2	4/2/2009 7:06:45 AM	2.695833	52.571	109.156	Initial Flow (2)
IS	4/2/2009 8:36:15 AM	4.1875	1418.682	111.689	Initial Shut-In
FF1	4/2/2009 8:37:30 AM	4.208333	56.194	111.516	Final Flow (1)
FF2	4/2/2009 9:37:30 AM	5.208333	131.924	114.514	Final Flow (2)
FS	4/2/2009 11:37:30 AM	7.208333	1393.405	114.355	Final Shut-In
FH	4/2/2009 11:43:45 AM	7.3125	2240.98	114.177	Final Hydro-static

GAS FLOWS

Min Into IFP Min Into FFP Gas Flows Pressure Choke

Company	Falcon Exploration Inc.	Lease Name	Lanterman	
Address	125 N. Market Ste 1252	Lease #	1-8	
CSZ	Wichita, KS 67202	Legal Desc	NW SE SE NE	Job Ticket 6012
Attn.	Micheal S Mitchell	Section	8	Range 30W
		Township	28S	
		County	Gray	State KS
		Drilling Cont	Val Drilling Rig #1	


Comments

GENERAL INFORMATION

Test # 3	Test Date 4/4/2009	Chokes 3/4	Hole Size 7 7/8
Tester Richard Holtz		Top Recorder # W1023	
Test Type Conventional Bottom Hole		Mid Recorder #	
Mis-run		Bott Recorder # 11027	
# of Packers 2.0	Packer Size 6 3/4	Mileage 232	Approved By
		Standby Time 0	
Mud Type Gel Chem		Extra Equipmnt Jars and safety joint	
Mud Weight 9.4	Viscosity 61.0	Time on Site 12:00 AM	
Filtrate 8.0	Chlorides 3000	Tool Picked Up 12:00 AM	
		Tool Layed Dwn 12:00 AM	
Drill Collar Len 0		Elevation 2812.00	Kelley Bushings 2822.00
Wght Pipe Len 0			
Formation Marrow Sand		Start Date/Time 4/4/2009 11:15 AM	
Interval Top 5070.0	Bottom 5120.0	End Date/Time 4/4/2009 2:57 PM	
Anchor Len Below 50.0	Between 0		
Total Depth 5120.0			
Blow Type	Misrun hit bridge at 1300' could not get to bottom.		

RECOVERY

Feet	Description	Gas	Oil	Water	Mud
DST Fluids	0				

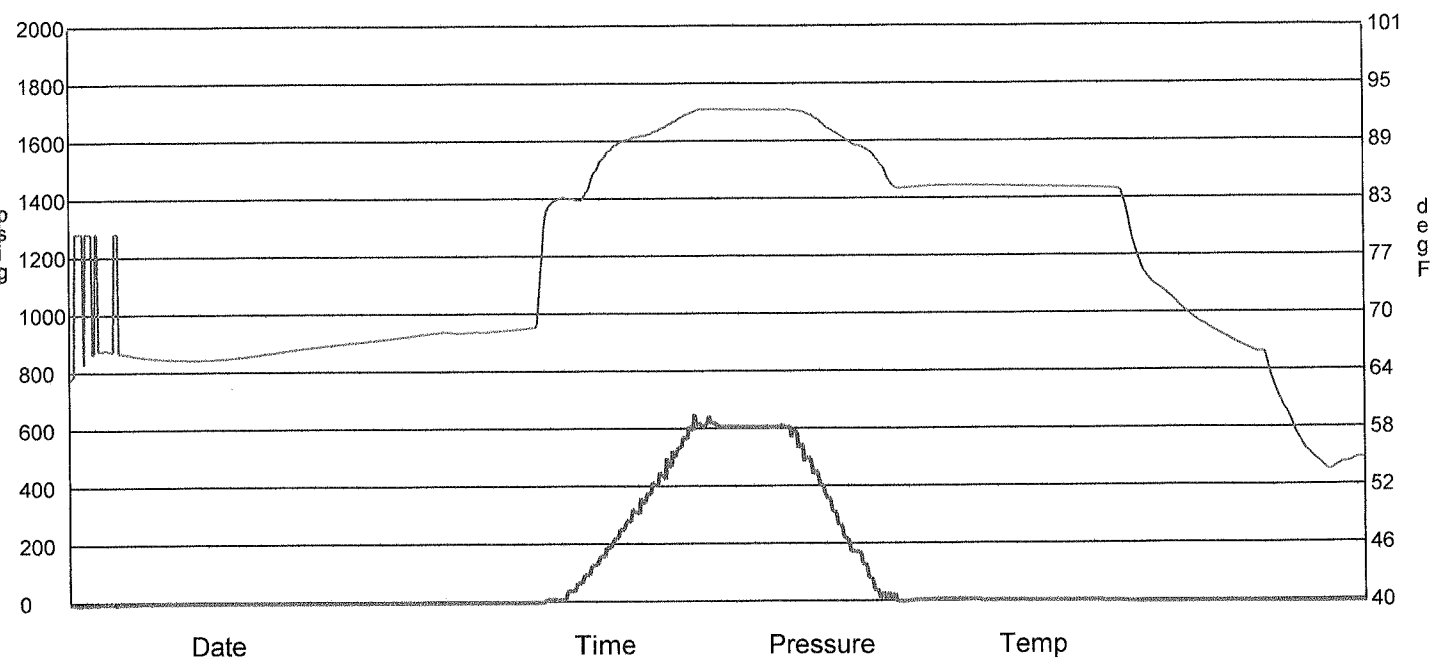

GAS FLOWS

Min Into IFP Min Into FFP Gas Flows Pressure Choke
