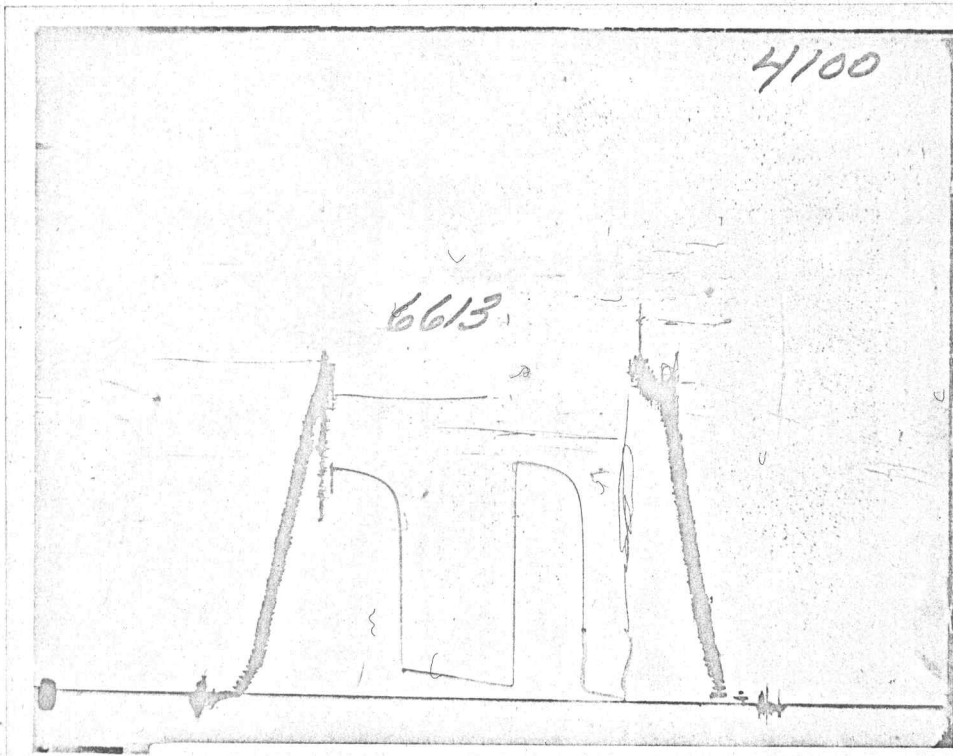
Date 1/1/71

## DRILL STEM TEST RECOVERY REPORT

Ticket No. 6613

Company American Exp. Contractor Sage Drlg.

Well No. 1 Lease Stucky County Kingman Sec. 30 Twp 29 Rng 5

Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 E.H.

Interval Tested From 3607 To 3629 Depth of Well 3629 Size Choke 5/8

Fluid Recovered In \_\_\_\_\_ Temp. 120 Elev. \_\_\_\_\_

Initial Hyd. 1935 P.S.I. Final Hyd. \_\_\_\_\_ P.S.I.

First Initial Flow Pressure 10 P.S.I. Opened Tool 10:30 ~~###~~ P.M.

First Final Flow Pressure 53 P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 1408 P.S.I. Initial Closed-in Pres. 60 Min.

Second Initial Flow Pressure 74 P.S.I. Second Flow Pres. 90 Min.

Second Final Flow Pressure 159 P.S.I. Final Closed-in Pres. 60 Min.

Final Closed-in Pressure 1367 P.S.I.

Blow Weak Thru-Out Test

Recovery 60' Gas In Pipe 360' Muddy Water W/ Trace Of Oil

Remarks \_\_\_\_\_

Approved By Elster Tester Smith




OIL WELL CEMENTING INC.

Date 1/2/71

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6614

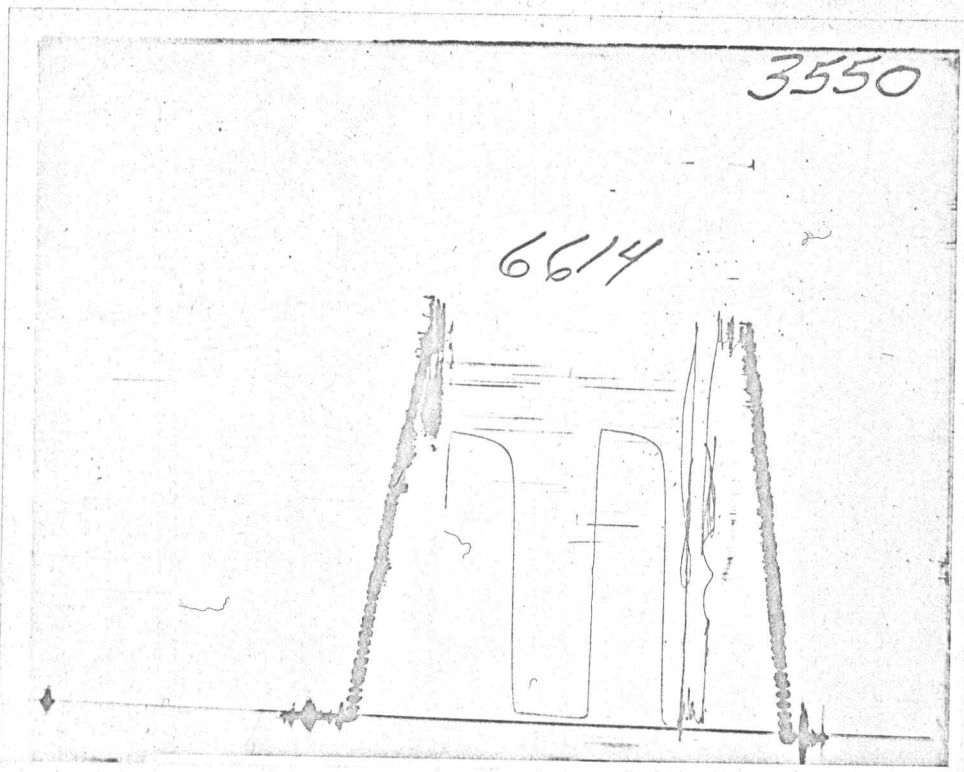

Company American Exp. Contractor Sage Drlg.

Well No. 1 Lease Stucky County Kingman Sec. 30 Twp 29 Rng 5

Test No. 2 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 E.H.

Interval Tested From 3665 To 3685 Depth of Well 3685 Size Choke 5/8

Fluid Recovered In \_\_\_\_\_ Temp. 120 Elev. \_\_\_\_\_

Initial Hyd. 2018 P.S.I. Final Hyd. \_\_\_\_\_ P.S.I.

First Initial Flow Pressure 21 P.S.I. Opened Tool 3:45 ~~###~~ P.M.

First Final Flow Pressure \_\_\_\_\_ P.S.I. First Flow Pres. 30 Min.

Initial Closed-in Pressure 1471 P.S.I. Initial Closed-in Pres. 60 Min.

Second Initial Flow Pressure 31 P.S.I. Second Flow Pres. 60 Min.

Second Final Flow Pressure 42 P.S.I. Final Closed-in Pres. 60 Min.


Final Closed-in Pressure 1439 P.S.I.

Blow Very Weak Dead In 4 Min. Flushed Tool on Initial Flow Dead In 1 Min.


Recovery 70' Drlg. Mud

Remarks \_\_\_\_\_

Approved By Elster Tester Smith

Date 1/6/71

## DRILL STEM TEST RECOVERY REPORT

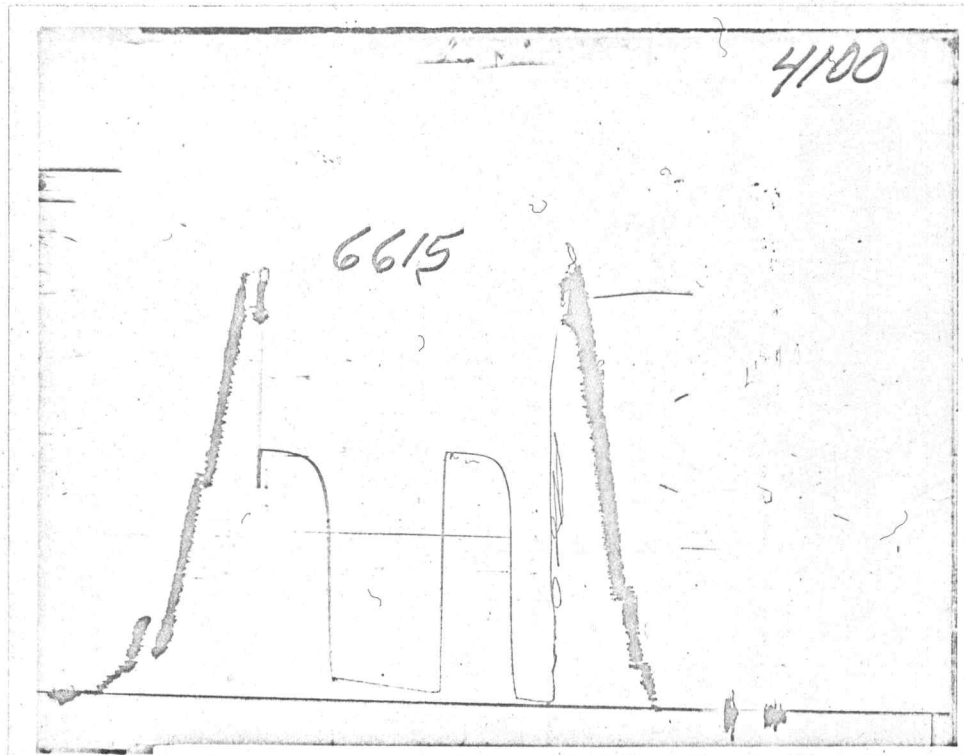Ticket No. 6615

Company American Exp. Contractor Sage Drlg.  
Well No. 1 Lease Stucky County Kingman Sec. 30 Twp 29 Rng 5  
Test No. 3 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 E.H.  
Interval Tested From 4442 To 4455 Depth of Well 4455 Size Choke 5/8  
Fluid Recovered In \_\_\_\_\_ Temp. 120 Elev. \_\_\_\_\_  
Initial Hyd. 2495 P.S.I. Final Hyd. \_\_\_\_\_ P.S.I.  
First Initial Flow Pressure 21 P.S.I. Opened Tool 2:00 A.M. ~~###~~  
First Final Flow Pressure 42 P.S.I. First Flow Pres. 30 Min.  
Initial Closed-in Pressure 1471 P.S.I. Initial Closed-in Pres. 60 Min.  
Second Initial Flow Pressure 53 P.S.I. Second Flow Pres. 90 Min.  
Second Final Flow Pressure 117 P.S.I. Final Closed-in Pres. 60 Min.  
Final Closed-in Pressure 1471 P.S.I.  
Blow Strong Thru-Out Test

Recovery 180' Gas In Pipe 240' Gassy Oil 60' Heavy Oil & Gas Cut Mud  
60' Gassy Slight Oil Cut Mud

Remarks \_\_\_\_\_

Approved By Elster Tester Smith
