

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 10-6-05 Location 28 30 14 Elevation 1873 County Barber

Company F.G. Holl, LLC Number of Copies 5

Charts Mailed to 9431 E Central, ST #100 Wichita Ks, 67206

Drilling Contractor Bill Ree

Length Drill Pipe 1967 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 Xh

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars 275 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 Xh

Top Packer Depth 2263 Bottom Packer Depth 2268 Number of Packers 3 Packer Size 6 3/4

TESTED FROM 2268 TO 2308 ANCHOR LENGTH 40ft TOTAL DEPTH 2358 Hole Size 7 7/8

LEASE & WELL NO. Ternes Trust 1-28 FORMATION TESTED _____ TEST NO. #1

Mud Weight 8.9 Viscosity 43 Water Loss 9.6 Chlorides - Pits 15,000 D.S.T. _____

Maximum Temp. 86 °F Initial Hydrostatic Pressure (A) 1064 P.S.I. Final Hydrostatic Pressure (H) 1011 P.S.I.

Tool Open I.F.P. from 6:15 m to 6:30 m 15 min

Tool Closed I.C.I.P. from 6:30 m to 7:00 m 30 min

Tool Open F.F.P. from 7:00 m to 7:15 m 15 min

Tool Closed F.C.I.P. from 7:15 m to 7:45 m 30 min

Initial Blow Weak Surface Blow 1" into Bucket 15 min

Final Blow Weak Surface Blow 1" into Bucket 15 min

Total Feet Recovered 15 feet mud Gravity of Oil _____ Corrected

15 Feet of mud %Gas _____ %Oil _____ %Mud _____ %Water _____

_____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

_____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

_____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

_____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

_____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

_____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

_____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

_____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

_____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

Remarks _____

Extra Equipment - Jars Yes Safety Joint Yes Extra Packer Yes Straddle Yes Hook Wall _____

Top Recorder No. 4023 Clock No. ELECT Depth 2327 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 47441 Depth 2355 Insurance _____

Price of Job _____

Tool Operator 4

Approved By _____

No 14635

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.


SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: F.G. HOLL LLC
 Lease & Well No. TERNES TRUST 1-28
 Test #: 1 Date: 10/06/05
 SEC. 28 TWP. 30
 RGE. 14

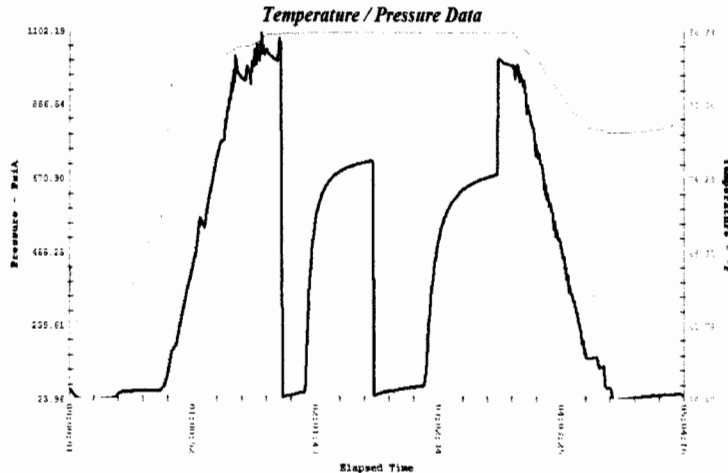

1	Initial Hydrostatic Pressure	1066
2	Initial Flow Pressure	33
3	Final Initial Flow Pressure	46
4	Initial Shut-In Pressure	724
5	Initial Final Flow Pressure	36
6	Final Flow Pressure	65
7	Final Shut-In Pressure	684
8	Final Hydrostatic Pressure	1011

Maximum Temperature 86

GENERAL INFORMATION

COMPANY NAME	 F.G.Holl LLC	LEASE AND WELL NUMBER	 TERNES TRUST
TEST DATE	 10/6/05	FORMATION TESTED	
SECTION-TOWN-RANGE	 28 30s 14w	DRILL STEM TEST NUMBER	 1
STATE	 KANSAS	REPORT NUMBER	 14635
COUNTY	 BABER	ELEVATION KELLY BUSHINGS	 1884
ELEVATION GROUND LEVEL	 1873	TESTING ENGINEER	 JARED SCHECK
COMPANY REPRESENTATIVE	 BILL REE		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	 2268	TOP PACKER DEPTH	 2263
TEST INTERVAL (to)	 2308	BOTTOM PACKER DEPTH	 2268
ANCHOR LENGTH	 40	NUMBER OF PACKERS	 3
TOTAL DEPTH (ft)	 2358	PACKER SIZE	 6 3/4
		HOLE SIZE	 7 7/8

FLOW TIMES

TOOL OPEN (from)	 6:15 P.M.	TOOL OPEN (from)	 7:00P
INITIAL OPEN TOOL OPEN (to)	 6:30 P.M.	FINAL OPEN TOOL OPEN (to)	 7:15
DURATION (min.)	 15 MIN	DURATION (min.)	 15 MIN
TOOL CLOSED (from)	 6:30 P.M.	TOOL CLOSED (from)	 7:15
INITIAL SHUT-IN TOOL CLOSED (to)	 7:00P.M.	FINAL SHUT-IN TOOL CLOSED (to)	 7:45
DURATION (min.)	 30 MIN	DURATION (min.)	 30 MIN


INITIAL FLOW WEAK SURFACE BLOW 1" INTO BUCKET IN 15 MIN

FINAL FLOW WEAK SURFACE BLOW 1" INTO BUCKET IN 15 MIN

FEET OF Recovery	RECOVERY DESCRIPTION	% GAS	% OIL	% MUD	% WATER
1) 15	MUD				
2)					
3)					
4)					
5)					
6)					

GREAT BEND, KANSAS 67530 (800)792-6902

Temperature / Pressure Data

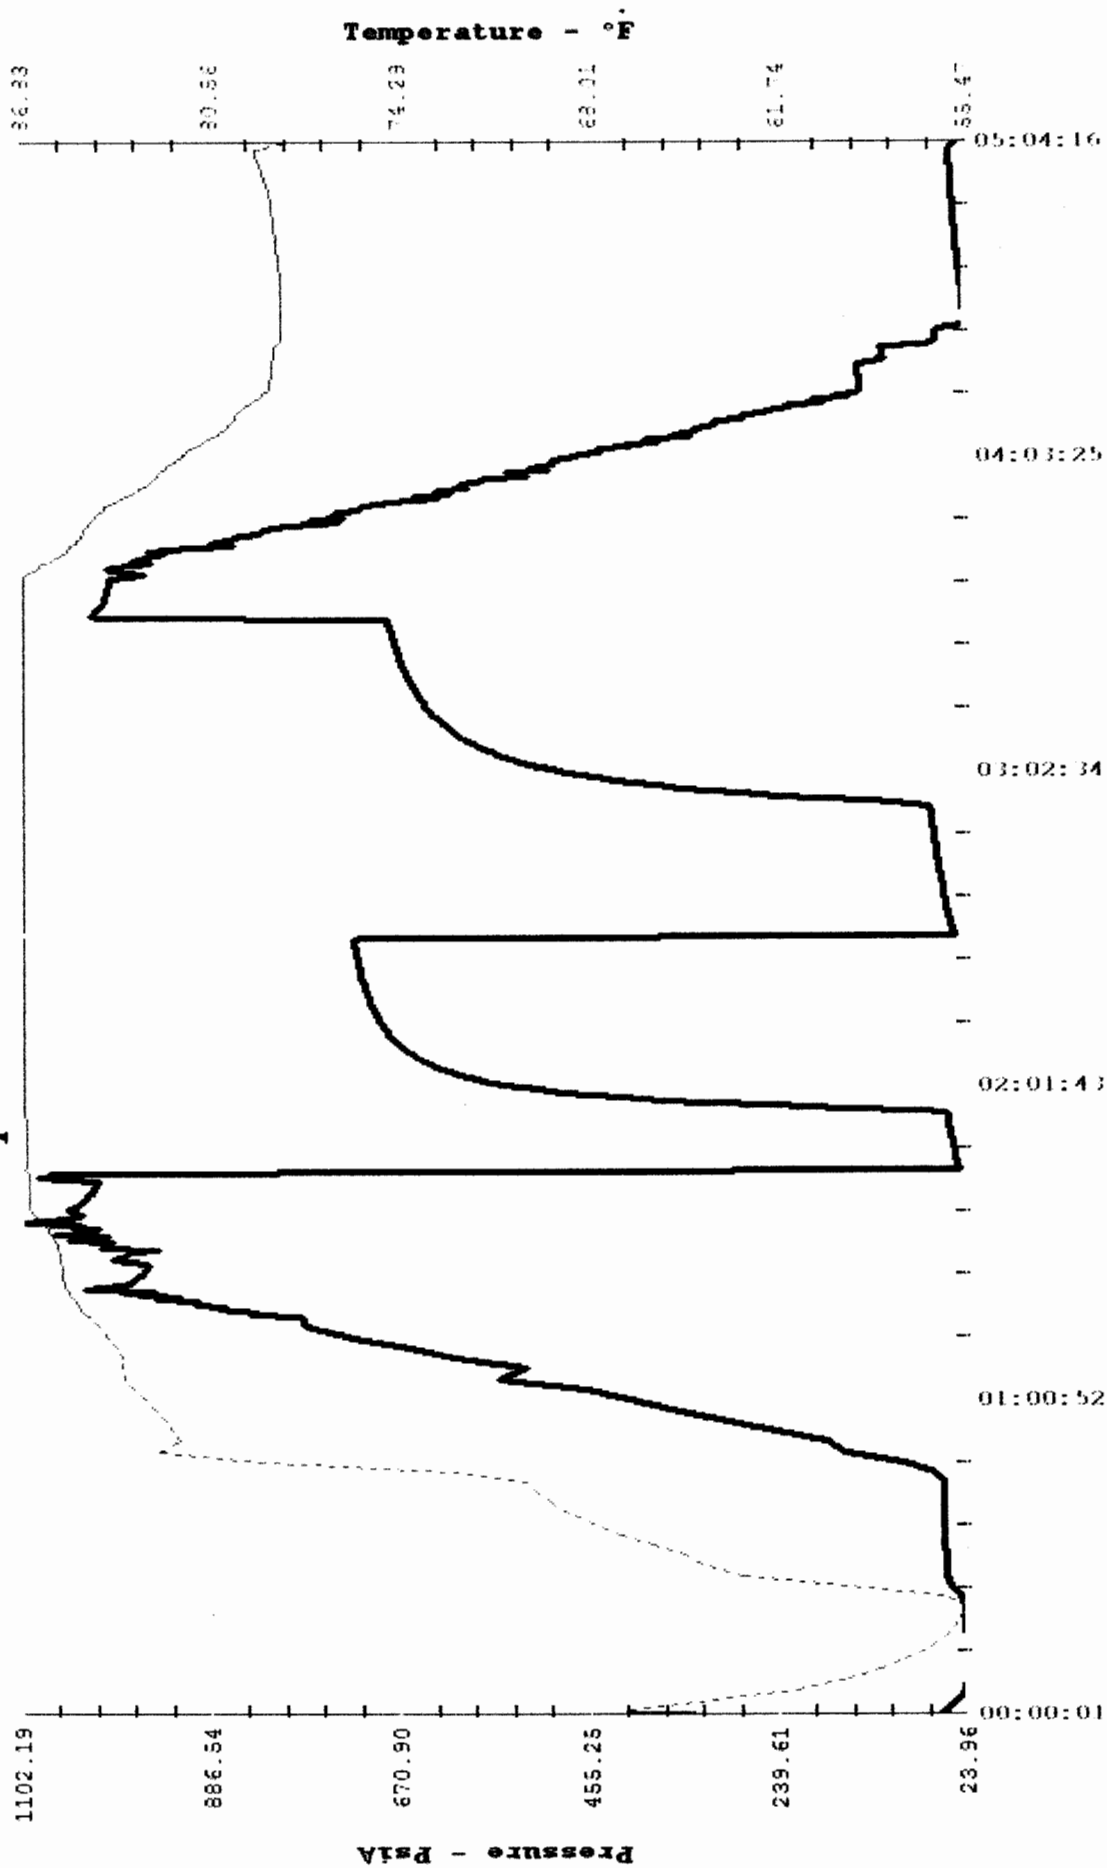

10/06/05

28 30S 14W

TERNES TRUST 1-28

F.G. HOLL LLC

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 10-9-05 Location 28 30 14 Elevation 1873 County Barber

Company F.G. Holl LHC Number of Copies 5

Charts Mailed to 9431 E Central St #100 Wichita KS 67206

Drilling Contractor Bill Ree

Length Drill Pipe 3144 I.D. Drill Pipe 3-8 Tool Joint Size 4 1/2 XH

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 3165 Bottom Packer Depth 3170 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 3170 TO 3200 ANCHOR LENGTH 30 TOTAL DEPTH 3200 Hole Size 7 7/8

LEASE & WELL NO. Ternes Trust 1-28 FORMATION TESTED _____ TEST NO. 2

Mud Weight 8.9 Viscosity 48 Water Loss 122 Chlorides - Pits 5300 D.S.T. _____

Maximum Temp. 86.83 °F Initial Hydrostatic Pressure (A) 1084 P.S.I. Final Hydrostatic Pressure (H) 1011 P.S.I.

Tool Open I.F.P. from 6:50 A to 7:20 m 30 min

Tool Closed I.C.I.P. from 7:20 m to 8:20 m 60 min

Tool Open F.F.P. from 8:20 m to 8:50 m 30 min

Tool Closed F.C.I.P. from 8:50 m to 9:50 m 60 min

Initial Blow Fair Blow, Blaw from Bottom of Bucket in 8 min. 30

Final Blow Fair Blow, 4 inches off Bottom of Bucket in 16 min 30

Total Feet Recovered 45 ft of mud Gravity of Oil _____ Corrected

45 Feet of Mud _____ % Gas 0 % Oil 0 % Mud 100 % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars Yas Safety Joint Yas Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4023 Clock No. Electron-6 Depth 3196 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. 47441 Depth 3197 Insurance _____

Price of Job _____

Tool Operator [Signature]

Approved By _____

No 14636

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.


SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: Lease & Well No. Test #: Date: SEC. TWP. RGE.

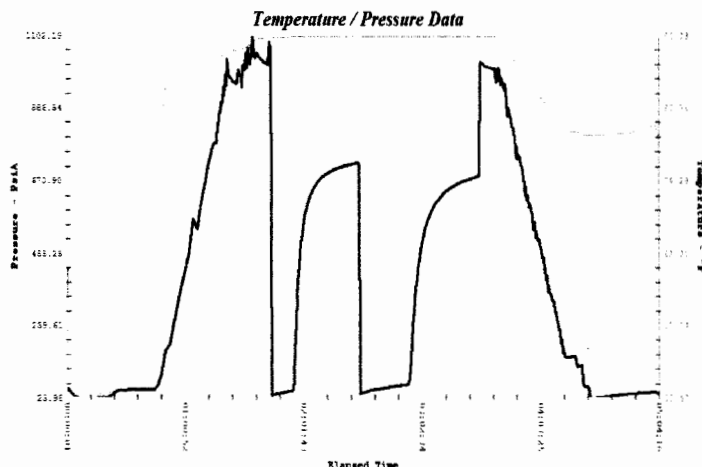

- 1 Initial Hydrostatic Pressure 1084
- 2 Initial Flow Pressure 1070
- 3 Final Initial Flow Pressure 76
- 4 Initial Shut-In Pressure 724
- 5 Initial Final Flow Pressure 716
- 6 Final Flow Pressure 85
- 7 Final Shut-In Pressure 684
- 8 Final Hydrostatic Pressure 1011

Maximum Temperature 86.83

GENERAL INFORMATION

COMPANY NAME F.G. HOLL LLC

TEST DATE 10/9/05

SECTION-TOWN-RANGE 28 30S 14W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1873

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER TERNES TRUST 1-28

FORMATION TESTED TARKEO

DRILL STEM TEST NUMBER 2

REPORT NUMBER 14636

ELEVATION KELLY BUSHINGS 1884

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3170

TEST INTERVAL (to)

ANCHOR LENGTH -3170

TOTAL DEPTH (ft) 3200

TOP PACKER DEPTH 3165

BOTTOM PACKER DEPTH 3170

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 6:50A

INITIAL OPEN TOOL OPEN (to) 7:20A

DURATION (min.) 30MIN

TOOL OPEN (from) --- 8:20A

TOOL OPEN (to) --- 8:50A

DURATION (min.) --- 30MIN

TOOL CLOSED (from) 7:20A

INITIAL SHUT-IN TOOL CLOSED (to) 8:20A

DURATION (min.) 60MIN

TOOL CLOSED (from) --- 8:50A

TOOL CLOSED (to) --- 9:50A

DURATION (min.) --- 60MIN

INITIAL FLOW

FAIR BLOW, BLEW FROM BOTTOM OF BUCKET IN 8MIN 30MIN

FINAL FLOW


FAIR BLOW. BLEW 4 INCHES OFF BOTTOM OF BUCKET IN 16MIN 30MIN

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 45	MUD				
2)					
3)					
4)					
5)					
6)					

GREAT BEND, KANSAS 67530 (800)792-6902

•

Temperature / Pressure Data

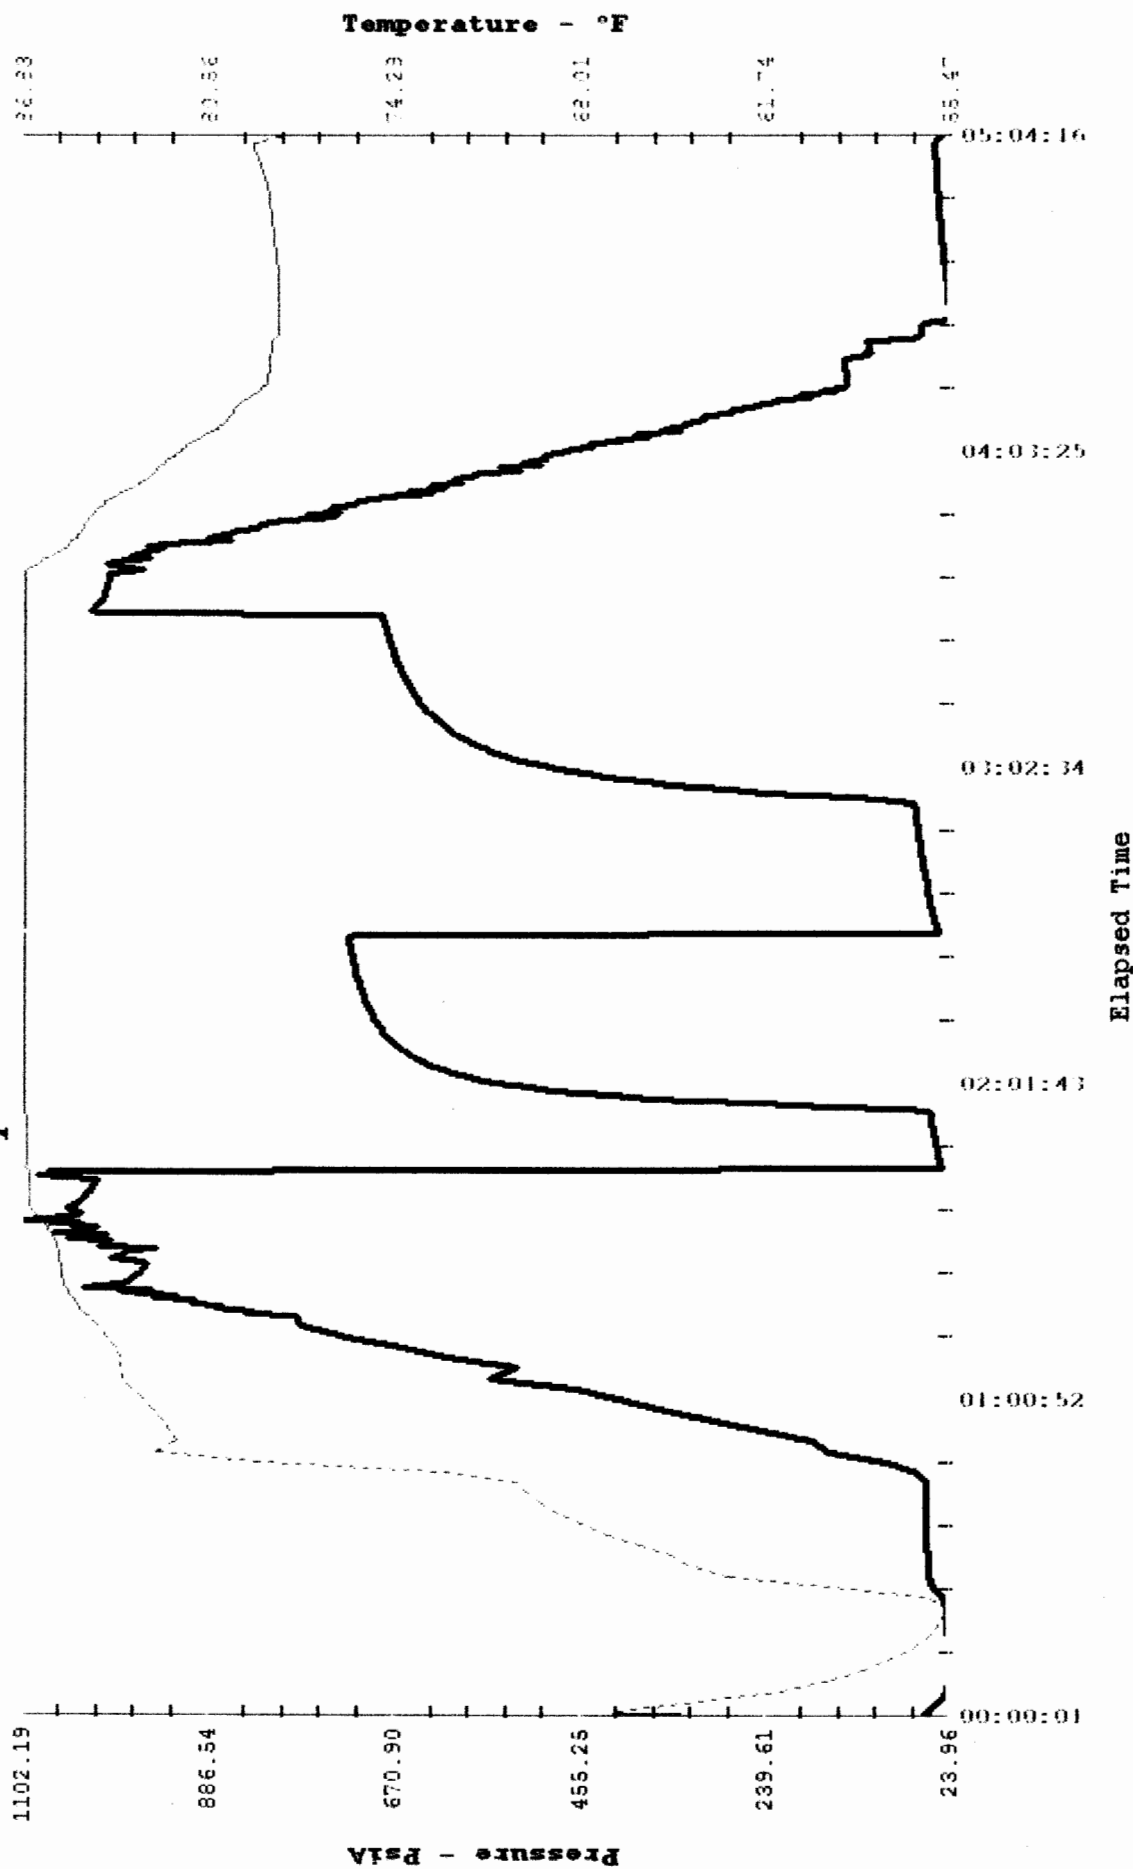

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 10/11/05 Location 28 30 14 Elevation 1873 County BaPher

Company F.G. Holl LLC Number of Copies 5

Charts Mailed to 9431 E Central ST #100 Wich. Taks 67206

Drilling Contractor Bill Ree

Length Drill Pipe 3759 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 X H

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 3780 Bottom Packer Depth 3785 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 3785 TO 3838 ANCHOR LENGTH 53 TOTAL DEPTH 3838 Hole Size 7 7/8

LEASE & WELL NO. Ternes Trust 1-28 FORMATION TESTED Toronto TEST NO. 3

Mud Weight 9.4 Viscosity 48 Water Loss 12.2 Chlorides - Pits 6800 D.S.T. _____

Maximum Temp. 104.92 °F Initial Hydrostatic Pressure (A) 1809.03 P.S.I. Final Hydrostatic Pressure (H) 1716.12 P.S.I.

Tool Open I.F.P. from 4:29 A m to 4:45 m 15 min

Tool Closed I.C.I.P. from 4:45 m to 5:15 m 30 min

Tool Open F.F.P. from 5:15 m to 6:00 m 45 min

Tool Closed F.C.I.P. from 6:00 m to 7:30 m 90 min

Initial Blow Fair Blow, Built To Bottom of Bucket in 12 min 15 min

Final Blow Fair Blow, Built To Bottom of Bucket in 12 min 45 min

Total Feet Recovered 40 FT of Slightly oil cut mud Gravity of Oil _____ Corrected _____

40 Feet of Slightly oil cut mud _____ % Gas _____ % Oil 80 % Mud 20 % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars Yes Safety Joint Yes Extra Packer NO Straddle NO Hook Wall NO

Top Recorder No. 4023 Clock No. ELECT Depth 3834 Cir. Sub _____ Sampler NO

Bottom Recorder No. 3088 Clock No. 47441 Depth 3835 Insurance _____

Price of Job _____

Tool Operator _____

Approved By _____

NO 14637

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.


1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: F.G.HOLL COMPANY L.L.C.

SEC. 28 TWP. 30S RGE. 14W
Lease & Well No. TERNES TRUST #1-28 Test #: 3 Date: 10-11-2005

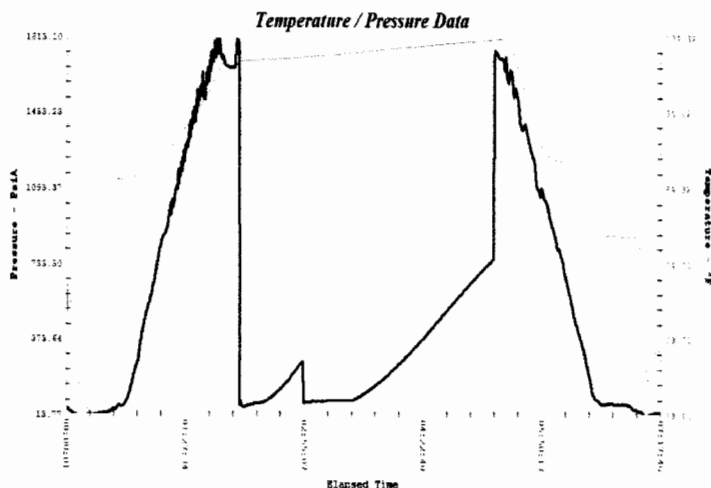

1	Initial Hydrostatic Pressure	1812
2	Initial Flow Pressure	61
3	Final Initial Flow Pressure	77
4	Initial Shut-In Pressure	267
5	Initial Final Flow Pressure	72
6	Final Flow Pressure	138
7	Final Shut-In Pressure	758
8	Final Hydrostatic Pressure	1750

Maximum Temperature 104

GENERAL INFORMATION

COMPANY NAME F.G. HOLL LLC

TEST DATE 10/11/05

SECTION-TOWN-RANGE 28 30 14

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1873

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER TERNES TRUST 1-28

FORMATION TESTED TORONTO

DRILL STEM TEST NUMBER 3

REPORT NUMBER 14637

ELEVATION KELLY BUSHINGS 1884

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3785

TEST INTERVAL (to) 3838

ANCHOR LENGTH 53

TOTAL DEPTH (ft) 3838

TOP PACKER DEPTH 3780

BOTTOM PACKER DEPTH 3785

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 4:30A

INITIAL OPEN

TOOL OPEN (to) 4:45A

FINAL OPEN

TOOL OPEN (from) 5:15

TOOL OPEN (to) 6:00A

DURATION (min.) 15 MIN

DURATION (min.) 45MIN

TOOL CLOSED (from) 4:45A

INITIAL SHUT-IN

TOOL CLOSED (to) 5:15A

FINAL SHUT-IN

TOOL CLOSED (from) 6:00A

TOOL CLOSED (to) 7:30A

DURATION (min.) 30 MIN

DURATION (min.) 90MIN

INITIAL FLOW

FAIR BLOW BUILT TO BOTTOM OF BUCKET IN 12MIN 15MIN

FINAL FLOW

FAIR BLOW BUILT TO BOTTOM OF BUCKET IN 10 MIN 45MIN

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 40	SLIGHTLY OIL CUT MUD			80	20
2)					
3)					
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G. HOLL LLC	LEASE AND WELL NUMBER	TERNES TRUST 1-28
TEST DATE	10/11/05	FORMATION TESTED	TORONTO
SECTION-TOWN-RANGE	28 30 14	DRILL STEM TEST NUMBER	3
STATE	KANSAS	REPORT NUMBER	14637
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1884
ELEVATION GROUND LEVEL	1873	TESTING ENGINEER	JARED SCHECK
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT


JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	184 MILES ROUND TRIP FROM	GREAT BEND KS	
TOP RECORDER DEPTH	3843	BOTTOM RECORDER DEPTH	3844
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG #1	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3759	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.4
WEIGHT PIPE I.D.	2.25	VISCOSITY	48
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	12.2
		CHLORIDES-PITS	6800
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

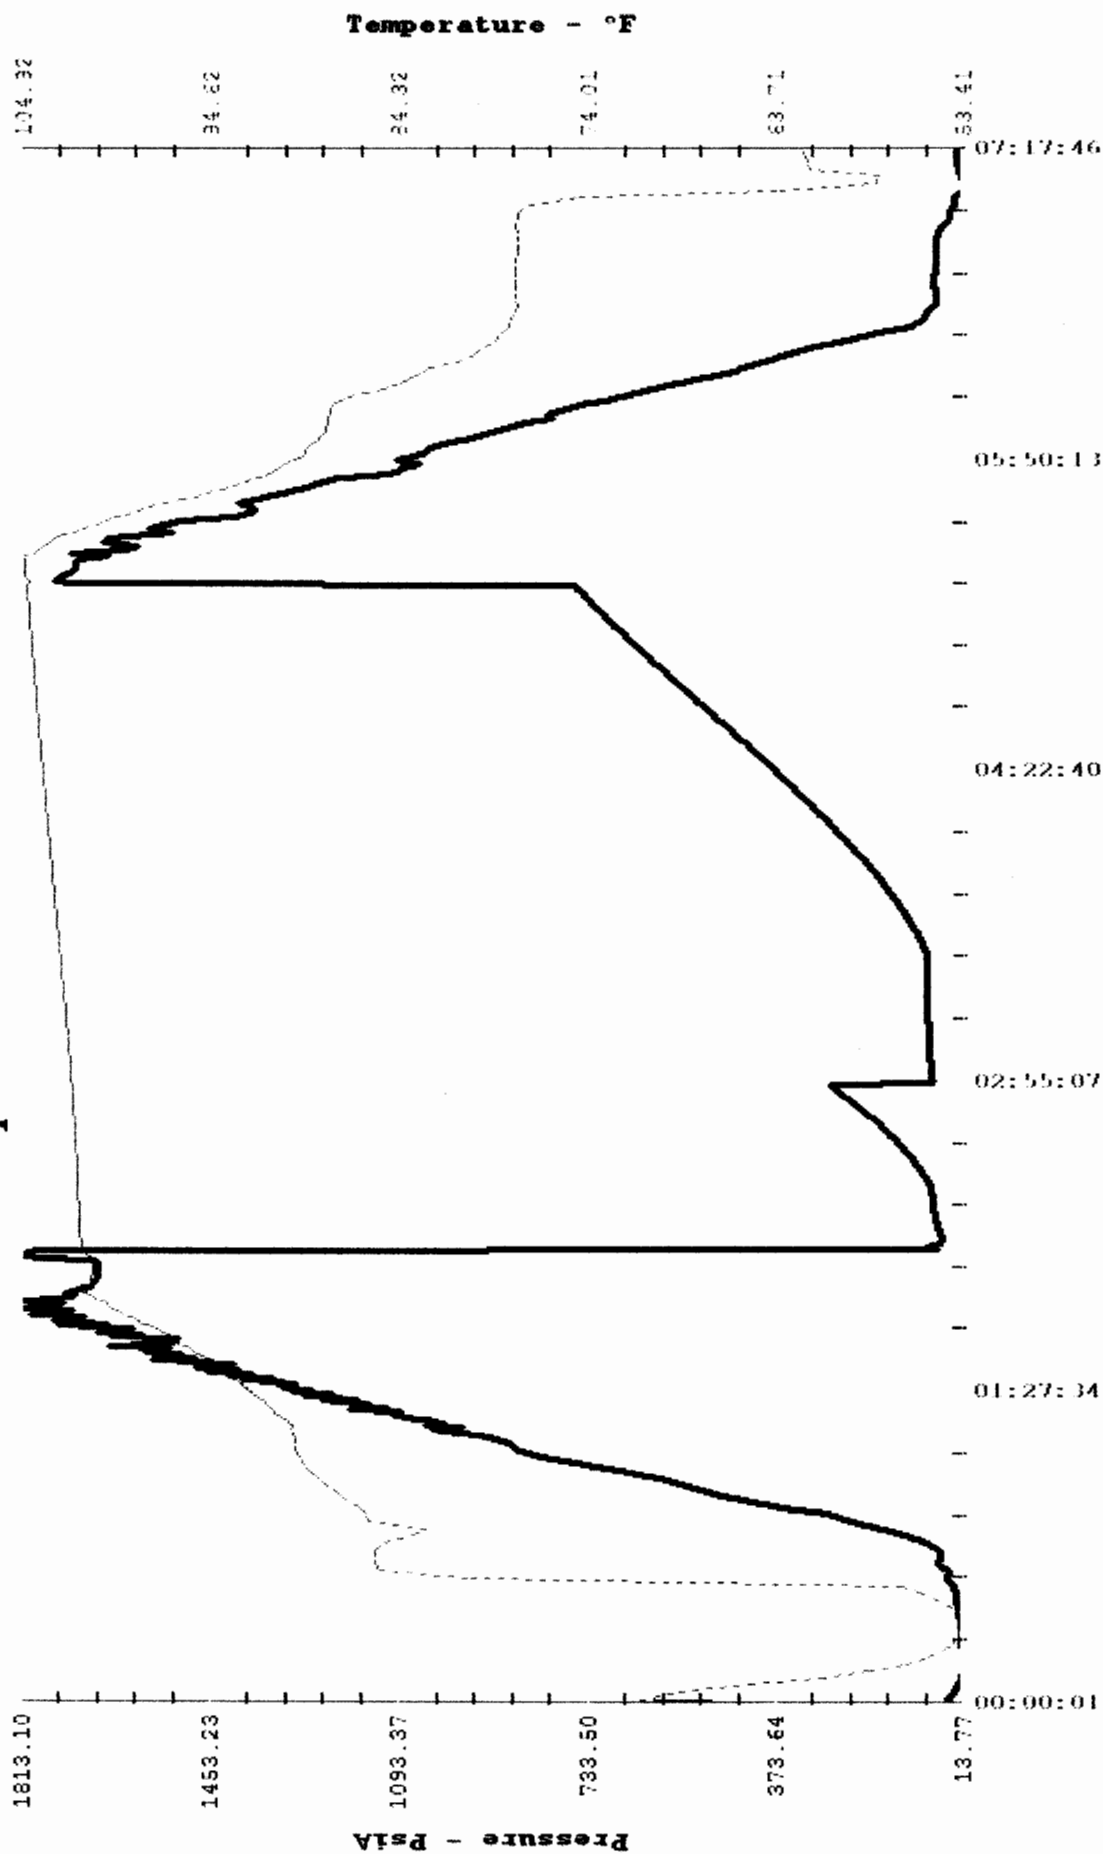

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 10/12/05 Location 28 30s 14w Elevation 1873 County Barber

Company F.G. Holl LLC Number of Copies 5

Charts Mailed to 9431 E Central St #100 Wichita Ks 67206

Drilling Contractor Bill Ree

Length Drill Pipe 3990 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 H

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 4011 Bottom Packer Depth 4016 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 4016 TO 4040 ANCHOR LENGTH 24 TOTAL DEPTH 4040 Hole Size 7 7/8

LEASE & WELL NO. Ternes Trust 1-28 FORMATION TESTED Lansing B TEST NO. 4

Mud Weight 9.2 Viscosity 47 Water Loss 9.6 Chlorides - Pits 5000 D.S.T. _____

Maximum Temp. 109° °F Initial Hydrostatic Pressure (A) 1941 P.S.I. Final Hydrostatic Pressure (H) 1931 P.S.I.

Tool Open I.F.P. from 9:49 A.m. to 9:54 A.m. 5 min

Tool Closed I.C.I.P. from 9:54 A.m. to 6:54 A.m. 60 min

Tool Open F.F.P. from 6:54 A.m. to 7:41 A.m. 45 min

Tool Closed F.C.I.P. from 7:41 m to 9:11 m 90 min

Initial Blow Heavy Blow Blew off Bottom of Bucket in 1min 3min

Final Blow Heavy Blow Blew off The Bottom of Bucket in under 1min 45min

Total Feet Recovered 50ft Gravity of Oil _____ Corrected _____

3000 Feet of Gas in Pipe % Gas _____ % Oil _____ % Mud _____ % Water _____

50 Feet of Gassy Thick heavy mud % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of Fair Show of Oil Between Tools % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars Yes Safety Joint Yes Extra Packer NO Straddle NO Hook Wall _____

Top Recorder No. 4023 Clock No. ELC Depth 4034 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3088 Clock No. _____ Depth 4035 Insurance _____

Price of Job _____

Tool Operator Gerard Ramsey

Approved By _____

No 14638

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.


SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: R.G. HOLL LLC
 Lease & Well No. TERNES TRUST #1-28
 Test #: 4
 Date: 10/12/05
 SEC. 28 TWP. 30S
 RGE. 14W

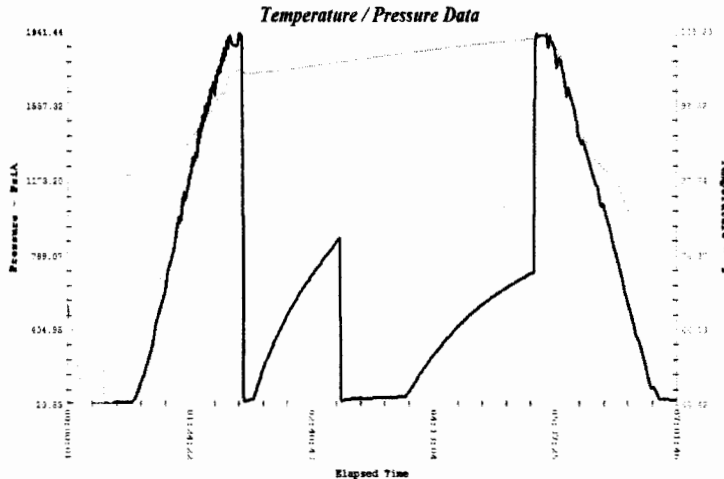

1	Initial Hydrostatic Pressure	1941
2	Initial Flow Pressure	40
3	Final Initial Flow Pressure	51
4	Initial Shut-In Pressure	881
5	Initial Final Flow Pressure	39
6	Final Flow Pressure	64
7	Final Shut-In Pressure	704
8	Final Hydrostatic Pressure	1931

Maximum Temperature 109

GENERAL INFORMATION

COMPANY NAME	 F.G. HOLL LLC	LEASE AND WELL NUMBER	 TERNES TRUST #1-28
TEST DATE	 10/12/05	FORMATION TESTED	 LANSING B
SECTION-TOWN-RANGE	 28 30S 14W	DRILL STEM TEST NUMBER	 4
STATE	 KANSAS	REPORT NUMBER	 14638
COUNTY	 BARBER	ELEVATION KELLY BUSHINGS	 1884
ELEVATION GROUND LEVEL	 1873	TESTING ENGINEER	 LEONARD RAMSEY
COMPANY REPRESENTATIVE	 BILL REE		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	 4016	TOP PACKER DEPTH	 4011
TEST INTERVAL (to)	 4040	BOTTOM PACKER DEPTH	 4016
ANCHOR LENGTH	 24	NUMBER OF PACKERS	 2
TOTAL DEPTH (ft)	 4040	PACKER SIZE	 6 3/4
		HOLE SIZE	 7 7/8

FLOW TIMES

TOOL OPEN (from)	 5:49A	TOOL OPEN (from)	 6:54A
INITIAL OPEN TOOL OPEN (to)	 5:54A	FINAL OPEN TOOL OPEN (to)	 7:41A
DURATION (min.)	 5MIN	DURATION (min.)	 45MIN
TOOL CLOSED (from)	 5:54A	TOOL CLOSED (from)	 7:41A
INITIAL SHUT-IN TOOL CLOSED (to)	 6:54A	FINAL SHUT-IN TOOL CLOSED (to)	 9:11A
DURATION (min.)	 60MIN	DURATION (min.)	 90MIN

INITIAL FLOW

STRIBG BLOW BLEW OFF BOTTOM OF BUCKET IN 1MIN

FINAL FLOW

STRONG BLOW BLEW OFF BOTTOM OF BUCKET IN LESS THAN 1MIN

FEET OF Recovery	RECOVERY DESCRIPTION	% GAS	% OIL	% MUD	% WATER
1) 3000	GAS IN PIPE				
2) 50	GASSY THICK HEAVY MUD				
3)	FAIR SHOW OF OIL BETWEEN TOOLS				
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G. HOLL LLC	LEASE AND WELL NUMBER	TERNES TRUST #1-28
TEST DATE	10/12/05	FORMATION TESTED	LANSING B
SECTION-TOWN-RANGE	28 30S 14W	DRILL STEM TEST NUMBER	4
STATE	KANSAS	REPORT NUMBER	14638
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1884
ELEVATION GROUND LEVEL	1873	TESTING ENGINEER	LEONARD RAMSEY
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT


JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	184 MILES ROUND TRIP FROM	GREAT BEND KS	
TOP RECORDER DEPTH	4034	BOTTOM RECORDER DEPTH	4035
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING #1	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	3990	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.2
WEIGHT PIPE I.D.	2.25	VISCOSITY	47
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	9.6
		CHLORIDES-PITS	5000
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

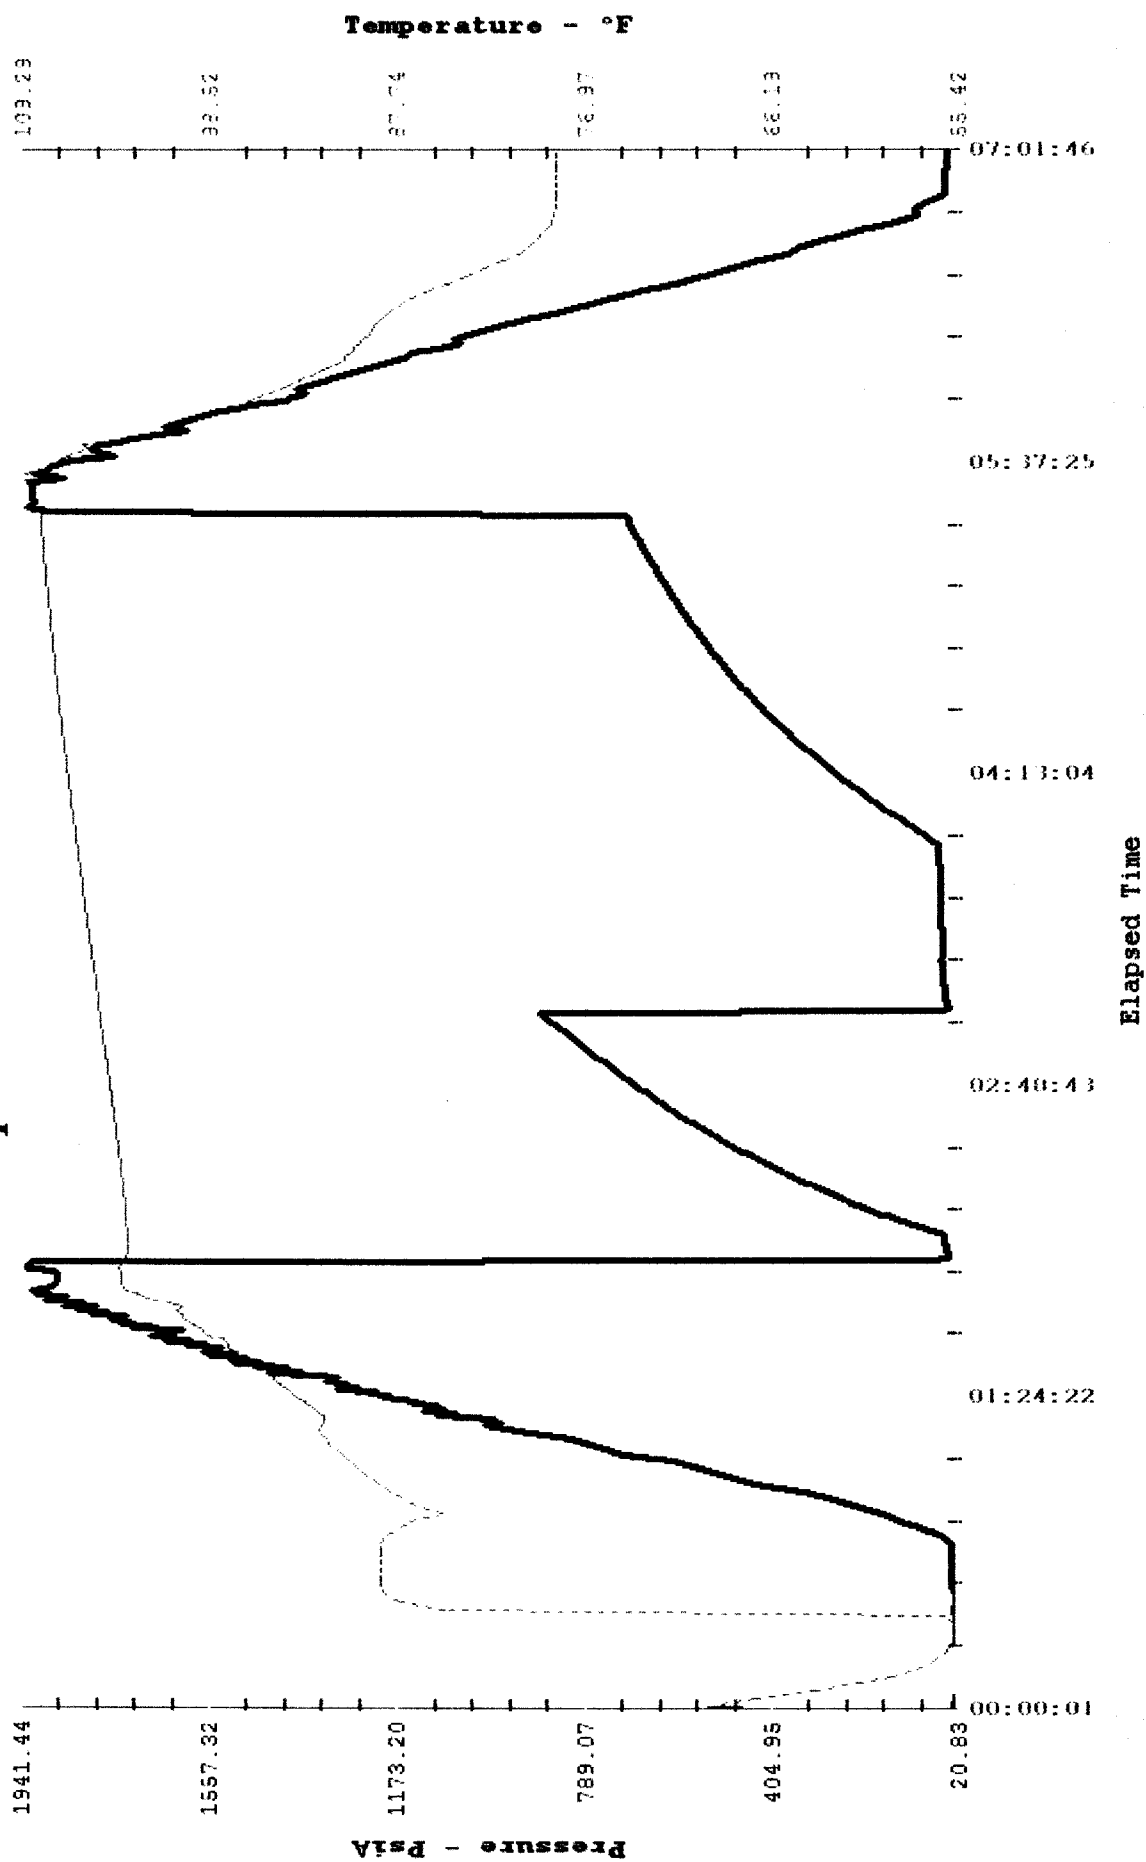

F.G. HOLL TERNES TRUST #1-28 28 30S 14W 10/12/05

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 10/12/05 Location 28 30s 14w Elevation 1873 County Barber

Company R.G. HOll LLC Number of Copies 5

Charts Mailed to 9431 E Central ST #100 Wichita Ks 67206

Drilling Contractor Bill Rec

Length Drill Pipe 4020 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 x 14

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 4041 Bottom Packer Depth 4046 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 4046 TO 4093 ANCHOR LENGTH 47 TOTAL DEPTH 4093 Hole Size 7 7/8

LEASE & WELL NO. Ternes Trust 1-28 FORMATION TESTED _____ TEST NO. 5

Mud Weight 9.1 Viscosity 45 Water Loss 8.8 Chlorides - Pits 5500 D.S.T. _____

Maximum Temp. 112 °F Initial Hydrostatic Pressure (A) 1946 P.S.I. Final Hydrostatic Pressure (H) 1935 P.S.I.

Tool Open I.F.P. from 12:15 m to 12:45 m 30 min

Tool Closed I.C.I.P. from 12:45 m to 1:45 m 60 min

Tool Open F.F.P. from 1:45 m to 2:30 m 45 min

Tool Closed F.C.I.P. from 2:30 m to 4:00 m 90 min

Initial Blow Strong Blow Blew off Bottom of Bucket in 9 min 30 min

Final Blow Strong Blow Blew off Bottom of Bucket in 10 min 45 min

Total Feet Recovered 110 Gravity of Oil _____ Corrected

110 Feet of Mud % Gas _____ % Oil X % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars Yes Safety Joint Yes Extra Packer NO Straddle NO Hook Wall NO

Top Recorder No. 4023 Clock No. Elec Depth 4089 Cir. Sub _____ Sampler NO

Bottom Recorder No. 3088 Clock No. 47441 Depth 4090 Insurance _____

Price of Job Guaranteed Ramsey

Tool Operator _____

Approved By _____

NO 14639

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530


Company: F.G. HOLL LLC
RGE. 14W

Lease & Well No. TERNES TRUST #1-28

Test #: 5 Date: 10/12/05

SEC. 28 TWP. 30S

Temperature / Pressure Data

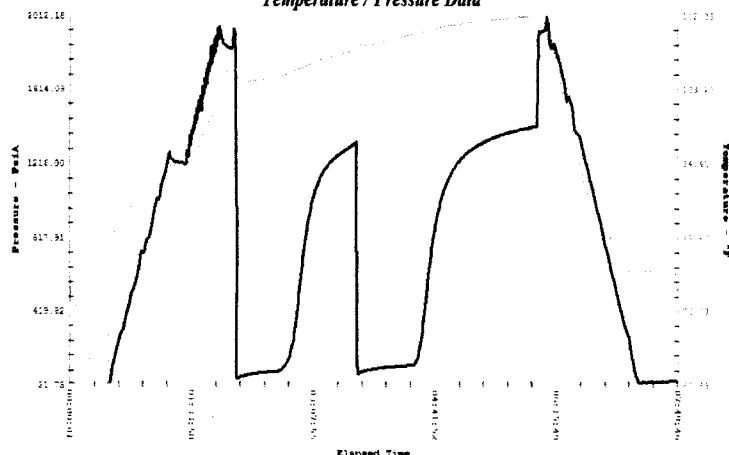

- 1 Initial Hydrostatic Pressure 1946
- 2 Initial Flow Pressure 68
- 3 Final Initial Flow Pressure 67
- 4 Initial Shut-In Pressure 1330
- 5 Initial Final Flow Pressure 160
- 6 Final Flow Pressure 143
- 7 Final Shut-In Pressure 1418
- 8 Final Hydrostatic Pressure

Maximum Temperature 112

GENERAL INFORMATION

COMPANY NAME F.G. HOLL LLC

TEST DATE 10/12/05

SECTION-TOWN-RANGE 28 30S 14W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1873

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER TERNES TRUST 1-28

FORMATION TESTED

DRILL STEM TEST NUMBER 5

REPORT NUMBER 14639

ELEVATION KELLY BUSHINGS 1884

TESTING ENGINEER LEONARD RAMSEY

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4046

TEST INTERVAL (to) 4093

ANCHOR LENGTH 47

TOTAL DEPTH (ft) 4093

TOP PACKER DEPTH 4041

BOTTOM PACKER DEPTH 4046

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 12:15

INITIAL OPEN TOOL OPEN (to) 12:45A

DURATION (min.) 30MIN

TOOL OPEN (from) 1:45A

FINAL OPEN TOOL OPEN (to) 2:30A

DURATION (min.) 45MIN

TOOL CLOSED (from) 12:45A

INITIAL SHUT-IN TOOL CLOSED (to) 1:45A

DURATION (min.) 60MIN

TOOL CLOSED (from) 2:30A

FINAL SHUT-IN TOOL CLOSED (to) 4:00A

DURATION (min.) 90MIN

INITIAL FLOW

STRONG BLOW BLEW OFF BOTTOM OF BUCKET IN 9MIN 30MIN

FINAL FLOW

STRONG BLOW BLEW OFF THE BOTTOM OF BUCKET IN 10MIN 45MIN

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 110	MUD			100	
2)					
3)					
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G. HOLL LLC	LEASE AND WELL NUMBER	TERNES TRUST 1-28
TEST DATE	10/12/05	FORMATION TESTED	
SECTION-TOWN-RANGE	28 30S 14W	DRILL STEM TEST NUMBER	5
STATE	KANSAS	REPORT NUMBER	14639
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1884
ELEVATION GROUND LEVEL	1873	TESTING ENGINEER	LEONARD RAMSEY
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT


JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	184 MILES ROUND TRIP FROM	SAMPLER	NO
	GREAT BEND KS		
TOP RECORDER DEPTH	4089	BOTTOM RECORDER DEPTH	4090
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG#1	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	4020	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.1
WEIGHT PIPE I.D.	2.25	VISCOSITY	45
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	5500
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

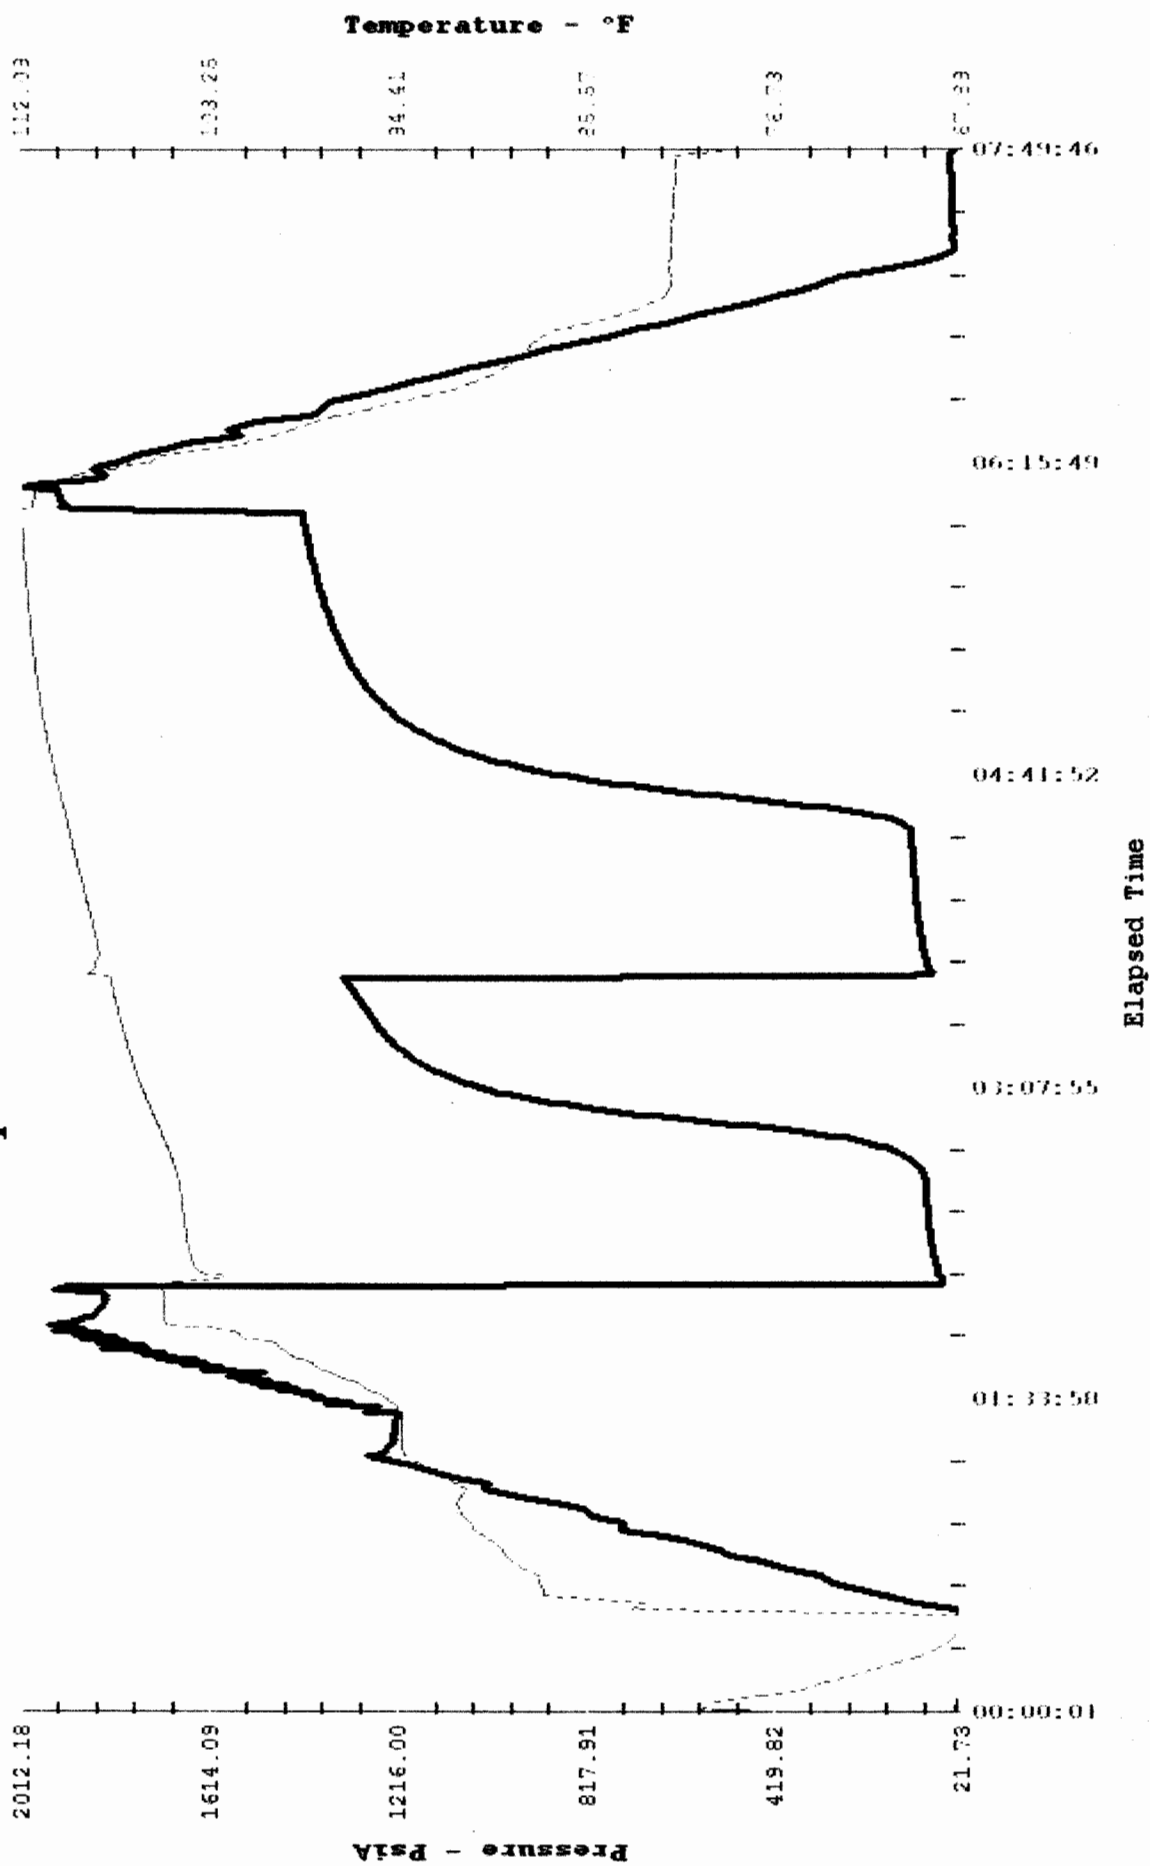

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 10/13/05 Location 28 30s 14w Elevation 1873 County Barber
Company E.G. Hall LLC. Number of Copies 5

Charts Mailed to 9431 E Central St #100 Wichita KS 67206

Drilling Contractor Bill Ree

Length Drill Pipe 4131 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 X H

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 4152 Bottom Packer Depth 4157 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 4157 TO 4174 ANCHOR LENGTH 17 TOTAL DEPTH 4174 Hole Size 7 7/8

LEASE & WELL NO. Tennet Trust #1-28 FORMATION TESTED Lansing H TEST NO. 6

Mud Weight 9.1 Viscosity 54 Water Loss 8.8 Chlorides - Pits 4,500 D.S.T. _____

Maximum Temp. 110 °F Initial Hydrostatic Pressure (A) 2077 P.S.I. Final Hydrostatic Pressure (H) 2063 P.S.I.

Tool Open I.F.P. from 5:25 p.m. to 5:30 p.m. 5 min

Tool Closed I.C.I.P. from 5:30 m to 6:30 m 60 min

Tool Open F.F.P. from 6:30 m to 7:30 m 60 min

Tool Closed F.C.I.P. from 7:30 m to 9:00 m 90 min

from [B] <u>137</u>	P.S.I. to [C] <u>62</u>	P.S.I.
[D] <u>1564</u>		P.S.I.
from [E] <u>60</u>	P.S.I. to [F] <u>59</u>	P.S.I.
[G] <u>1494</u>		P.S.I.

Initial Blow Strong Blow, Blow from Bottom of Bucket in under 1 min 5 min

Final Blow Strong Blow, Blow from Bottom of Bucket right at opening 10 min

Total Feet Recovered 50 ft gassy mud Gravity of Oil _____ Corrected _____

50 Feet of gassy mud % Gas _____ % Oil X % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars Yes Safety Joint Yes Extra Packer NO Straddle NO Hook Wall NO

Top Recorder No. 4023 Clock No. Electronic Depth 4070 Cir. Sub _____ Sampler NO

Bottom Recorder No. 3088 Clock No. 47441 Depth 4071 Insurance _____

Price of Job _____

Tool Operator Geonard Ramsey

Approved By _____

No 14640


Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

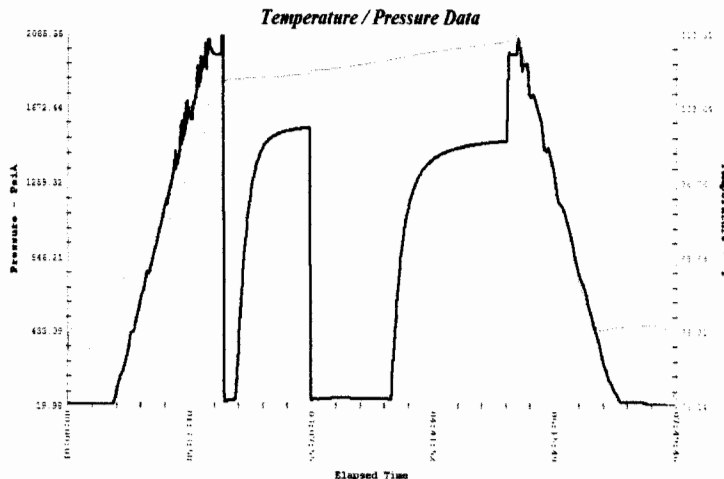

1	Initial Hydrostatic Pressure	2077
2	Initial Flow Pressure	137
3	Final Initial Flow Pressure	62
4	Initial Shut-In Pressure	1564
5	Initial Final Flow Pressure	60
6	Final Flow Pressure	59
7	Final Shut-In Pressure	1494
8	Final Hydrostatic Pressure	2063

Maximum Temperature 110

GENERAL INFORMATION

COMPANY NAME	 F.G. HOLL LLC	LEASE AND WELL NUMBER	 TERNES TRUST #1-28
TEST DATE	 10/13/05	FORMATION TESTED	 LANSING H
SECTION-TOWN-RANGE	 28 30S 14W	DRILL STEM TEST NUMBER	 6
STATE	 KANSAS	REPORT NUMBER	 14640
COUNTY	 BARBER	ELEVATION KELLY BUSHINGS	 1884
ELEVATION GROUND LEVEL	 1873	TESTING ENGINEER	 LEONARD RAMSEY
COMPANY REPRESENTATIVE	 BILL REE		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	__ 4157	TOP PACKER DEPTH	-- 4152
TEST INTERVAL (to)	__ 4174	BOTTOM PACKER DEPTH	-- 4157
ANCHOR LENGTH	__ 17	NUMBER OF PACKERS	 2
TOTAL DEPTH (ft)	__ 4174	PACKER SIZE	 6 3/4
		HOLE SIZE	 7 7/8

FLOW TIMES

TOOL OPEN (from)	 5:25 PM	TOOL OPEN (from)	 6:30
INITIAL OPEN TOOL OPEN (to)	 5:30P	FINAL OPEN TOOL OPEN (to)	 7:30P
DURATION (min.)	 5MIN	DURATION (min.)	 60MIN
TOOL CLOSED (from)	 5:30	TOOL CLOSED (from)	 7:30
INITIAL SHUT-IN TOOL CLOSED (to)	 6:30P	FINAL SHUT-IN TOOL CLOSED (to)	 9:00P
DURATION (min.)	 60MIN	DURATION (min.)	 90MIN

INITIAL FLOW

STRONG BLOW BLEW FROM BOTTOM OF BUCKET IN 1 MIN 5MIN

FINAL FLOW

STRONG BLOW BLEW FROM BOTTOM OF BUCKET IN UNDER 1MIN 60MIN

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 50	GASSY MUD				
2)					
3)					
4)					
5)					
6)					

Company: F.G. HOLL LLC

Lease & Well No. TERNES TRUST #1-28

Test #: 6 Date: 10/13/05

SEC. 28 TWP. 30S RGE. 14W

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G. HOLL LLC	LEASE AND WELL NUMBER	TERNES TRUST #1-28
TEST DATE	10/13/05	FORMATION TESTED	LANSING H
SECTION-TOWN-RANGE	28 30S 14W	DRILL STEM TEST NUMBER	6
STATE	KANSAS	REPORT NUMBER	14640
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1884
ELEVATION GROUND LEVEL	1873	TESTING ENGINEER	LEONARD RAMSEY
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT

JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	184 MILES ROUND TRIP FROM	SAMPLER	NO
	GREAT BEND KS		
TOP RECORDER DEPTH	4070	BOTTOM RECORDER DEPTH	4071
RECORDER NUMBER	91981	RECORDER NUMBER	5463


WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG #1	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	4131	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.1
WEIGHT PIPE I.D.	2.25	VISCOSITY	54
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	4500
		CHLORIDES-DST	

COMMENTS

THERE WAS A GAS SAMPLE TAKEN

Temperature / Pressure Data

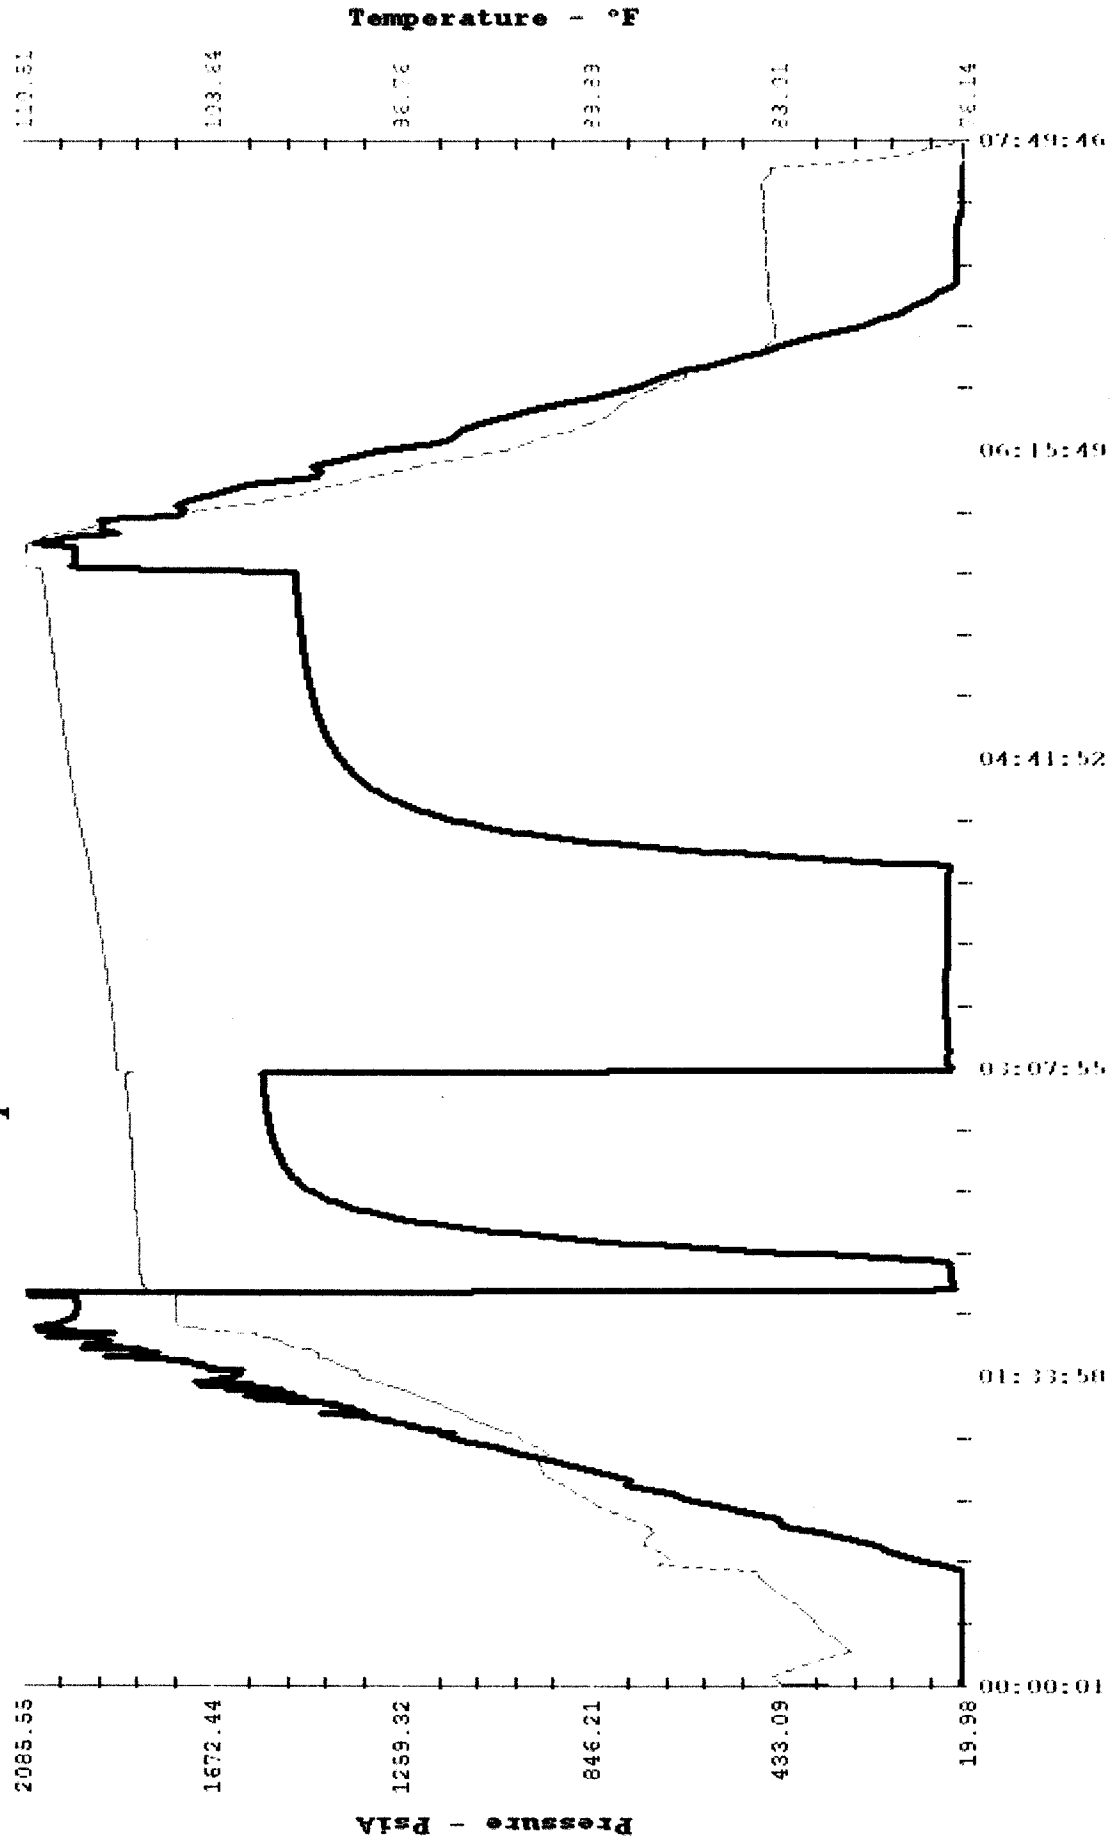

103250

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 10-15-05 Location 28 30s 14w Elevation 1873 County BarberCompany R.G. Hall LLC Number of Copies 5Charts Mailed to 9431 E Central #100 Wichita Ks 67206Drilling Contractor Bill ReeLength Drill Pipe 4388 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 x H

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 4409 Bottom Packer Depth 4414 Number of Packers 2 Packer Size 6 3/4TESTED FROM 4414 TO 4525 ANCHOR LENGTH 111 TOTAL DEPTH 4525 Hole Size 7 7/8LEASE & WELL NO. Jernes Trust 1-28 FORMATION TESTED Viola TEST NO. 7Mud Weight 9.2 Viscosity 54 Water Loss 8.8 Chlorides - Pits 7,000 D.S.T. _____Maximum Temp. 117 °F Initial Hydrostatic Pressure (A) 2345 P.S.I. Final Hydrostatic Pressure (H) 2252 P.S.I.Tool Open I.F.P. from 9:15 m to 9:45 m 30 minTool Closed I.C.I.P. from 9:45 m to 10:45 m 60 minTool Open F.F.P. from 10:45 m to 11:45 m 60 minTool Closed F.C.I.P. from 11:45 m to 1:15 m 90 minInitial Blow Fair Surface Blow, Blew off Bottom of Bucket in 20 minFinal Blow Fair Surface Blow, Blew off Bottom of Bucket in 2 minTotal Feet Recovered 45 Fr mud Gravity of Oil _____ Corrected25 Feet of Slightly gassy mud % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of Packer Torn and replaced % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars Yes Safety Joint Yes Extra Packer NO Straddle NO Hook Wall NOTop Recorder No. 4023 Clock No. Electric Depth 4521 Cir. Sub _____ Sampler NOBottom Recorder No. 3088 Clock No. 47441 Depth 4522 Insurance _____

Price of Job _____

Tool Operator Edward Ramsey

Approved By _____

Nº 14641

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.


SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: F.G. HOLL LLC
 Lease & Well No. TERNES TRUST 1-28
 Test #: 7
 Date: 10/15/05
 SEC. 28 TWP. 30S
 RGE. 14W

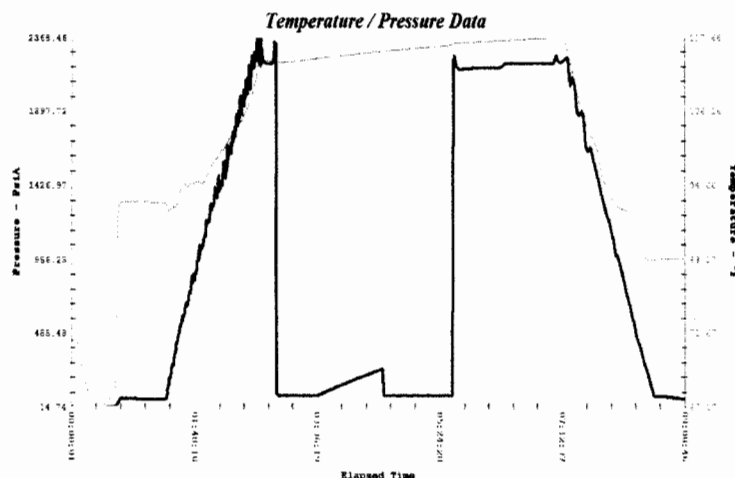

1	Initial Hydrostatic Pressure	2345
2	Initial Flow Pressure	88
3	Final Initial Flow Pressure	98
4	Initial Shut-In Pressure	255
5	Initial Final Flow Pressure	89
6	Final Flow Pressure	91
7	Final Shut-In Pressure	2205
8	Final Hydrostatic Pressure	2252

Maximum Temperature 117

GENERAL INFORMATION

COMPANY NAME	F.G. HOLL LLC	LEASE AND WELL NUMBER	TERNES TRUST 1-28
TEST DATE	10/15/05	FORMATION TESTED	VIOLA
SECTION-TOWN-RANGE	28 30S 14W	DRILL STEM TEST NUMBER	7
STATE	KANSAS	REPORT NUMBER	1461
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1884
ELEVATION GROUND LEVEL	1873	TESTING ENGINEER	LEONARD RAMSEY
COMPANY REPRESENTATIVE	BILL REE		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	4414	TOP PACKER DEPTH	4409
TEST INTERVAL (to)	4525	BOTTOM PACKER DEPTH	4414
ANCHOR LENGTH	111	NUMBER OF PACKERS	2
TOTAL DEPTH (ft)	4525	PACKER SIZE	6 3/4
		HOLE SIZE	7 7/8

FLOW TIMES

TOOL OPEN (from)	9:15A	TOOL OPEN (from)	10:45
INITIAL OPEN TOOL OPEN (to)	9:45A	FINAL OPEN TOOL OPEN (to)	11:45A
DURATION (min.)	30MIN	DURATION (min.)	60MIN
TOOL CLOSED (from)	9:45A	TOOL CLOSED (from)	11:45A
INITIAL SHUT-IN TOOL CLOSED (to)	10:45A	FINAL SHUT-IN TOOL CLOSED (to)	1:15P
DURATION (min.)	60MIN	DURATION (min.)	90MIN

INITIAL FLOW FAIR BLOW BLEW OFF BOTTOM OF THE BUCKET IN 20 MIN 30MIN

FINAL FLOW FAIR BLOW BLEW OFF BOTTOM OF THE BUCKET IN 2MIN 60MIN

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 45	SLIGHTLY GASSY MUD				
2)					
3)					
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G. HOLL LLC	LEASE AND WELL NUMBER	TERNES TRUST 1-28
TEST DATE	10/15/05	FORMATION TESTED	VIOLA
SECTION-TOWN-RANGE	28 30S 14W	DRILL STEM TEST NUMBER	7
STATE	KANSAS	REPORT NUMBER	1461
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1884
ELEVATION GROUND LEVEL	1873	TESTING ENGINEER	LEONARD RAMSEY
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT

JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	184 MILES ROUND TRIP FROM		
TOP RECORDER DEPTH	4521	GREAT BEND KS	
RECORDER NUMBER	91981	BOTTOM RECORDER DEPTH	4522
		RECORDER NUMBER	5463


WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG #1	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	4388	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.2
WEIGHT PIPE I.D.	2.25	VISCOSITY	54
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	7000
		CHLORIDES-DST	

COMMENTS

PACKER TORN AND REPLACED

Temperature / Pressure Data

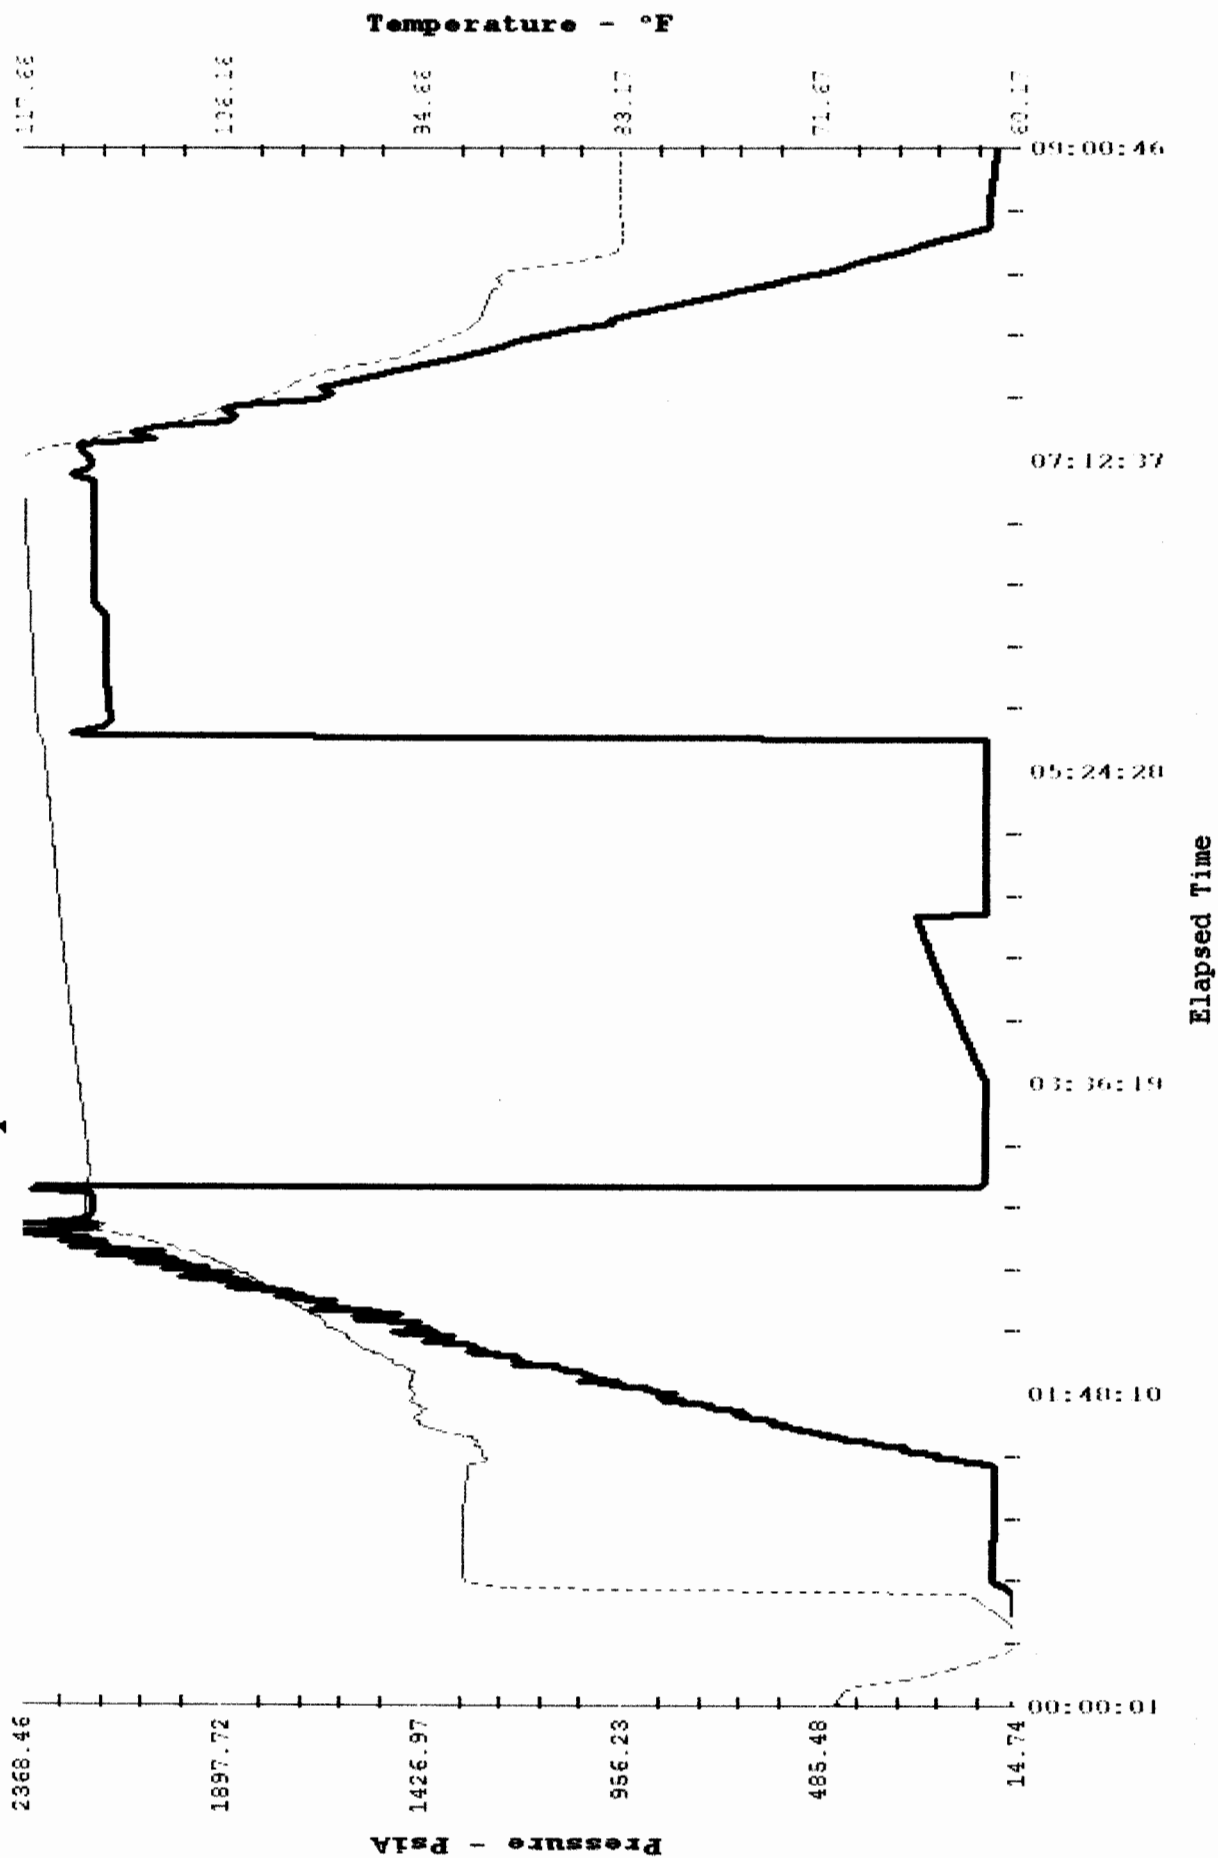

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 10/16/11 Location 28 30 Elevation 1418 1873 County Barber

Company F.G. Hall LLC Number of Copies 5

Charts Mailed to 9031 Central # 100 Wichita KS 67204

Drilling Contractor Bill Rice

Length Drill Pipe 4502 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 x 11

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 4528 Bottom Packer Depth 4528 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 4528 TO 4545 ANCHOR LENGTH 17 TOTAL DEPTH 4545 Hole Size 7 7/8

LEASE & WELL NO. Texas Gulf 1-28 FORMATION TESTED Simpson TEST NO. 8

Mud Weight 9.5 Viscosity 42 Water Loss 10.4 Chlorides - Pits 7000 D.S.T. _____

Maximum Temp. 122 °F Initial Hydrostatic Pressure (A) 2292 P.S.I. Final Hydrostatic Pressure (H) 2237 P.S.I.

Tool Open I.F.P. from 5:25 to 5:30 m 5 min

Tool Closed I.C.I.P. from 5:30 to 6:30 m 60 min

Tool Open F.F.P. from 6:30 to 7:30 m 60 min

Tool Closed F.C.I.P. from 7:30 to 9:00 m 90 min

Initial Blow Strong Blow, Blw off BUT in 1st Bucket, 1st 2nd

Final Blow Strong blow, through out 2nd opening

Total Feet Recovered 270 feet 270 Gravity of Oil _____ Corrected _____

30 Feet of Mud % Gas _____ % Oil _____ % Mud _____ % Water _____

60 Feet of Slightly water cut mud % Gas _____ % Oil _____ % Mud _____ % Water _____

180 Feet of Salt Water % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars YES Safety Joint YES Extra Packer NO Straddle NO Hook Wall NO

Top Recorder No. 4023 Clock No. EVCT Depth 4499 Cir. Sub NO Sampler NO

Bottom Recorder No. 3088 Clock No. 47441 Depth 4500 Insurance _____

Price of Job _____

Tool Operator James Farnsworth

Approved By _____

NO 14642

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT


GREAT BEND, KANSAS 67530

Company: F.G. HOLL LLC

Lease & Well No. TERNES TRUST #1-28

Test #: 8 Date: 10/16/05

SEC. 28 TWP. 30S RGE. 14W

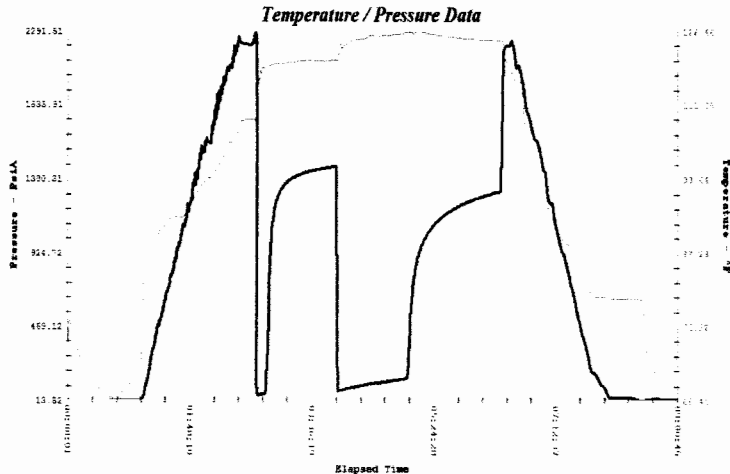

1	Initial Hydrostatic Pressure	2292
2	Initial Flow Pressure	50
3	Final Initial Flow Pressure	61
4	Initial Shut-In Pressure	1460
5	Initial Final Flow Pressure	79
6	Final Flow Pressure	150
7	Final Shut-In Pressure	1309
8	Final Hydrostatic Pressure	2237

Maximum Temperature 122

GENERAL INFORMATION

COMPANY NAME F.G. HOLL LLC

TEST DATE 10/16/05

SECTION-TOWN-RANGE 28 30S 14W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1873

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER TERNES TRUST #1-28

FORMATION TESTED SIMPSON SAND

DRILL STEM TEST NUMBER 8

REPORT NUMBER 14642

ELEVATION KELLY BUSHINGS 1884

TESTING ENGINEER LEONARD RAMSEY

TOOL SETTING INFORMATION

TEST INTERVAL (From) __ 4528

TEST INTERVAL (to) __ 4545

ANCHOR LENGTH __ 17

TOTAL DEPTH (ft) __ 4545

TOP PACKER DEPTH -- 4524

BOTTOM PACKER DEPTH -- 4528

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 5:25 PM

INITIAL OPEN TOOL OPEN (to) 5:30P

DURATION (min.) 5MIN

TOOL CLOSED (from) 5:30

INITIAL SHUT-IN TOOL CLOSED (to) 6:30P

DURATION (min.) 60MIN

TOOL OPEN (from) 6:30

TOOL OPEN (to) 7:30P

DURATION (min.) 60MIN

TOOL CLOSED (from) 7:30

TOOL CLOSED (to) 9:00P

DURATION (min.) 90MIN

INITIAL FLOW

STRONG BLOW BLEW FROM BOTTOM OF BUCKET IN 1 MIN 5MIN

FINAL FLOW

STRONG BLOW BLEW FROM BOTTOM OF BUCKET IN UNDER 1MIN 60MIN

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 30	MUD				
2) 60	SLIGHTLY WATER CUT MUD				
3) 180	SALTWATER				
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G. HOLL LLC	LEASE AND WELL NUMBER	TERNES TRUST #1-28
TEST DATE	10/15/05	FORMATION TESTED	SIMPSON SAND
SECTION-TOWN-RANGE	28 30S 14W	DRILL STEM TEST NUMBER	8
STATE	KANSAS	REPORT NUMBER	14642
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1884
ELEVATION GROUND LEVEL	1873	TESTING ENGINEER	LEONARD RAMSEY
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT


JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	184 MILES ROUND TRIP FROM	SAMPLER	NO
	GREAT BEND KS		
TOP RECORDER DEPTH	4499	BOTTOM RECORDER DEPTH	4500
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG #1	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	4502	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.5
WEIGHT PIPE I.D.	2.25	VISCOSITY	42
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	10.4
		CHLORIDES-PITS	7000
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

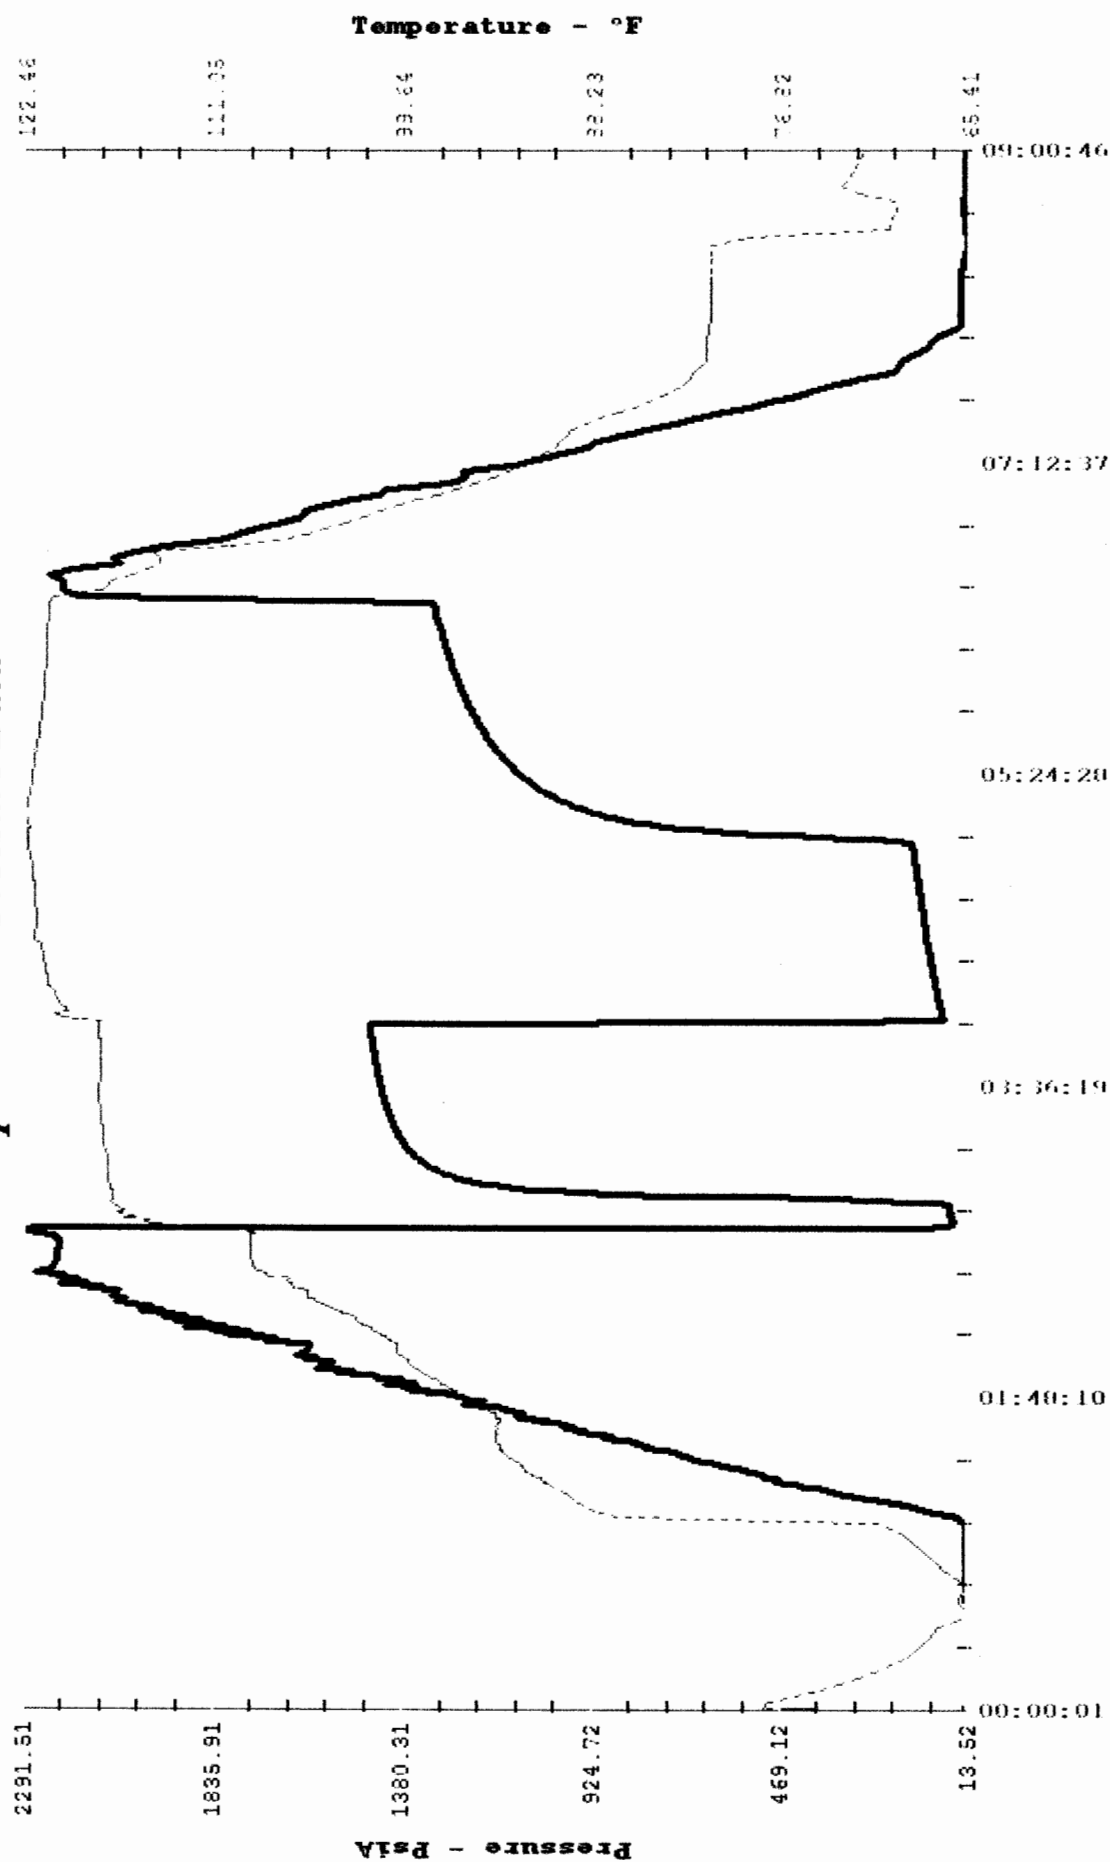

F.G. HOLL LLC TERNESTRUST#1-28 28 30S 14W 10/1:16/05

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 10/16/05 Location 28 30w 14s Elevation 1873 County Barber

Company E.G. Hall LLC Number of Copies 5

Charts Mailed to 9431 Central #100 Wichita KS 67206

Drilling Contractor Duke Drilling & P.

Length Drill Pipe 4520 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 X H

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 4541 Bottom Packer Depth 4546 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 4546 TO 4567 ANCHOR LENGTH 21 TOTAL DEPTH 4567 Hole Size _____

LEASE & WELL NO. Ternes Trust 1-28 FORMATION TESTED Simpson TEST NO. 9

Mud Weight 9.4 Viscosity 51 Water Loss 9.6 Chlorides - Pits 5000 D.S.T. 63,000

Maximum Temp. 120 °F Initial Hydrostatic Pressure (A) 2259 P.S.I. Final Hydrostatic Pressure (H) 2193 P.S.I.

Tool Open I.F.P. from 10:00 m to 10:05 m 5 min

Tool Closed I.C.I.P. from 10:05 m to 11:20 m 75 min

Tool Open F.F.P. from 11:20 m to 12:50 m 90 min

Tool Closed F.C.I.P. from 12:50 m to 2:50 m 120 min

Initial Blow Strong Blow, Blew off bottom of bucket instantly. 3 min

Final Blow Strong Blow, Blew off bottom of bucket instantly. 90 min

Total Feet Recovered 2520 Gravity of Oil _____ Corrected _____

150 Feet of gassy, slightly oilcut mud % Gas show % Oil 65 % Mud 35 % Water

2370 Feet of gassy salt water % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars Yes Safety Joint Yes Extra Packer NO Straddle NO Hook Wall NO

Top Recorder No. 4023 Clock No. ELECT. Depth 4563 Cir. Sub NO Sampler NO

Bottom Recorder No. 3088 Clock No. 47441 Depth 4564 Insurance _____

Price of Job _____

Tool Operator James Ramsey

Approved By _____

NO 14643


Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

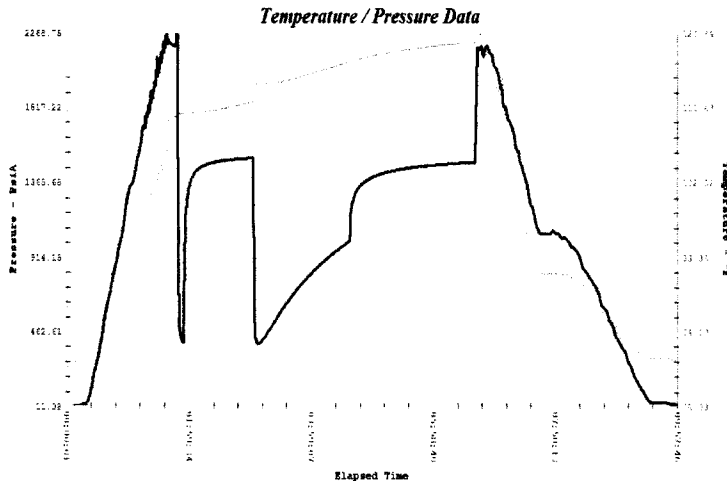

1	Initial Hydrostatic Pressure	2259
2	Initial Flow Pressure	420
3	Final Initial Flow Pressure	398
4	Initial Shut-In Pressure	1515
5	Initial Final Flow Pressure	417
6	Final Flow Pressure	1015
7	Final Shut-In Pressure	1490
8	Final Hydrostatic Pressure	2193

Maximum Temperature 120

PROPERTY OWNED F.G. HOLL LLC

TEST DATE 10/16/05

SECTION-TOWN-RANGE 28 30W 14S

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1873

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER TERNES TRUST1-28

FORMATION TESTED SIMPSON

DRILL STEM TEST NUMBER 9

REPORT NUMBER 14643

ELEVATION KELLY BUSHINGS 1884

TESTING ENGINEER GENE BUDIG

TOOL JOBS INFORMATION

TEST INTERVAL (ft) 4546

TEST INTERVAL (ft) 4567

ANCHOR LENGTH 21

TOTAL DEPTH (ft) 4567

TOP PACKER DEPTH 4541

BOTTOM PACKER DEPTH 4540

NUMBER OF PACKERS 1

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

TOOL OPEN (min) 10:00P

TOOL OPEN (min) 10:00P

DURATION (min) 5MIN

TOOL CLOSED (from) 10:05

INITIAL SHUT-IN TOOL CLOSED (to) 11:20

DURATION (min.) 75MIN

TOOL OPEN (min) 11:20P

TOOL OPEN (min) 11:20P

DURATION (min.) 90MIN

TOOL CLOSED (from) 12:50A

FINAL SHUT-IN TOOL CLOSED (to) 2:50A

DURATION (min.) 120MIN

STRONG BLOW BLEW OFF THE BOTTOM OF BUCKET INSTANTLY 5MIN

STRONG BLOW BLEW OFF THE BOTTOM OF THE BUCKET INSTANTLY 90MIN

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
150	GASSY SLIGHTLY OIL CUT MUD			65	35
2370	GASSY SALTWATER				100
4)					
5)					

14S

CC anyil : HOLL LLC

Lease & Well ID: TERNES TRUST1-28

Test Date: 10/16/05

28 TW 30W RGE

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G. HOLL LLC	LEASE AND WELL NUMBER	TERNES TRUST1-28
TEST DATE	10/16/05	FORMATION TESTED	SIMPSON
SECTION-TOWN-RANGE	28 30W 14S	DRILL STEM TEST NUMBER	9
STATE	KANSAS	REPORT NUMBER	14643
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1884
ELEVATION GROUND LEVEL	1873	TESTING ENGINEER	LEONARD RAMSEY
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT

JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	184 MILES ROUND TRIP FROM	SAMPLER	NO
	GREAT BEND KS		
TOP RECORDER DEPTH	4563	BOTTOM RECORDER DEPTH	4564
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG 1	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	4520	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.4
WEIGHT PIPE I.D.	2.25	VISCOSITY	51
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	9.6
		CHLORIDES-PITS	5000
		CHLORIDES-DST	

COMMENTS

SUPERIOR TESTERS ENTERPRISES INC.

GREAT BEND, KANSAS

GAS FLOW RATE

(800) 792-6902

#

STATE..... KANSAS

Test Date #####

COUNTY..... BARBER

Sec Town Range 28 30W 14S

FIELD.....

Report Number 14643

Initial Flow

Comments	Time (hh:mm:ss)	Period dt (min)	Inches H2O Orifice Tester	PSI on Orifice Tester	PSI on Pitot Tube	Choke Size (in)	Gas Rate (MCF/Day)

Final Flow

Comments	Time (hh:mm:ss)	Period dt (min)	Inches H2O Orifice Tester	PSI on Orifice Tester	PSI on Pitot Tube	Choke Size (in)	Gas Rate (MCF/Day)
TOOL OPENED	11:25	10	50			1IN	183.000
AT 11:20 WITH GAS	11:35	20	24			1IN	126.000
TO SURFACE	11:45	30	30			3/4	77.800
5MIN	11:55	40	24			3/4	63.500
AT 11:25	12:05	50	22			3/4	66.600
	12:15	60	10			3/4	44.800
	12:25	70	10			3/4	44.800
	12:35	80	10			3/4	44.800
	12:45	90	5			3/4	31.600
	12:50	100	5			3/4	31.600

Temperature / Pressure Data



F.G. HOLL LLC TERNES TRUST 1-28 28 30W14S 10/16/05

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 10/17/05 Location 28 30s 14w Elevation 1873 County Barber

Company F.G. Hall LLC Number of Copies 5

Charts Mailed to 9431 Central ST #100 Wichita KS 67206

Drilling Contractor Bill Ree

Length Drill Pipe 45 45 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 X H

Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____

Top Packer Depth 4566 Bottom Packer Depth 4571 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 4571 TO 4587 ANCHOR LENGTH 16 TOTAL DEPTH 4587 Hole Size 7 7/8

LEASE & WELL NO. Ternes Trust 1-28 FORMATION TESTED Simpson TEST NO. 10

Mud Weight 9.1 Viscosity 74 Water Loss 8.8 Chlorides - Pits 6500 D.S.T. _____

Maximum Temp. _____ °F Initial Hydrostatic Pressure (A) 2298 P.S.I. Final Hydrostatic Pressure (H) 2222 P.S.I.

Tool Open I.F.P. from 7:00 m to 7:15 m 15 min
 Tool Closed I.C.I.P. from 7:15 m to 8:45 m 30 min

Tool Open F.F.P. from 7:45 m to 8:30 m 45 min
 Tool Closed F.C.I.P. from 8:30 m to 10:00 m 90 min

Initial Blow Weak Blow, with a mild build, to 3 inches into 15 min

Final Blow Weak Blow, Built to one inch into bucket 45 min

Total Feet Recovered 35 Gravity of Oil _____ Corrected _____

35 Feet of Oily Gassy cut Mud %Gas _____ %Oil _____ %Mud _____ %Water _____

Feet of With a show of oil between %Gas _____ %Oil _____ %Mud _____ %Water _____

Feet of Tools %Gas _____ %Oil _____ %Mud _____ %Water _____

Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

Remarks _____

Extra Equipment - Jars Yes Safety Joint Yes Extra Packer NO Straddle NO Hook Wall NO

Top Recorder No. 4023 Clock No. Elect Depth 4583 Cir. Sub _____ Sampler NO

Bottom Recorder No. 3088 Clock No. 47441 Depth 4584 Insurance _____

Price of Job _____

Tool Operator Leonard Ramon

Approved By _____

No 14644

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.


1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: F.G. HOLL LLC
RGE. 14W
Lease & Well No. TERNES TRUST 1-28
Test #: 10
Date: 10/17/05
SEC. 28 TWP. 30S

Temperature / Pressure Data

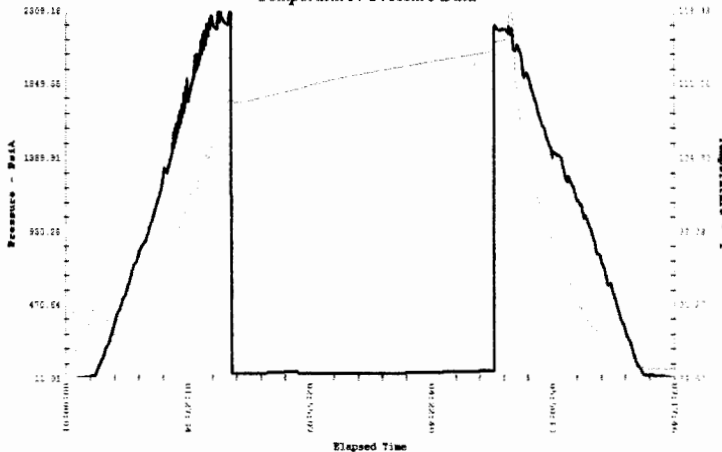

1	Initial Hydrostatic Pressure	2298
2	Initial Flow Pressure	43
3	Final Initial Flow Pressure	47
4	Initial Shut-In Pressure	54
5	Initial Final Flow Pressure	48
6	Final Flow Pressure	53
7	Final Shut-In Pressure	61
8	Final Hydrostatic Pressure	2222

Maximum Temperature 118

GENERAL INFORMATION

COMPANY NAME F.G. HOLL LLC

TEST DATE 10/17/05

SECTION-TOWN-RANGE 28 30S 14W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1873

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER TERNES TRUST 1-28

FORMATION TESTED SIMPSON

DRILL STEM TEST NUMBER 10

REPORT NUMBER 14644

ELEVATION KELLY BUSHINGS 1884

TESTING ENGINEER LEONARD RAMSEY

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4571

TEST INTERVAL (to) 4587

ANCHOR LENGTH 16

TOTAL DEPTH (ft) 4587

TOP PACKER DEPTH 4583

BOTTOM PACKER DEPTH 4588

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 7:00P

INITIAL OPEN TOOL OPEN (to) 7:15P

DURATION (min.) 15MIN

TOOL CLOSED (from) 7:15P

INITIAL SHUT-IN TOOL CLOSED (to) 7:45P

DURATION (min.) 30MIN

TOOL OPEN (from) 7:45P

FINAL OPEN TOOL OPEN (to) 8:30P

DURATION (min.) 45MIN

TOOL CLOSED (from) 8:30P

FINAL SHUT-IN TOOL CLOSED (to) 10:00P

DURATION (min.) 90MIN

INITIAL FLOW

WEAK BLOW, WITH A MILD BUILD TO 3 INCHES INTO BUCKET 15 MIN

FINAL FLOW

WEAK BLOW. BUILT TO ONE INCH INTO BUCKET IN 45 MIN 45 MIN

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 35	oily gassy mud with show of oil between tools				
2)					
3)					
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G. HOLL LLC	LEASE AND WELL NUMBER	TERNES TRUST 1-28
TEST DATE	10/17/05	FORMATION TESTED	SIMPSON
SECTION-TOWN-RANGE	28 30S 14W	DRILL STEM TEST NUMBER	10
STATE	KANSAS	REPORT NUMBER	14644
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1884
ELEVATION GROUND LEVEL	1873	TESTING ENGINEER	LEONARD RAMSEY
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT


JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	184 MILES ROUND TRIP FROM	SAMPLER	NO
	GREAT BEND KS		
TOP RECORDER DEPTH	4583	BOTTOM RECORDER DEPTH	4584
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG 1	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	4545	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.1
WEIGHT PIPE I.D.	2.25	VISCOSITY	74
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	6500
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

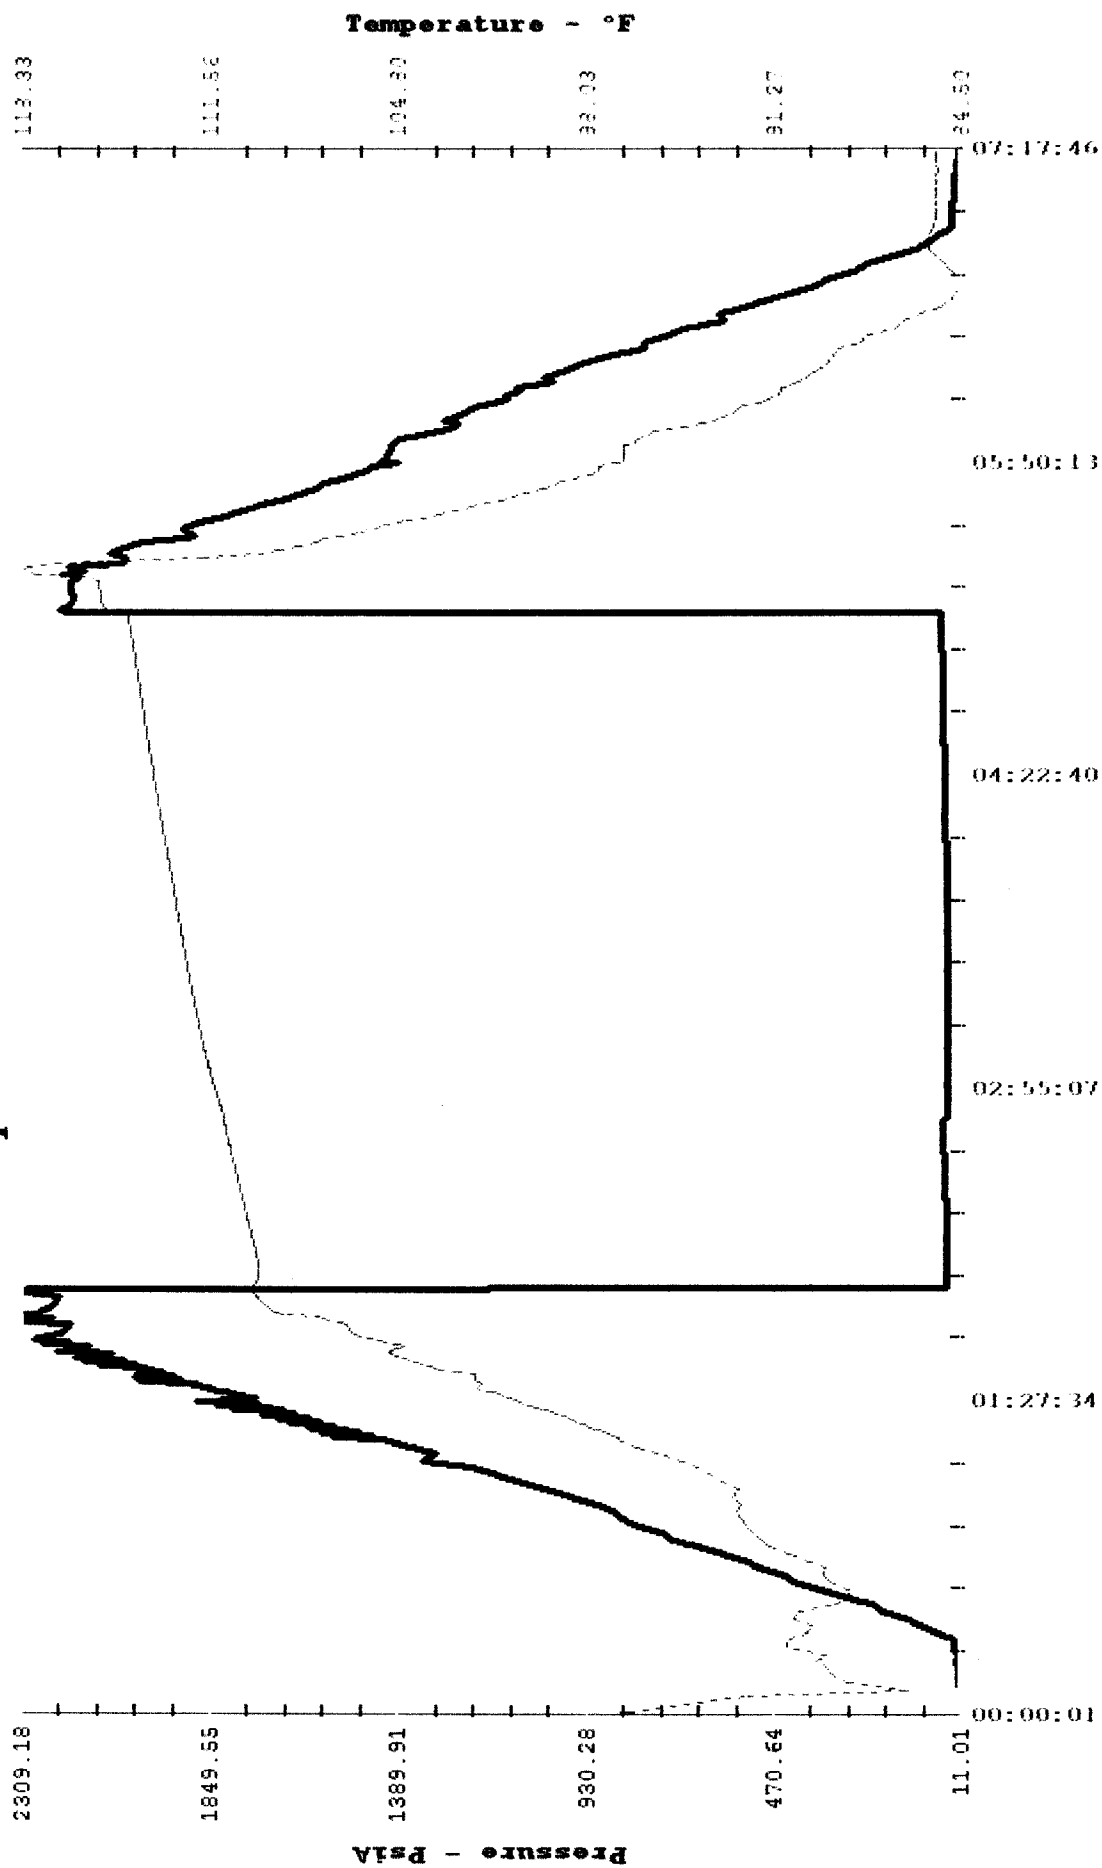

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 10/18/05 Location 28 30s 14w Elevation 1873 County Barber
 Company F.G. HOH LLC Number of Copies 5
 Charts Mailed to 9431 Central St #100 Wichita Ks 67206
 Drilling Contractor Bill Ree Duke Drilling Rig #1
 Length Drill Pipe 4609 I.D. Drill Pipe 3.8 Tool Joint Size 4 1/2 X H
 Length Weight Pipe _____ I.D. Weight Pipe _____ Tool Joint Size _____
 Length Drill Collars _____ I.D. Drill Collars _____ Tool Joint Size _____
 Top Packer Depth 4630 Bottom Packer Depth 4635 Number of Packers 2 Packer Size 6 3/4
 ESTED FROM 4635 TO 4647 ANCHOR LENGTH 12 TOTAL DEPTH 4647 Hole Size 7 7/8
 CASE & WELL NO. Ternes Trust 1-28 FORMATION TESTED Arbuckle TEST NO. 11
 Mud Weight 9.1 Viscosity 82 Water Loss 8.8 Chlorides - Pits 9000 D.S.T. 64,000
 Maximum Temp. _____ °F Initial Hydrostatic Pressure (A) 2341 P.S.I. Final Hydrostatic Pressure (H) 2303 P.S.I.
 Tool Open I.F.P. from 4:45 p.m. to 4:50 p.m. 5 min
 Tool Closed I.C.I.P. from 4:50 p.m. to 5:50 p.m. 60 min
 Tool Open F.F.P. from 5:50 p.m. to 6:05 p.m. 15 min
 Tool Closed F.C.I.P. from 6:05 p.m. to 7:05 p.m. 60 min
 Initial Blow Strong Blow Blow from Bottom of Bucket in 2 min 3 min
 Final Blow Strong Blow Blow from Bottom of Bucket in 2 min 15 min
 Total Feet Recovered 1560 Foot of Fluid _____ Gravity of Oil _____ Corrected _____
 _____ Feet of Slightly oil speckled mud %Gas _____ %Oil _____ %Mud _____ %Water _____
 _____ Feet of Water cut mud %Gas _____ %Oil _____ %Mud _____ %Water _____
 _____ Feet of Salt Water %Gas _____ %Oil _____ %Mud _____ %Water _____
 _____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____
 _____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____
 _____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____
 _____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____
 _____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____
 _____ Feet of _____ %Gas _____ %Oil _____ %Mud _____ %Water _____

Remarks _____

Extra Equipment - Jars Yes Safety Joint Yes Extra Packer NO Straddle NO Hook Wall NO
 Top Recorder No. 4023 Clock No. Elect Depth 4643 Cir. Sub NO Sampler NO
 Bottom Recorder No. 3088 Clock No. 47441 Depth 4644 Insurance _____

Price of Job _____
 Tool Operator Jonathan Ramsey
 Approved By _____

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.


NO 14645

SUPERIOR TESTERS ENTERPRISES INC.

(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

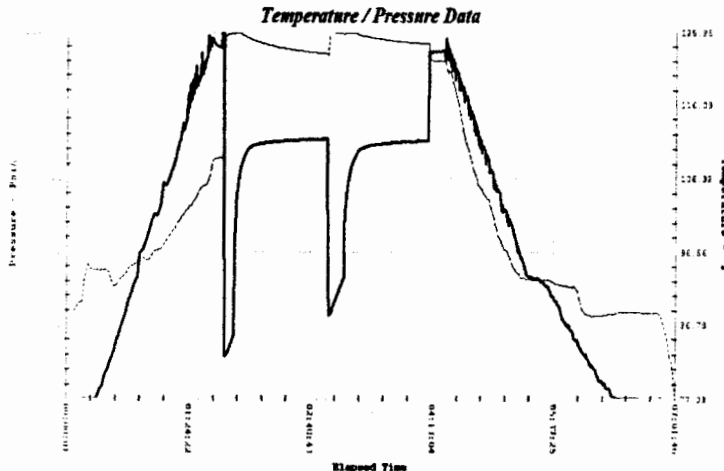

1	Initial Hydrostatic Pressure	2341
2	Initial Flow Pressure	279
3	Final Initial Flow Pressure	400
4	Initial Shut-In Pressure	1659
5	Initial Final Flow Pressure	534
6	Final Flow Pressure	770
7	Final Shut-In Pressure	1650
8	Final Hydrostatic Pressure	2303

Maximum Temperature 125

GENERAL INFORMATION

COMPANY NAME F.G. HOLL LLC

TEST DATE 10/18/05

SECTION-TOWN-RANGE 28 30S 14W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1873

COMPANY REPRESENTATIVE BILL REE

LEASE AND WELL NUMBER TERNES TRUST 1-28

FORMATION TESTED ARBUCKLE

DRILL STEM TEST NUMBER 11

REPORT NUMBER 14645

ELEVATION KELLY BUSHINGS 1884

TESTING ENGINEER LEONARD RAMSEY

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4635

TEST INTERVAL (to) 4647

ANCHOR LENGTH 12

TOTAL DEPTH (ft) 4647

TOP PACKER DEPTH 4630

BOTTOM PACKER DEPTH 4635

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 4:45

INITIAL OPEN TOOL OPEN (to) 4:50

DURATION (min.) 5MIN

TOOL OPEN (from) 5:50P

FINAL OPEN TOOL OPEN (to) 6:05P

DURATION (min.) 15MIN

TOOL CLOSED (from) 4:50

INITIAL SHUT-IN TOOL CLOSED (to) 5:50P

DURATION (min.) 60MIN

TOOL CLOSED (from) 6:05P

FINAL SHUT-IN TOOL CLOSED (to) 7:05

DURATION (min.) 60MIN

INITIAL FLOW

STRONG BLOW BLEW FROM BOTTOM OF BUCKET IN 2MIN 5MIN

FINAL FLOW

STRONG BLOW BLEW FROM BOTTOM OF BUCKET IN 2MIN 15 MIN

FEET OF Recovery	RECOVERY DESCRIPTION	% GAS	% OIL	% MUD	% WATER
1) 30	SLIGHTLY OIL SPECKLED MUD				
2) 30	WATER CUT MUD				
3) 1500	SALT WATER				
4)					
5)					
6)					

Company: F.G. HOLL LLC Lease & Well No. TERNES TRUST 1-28 Test #: 11 Date: 10/18/05 SEC. 28 TWP. 30S RGE. 14W

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G. HOLL LLC	LEASE AND WELL NUMBER	TERNES TRUST1-28
TEST DATE	10/18/05	FORMATION TESTED	ARBUCKLE
SECTION-TOWN-RANGE	28 30S 14W	DRILL STEM TEST NUMBER	11
STATE	KANSAS	REPORT NUMBER	14645
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1884
ELEVATION GROUND LEVEL	1873	TESTING ENGINEER	LEONARD RAMSEY
COMPANY REPRESENTATIVE	BILL REE		

EXTRA EQUIPMENT

JARS	YES	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	184 MILES ROUND TRIP FROM	SAMPLER	NO
	GREAT BEND KS		
TOP RECORDER DEPTH	4643	BOTTOM RECORDER DEPTH	4644
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	DUKE DRILLING RIG 1	DRILL COLLAR LENGTH	
DRILL PIPE LENGTH	4609	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.1
WEIGHT PIPE I.D.	2.25	VISCOSITY	82
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	9000
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data



F.G. HOLL LLC TERNES TRUST 1-28 28-30S-14W 10/18/05
