

Globe Operating, Inc.
Ivan 1

20-31S-11W
E2 NE SE

API 15-007-22958-00-00

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 01-09-2005 Location E₁/2-N₁/2-S₁/4 20-31S-11W Elevation 1708 LH County Barber

Company GLOBE OPERATING INC. Number of Copies 5

Charts Mailed to P.O. Box 12 Great Bend, Kansas 67530

Drilling Contractor Southwind Drilling Co #2

Length Drill Pipe 4376 I.D. Drill Pipe 3.80 Tool Joint Size 4 1/2" X 1 1/4"

Length Weight Pipe NONE I.D. Weight Pipe NONE Tool Joint Size NONE

Length Drill Collars 30 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2" X 1 1/4"

Top Packer Depth 4420 Bottom Packer Depth 4425 Number of Packers 2 Packer Size 6 3/4"

TESTED FROM 4425 TO 4486 ANCHOR LENGTH 61 TOTAL DEPTH 4486 Hole Size 7 7/8"

EASE & WELL NO. Ivan #1 FORMATION TESTED Mississippian TEST NO. 1

Mud Weight 9.5 Viscosity 46 Water Loss 8.8 Chlorides - Pits 6000 D.S.T. 20000

Maximum Temp. 115 °F Initial Hydrostatic Pressure (A) 2269 P.S.I. Final Hydrostatic Pressure (H) 2281 P.S.I.

Tool Open I.F.P. from 4:15 A.M. to 4:45 A.M. 30 min

Tool Closed I.C.I.P. from 4:45 A.M. to 5:30 A.M. 45 min

Tool Open F.F.P. from 5:30 A.M. to 6:30 A.M. 60 min

Tool Closed F.C.I.P. from 6:30 A.M. to 7:30 A.M. 60 min

Initial Blow Fair blow built to the bottom of a 5 gallon bucket in 1 minute

Final Blow Fair blow - Gas to Surface in 30 seconds - See Gas flow Report

Total Feet Recovered 250 Gravity of Oil _____ Corrected _____

130 Feet of Oil & Gas Cut mud 0% Gas 5% Oil 95% Mud 0% Water

120 Feet of HEAVY OIL & Gas cut watery mud 0% Gas 28% Oil 50% Mud 22% Water

Feet of CHLORIDES 20000 % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars NONE Safety Joint NONE Extra Packer NONE Straddle NONE Hook Wall NONE

Top Recorder No. 91981 Clock No. Electron Depth 4482 Cir. Sub NONE Sampler NONE

Bottom Recorder No. 5463 Clock No. 47441 Depth 4483 Insurance NONE

Price of Job _____

Tool Operator Don Rudy

Approved By _____

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.


(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: GLOBE OPERATING INC. Lease & Well No. IVAN # 1 Test #: 1 Date: 01-09-2006 SEC. 20 TWP. 31S RGE. 11W

Temperature / Pressure Data

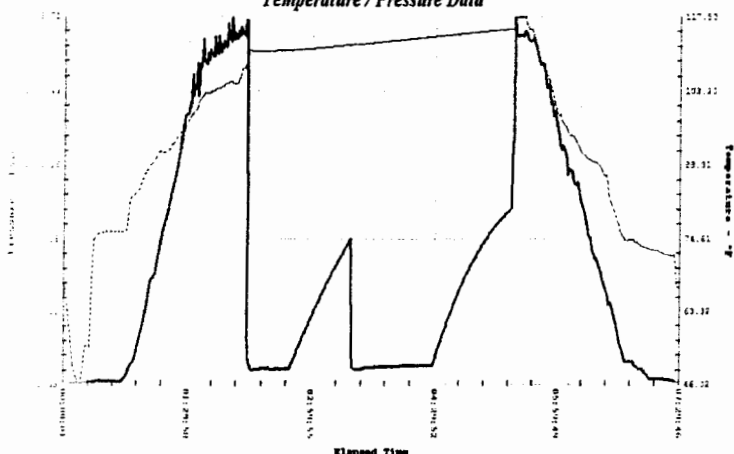

1	Initial Hydrostatic Pressure	2269
2	Initial Flow Pressure	180
3	Final Initial Flow Pressure	103
4	Initial Shut-In Pressure	913
5	Initial Final Flow Pressure	99
6	Final Flow Pressure	120
7	Final Shut-In Pressure	1102
8	Final Hydrostatic Pressure	2288

Maximum Temperature 115

GENERAL INFORMATION

COMPANY NAME GLOBE OPERATING INC.

TEST DATE 1/9/06

SECTION-TOWN-RANGE 20-31S-11W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1700

COMPANY REPRESENTATIVE JIM MUSGROVE

LEASE AND WELL NUMBER IVAN #1

FORMATION TESTED MISSISSIPPI

DRILL STEM TEST NUMBER 1

REPORT NUMBER 14555

ELEVATION KELLY BUSHINGS 1708

TESTING ENGINEER GENE BUDIG

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4425

TEST INTERVAL (to) 4486

ANCHOR LENGTH 61

TOTAL DEPTH (ft) 4486

TOP PACKER DEPTH 4420

BOTTOM PACKER DEPTH 4425

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 4:15

TOOL OPEN (from) 5:30

INITIAL OPEN TOOL OPEN (to) 4:45

FINAL OPEN TOOL OPEN (to) 6:30

DURATION (min.) 30

DURATION (min.) 60

TOOL CLOSED (from) 4:45

TOOL CLOSED (from) 6:30

INITIAL SHUT-IN TOOL CLOSED (to) 5:30

FINAL SHUT-IN TOOL CLOSED (to) 7:30

DURATION (min.) 45

DURATION (min.) 60

INITIAL FLOW

FAIR BLOW BUILT TO THE BOTTOM OF A 5 GALLON BUCKET IN 1 MINUTE

FINAL FLOW

FAIR BLOW WITH GAS TO SURFACE IN 30 SECONDS-SEE GAS FLOW REPORT

FEET OF Recovery	RECOVERY DESCRIPTION	% GAS	% OIL	% MUD	% WATER
1) 30	OIL AND GAS CUT MUD		5	95	
2) 20	HEAVY OIL AND GAS CUT WATERY MUD		28	50	22
3)	CHLORIDES 20000				
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GOBE OPERATING INC.	LEASE AND WELL NUMBER	IVAN #1
TEST DATE	1/9/06	FORMATION TESTED	MISSISSIPPI
SECTION-TOWN-RANGE	20-31S-11W	DRILL STEM TEST NUMBER	1
STATE	KANSAS	REPORT NUMBER	14555
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1708
ELEVATION GROUND LEVEL	1700	TESTING ENGINEER	GENE BUDIG
COMPANY REPRESENTATIVE	JIM MUSGROVE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	80 MILES ROUND TRIP FROM	SAMPLER	NO
	PRATT		
TOP RECORDER DEPTH	4482	BOTTOM RECORDER DEPTH	4483
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	SOUTHWIND DRILLING RIG #2		
DRILL PIPE LENGTH	4376	DRILL COLLAR LENGTH	30
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.5
WEIGHT PIPE I.D.	2.25	VISCOSITY	46
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	6000
		CHLORIDES-DST	

COMMENTS

SUPERIOR TESTERS ENTERPRISES L.L.C.

GREAT BEND, KANSAS

GAS FLOW RATE

(800) 792-6902

#

STATE..... KANSAS

Test Date 1/0/1900

COUNTY..... BARBER

Sec Town Range 20-31S-11W

FIELD.....

Report Number 14555


Initial Flow

Comments	Time (hh:mm:ss)	Period or (min)	Inches H2O Orifice Tester	PSI on Orifice Tester	PSI on Pitot Tube	Choke Size (in)	Gas Rate (MCF/Day)

Final Flow

Comments	Time (hh:mm:ss)	Period or (min)	Inches H2O Orifice Tester	PSI on Orifice Tester	PSI on Pitot Tube	Choke Size (in)	Gas Rate (MCF/Day)
TOOL OPENED AT	5:40	10	20			3/8	15.900
5:30 WITH GAS	5:50	20	60			3/8	27.600
TO SURFACE	6:00	30	64			3/8	28.500
	6:10	40	62			3/8	28.000
	6:20	50	60			3/8	27.600
	6:30	60	60			3/8	27.600
THERE WAS A GAS SAMPLE TAKEN							

Temperature / Pressure Data

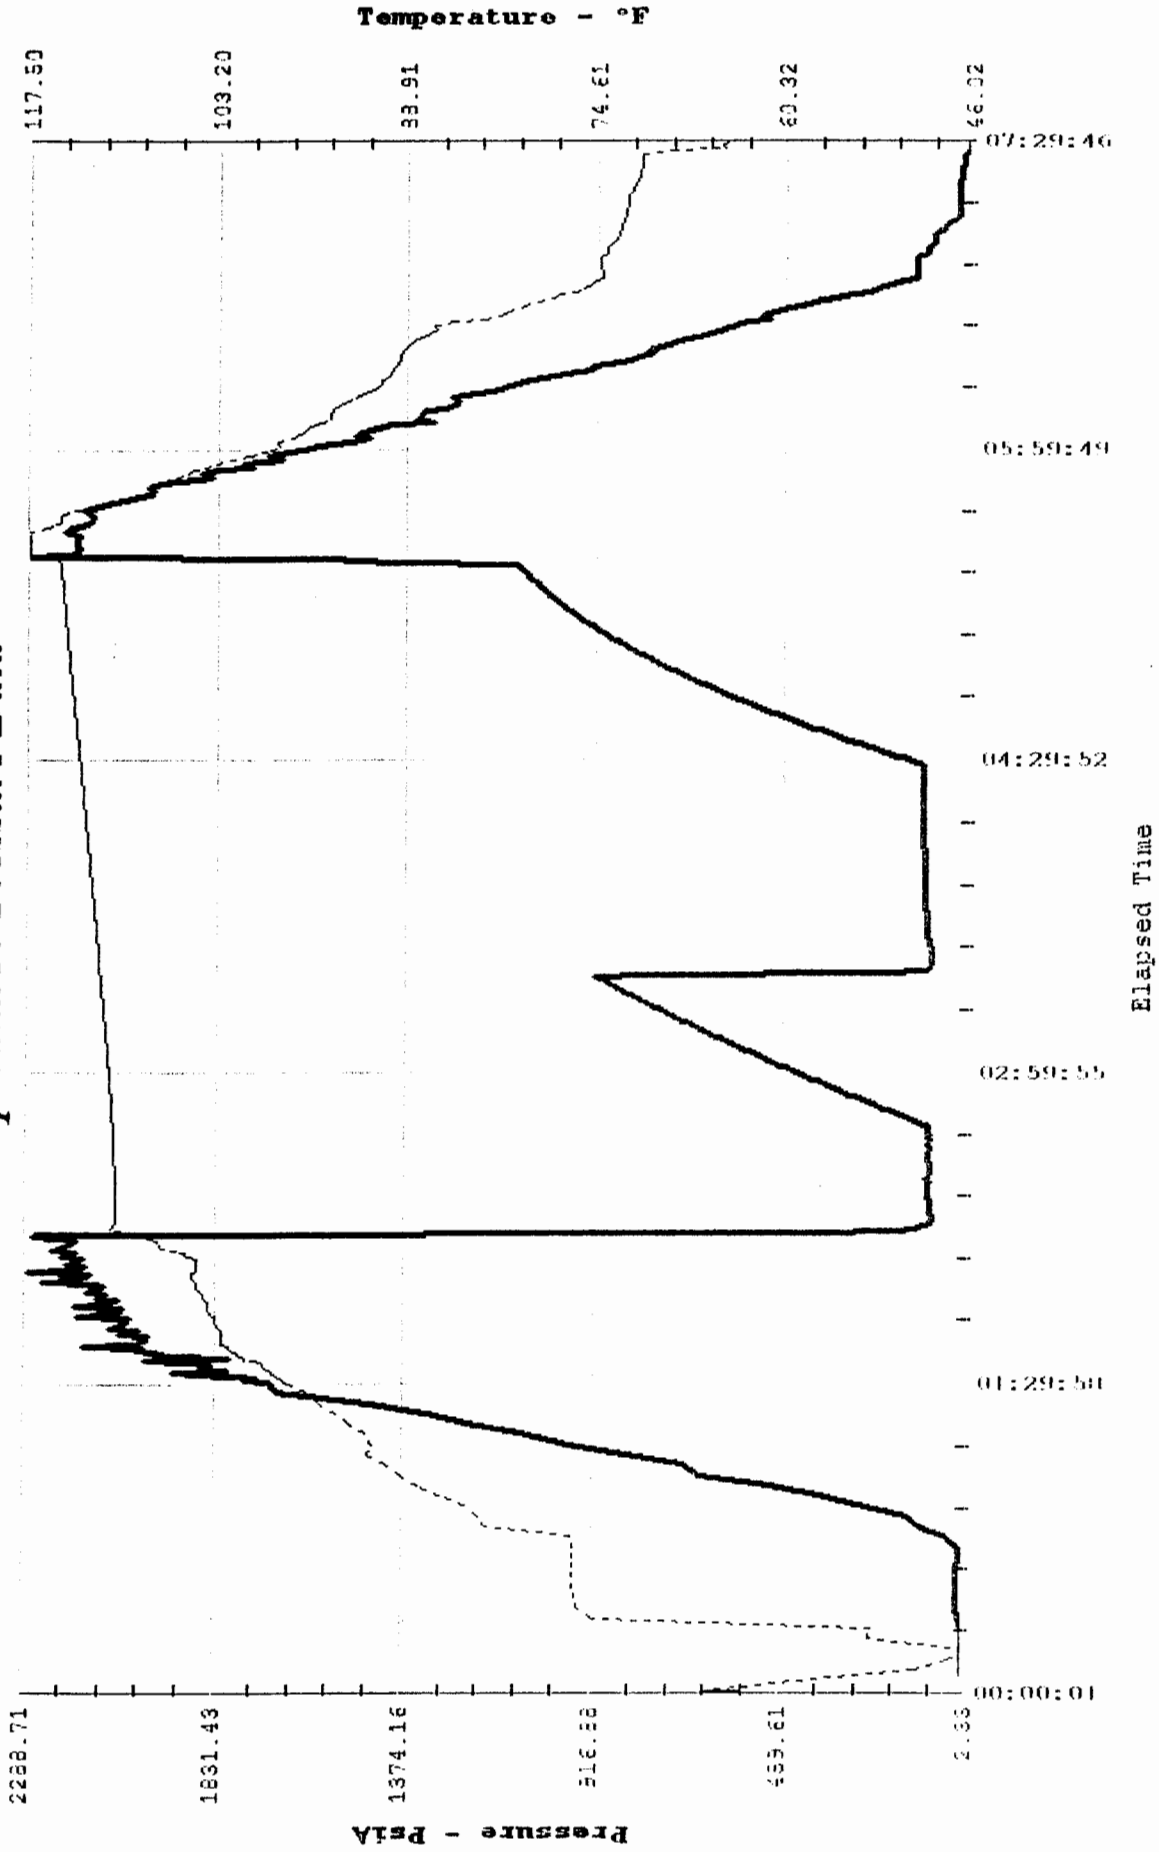

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

1708KE

Date 1-10-06 Location 6 1/2 ME - S/E 20-31-N Elevation 170066 County BARBER

Company GLOBE OPERATIONS INC. Number of Copies 5

Parts Mailed to P.O. BOX 12 Great Bend KS 67530

Drilling Contractor Southwind Drilling RIG #2

Length Drill Pipe 4540 I.D. Drill Pipe 2.50 Tool Joint Size 4 1/2 X

Length Weight Pipe NONE I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars 150 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 X

Top Packer Depth 4704 Bottom Packer Depth 4709 Number of Packers 2 Packer Size _____

TESTED FROM 4709 TO 4746 ANCHOR LENGTH 37 TOTAL DEPTH 4746 Hole Size 7 3/8

LEASE & WELL NO. IVAN #1 FORMATION TESTED VIOLA TEST NO. 2

Mud Weight 9.4 Viscosity 44 Water Loss 12.0 Chlorides - Pits 6.500 D.S.T. _____

Maximum Temp. 115 °F Initial Hydrostatic Pressure (A) 2424 P.S.I. Final Hydrostatic Pressure (H) 2341 P.S.I.

Tool Open I.F.P. from 4:00 m to 4:30 m 30 min

Tool Closed I.C.I.P. from 4:30 m to 5:00 m 30 min

Tool Open F.F.P. from 5:00 m to 5:30 m 30 min

Tool Closed F.C.I.P. from 5:30 m to 6:00 m 30 min

Final Blow BKW for 12 min and died

from [B] <u>25</u> P.S.I. to [C] <u>28</u> P.S.I.
[D] <u>50</u> P.S.I.
from [E] <u>31</u> P.S.I. to [F] <u>33</u> P.S.I.
[G] <u>45</u> P.S.I.

Final Blow no blow

Total Feet Recovered 15 Gravity of Oil _____ Corrected _____

15 Feet of Drilling mud % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars NONE Safety Joint NONE Extra Packer NONE Straddle NONE Hook Wall NONE

Log Recorder No. 91981 Clock No. Electronic Depth 4742 Cir. Sub NONE Sampler NONE

Bottom Recorder No. 5469 Clock No. 47441 Depth 4743 Insurance NONE

Name of Job _____

Well Operator Gene Sudley

Approved By _____

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

110 11556

SUPERIOR TESTERS ENTERPRISES L.L.C.

(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: 31S RGE.11W


GLOBE PRODUCTIONS INC.

Lease & Well No. IVAN#2

Test #:2

Date: 01-10-2006

SEC. 20 TWP.

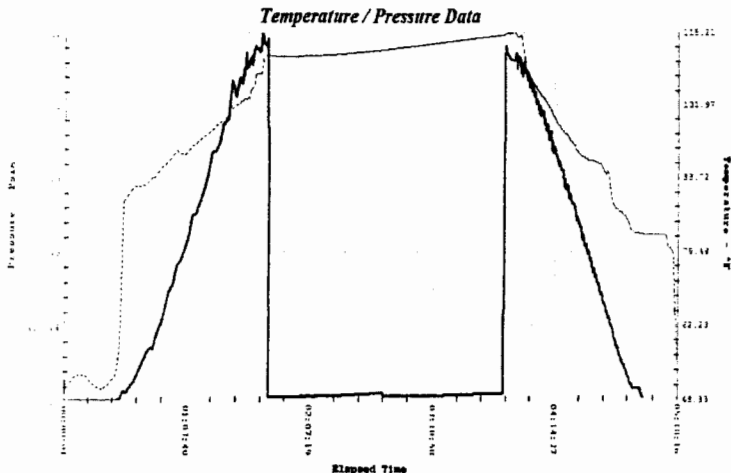

1	Initial Hydrostatic Pressure	2424
2	Initial Flow Pressure	25
3	Final Initial Flow Pressure	28
4	Initial Shut-In Pressure	50
5	Initial Final Flow Pressure	31
6	Final Flow Pressure	33
7	Final Shut-In Pressure	45
8	Final Hydrostatic Pressure	2341

Maximum Temperature 115

GENERAL INFORMATION

COMPANY NAME GOBE OPERATOINS INC.

TEST DATE 1/10/06

SECTION-TOWN-RANGE 20-31S-11W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1700

COMPANY REPRESENTATIVE JIM MUSGROVE

LEASE AND WELL NUMBER IVAN #1

FORMATION TESTED VIOLA

DRILL STEM TEST NUMBER #2

REPORT NUMBER 14556

ELEVATION KELLY BUSHINGS 1708

TESTING ENGINEER GENE BUDIG

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4709

TEST INTERVAL (to) 4746

ANCHOR LENGTH 37

TOTAL DEPTH (ft) 4746

TOP PACKER DEPTH 4704

BOTTOM PACKER DEPTH 4709

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 4:00

TOOL OPEN (from) 5:00

INITIAL OPEN TOOL OPEN (to) 4:30

FINAL OPEN TOOL OPEN (to) 5:30

DURATION (min.) 30

DURATION (min.) 30

TOOL CLOSED (from) 4:30

TOOL CLOSED (from) 5:30

INITIAL SHUT-IN TOOL CLOSED (to) 5:00

FINAL SHUT-IN TOOL CLOSED (to) 6:00

DURATION (min.) 30

DURATION (min.) 30

INITIAL FLOW WEAK SURFACE BLOW FOR 12 MINUTES AND DIED

INITIAL FLOW NO BLOW

FEET OF Recovery	RECOVERY DESCRIPTION	% GAS	% OIL	% MUD	% WATER
1) 15	DRILLING MUD				
2)					
3)					
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GOBE OPERATOINS INC.	LEASE AND WELL NUMBER	IVAN #1
TEST DATE	1/10/06	FORMATION TESTED	VIOLA
SECTION-TOWN-RANGE	20-31S-11W	DRILL STEM TEST NUMBER	#2
STATE	KANSAS	REPORT NUMBER	14556
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1708
ELEVATION GROUND LEVEL	1700	TESTING ENGINEER	GENE BUDIG
COMPANY REPRESENTATIVE	JIM MUSGROVE		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	80 MILES ROUND TRIP FROM	PRATT	
TOP RECORDER DEPTH	4742	BOTTOM RECORDER DEPTH	4743
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	SOUTHWIND #2	DRILL COLLAR LENGTH	150
DRILL PIPE LENGTH	4540	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH		MUD WEIGHT #/GAL	9.4
WEIGHT PIPE I.D.	2.25	VISCOSITY	44
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	12
		CHLORIDES-PITS	6500
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

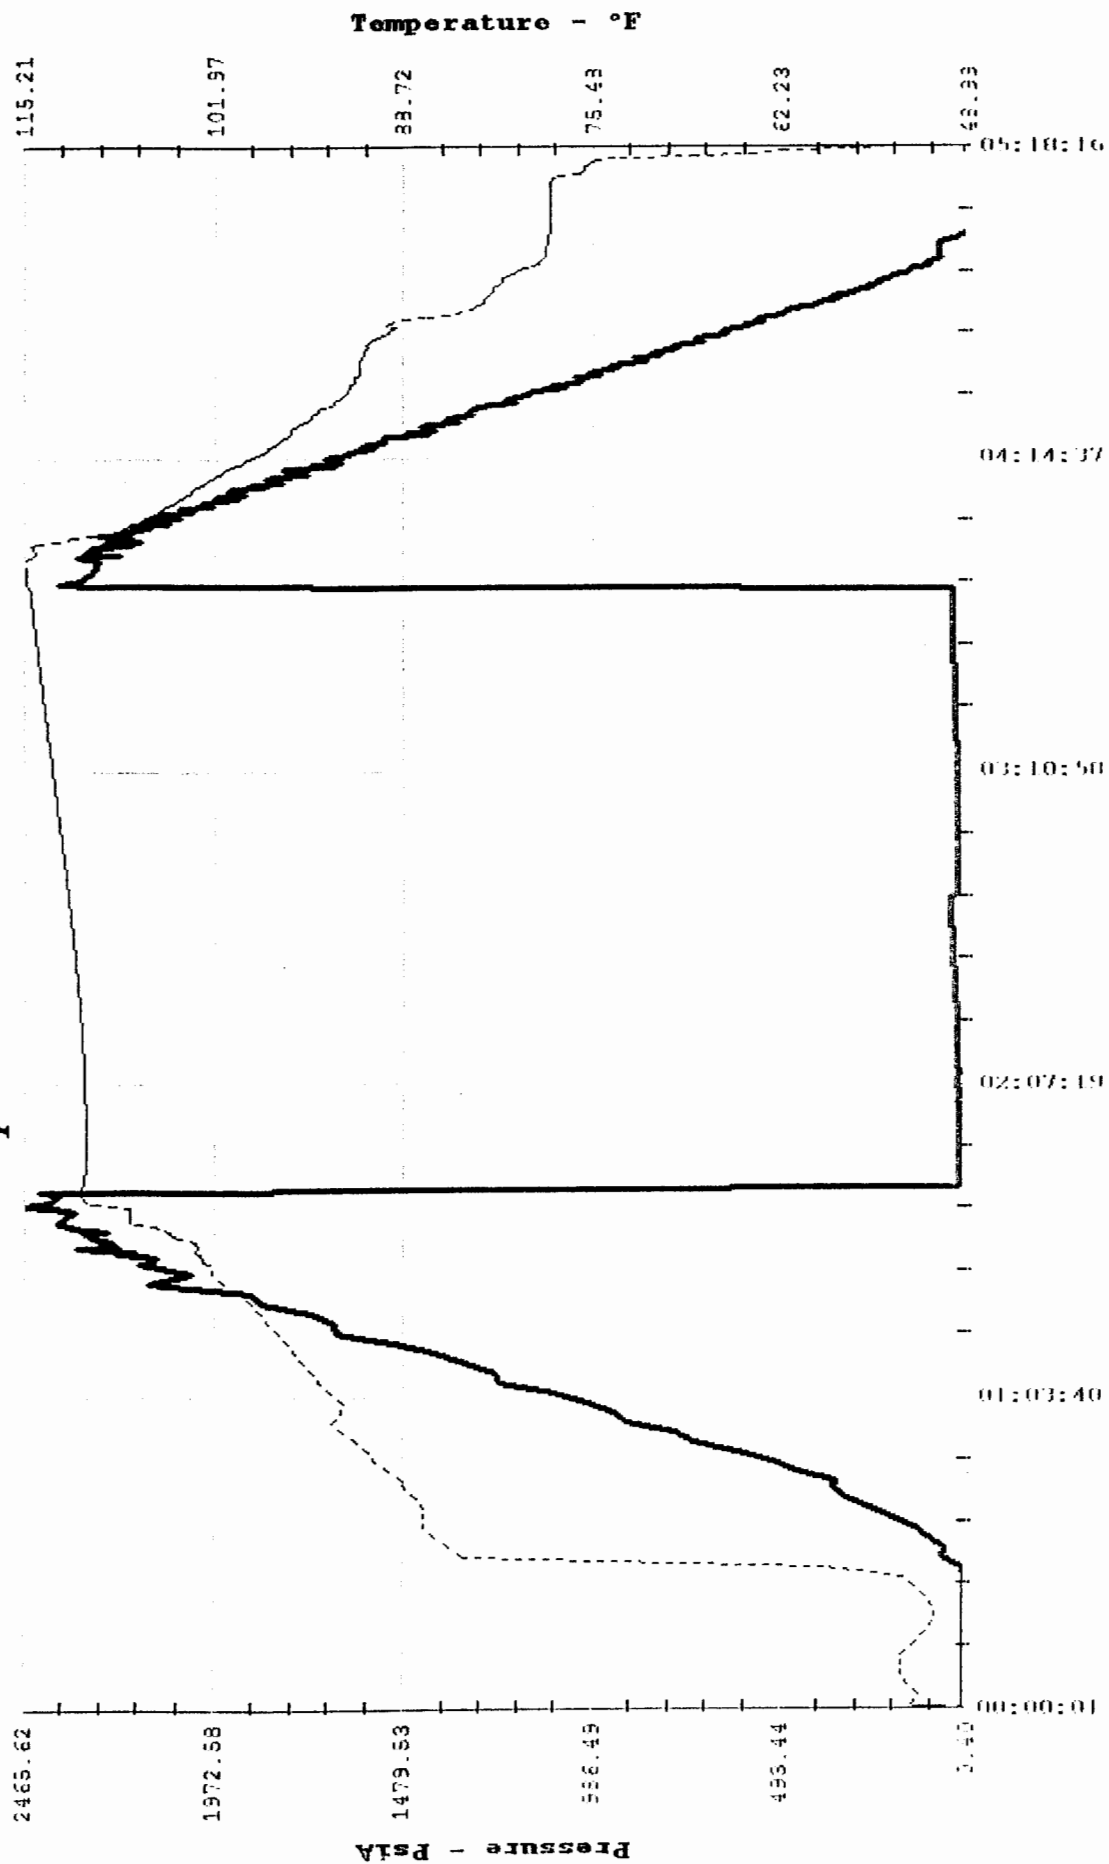

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

1708 KB

Date 1-11-06 Location E/2 - N/2 - S/4 20-31S-11W Elevation 1700 GL County BARBER

Company GLOBE OPERATIONS INC. Number of Copies 5

Charts Mailed to P.O. Box 12 Great Bend KS

Drilling Contractor Southwind Drilling REG #2

Length Drill Pipe 4507 I.D. Drill Pipe 2 3/8 Tool Joint Size 4 1/2 X. H

Length Weight Pipe NONE I.D. Weight Pipe NONE Tool Joint Size NONE

Length Drill Collars 235 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 X. H

Top Packer Depth 4756 Bottom Packer Depth 4761 Number of Packers 2 Packer Size _____

TESTED FROM 4761 TO 4788 ANCHOR LENGTH 27' TOTAL DEPTH 4788 Hole Size 7 7/8

LEASE & WELL NO. IVAN #1 FORMATION TESTED Simpson TEST NO. 3

Mud Weight 9.4 Viscosity 45 Water Loss 11.2 Chlorides - Pits 5000 D.S.T. _____

Maximum Temp. 124 °F Initial Hydrostatic Pressure (A) 2444 P.S.I. Final Hydrostatic Pressure (H) 2387 P.S.I.

Tool Open I.F.P. from 10:45 m to 11:15 m 30 min

Tool Closed I.C.I.P. from 11:15 m to 12:00 m 45 min

Tool Open F.F.P. from 12:00 m to 12:45 m 45 min

Tool Closed F.C.I.P. from 12:45 m to 1:45 m 60 min

from [B] <u>21</u>	P.S.I. to [C] <u>88</u>	P.S.I.
[D] <u>1434</u>		P.S.I.
from [E] <u>62</u>	P.S.I. to [F] <u>104</u>	P.S.I.
[G] <u>1522</u>		P.S.I.

Initial Blow And good slow in bucket first 9 min the picked up and blew good

Final Blow got gas after being open for 8 min

Total Feet Recovered 330 Gravity of Oil _____ Corrected _____

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

330 Feet of Very Heavy oil & Gas cut mud 27 % Gas 55 % Oil 18 % Mud 0 % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars _____ Safety Joint _____ Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 91981 Clock No. Electronic Depth 4784 Cir. Sub _____ Sampler _____

Bottom Recorder No. 5463 Clock No. 47441 Depth 4785 Insurance _____

Price of Job _____

Tool Operator _____

Approved By _____

NO 14557

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.


(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: GLOBE OPERATING INC.
RGE. 11W

Lease & Well No. IVAN#1 Test #: 3 Date: 01-11-06 SEC. 20 TWP. 31S

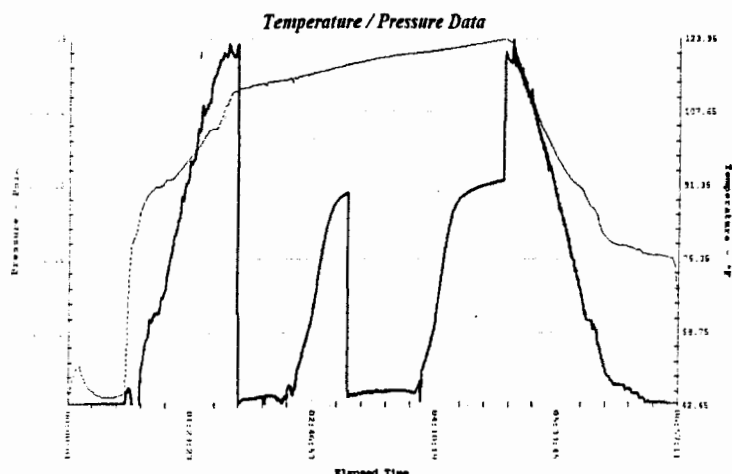

1	Initial Hydrostatic Pressure	2444
2	Initial Flow Pressure	21
3	Final Initial Flow Pressure	88
4	Initial Shut-In Pressure	1434
5	Initial Final Flow Pressure	62
6	Final Flow Pressure	104
7	Final Shut-In Pressure	1522
8	Final Hydrostatic Pressure	2387

Maximum Temperature 124

GENERAL INFORMATION

COMPANY NAME GLOBE OPERATIONS INC.

TEST DATE 1/11/06

SECTION-TOWN-RANGE 20-31S-11W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1700

COMPANY REPRESENTATIVE JIM MUSGROVE

LEASE AND WELL NUMBER IVAN#1

FORMATION TESTED SIMPSON

DRILL STEM TEST NUMBER 3

REPORT NUMBER 14557

ELEVATION KELLY BUSHINGS 1708

TESTING ENGINEER GENE BUDIG

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4761

TEST INTERVAL (to) 4788

ANCHOR LENGTH 27

TOTAL DEPTH (ft) 4788

TOP PACKER DEPTH 4756

BOTTOM PACKER DEPTH 4761

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 10:45

INITIAL OPEN

TOOL OPEN (to) 11:15

FINAL OPEN

TOOL OPEN (from) 12:00

TOOL OPEN (to) 12:45

DURATION (min.) 30

DURATION (min.) 45

TOOL CLOSED (from) 11:15

INITIAL SHUT-IN

TOOL CLOSED (to) 12:00

FINAL SHUT-IN

TOOL CLOSED (from) 12:45

TOOL CLOSED (to) 1:45

DURATION (min.) 45

DURATION (min.) 60

INITIAL FLOW

WEAK BUILDING BLOW BUILT TO THE BOTTOM OF A 5 GALLON BUCKET IN 9 MINUTES

FINAL FLOW

GOOD BLOW BUILT TO THE BOTTOM OF A 5 GALLON BUCKET IN 30 SECONDS WITH GAS TO SURFACE IN 18 MINUTES-SEE GAS FLOW REPORT

FEET OF	RECOVERY	%	%	%	%
Recovery	DESCRIPTION	GAS	OIL	MUD	WATER
1) 0-20	VERY HEAVY OIL AND GAS CUT MUD	27	55	18	
2)					
3)					
4)					
5)					
6)					

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GLOBE OPERATIONS INC.	LEASE AND WELL NUMBER	IVAN#1
TEST DATE	1/11/06	FORMATION TESTED	SIMPSON
SECTION-TOWN-RANGE	20-31S-11W	DRILL STEM TEST NUMBER	3
STATE	KANSAS	REPORT NUMBER	14557
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1708
ELEVATION GROUND LEVEL	1700	TESTING ENGINEER	GENE BUDIG
COMPANY REPRESENTATIVE	JIM MUSGROVE		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	80 MILES ROUND TRIP FROM	PRATT	
TOP RECORDER DEPTH	4784	BOTTOM RECORDER DEPTH	4785
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	SOUTHWIND DRILLING RIG #2		
DRILL PIPE LENGTH	4507	DRILL COLLAR LENGTH	235
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.
WEIGHT PIPE LENGTH	NONE	MUD WEIGHT #/GAL	9.4
WEIGHT PIPE I.D.	2.25	VISCOSITY	45
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	11.2
		CHLORIDES-PITS	5000
		CHLORIDES-DST	

COMMENTS

BLOW WAS SLOW AT FIRST AND THEN PICKED UP AFTER THE FIRST 9 MIN. AND THEN BLEW GOOD

SUPERIOR TESTERS ENTERPRISES L.L.C.

GREAT BEND, KANSAS

GAS FLOW RATE

(800) 792-6902

#

STATE..... KANSAS

Test Date 1/0/1900

COUNTY..... BARBER

Sec Town Range 20-31S-11W

FIELD.....

Report Number 14557

Initial Flow

Comments	Time (hh:mm:ss)	Period dt (min)	Inches H2O Orifice Tester	PSI on Orifice Tester	PSI on Pilot Tube	Choke Size (in)	Gas Rate (MCF/Day)

Final Flow

Comments	Time (hh:mm:ss)	Period dt (min)	Inches H2O Orifice Tester	PSI on Orifice Tester	PSI on Pilot Tube	Choke Size (in)	Gas Rate (MCF/Day)
TOOL OPENED AT	12:20	20	9			3/8	10.700
12:00 WITH GAS	12:30	30	7			3/8	9.450
TO SURFACE IN	12:40	40	5			3/8	7.980
18 MINUTES AT	12:45	45	4			3/8	7.140
12:18							

Temperature / Pressure Data

