

Globe Operating 15-007-22980-00-00
Elaine 1

16-315-11W

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530
(316) 792-6902 KB1797

Date 03/02/06 Location 16-315-11W Elevation 1789 County Barber
Company Globe Operating INC. Number of Copies 5
Charts Mailed to P.O. Box 12 Great Bend KS 67530
Drilling Contractor Southwind Drilling RIG #2 Tool Joint Size 4 1/2 XH
Length Drill Pipe 3672 I.D. Drill Pipe 2.80 Tool Joint Size 4 1/2 XH
Length Weight Pipe NONE I.D. Weight Pipe 2.25 Tool Joint Size 4 1/2 XH
Length Drill Collars 30 I.D. Drill Collars 2.25 Tool Joint Size 6 3/4
Top Packer Depth 3717 Bottom Packer Depth 3722 Number of Packers 2 Packer Size 6 3/4
TESTED FROM 3722 TO 3796 ANCHOR LENGTH 74 TOTAL DEPTH 3796 Hole Size 7 7/8
EASE & WELL NO. Elaine #1 FORMATION TESTED Douglas Sand TEST NO. 1
Mud Weight 8.7 Viscosity 50 Water Loss 10.4 Chlorides - Pits 5,000 D.S.T. 1799 P.S.I.
Maximum Temp. 103 °F Initial Hydrostatic Pressure (A) 1807 P.S.I. Final Hydrostatic Pressure (H) 1799 P.S.I.

Tool Open I.F.P. from 3:10 m to 3:40 m 30 min
Tool Closed I.C.I.P. from 3:40 m to 4:10 m 30 min
Tool Open F.F.P. from 4:10 m to 4:40 m 30 min
Tool Closed F.C.I.P. from 4:40 m to 5:10 m 30 min

from [B]	<u>45</u>	P.S.I. to [C]	<u>51</u>	P.S.I.
[D]	<u>258</u>			P.S.I.
from [E]	<u>55</u>	P.S.I. to [F]	<u>61</u>	P.S.I.
[G]	<u>106</u>			P.S.I.

Initial Blow weak building blow built 5 inches in 5 gallon bucket in 30 minutes
Final Blow very weak blow built to 1 3/4 inches in 5 gallon bucket in 30 minutes

Initial Feet Recovered 65
65 Feet of Drilling mud
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water
____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars _____ Safety Joint _____ Extra Packer _____ Straddle _____ Hook Wall _____
Top Recorder No. 4005 Clock No. electronic Depth 3792 Cir. Sub _____ Sampler _____
Bottom Recorder No. 3875 Clock No. 3539 Depth 3793 Insurance _____

Price of Job _____
Tool Operator NATHAN MARKS #6
Approved By _____

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 6, 530

1(800)792-6902


Company: GLOBE OPERATING INC.
31S RGE 11W

Lease & Well No. ELAINE #1

Test #: 1

Date: 03-02-2006

SEC. 16 TWP.

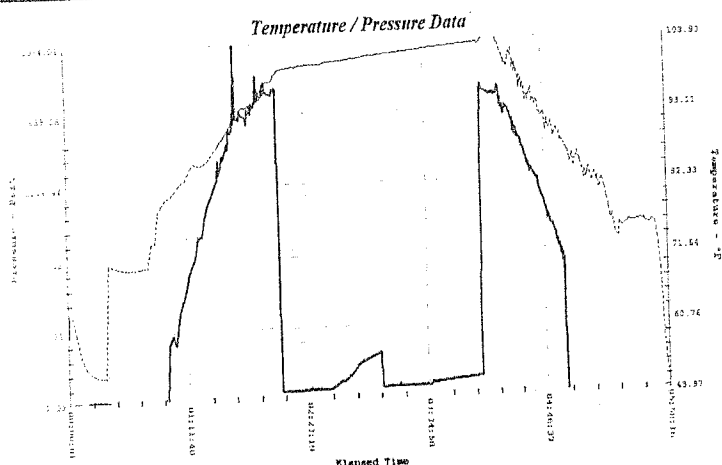

1	Initial Hydrostatic Pressure	1807
2	Initial Flow Pressure	45
3	Final Initial Flow Pressure	51
4	Initial Shut-In Pressure	258
5	Initial Final Flow Pressure	55
6	Final Flow Pressure	61
7	Final Shut-In Pressure	106
8	Final Hydrostatic Pressure	1799

Maximum Temperature 103

GENERAL INFORMATION

COMPANY NAME GLOBE OPERATING INC.

TEST DATE 3/2/06

SECTION-TOWN-RANGE 16-31S-11W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1789

COMPANY REPRESENTATIVE JOSH

LEASE AND WELL NUMBER ELAINE #1

FORMATION TESTED DOUGLAS SAND

DRILL STEM TEST NUMBER 1

REPORT NUMBER 14443

ELEVATION KELLY BUSHINGS 1797

TESTING ENGINEER NATHAN MANRING

TEST INTERVAL (ft) 3722

TEST INTERVAL (ft) 3796

ANCHOR LENGTH 74

TOTAL DEPTH (ft) 3796

TESTER NAME JOSH

TESTER PHONE NUMBER 316-234-2222

TESTER ADDRESS 1000 E. 10TH ST.

PACKER SIZE 5 1/2"

HOLE SIZE 7 7/8"

FLOW TIMES

TOOL OPEN (from) 3:10

INITIAL OPEN

TOOL OPEN (to) 3:40

DURATION (min.) 30

FINAL OPEN

TOOL OPEN (from) 4:10

TOOL OPEN (to) 4:40

DURATION (min.) 30

TOOL CLOSED (from) 3:40

INITIAL SHUT-IN TOOL CLOSED (to) 4:10

DURATION (min.) 30

FINAL SHUT-IN

TOOL CLOSED (from) 4:40

TOOL CLOSED (to) 5:10

DURATION (min.) 30

INITIAL FLOW

WEAK BUILDING BLOW BUILT TO 5 INCHES IN 5 GALLON BUCKET IN 30 MINUTE

FINAL FLOW

VEARY WEAK BLOW BUILT TO 1 3/4 INCHES IN FIVE GALLON BUCKET IN 30 MINUTES

FEET OF	RECOVERY	RESISTIVITY	AT	DEGREES	CHLORIDES			
					% GAS	% OIL	% MUD	% WATER
Recovery	65							
1) 65								
2)								
3)								

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GLOBE OPERATING INC.	LEASE AND WELL NUMBER	ELAINE #1
TEST DATE	3/2/06	FORMATION TESTED	DOUGLAS SAND
SECTION-TOWN-RANGE	16-31S-11W	DRILL STEM TEST NUMBER	1
STATE	KANSAS	REPORT NUMBER	14443
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1797
ELEVATION GROUND LEVEL	1789	TESTING ENGINEER	NATHAN MANRING
COMPANY REPRESENTATIVE	JOSH		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	70 MILES ROUND TRIP FROM	SAMPLER	NO
TOP RECORDER DEPTH	3792	PRATT	
RECORDER NUMBER	91981	BOTTOM RECORDER DEPTH	3793
		RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	SOUTHWIND DRILLING RIG #2	DRILL COLLAR LENGTH	30
DRILL PIPE LENGTH	3672	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH	NONE	MUD WEIGHT #/GAL.	8.7
WEIGHT PIPE I.D.	2.25	VISCOSITY	50
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	10.4
		CHLORIDES-PITS	5,000
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

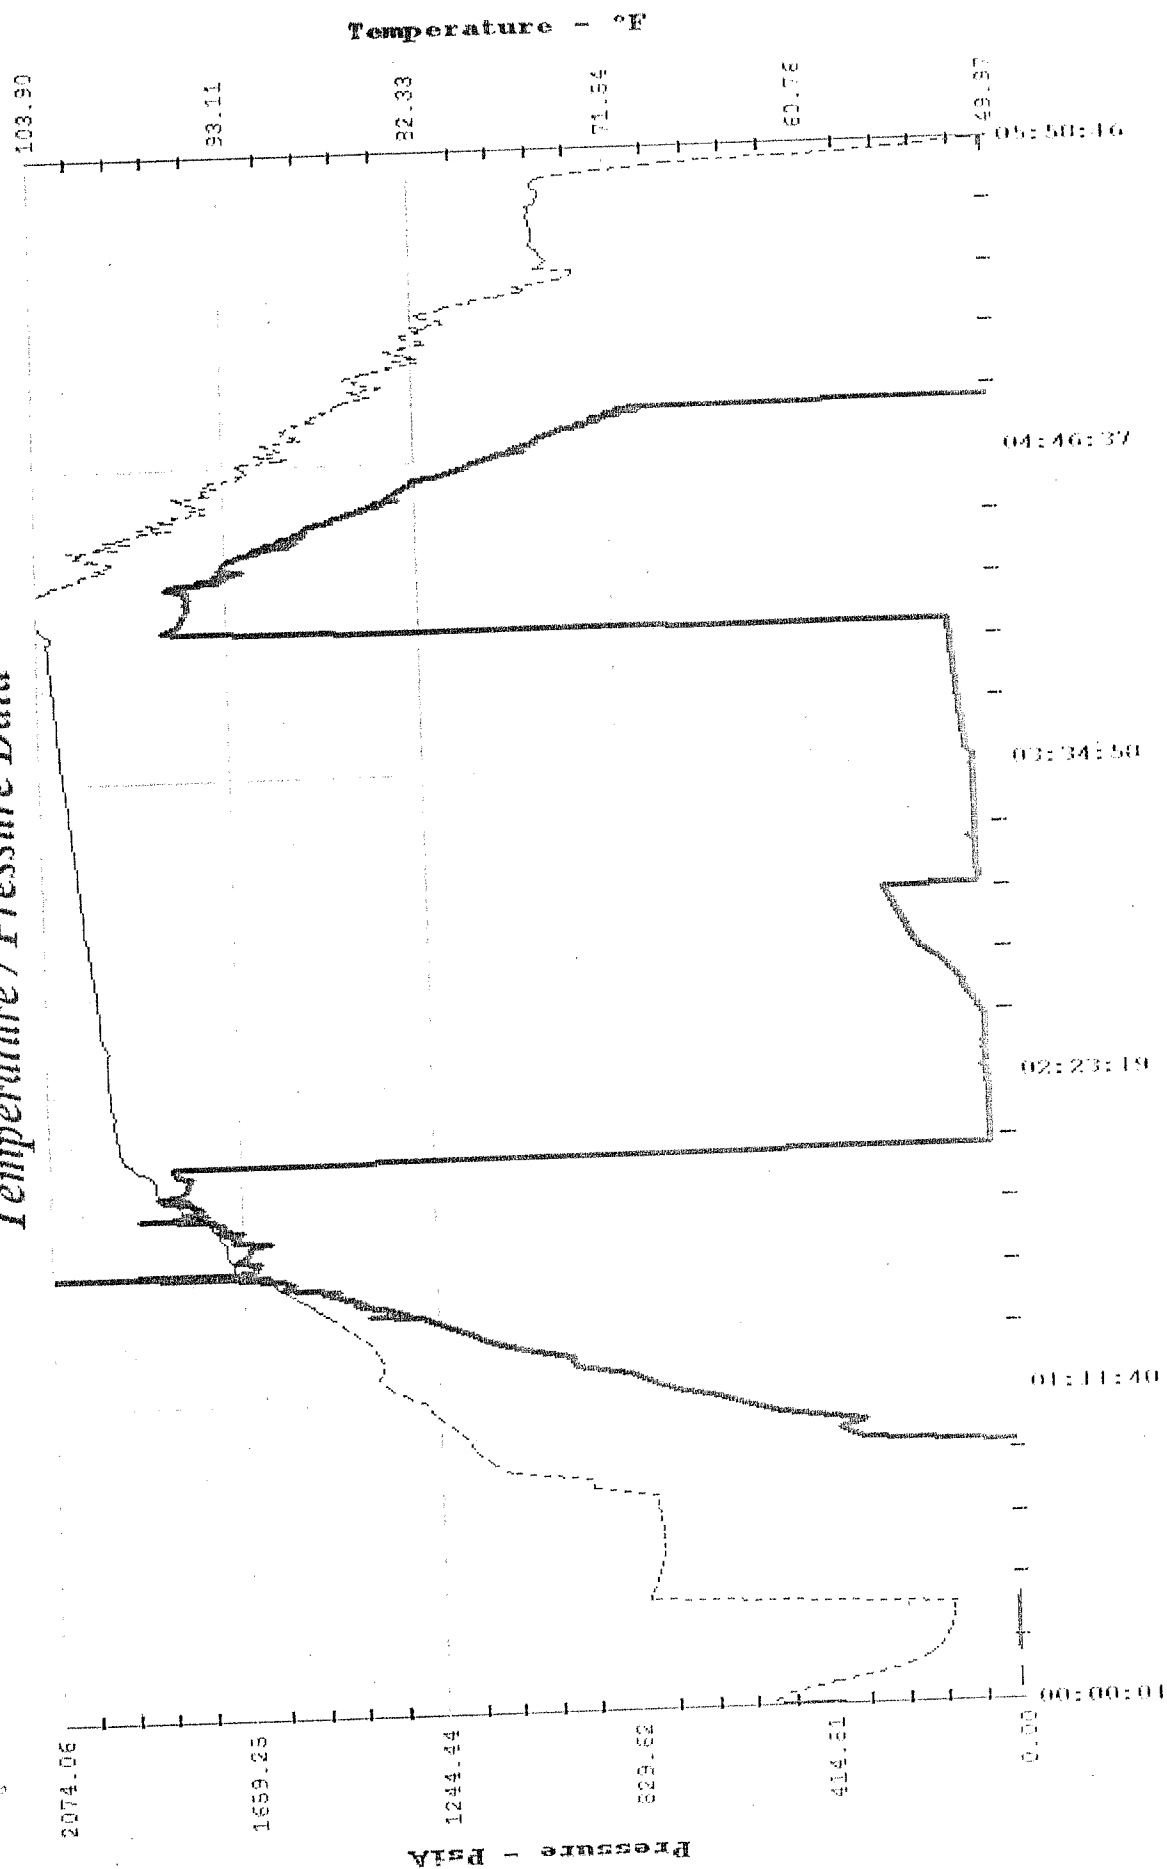

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

KB 1797

3-2-06 Location 16-31-11 W Elevation 1789 County BARBER

Company Globe Operating INC Number of Copies 5

Tests Mailed to PO Box 12 Great Bend KS

Drilling Contractor Southwind Drilling RIG #2

1st Drill Pipe 3675 I.D. Drill Pipe 3.80 Tool Joint Size 4 1/2 XH

2nd Weight Pipe NONE I.D. Weight Pipe Tool Joint Size

3rd Drill Collars 30 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 XH

Packer Depth 3720 Bottom Packer Depth 3725 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 3725 TO 3815 ANCHOR LENGTH 90 TOTAL DEPTH 3815 Hole Size 7 1/2

TEST & WELL NO. Elgin #1 FORMATION TESTED Douglas SAND TEST NO. 2

Fluid Weight 8.8 Viscosity 52 Water Loss 12 Chlorides - Pits 6000 D.S.T.

Minimum Temp. 112 °F Initial Hydrostatic Pressure (A) 1839 P.S.I. Final Hydrostatic Pressure (H) 1735 P.S.I.

1st Open I.F.P. from 4:00 m to 4:30 m 30 min

1st Closed I.C.I.P. from 4:30 m to 5:15 m 45 min

1st Open F.F.P. from 5:15 m to 6:15 m 60 min

1st Closed F.C.I.P. from 6:15 m to 7:15 m 60 min

Initial Blow strong blow gas to surface in 13 minutes

Initial Blow strong blow see gas flow report

Initial Feet Recovered 1095 Gravity of Oil Corrected

55 Feet of Drilling Muddy Mud %Gas %Oil %Mud %Water

40 Feet of WATER %Gas %Oil %Mud %Water

Feet of %Gas %Oil %Mud %Water

Feet of %Gas %Oil %Mud %Water

Feet of %Gas %Oil %Mud %Water

Feet of %Gas %Oil %Mud %Water

Feet of %Gas %Oil %Mud %Water

Feet of %Gas %Oil %Mud %Water

Feet of %Gas %Oil %Mud %Water

Remarks

Surface Equipment - Jars Safety Joint Extra Packer Straddle Hook Wall

Recorder No. 4005 Clock No. 3811 Depth 3811 Cir. Sub Sampler

Bottom Recorder No. 3875 Clock No. 3539 Depth 3812 Insurance

Use of Job Operator NATHAN MANN

Approved By

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

(800)792-6902

GREAT BEND, KANSAS 67530


Company: GLOBE OPERATING INC.
RGE. 11W

Lease & Well No. ELAINE #1

Test #: 2

Date: 03-02-2006

SEC. 16 TWP. 31S

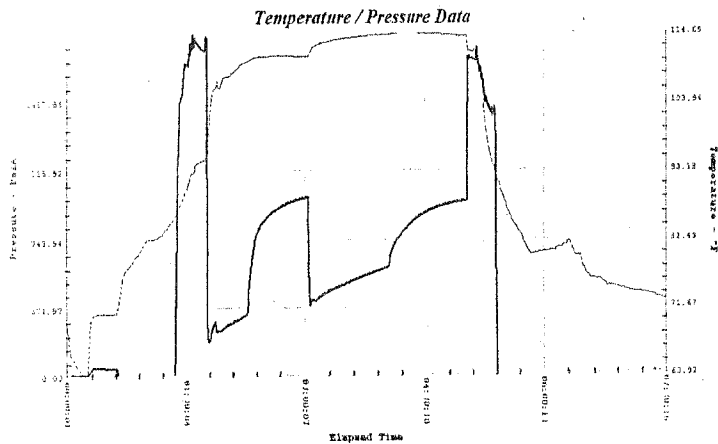

- 1 Initial Hydrostatic Pressure 1839
- 2 Initial Flow Pressure 183
- 3 Final Initial Flow Pressure 330
- 4 Initial Shut-In Pressure 974
- 5 Initial Final Flow Pressure 380
- 6 Final Flow Pressure 592
- 7 Final Shut-In Pressure 952
- 8 Final Hydrostatic Pressure 1735

Maximum Temperature 112

GENERAL INFORMATION

COMPANY NAME GLOBE OPERATING INC.

TEST DATE 3/2/06

SECTION-TOWN-RANGE 16-31S-11W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1789

COMPANY REPRESENTATIVE JOSH

LEASE AND WELL NUMBER ELAINE #1

FORMATION TESTED DOUGLAS SAND

DRILL STEM TEST NUMBER 2

REPORT NUMBER 14444

ELEVATION KELLY BUSHINGS 1797

TESTING ENGINEER NATHAN MANRING

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3725

TEST INTERVAL (to) 3815

ANCHOR LENGTH 90

TOTAL DEPTH (ft) 3815

TOP PACKER DEPTH 3720

BOTTOM PACKER DEPTH 3725

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 4:00

INITIAL OPEN TOOL OPEN (to) 4:30

DURATION (min.) 30

FINAL OPEN

TOOL OPEN (from) 5:15

TOOL OPEN (to) 6:15

DURATION (min.) 60

TOOL CLOSED (from) 4:30

INITIAL SHUT-IN TOOL CLOSED (to) 5:15

DURATION (min.) 45

FINAL SHUT-IN

TOOL CLOSED (from) 6:15

TOOL CLOSED (to) 7:15

DURATION (min.) 60

INITIAL FLOW

STRONG BLOW GAS TO SURFACE IN 13 MINUTES

FINAL FLOW

STRONG BLOW SEE GAS FLOW REPORTS

FEET OF Recovery	RESISTIVITY		AT		DEGREES		CHLORIDES			
	CP	RECOVERY	DESCRIPTION		%	%	%	%		
					GAS	OIL	MUD	WATER		
535			GASSY DRILLING MUD							
540			WATER							

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GLOBE OPERATING INC.	LEASE AND WELL NUMBER	ELAINE #1
TEST DATE	3/2/06	FORMATION TESTED	DOUGLAS SAND
SECTION-TOWN-RANGE	16-31S-11W	DRILL STEM TEST NUMBER	2
STATE	KANSAS	REPORT NUMBER	14444
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1797
ELEVATION GROUND LEVEL	1789	TESTING ENGINEER	NATHAN MANRING
COMPANY REPRESENTATIVE	JOSH		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	70 MILES ROUND TRIP FROM	PRATT	
TOP RECORDER DEPTH	3811	BOTTOM RECORDER DEPTH	3812
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	SOUTHWIND DRILLING RIG #2		
DRILL PIPE LENGTH	3675	DRILL COLLAR LENGTH	30
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.
WEIGHT PIPE LENGTH	NONE	MUD WEIGHT #/GAL	8.8
WEIGHT PIPE I.D.	2.25	VISCOSITY	52
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	12
		CHLORIDES-PITS	6,000
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

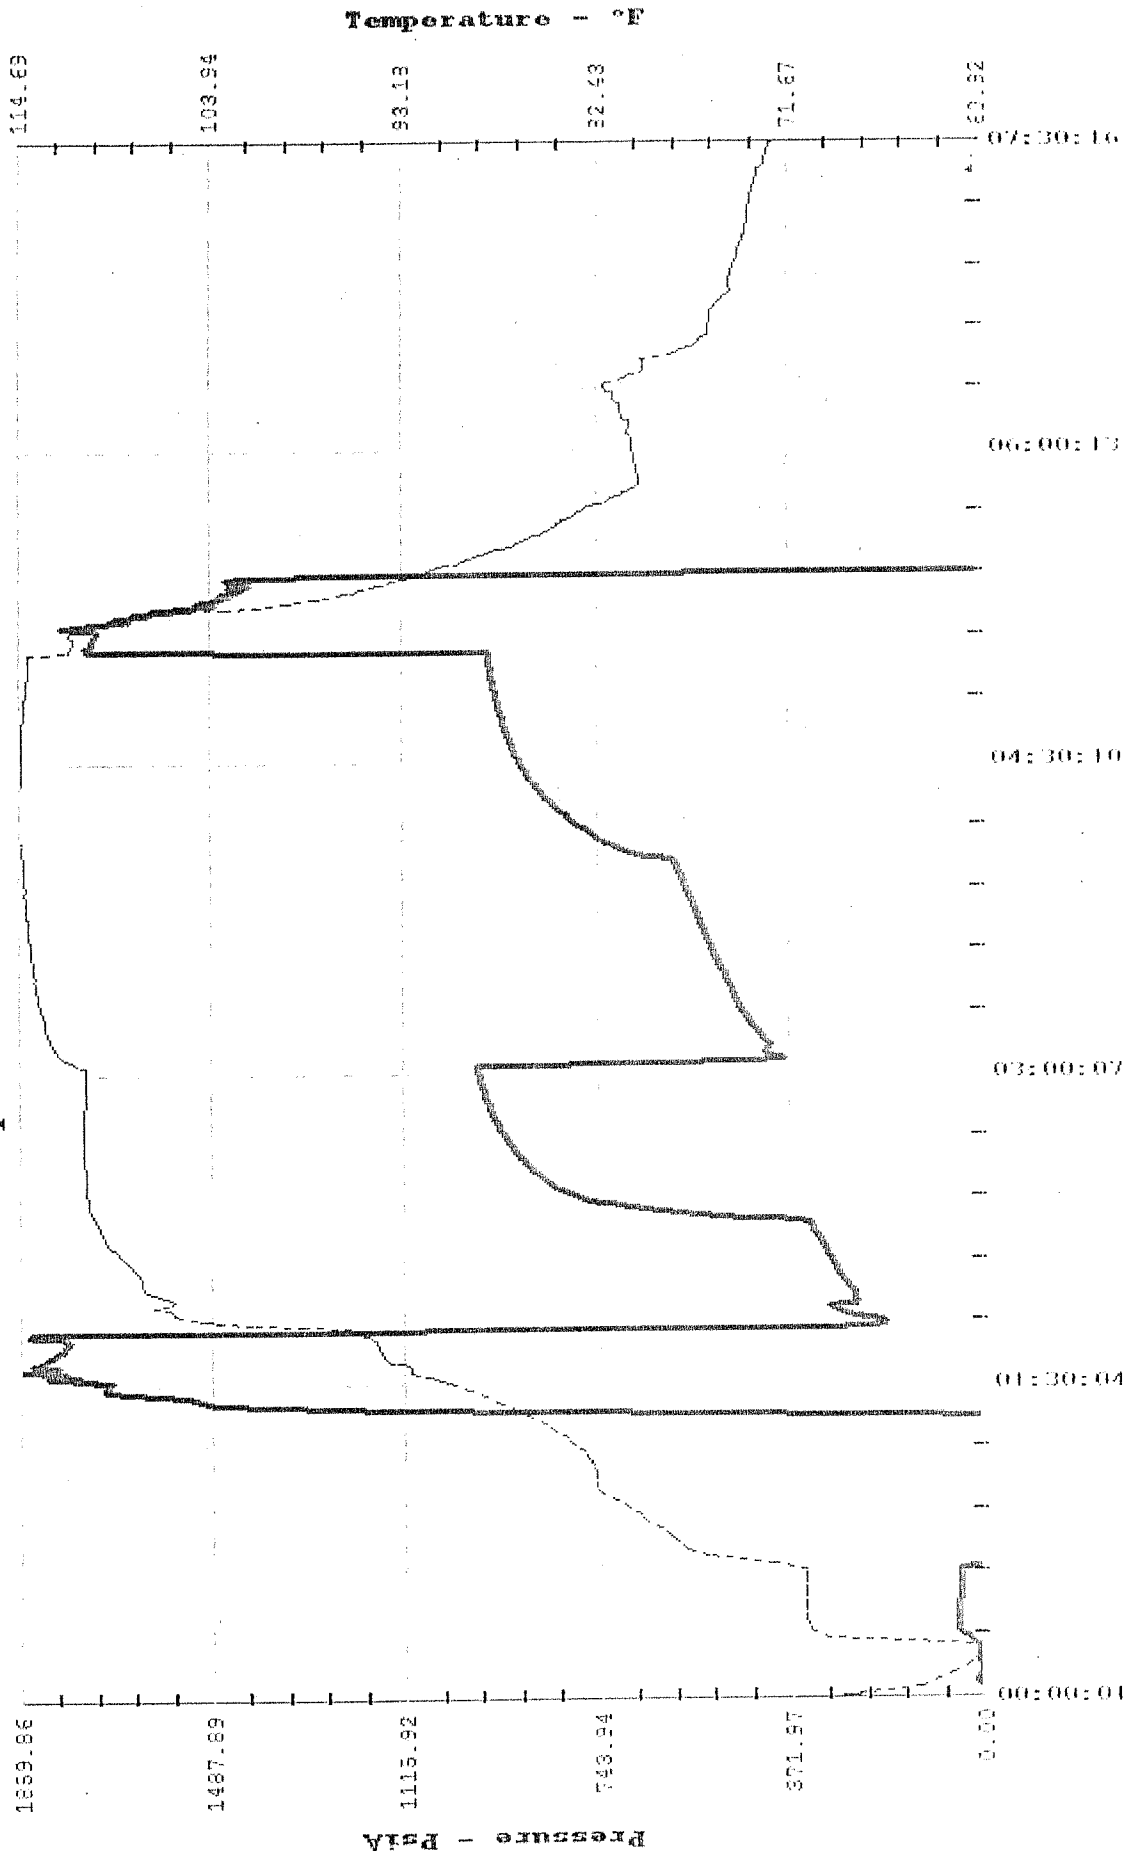

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902 KCB 1797

Date 3/4/06 Location 16-315-11W Elevation 1789 County Barber
 Company Globe Operating INC. Number of Copies 5

Parts Mailed to P.O. BOX 12 Great Bend KS 67530

Drilling Contractor ~~SWAPE~~ Southwind Drilling KCB #2

Length Drill Pipe ~~4248~~ 4248 I.D. Drill Pipe 3.80 Tool Joint Size 4 1/2 XH

Length Weight Pipe ~~80~~ NONE I.D. Weight Pipe --- Tool Joint Size ---

Length Drill Collars 30 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 XH

Top Packer Depth 4293 Bottom Packer Depth 4298 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 4298 TO 4330 ANCHOR LENGTH 32 TOTAL DEPTH 4330 Hole Size 7 3/4

WELL NO. E LAINE #1 FORMATION TESTED SWAPE TEST NO. 3

Mud Weight 9.4 Viscosity 36 Water Loss 10.8 Chlorides - Pits 7,000 D.S.T. ---

Maximum Temp. 110 °F Initial Hydrostatic Pressure (A) 2155 P.S.I. Final Hydrostatic Pressure (H) 2151 P.S.I.

Open I.F.P. from 1:45 m to 2:15 m 30 min

Closed I.C.I.P. from 2:15 m to 2:45 m 30 min

Open F.F.P. from 2:45 m to 3:15 m 30 min

Closed F.C.I.P. from 3:15 m to 3:45 m 30 min

Blow Very weak surface blow

Blow Very weak intermediate surface blow

Feet Recovered 600 Gravity of Oil --- Corrected ---

Feet of Drilling Mud % Gas --- % Oil --- % Mud --- % Water ---

Feet of --- % Gas --- % Oil --- % Mud --- % Water ---

Feet of --- % Gas --- % Oil --- % Mud --- % Water ---

Feet of --- % Gas --- % Oil --- % Mud --- % Water ---

Feet of --- % Gas --- % Oil --- % Mud --- % Water ---

Feet of --- % Gas --- % Oil --- % Mud --- % Water ---

Feet of --- % Gas --- % Oil --- % Mud --- % Water ---

Feet of --- % Gas --- % Oil --- % Mud --- % Water ---

Feet of --- % Gas --- % Oil --- % Mud --- % Water ---

Feet of --- % Gas --- % Oil --- % Mud --- % Water ---

Remarks ---

Extra Equipment - Jars --- Safety Joint --- Extra Packer --- Straddle --- Hook Wall ---

Top Recorder No. 4605 Clock No. electronic Depth 4326 Cir. Sub. --- Sampler ---

Bottom Recorder No. 3875 Clock No. 3539 Depth 4327 Insurance ---

Price of Job ---

Tool Operator NATHAN MANIASE

Approved By ---

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.


SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

(792-6902)

Company: GLOBE OPERATING INC.
RGE. 11W

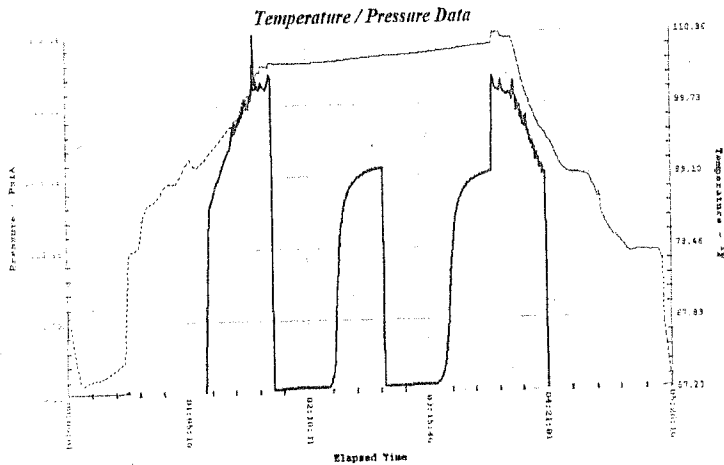

1	Initial Hydrostatic Pressure	2155
2	Initial Flow Pressure	22
3	Final Initial Flow Pressure	38
4	Initial Shut-In Pressure	1533
5	Initial Final Flow Pressure	42
6	Final Flow Pressure	48
7	Final Shut-In Pressure	1496
8	Final Hydrostatic Pressure	2151

Maximum Temperature 110

GENERAL INFORMATION

COMPANY NAME GLOBE OPERATING INC.

TEST DATE 3/4/06

SECTION-TOWN-RANGE 16-31S-11W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1789

COMPANY REPRESENTATIVE JOSH

LEASE AND WELL NUMBER ELAINE #1

FORMATION TESTED SWOPE

DRILL STEM TEST NUMBER 3

REPORT NUMBER 14445

ELEVATION KELLY BUSHINGS 1797

TESTING ENGINEER NATHAN MANRING

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4298

TEST INTERVAL (to) 4330

ANCHOR LENGTH 32

TOTAL DEPTH (ft) 4330

TOP PACKER DEPTH 4293

BOTTOM PACKER DEPTH 4298

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 1:45

INITIAL OPEN

TOOL OPEN (to) 2:15

FINAL OPEN

DURATION (min.) 30

TOOL OPEN (from) 2:45

TOOL OPEN (to) 3:15

DURATION (min.) 30

TOOL CLOSED (from) 2:15

INITIAL SHUT-IN

TOOL CLOSED (to) 2:45

FINAL SHUT-IN

DURATION (min.) 30

TOOL CLOSED (from) 3:15

TOOL CLOSED (to) 3:45

DURATION (min.) 30

INITIAL FLOW

VERY WEAK SURFACE BLOW

FINAL FLOW

VERY WEAK INTERMEDIATE SURFACE BLOW

DEPTH	RECOVERY	DESCRIPTION	CHLORIDES			
			% GAS	% OIL	% MUD	% WATER
60		DRILLING MUD				

Lease & Well No. ELAINE #1

Test #: 3

Date: 03-04-2006

SEC. 16 TWP. 31S

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GLOBE OPERATING INC.	LEASE AND WELL NUMBER	ELAINE #1
TEST DATE	3/4/06	FORMATION TESTED	SWOPE
SECTION-TOWN-RANGE	16-31S-11W	DRILL STEM TEST NUMBER	3
STATE	KANSAS	REPORT NUMBER	14445
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1797
ELEVATION GROUND LEVEL	1789	TESTING ENGINEER	NATHAN MANRING
COMPANY REPRESENTATIVE	JOSH		

EXTRA EQUIPMENT


JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
		PRATT	
TOP RECORDER DEPTH	4326	BOTTOM RECORDER DEPTH	4327
RECORDER NUMBER	4005	RECORDER NUMBER	3875

WELL INFORMATION

DRILLING CONTRACTOR	SOUTHWIND DRILLING RIG #2		
DRILL PIPE LENGTH	4248	DRILL COLLAR LENGTH	30
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.
WEIGHT PIPE LENGTH	NONE	MUD WEIGHT #/GAL	8.4
WEIGHT PIPE I.D.	2.25	VISCOSITY	46
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	10.8
		CHLORIDES-PITS	7,000
		CHLORIDES-DST	

COMMENTS

Temperature / Pressure Data

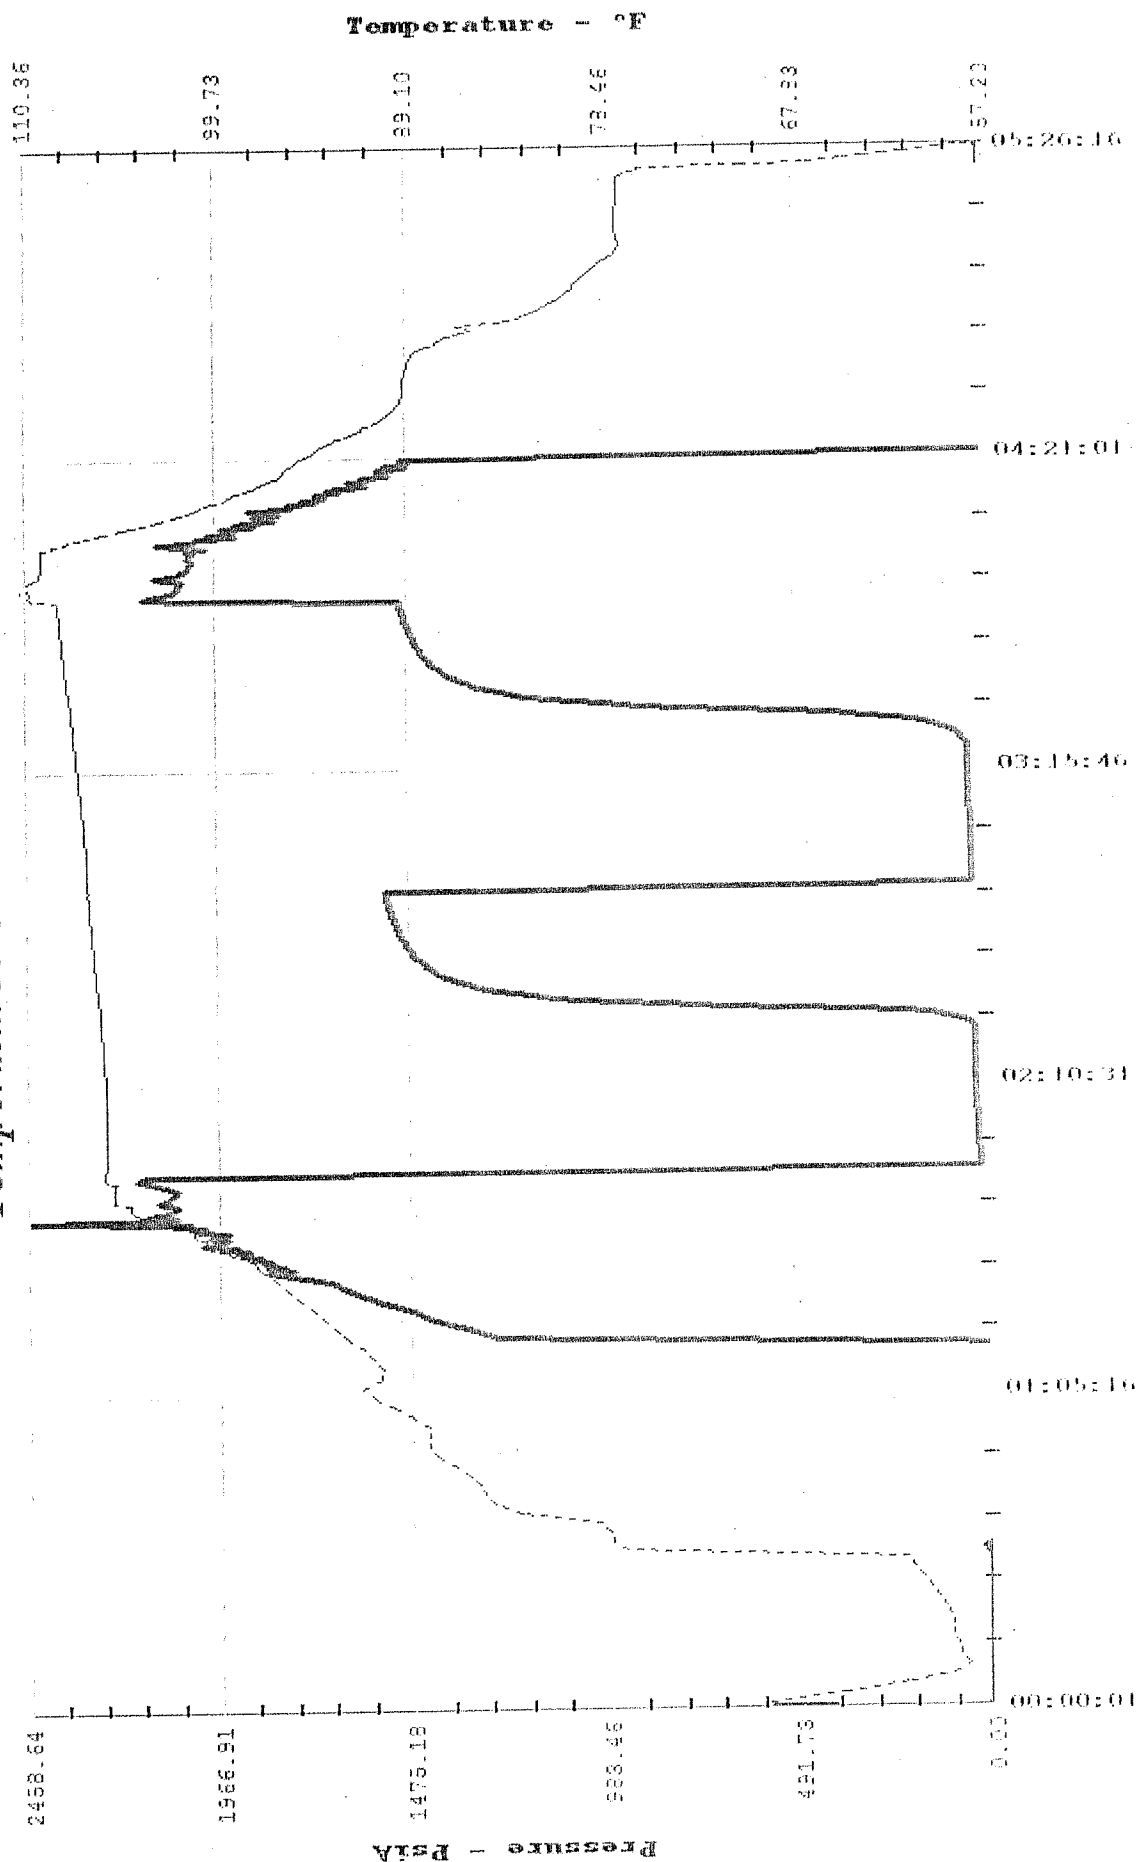

3-04-2006

16-31S-11W

ELAINE #1

GLOBE OPERATING INC.

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

KB 1797

Date 3/5/06 Location 16-31^S-11^W Elevation 1789 County Barber

Company Globe Operating Inc. Number of Copies _____

Parts Mailed to PO BOX 12 Great Bend KS 67530

Drilling Contractor Southwind Drilling KFC #2

Length Drill Pipe 4402 I.D. Drill Pipe 3.80 Tool Joint Size 4 1/2 X 14

Length Weight Pipe NONE I.D. Weight Pipe _____ Tool Joint Size _____

Length Drill Collars 30 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 X 14

Top Packer Depth 4447 Bottom Packer Depth 4452 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 4452 TO 4545 ANCHOR LENGTH 93 TOTAL DEPTH 4545 Hole Size 7 7/8

Case & Well No. Elaine #1 FORMATION TESTED Mississippi TEST NO. 4

Mud Weight 9.4 Viscosity 48 Water Loss 11.4 Chlorides - Pits 8,000 D.S.T. _____

Maximum Temp. 118 °F Initial Hydrostatic Pressure (A) 2302 P.S.I. Final Hydrostatic Pressure (H) 2196 P.S.I.

Time of Open I.F.P. from 4:30 m to 5:00 m 30 min

Time of Closed I.C.I.P. from 5:00 m to 5:45 m 45 min

Time of Open F.F.P. from 5:45 m to 6:45 m 60 min

Time of Closed F.C.I.P. from 6:45 m to 8:00 m 75 min

from [B] <u>87</u>	P.S.I. to [C] <u>268</u>	P.S.I.
[D] <u>951</u>		P.S.I.
from [E] <u>140</u>	P.S.I. to [F] <u>159</u>	P.S.I.
[G] <u>856</u>		P.S.I.

Initial Blow Fair blow built to bottom of 5 gallon bucket in 23 minutes

Final Blow Strong blow built to bottom of 5 gallon bucket less than 1 minute gas in 5

Total Feet Recovered 285 Gravity of Oil _____ Corrected _____

285 Feet of Gassy cut Drilling mud % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

_____ Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water _____

Remarks _____

Extra Equipment - Jars _____ Safety Joint _____ Extra Packer _____ Straddle _____ Hook Wall _____

Top Recorder No. 4005 Clock No. Electronic Depth 4341 Cir. Sub _____ Sampler _____

Bottom Recorder No. 3875 Clock No. 3539 Depth 4342 Insurance _____

Office of Job _____

Tool Operator NATHAN MANIREN

Approved By _____

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

(800)792-6902

Company: GLOBE OPERATING INC.
RGE. 11W


Lease & Well No. ELAINE #1

Test #: 4

Date: 03-05-2006

SEC. 16 TWP. 31S

Temperature / Pressure Data

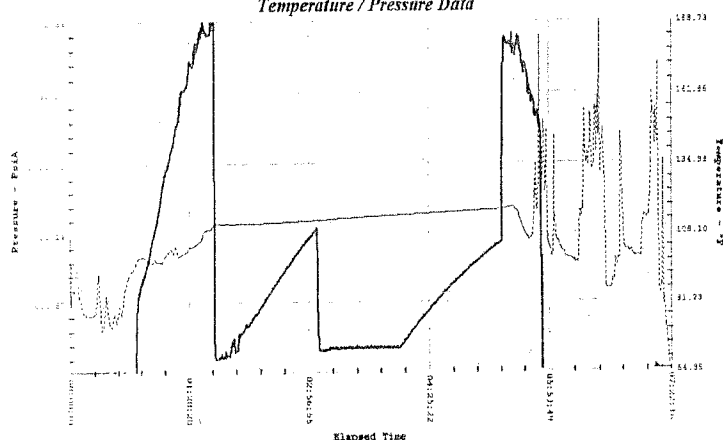

1	Initial Hydrostatic Pressure	2302
2	Initial Flow Pressure	87
3	Final Initial Flow Pressure	268
4	Initial Shut-In Pressure	951
5	Initial Final Flow Pressure	140
6	Final Flow Pressure	159
7	Final Shut-In Pressure	856
8	Final Hydrostatic Pressure	2196

Maximum Temperature 118

GENERAL INFORMATION

COMPANY NAME GLOBE OPERATING INC.

TEST DATE 3/5/06

SECTION-TOWN-RANGE 16-31S-11W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1789

COMPANY REPRESENTATIVE JOSH

LEASE AND WELL NUMBER ELAINE #1

FORMATION TESTED MISSISSIPPI

DRILL STEM TEST NUMBER 4

REPORT NUMBER 14446

ELEVATION KELLY BUSHINGS 1797

TESTING ENGINEER NATHAN MANRING

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4452

TEST INTERVAL (to) 4545

ANCHOR LENGTH 93

TOTAL DEPTH (ft) 4545

TOP PACKER DEPTH 4447

BOTTOM PACKER DEPTH 4452

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

TIME LOGS

TOOL OPEN (from) 4:30

INITIAL OPEN TOOL OPEN (to) 5:00

DURATION (min.) 30

TOOL OPEN (from) 5:45

TOOL OPEN (to) 6:45

DURATION (min.) 60

TOOL CLOSED (from) 5:00

INITIAL SHUT-IN TOOL CLOSED (to) 5:45

DURATION (min.) 45

TOOL CLOSED (from) 6:45

TOOL CLOSED (to) 8:00

DURATION (min.) 75

INITIAL FLOW FAIR BLOW BOTTOM OF 5 GALLON BUCKET IN 23 MINUTES

FINAL FLOW STRONG BLOW BOTTOM OF 5 GALLON BUCKET LESS THAN 1 MINUTE WITH GAS TO SURFACE IN 5 MINUTES SEE GAS FLOW REPORT

RECOVERY	RECOVERY DESCRIPTION	CHLORIDES			
		% GAS	% OIL	% MUD	% WATER
285	GASSY CUT DRILLING MUD				

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GLOBE OPERATING INC.	LEASE AND WELL NUMBER	ELAINE #1
TEST DATE	3/5/06	FORMATION TESTED	MISSISSIPPI
SECTION-TOWN-RANGE	16-31S-11W	DRILL STEM TEST NUMBER	4
STATE	KANSAS	REPORT NUMBER	14446
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1797
ELEVATION GROUND LEVEL	1789	TESTING ENGINEER	NATHAN MANRING
COMPANY REPRESENTATIVE	JOSH		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	70 MILES ROUND TRIP FROM	SAMPLER	NO
	PRATT		
TOP RECORDER DEPTH	4341	BOTTOM RECORDER DEPTH	4342
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	SOUTHWIND DRILLING RIG #2		
DRILL PIPE LENGTH	4402	DRILL COLLAR LENGTH	30
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.
WEIGHT PIPE LENGTH	NONE	MUD WEIGHT #/GAL	9.4
WEIGHT PIPE I.D.	2.25	VISCOSITY	48
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	11.4
		CHLORIDES-PITS	8,000
		CHLORIDES-DST	

COMMENTS

SUPERIOR TESTERS ENTERPRISES L.L.C.

GREAT BEND, KANSAS

GAS FLOW RATE

(800) 792-6902

#

STATE..... KANSAS

Test Date 1/0/1900

COUNTY..... BARBER

Sec Town Range 16-31S-11W

FIELD.....

Report Number 14446


Initial Flow

Comments	Time (hh:mm:ss)	Period dt (min)	Inches H2O Office Tester	PSI on Office Tester	PSI on Pitot Tube	Choke Size (in)	Gas Rate (MCF/Day)

Final Flow

Comments	Time (hh:mm:ss)	Period dt (min)	Inches H2O Office Tester	PSI on Office Tester	PSI on Pitot Tube	Choke Size (in)	Gas Rate (MCF/Day)
STRONG BLOW	6:00	10	4			1/4	3.170
GAS TO SURFACE	6:10	20	80			1/4	15.000
IN 5 MINUTES	6:20	30	20			1/2	28.000
	6:30	40	14			1/2	23.700
	6:40	50	12			1/2	21.900
	6:45	55	8			1/2	17.200

Temperature / Pressure Data

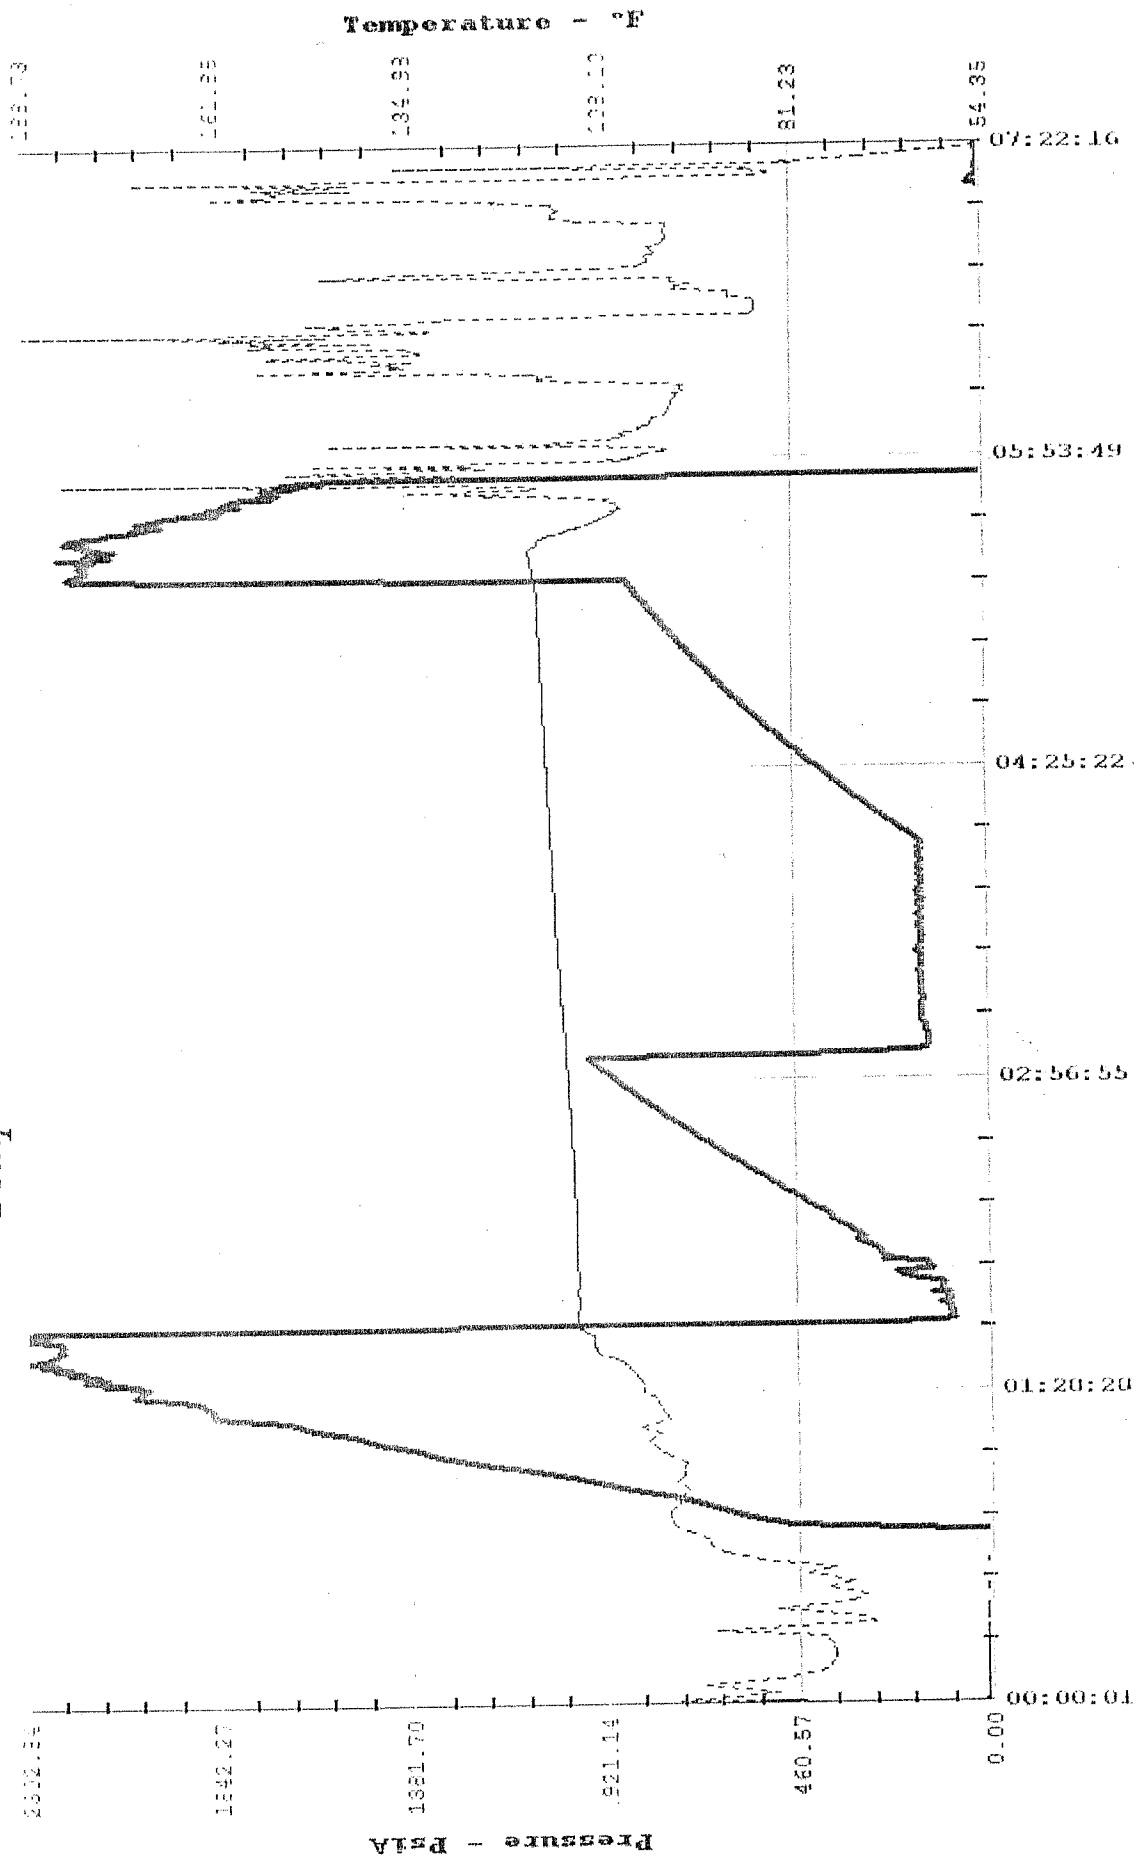

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

KD 1797

Date 3/6/06 Location 16-31^s-11^w Elevation 1789 County PARBET

Company Globe Operating INC Number of Copies 5

Charts Mailed to P.O. Box 12 Great Bend KS 67530

Drilling Contractor Southwind Drilling Rig #2

Length Drill Pipe 4568 I.D. Drill Pipe 3.80 Tool Joint Size 4 1/2 XH

Length Weight Pipe None I.D. Weight Pipe --- Tool Joint Size ---

Length Drill Collars 30 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 - XH

Top Packer Depth 4613 Bottom Packer Depth 4618 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 4618 TO 4633 ANCHOR LENGTH 15 TOTAL DEPTH 4633 Hole Size 7 1/8

EASE & WELL NO. Elaine #1 FORMATION TESTED Mississippi TEST NO. 5

Mud Weight 9.3 Viscosity 48 Water Loss 8.8 Chlorides - Pits 9000 D.S.T. ---

Maximum Temp. 116 °F Initial Hydrostatic Pressure (A) 2331 P.S.I. Final Hydrostatic Pressure (H) 2306 P.S.I.

Tool Open I.F.P. from 1:30 m to 1:58 m 28 min

Tool Closed I.C.I.P. from 1:58 m to 2:13 m 15 min

Tool Open F.F.P. from 2:13 m to 2:28 m 15 min

Tool Closed F.C.I.P. from 2:28 m to 2:47 m 15 min

from [B] <u>19.2</u> P.S.I. to [C] <u>21</u> P.S.I.
[D] <u>22</u> P.S.I.
from [E] <u>22</u> P.S.I. to [F] <u>22</u> P.S.I.
[G] <u>29</u> P.S.I.

Initial Blow very weak intermediate surface blow flush tool no help same blow

Final Blow No blow

Total Feet Recovered 2 feet Gravity of Oil --- Corrected

2 Feet of Drilling Mud %Gas --- %Oil --- %Mud --- %Water ---

Feet of --- %Gas --- %Oil --- %Mud --- %Water ---

Feet of --- %Gas --- %Oil --- %Mud --- %Water ---

Feet of --- %Gas --- %Oil --- %Mud --- %Water ---

Feet of --- %Gas --- %Oil --- %Mud --- %Water ---

Feet of --- %Gas --- %Oil --- %Mud --- %Water ---

Feet of --- %Gas --- %Oil --- %Mud --- %Water ---

Feet of --- %Gas --- %Oil --- %Mud --- %Water ---

Feet of --- %Gas --- %Oil --- %Mud --- %Water ---

Remarks 4 1/2 bridge at 3733 ft and 4000 ft

1-3873 feet shut slide for 60 feet

Extra Equipment - Jars --- Safety Joint --- Extra Packer --- Straddle --- Hook Wall ---

Top Recorder No. 4005 Clock No. Electronic Depth 4629 Cir. Sub --- Sampler ---

Bottom Recorder No. 3873 Clock No. 3539 Depth 4630 Insurance ---

Price of Job ---

Tool Operator [Signature]

Approved By ---

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.


SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

1(800)792-6902

GREAT BEND, KANSAS 67530

Company: GLOBE OPERATING INC.
RGE. 11W

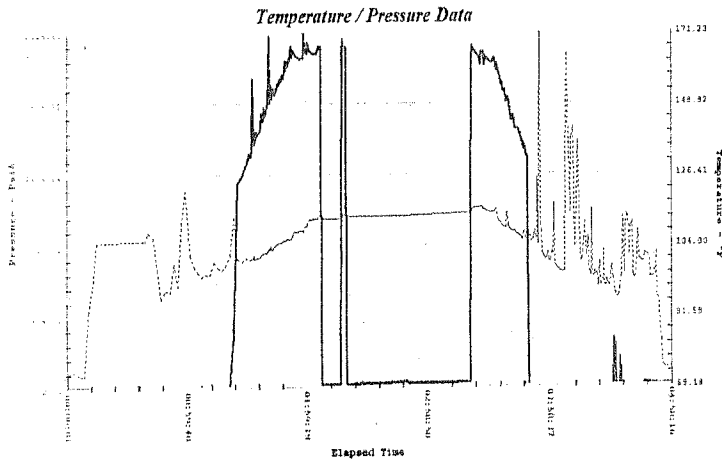

1	Initial Hydrostatic Pressure	2331
2	Initial Flow Pressure	19
3	Final Initial Flow Pressure	21
4	Initial Shut-In Pressure	22
5	Initial Final Flow Pressure	21
6	Final Flow Pressure	22
7	Final Shut-In Pressure	29
8	Final Hydrostatic Pressure	2306

Maximum Temperature 116

GENERAL INFORMATION

COMPANY NAME GLOBE OPERATING INC.

TEST DATE 3/6/06

SECTION-TOWN-RANGE 16-31S-11W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1789

COMPANY REPRESENTATIVE JOSH

LEASE AND WELL NUMBER ELAINE #1

FORMATION TESTED MISSISSIPPI

DRILL STEM TEST NUMBER 5

REPORT NUMBER 14447

ELEVATION KELLY BUSHINGS 1797

TESTING ENGINEER NATNAN MANRING

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4618

TEST INTERVAL (to) 4633

ANCHOR LENGTH 15

TOTAL DEPTH (ft) 4633

TOP PACKER DEPTH 4613

BOTTOM PACKER DEPTH 4618

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 1:30

INITIAL OPEN TOOL OPEN (to) 1:58

DURATION (min.) 28

FINAL OPEN

TOOL OPEN (from) 2:13

TOOL OPEN (to) 2:28

DURATION (min.) 15

TOOL CLOSED (from) 1:58

INITIAL SHUT-IN TOOL CLOSED (to) 2:13

DURATION (min.) 15

FINAL SHUT-IN

TOOL CLOSED (from) 2:28

TOOL CLOSED (to) 2:43

DURATION (min.) 15

INITIAL FLOW

VERY WEAK INTERMEDIATE SURFACE BLOW FLUSHED TOOL GOOD SURGE
NO HELP BLOW STILL THE SAME AND DIED 13 MIN AFTER FLUSH

FINAL FLOW

NO BLOW

RESISTIVITY		AT	DEGREES	CHLORIDES			
FEET OF	RECOVERY	DESCRIPTION		% GAS	% OIL	% MUD	% WATER
Recovery	2						
1)	2	DRILLING MUD					
2)							
3)							
4)							
5)							

Lease & Well No. ELAINE #1

Test #: 5

Date: 03-06-2006

SEC. 16 TWP. 31S

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GLOBE OPERATING INC.	LEASE AND WELL NUMBER	ELAINE #1
TEST DATE	3/6/06	FORMATION TESTED	MISSISSIPPI
SECTION-TOWN-RANGE	16-31S-11W	DRILL STEM TEST NUMBER	5
STATE	KANSAS	REPORT NUMBER	14447
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1797
ELEVATION GROUND LEVEL	1789	TESTING ENGINEER	NATHAN MANRING
COMPANY REPRESENTATIVE	JOSH		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	70 MILES ROUND TRIP FROM	PRATT	
TOP RECORDER DEPTH	4629	BOTTOM RECORDER DEPTH	4630
RECORDER NUMBER	91981	RECORDER NUMBER	5463


WELL INFORMATION

DRILLING CONTRACTOR	SOUTHWIND RIG #2	DRILL COLLAR LENGTH	30
DRILL PIPE LENGTH	4568	DRILL COLLAR I.D.	2.25
DRILL PIPE I.D.	3.8	TOOL JOINT SIZE	4 1/2 X.H.
TOOL JOINT SIZE	4 1/2 X.H.		
WEIGHT PIPE LENGTH	NONE	MUD WEIGHT #/GAL	9.3
WEIGHT PIPE I.D.	2.25	VISCOSITY	48
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	8.8
		CHLORIDES-PITS	9,000
		CHLORIDES-DST	

COMMENTS

HIT BRIDGE AT 3733 FEET AND ANOTHER AT 3973 THAT SLID ABOUT 60 FEET

Temperature / Pressure Data

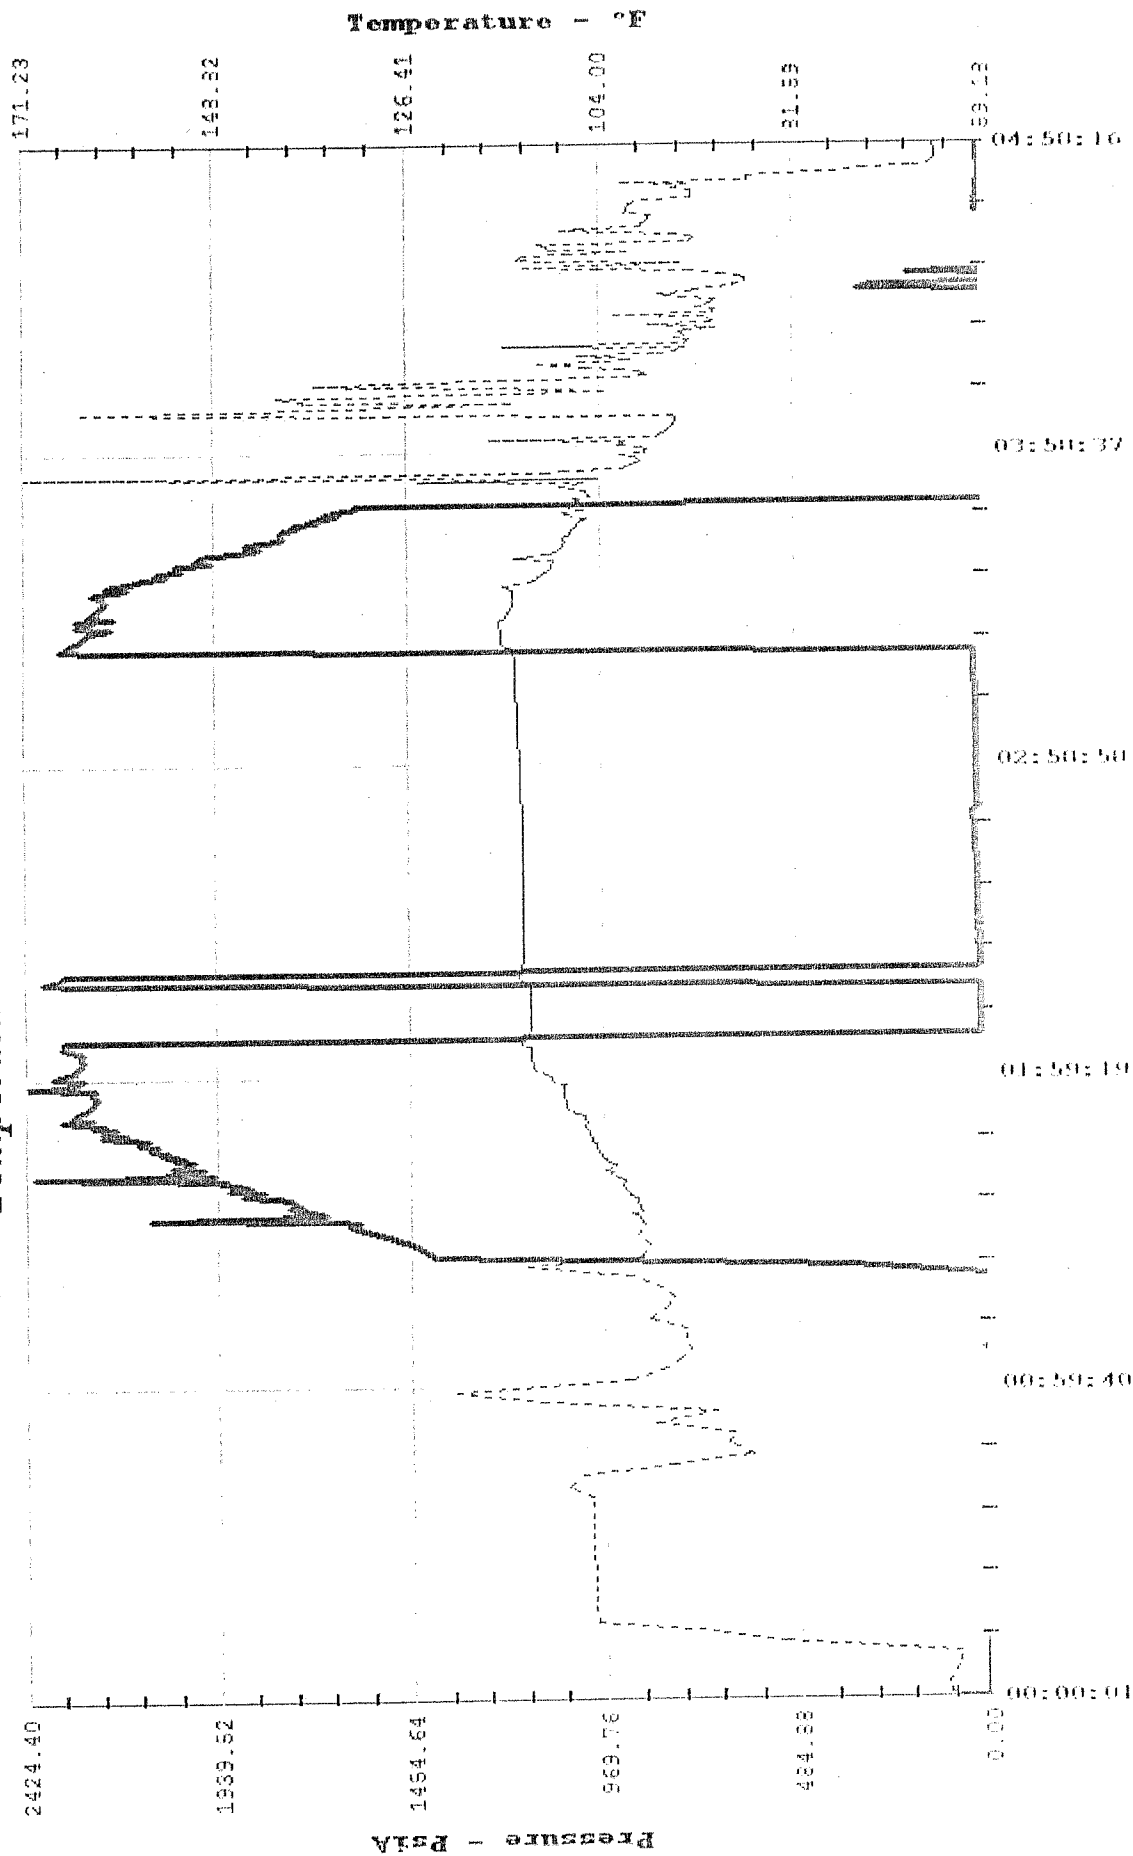

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

KB 1797

Date 3-7-06 Location 16-215-11^W Elevation 1784 County Barber

Company Caloche Operating Inc Number of Copies 5

Charts Mailed to R.D. Box 12 Great Bend KS

Drilling Contractor Southwind Drilling Rig #2

Length Drill Pipe 4802 I.D. Drill Pipe 3.80 Tool Joint Size 4 1/2 XH

Length Weight Pipe NONE I.D. Weight Pipe --- Tool Joint Size ---

Length Drill Collars 30 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 XH

Top Packer Depth 4847 Bottom Packer Depth 4852 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 4852 TO 4874 ANCHOR LENGTH 22 TOTAL DEPTH 4874 Hole Size 7 7/8

LEASE & WELL NO. ELaine #1 FORMATION TESTED Simpson TEST NO. Lo

Fluid Weight 9.4 Viscosity 45 Water Loss 10.0 Chlorides - Pits 9,500 D.S.T. 18,000

Maximum Temp. 118 °F Initial Hydrostatic Pressure (A) 2380 P.S.I. Final Hydrostatic Pressure (H) 2546 P.S.I.

Oil Open I.F.P. from 9:40 m to 9:55 m 15 min

Oil Closed I.C.I.P. from 9:55 m to 10:25 m 30 min

Oil Open F.F.P. from 10:25 m to 10:40 m 15 min

Oil Closed F.C.I.P. from 10:40 m to 11:10 m 30 min

Initial Blow Very weak surface blow flushed tool good surge no help same blow

Final Blow no blow flushed tool good surge weak surface blow

Total Feet Recovered 58 Gravity of Oil --- Corrected

58 Feet of NATURAL DRILLING MUD % Gas --- % Oil 60 % Mud 40 % Water

Feet of --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- % Gas --- % Oil --- % Mud --- % Water

Remarks ---

Extra Equipment - Jars --- Safety Joint --- Extra Packer --- Straddle --- Hook Wall ---

Top Recorder No. 4005 Clock No. electronic Depth 4870 Cir. Sub --- Sampler ---

Bottom Recorder No. 3875 Clock No. 3539 Depth 4871 Insurance ---

Price of Job ---

Oil Operator NATHAN MAJRTUL

Approved By ---

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530


1(800)792-6902

Company: GLOBE OPERATING INC.
RGE. 11W

Lease & Well No. ELAINE #1

Test #: 6 Date: 03-07-2006

SEC. 16 TWP. 31S

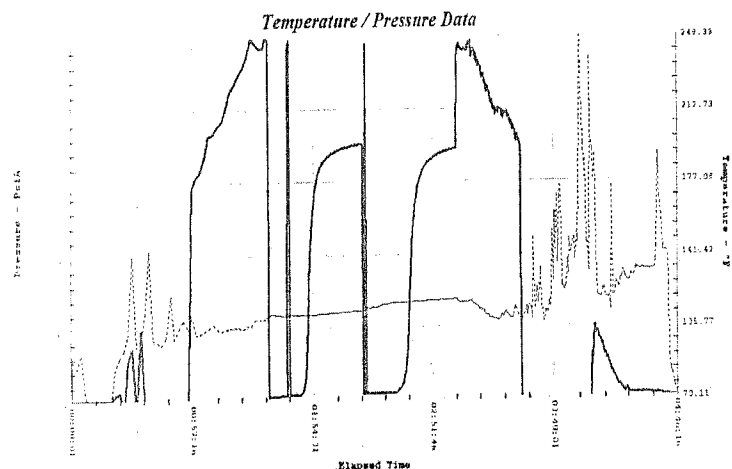

1	Initial Hydrostatic Pressure	2380
2	Initial Flow Pressure	20
3	Final Initial Flow Pressure	34
4	Initial Shut-In Pressure	1688
5	Initial Final Flow Pressure	40
6	Final Flow Pressure	42
7	Final Shut-In Pressure	1654
8	Final Hydrostatic Pressure	2346

Maximum Temperature 118

GENERAL INFORMATION

COMPANY NAME GLOBE OPERATING INC.

TEST DATE 3/7/06

SECTION-TOWN-RANGE 16-31S-11W

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1789

COMPANY REPRESENTATIVE JOSH

LEASE AND WELL NUMBER ELAINE #1

FORMATION TESTED SIMPSON

DRILL STEM TEST NUMBER 6

REPORT NUMBER 14448

ELEVATION KELLY BUSHINGS 1797

TESTING ENGINEER NATHAN MANRING

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4852

TEST INTERVAL (to) 4874

ANCHOR LENGTH 22

TOTAL DEPTH (ft) 4874

TOP PACKER DEPTH 4847

BOTTOM PACKER DEPTH 4852

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

TIME LOGS

TOOL OPEN (from) 9:40

INITIAL OPEN TOOL OPEN (to) 9:55

DURATION (min.) 15

FINAL OPEN

TOOL OPEN (from) 10:25

TOOL OPEN (to) 10:40

DURATION (min.) 15

TOOL CLOSED (from) 9:55

INITIAL SHUT-IN TOOL CLOSED (to) 10:25

DURATION (min.) 30

FINAL SHUT-IN

TOOL CLOSED (from) 10:40

TOOL CLOSED (to) 11:10

DURATION (min.) 30

INITIAL FLOW

VERY WEAK SURFACE BLOW FLUSHED TOOL GOOD SURGE NO HELP STILL
HAD SAME BLOW

FINAL FLOW

NO BLOW FLUSHED TOOL GOOD SURGE THEN HAD WEAK SURFACE BLOW

ELT OF	RECOVERY	DESCRIPTION	CHLORIDES			
			% GAS	% OIL	% MUD	% WATER
58	58	WATERY DRILLING MUD			60	40
1)	33					
2)						
3)						
4)						
5)						

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GLOBE OPERATING INC.	LEASE AND WELL NUMBER	ELAINE #1
TEST DATE	3/7/06	FORMATION TESTED	SIMPSON
SECTION-TOWN-RANGE	16-31S-11W	DRILL STEM TEST NUMBER	6
STATE	KANSAS	REPORT NUMBER	14448
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1797
ELEVATION GROUND LEVEL	1789	TESTING ENGINEER	NATHAN MANRING
COMPANY REPRESENTATIVE	JOSH		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
		SAMPLER	NO
	70 MILES ROUND TRIP FROM	PRATT	
TOP RECORDER DEPTH	4870	BOTTOM RECORDER DEPTH	4871
RECORDER NUMBER	91981	RECORDER NUMBER	5463


WELL INFORMATION

DRILLING CONTRACTOR	SOUTHWIND DRILLING RIG #2		
DRILL PIPE LENGTH	4802	DRILL COLLAR LENGTH	30
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.
WEIGHT PIPE LENGTH	NONE	MUD WEIGHT #/GAL	9.4
WEIGHT PIPE I.D.	2.25	VISCOSITY	45
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	10
		CHLORIDES-PITS	9,500
		CHLORIDES-DST	

COMMENTS

HIT BRIDGE AT 3673 SLIDE 30 FEET

Temperature / Pressure Data

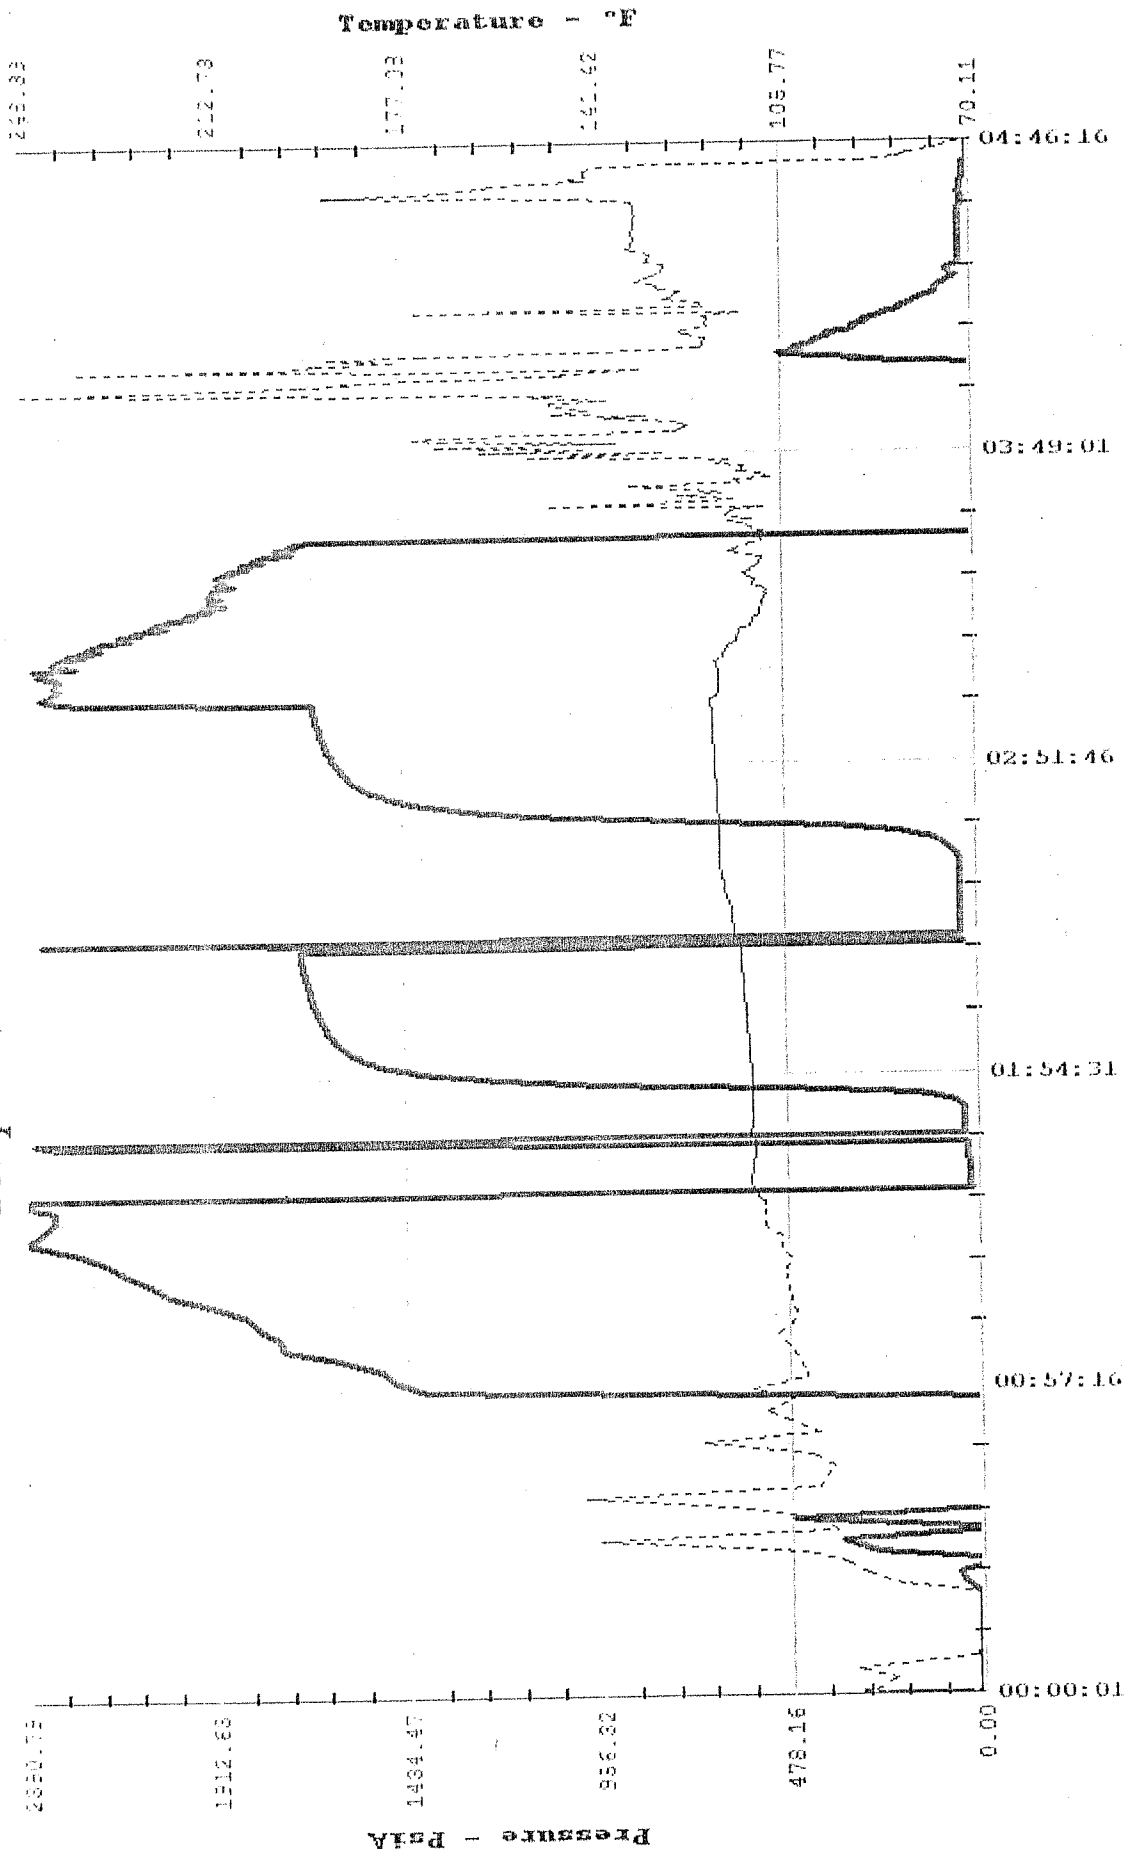

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902 KD 1797

Date 3/8/06 Location 16-31^S-11^W Elevation 1789 County Barber

Company Globe Operating Inc Number of Copies 5

Parts Mailed to P.O. BOX 12 Great Bend KS 67530

Drilling Contractor Southwind Drilling RIC #2

Length Drill Pipe 4803 I.D. Drill Pipe 3.80 Tool Joint Size 4 1/2 XH

Length Weight Pipe NONE I.D. Weight Pipe --- Tool Joint Size ---

Length Drill Collars 30 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2 XH

Top Packer Depth 4848 Bottom Packer Depth 4853 Number of Packers 2 Packer Size 6 3/4

TESTED FROM 4853 TO 4880 ANCHOR LENGTH 27 TOTAL DEPTH 4880 Hole Size 7 7/8

EASE & WELL NO. ELAIRE #2 FORMATION TESTED Simspon TEST NO. 7

Mud Weight 9.3 Viscosity 600 Water Loss 12.8 Chlorides - Pits 6,100 D.S.T. 26,000

Maximum Temp. 119 °F Initial Hydrostatic Pressure (A) 2389 P.S.I. Final Hydrostatic Pressure (H) 2353 P.S.I.

Tool Open I.F.P. from 10:00 m to 10:45 m 45 min

Tool Closed I.C.I.P. from 10:45 m to 11:15 m 38 min

Tool Open F.F.P. from 12:15 m to 12:40 m 45 min

Tool Closed F.C.I.P. from 12:00 m to 1:00 m 60 min

Initial Blow Very Weak blow built to 33 1/4 inches in 5 gallon bucket in 45 minutes

Final Blow Very Weak blow built to 1 1/2 inches in 5 gallon bucket in 45 minutes

Total Feet Recovered 115

Feet of 50 trace oil cut watery mud

Feet of 5 95% mud, water, cut oil

Feet of 60 trace oil cut muddy water

Feet of --- --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- --- % Gas --- % Oil --- % Mud --- % Water

Feet of --- --- % Gas --- % Oil --- % Mud --- % Water

Remarks ---

Extra Equipment - Jars --- Safety Joint --- Extra Packer --- Straddle --- Hook Wall ---

Top Recorder No. 4005 Clock No. electronic Depth 4876 Cir. Sub --- Sampler ---

Bottom Recorder No. 3875 Clock No. 3539 Depth 4877 Insurance ---

Price of Job ---

Tool Operator NATHAN MANRING

Approved By ---

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, of for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

1(800)792-6902


GREAT BEND, KANSAS 67530

Company: GLOBE OPERATING INC
RGE. 11W

Lease & Well No. ELAINE #1

Test #: Date: 03-08-2006

SEC. 16 TWP. 31S

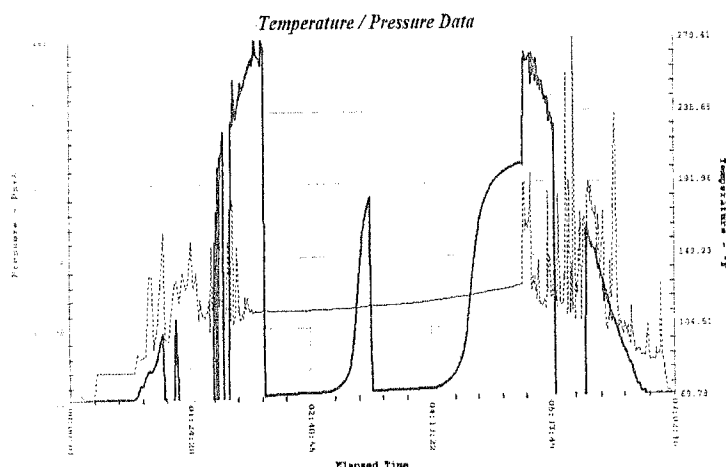

1	Initial Hydrostatic Pressure	2389
2	Initial Flow Pressure	26
3	Final Initial Flow Pressure	52
4	Initial Shut-In Pressure	1378
5	Initial Final Flow Pressure	59
6	Final Flow Pressure	72
7	Final Shut-In Pressure	1603
8	Final Hydrostatic Pressure	2353

Maximum Temperature 119

GENERAL INFORMATION

COMPANY NAME GLOBE OPERATING INC.

TEST DATE 3/8/06

SECTION-TOWN-RANGE 16-31S-11

STATE KANSAS

COUNTY BARBER

ELEVATION GROUND LEVEL 1789

COMPANY REPRESENTATIVE JOSH

LEASE AND WELL NUMBER ELAINE #1

FORMATION TESTED SIMPSON

DRILL STEM TEST NUMBER 7

REPORT NUMBER 14449

ELEVATION KELLY BUSHINGS 1797

TESTING ENGINEER NATHAN MANRING

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4853

TEST INTERVAL (to) 4880

ANCHOR LENGTH 27

TOTAL DEPTH (ft) 4880

TOP PACKER DEPTH 4848

BOTTOM PACKER DEPTH 4853

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 10:00

INITIAL OPEN TOOL OPEN (to) 10:45

DURATION (min.) 45

TOOL CLOSED (from) 10:45

INITIAL SHUT-IN TOOL CLOSED (to) 11:15

DURATION (min.) 30

TOOL OPEN (from) 11:15

TOOL OPEN (to) 12:00

DURATION (min.) 45

TOOL CLOSED (from) 12:00

TOOL CLOSED (to) 1:00

DURATION (min.) 60

INITIAL FLOW VERY WEAK BLOW BUILT TO 3 3/4 INCHES IN 5 GALLON BUCKET IN 45 MINUTES

INITIAL FLOW VERY WEAK BLOW BUILT TO 1 1/2 INCHES IN 5 GALLON BUCKET IN 45 MINUTES

ELT OF	RESISTIVITY		AT	DEGREES	CHLORIDES		26000
	150 GAS	RECOVERY			%	%	%
to recovery	115	DESCRIPTION			GAS	OIL	MUD
1) 50		TRACE OIL CUT Watery MUD				TRACE	55
2) 5		MUD WATER CUT OIL				95	5
3) 60		TRACE OIL CUT MUDDY WATER				TRACE	45
4)							55
5)							

SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME	GLOBE OPERATING INC.	LEASE AND WELL NUMBER	ELAINE #1
TEST DATE	3/8/06	FORMATION TESTED	SIMPSON
SECTION-TOWN-RANGE	16-31S-11	DRILL STEM TEST NUMBER	7
STATE	KANSAS	REPORT NUMBER	14449
COUNTY	BARBER	ELEVATION KELLY BUSHINGS	1797
ELEVATION GROUND LEVEL	1789	TESTING ENGINEER	NATHAN MANRING
COMPANY REPRESENTATIVE	JOSH		

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	NO	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOK WALL	NO
	70 MILES ROUND TRIP FROM	SAMPLER	NO
	PRATT		
TOP RECORDER DEPTH	4876	BOTTOM RECORDER DEPTH	4877
RECORDER NUMBER	91981	RECORDER NUMBER	5463

WELL INFORMATION

DRILLING CONTRACTOR	SOUTHWIND DRILLING RIG #2		
DRILL PIPE LENGTH	4803	DRILL COLLAR LENGTH	30
DRILL PIPE I.D.	3.8	DRILL COLLAR I.D.	2.25
TOOL JOINT SIZE	4 1/2 X.H.	TOOL JOINT SIZE	4 1/2 X.H.
WEIGHT PIPE LENGTH	NONE	MUD WEIGHT #/GAL	9.3
WEIGHT PIPE I.D.	2.25	VISCOSITY	60
TOOL JOINT SIZE	4 1/2 X.H.	WATER LOSS	12.8
		CHLORIDES-PITS	6,000
		CHLORIDES-DST	

COMMENTS

HIT BRIDGE AT 3980 SLIDE ABOUT 15 FEET

Temperature / Pressure Data

