

Company	Falcon Exploration, Inc.	Lease Name	Fulton	
Address	125 N. Market, Ste 1252	Lease #	2-11	
CSZ	Wichita, KS 67202	Legal Desc	SW-NW-SE-NE	Job Ticket 2020
Attn.	Keith Reavis	Section	11	Range 22W
		Township	31S	
		County	Clark	State KS
		Drilling Cont	Val Energy, Inc. Rig #2	
Comments	Charged double for mileage because I had to go back and get my tool.			

GENERAL INFORMATION

Test # **1** Test Date **10/13/2007**
 Tester **Tim Venters**
 Test Type **Conventional Bottom Hole**
 Successful Test
 # of Packers **2.0** Packer Size **6 3/4**

Mud Type **Gel Chem**
 Mud Weight **8.8** Viscosity **62.0**
 Filtrate **9.6** Chlorides **4500**

Drill Collar Len **0**
 Wght Pipe Len **0**

Formation **Morrow/Mississippian**
 Interval Top **5133.0** Bottom **5183.0**
 Anchor Len Below **50.0** Between **0**

Total Depth **5183.0**
 Blow Type **Weak surface blow at the start of the initial flow period, building to 1/4 inch, but after 3 minutes, depleting ending with a very weak surface blow. Weak blow at the start of the final flow period, that built to 6 inches. Times: 6, 75, 120, 180.**

Chokes **3/4** Hole Size **7 7/8**
 Top Recorder # **W1022**
 Mid Recorder #
 Bott Recorder # **13565**


Mileage **312** Approved By
 Standby Time **14**
 Extra Equipmnt **Jars & Safety joint**
 Time on Site **3:45 PM**
 Tool Picked Up **8:00 AM**
 Tool Layed Dwn **8:10 PM**

Elevation **2157.00** Kelley Bushings **2167.00**

Start Date/Time **10/13/2007 7:39 AM**
 End Date/Time **10/13/2007 8:36 PM**

RECOVERY

Feet	Description	Gas	Oil	Water	Mud
35	Very small trace of oil cut mud	0% 0ft	trace	0% 0ft	100% 35ft
DST Fluids 0					

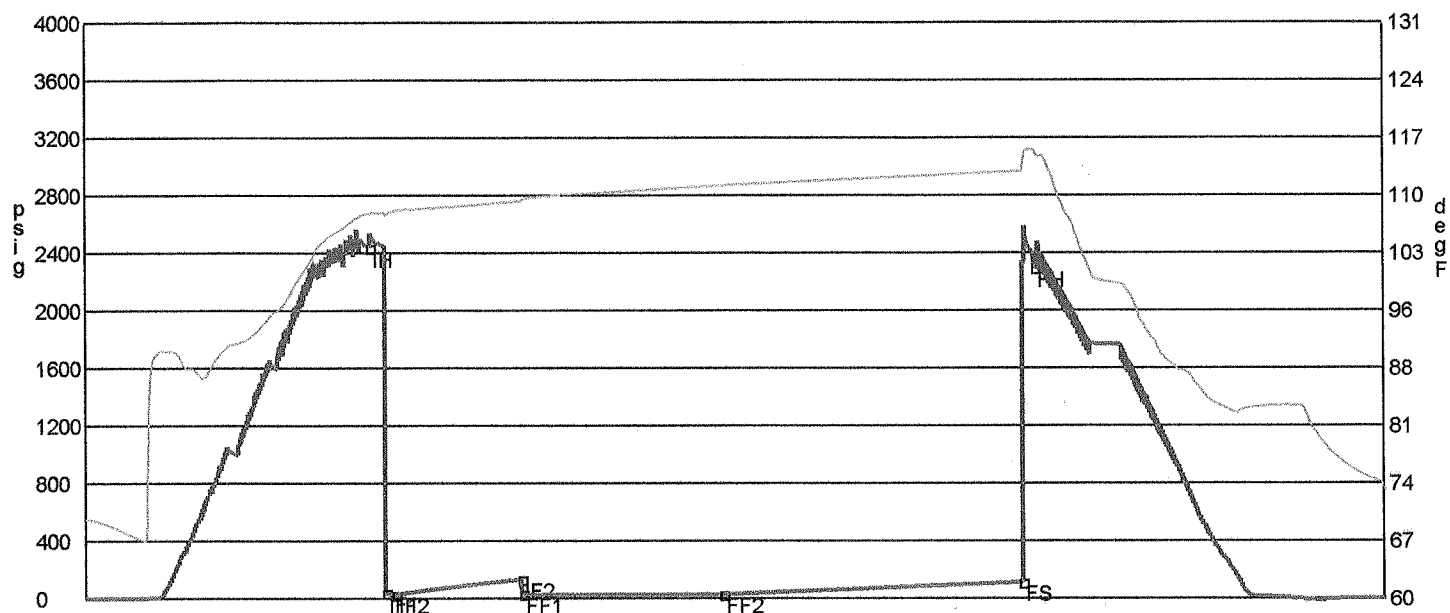

	Date	Time	Pressure	Temp	
IH	10/13/2007 10:28:00 AM	2.816667	2437.282	107.46	Initial Hydro-static
IF1	10/13/2007 10:37:15 AM	2.970833	40.458	107.33	Initial Flow (1)
IF2	10/13/2007 10:43:00 AM	3.066667	29.937	107.818	Initial Flow (2)
IF2	10/13/2007 11:58:30 AM	4.325	134.213	109.047	Initial Flow (2)
FF1	10/13/2007 11:59:15 AM	4.3375	32.824	109.086	Final Flow (1)
FF2	10/13/2007 1:58:45 PM	6.329167	28.91	110.944	Final Flow (2)
FS	10/13/2007 4:57:45 PM	9.3125	114.182	112.67	Final Shut-In
FH	10/13/2007 5:05:30 PM	9.441667	2294.833	115.236	Final Hydro-static

GAS FLOWS

Min Into IFP Min Into FFP Gas Flows Pressure Choke
