


Flow Time	1st Min.	2nd Min.	30	Date	3-13-62	Ticket Number	300235
Closed In Press. Time	1st Min.	2nd Min.	30	Kind of Job	Open Hole	Halliburton District	Elkhart
Pressure Readings	Field	Office Corrected		Tester	T.L. Dodson	Witness	Edgar Carson
Depth Top Gauge	4802 Ft.	No Blanked Off		Drilling Contractor	Lohman - Johnson		
BT. P.R.D. No.	373	- Hour Clock		Elevation	-	Top Packer	-
Initial Hydro Mud Pressure	2280	2272		Total Depth	4910'	Bottom Packer	4890'
Initial Closed in Pres.				Interval Tested	4890-4910'	Formation Tested	Morrow
Initial Flow Pres.	5	2 11		Casing or Hole Size	7 7/8"	Casing Perfs. } Top	
Final Flow Pres.	5	2 11		Surface Choke	1"	Bottom Choke	1/2"
Final Closed in Pres.	10	21		Size & Kind Drill Pipe	4 1/2" FH	Drill Collars Above Tester	2 1/4" x 238'
Final Hydro Mud Pressure	2280	2272		Mud Weight	9.4	Mud Viscosity	47
Depth Cen. Gauge		Blanked Off		Temperature	120 °F Est.	Anchor Size & Length	ID 3" OD 5" X 20'
BT. P.R.D. No.		Hour Clock		Depths Mea. From	KB	Depth of Tester Valve	4797' Ft.
Initial Hydro Mud Pres.				Cushion		Depth Back Pres. Valve	4892' Ft.
Initial Closed in Pres.				Recovered	2 Feet of	drlg mud	
Initial Flow Pres.		2		Recovered		Feet of	
Final Flow Pres.		2		Recovered		Feet of	
Final Closed in Pres.				Recovered		Feet of	
Final Hydro Mud Pres.				Oil A.P.I. Gravity		Water Spec. Gravity	
Depth Bot. Gauge	4910 Ft.	Yes Blanked Off		Gas Gravity		Surface Pressure	psi
BT. P.R.D. No.	376	- Hour Clock		Tool Opened	10:34 A.M.	Tool Closed	11:04 A.M.
Initial Hydro Mud Pres.	2615	2567		Remarks	Open tool with a weak blow and dying		
Initial Closed in Pres.				to no blow in 15 mins. Off bottom at 11:34 AM.			
Initial Flow Pres.	15	2 36					
Final Flow Pres.	15	2 36					
Final Closed in Pres.	20	46					
Final Hydro Mud Pres.	2615	2567					


FORMATION TEST DATA

* Potentiometric Surface Reference to Rotary Table When Elevation Not Given, Fresh Water Corrected to 100° F.

↑ PRESSURE ↓

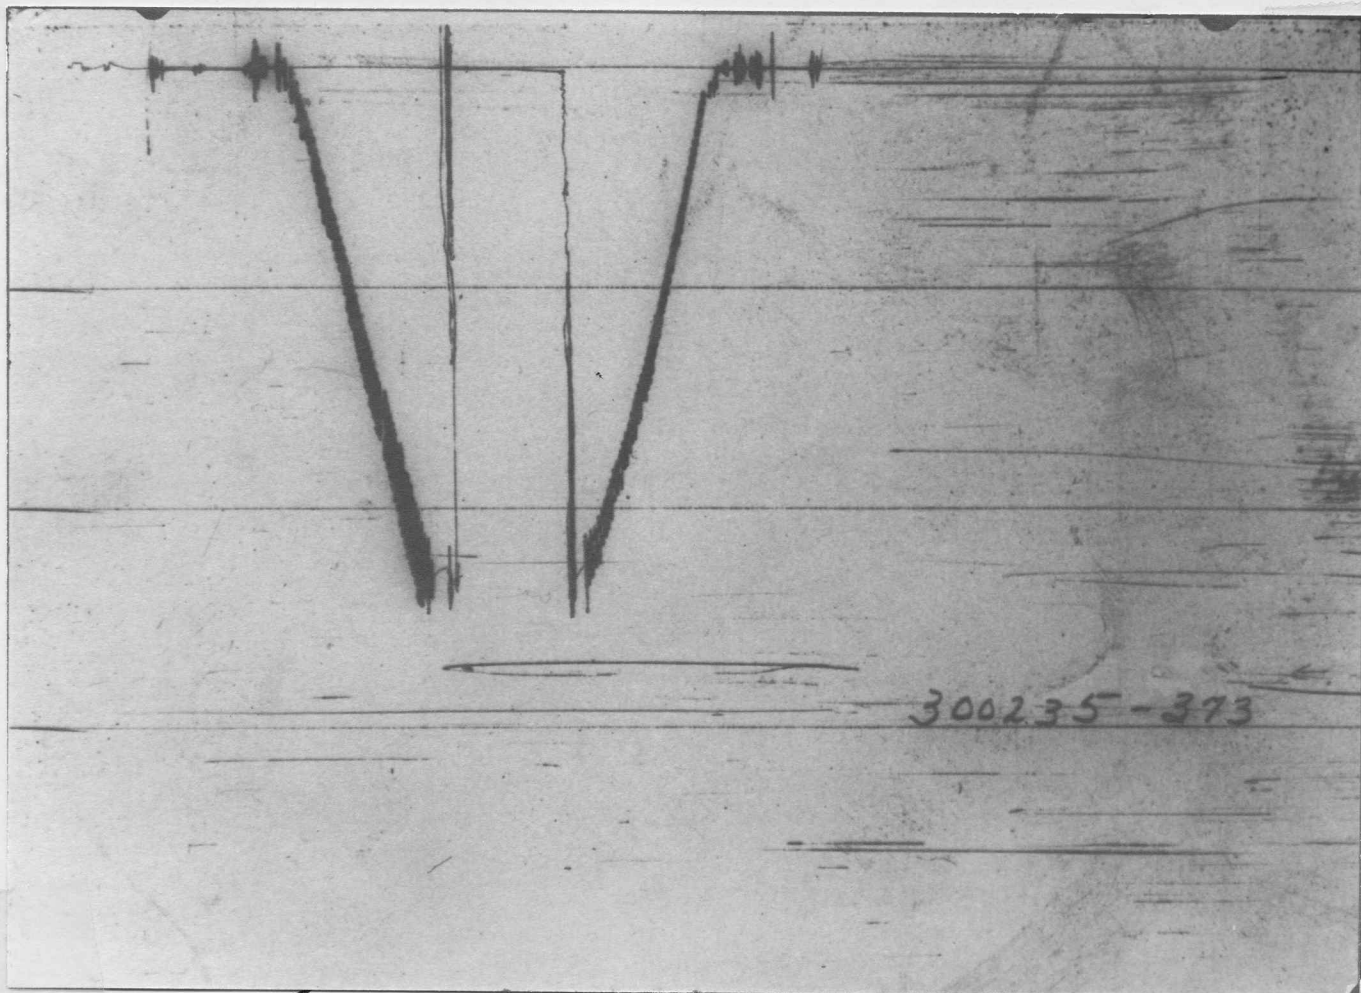

← TIME →

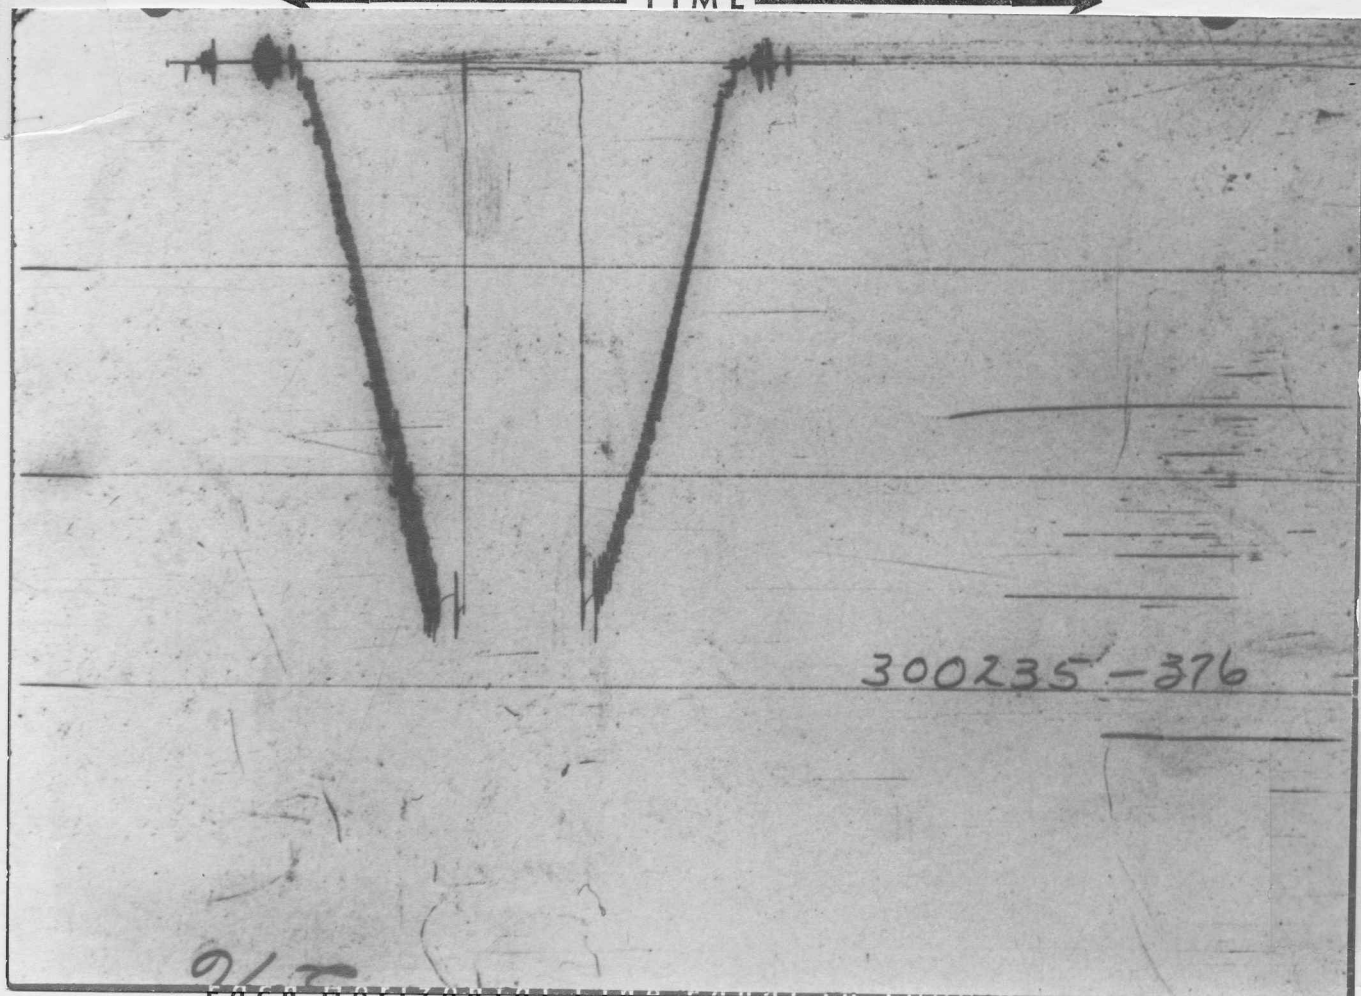

9/5
Each horizontal line equal to 1000 p.s.i.
