

36-4s-30w



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Prepared For: **Dark Horse Oil Company**

34861 Forest Park Drive
Elizabeth, CO 80107

ATTN: Paul Gunzelman

36-4s-30w Decatur

Robison 1-36

Start Date: 2006.01.24 @ 23:18:24

End Date: 2006.01.25 @ 05:16:48

Job Ticket #: 23178 DST #: 1

15-039-20956-0000

Trilobite Testing, Inc

PO Box 362 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620

RECEIVED
MAY 15 2006
KCC WICHITA



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Dark Horse Oil Company

34861 Forest Park Drive
Elizabeth, CO 80107

ATTN: Paul Gunzelman

Robison 1-36

36-4s-30w Decatur

Job Ticket: 23178

DST#: 1

Test Start: 2006.01.24 @ 23:18:24

GENERAL INFORMATION:

Formation: Toronto LKC- A

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 01:02:49

Time Test Ended: 05:16:48

Test Type: Conventional Bottom Hole

Tester: Brandon Turley

Unit No: 35

Interval: 3896.00 ft (KB) To 3964.00 ft (KB) (TVD)

Total Depth: 3964.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Good

Reference Elevations: 2851.00 ft (KB)

2846.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: 6772

Inside

Press@RunDepth: 56.90 psig @ 3897.00 ft (KB)

Start Date: 2006.01.24

End Date:

2006.01.25

Start Time: 23:18:24

End Time:

05:16:48

Capacity: 7000.00 psig

Last Calib.: 2006.01.25

Time On Btm: 2006.01.25 @ 00:56:04

Time Off Btm: 2006.01.25 @ 03:33:34


TEST COMMENT: IF: 1/4 blow built to 1/2 died to surface blow.

IS: No return.

FF: Weak surface blow built to 1/4.

FS: No return.

Pressure vs. Time

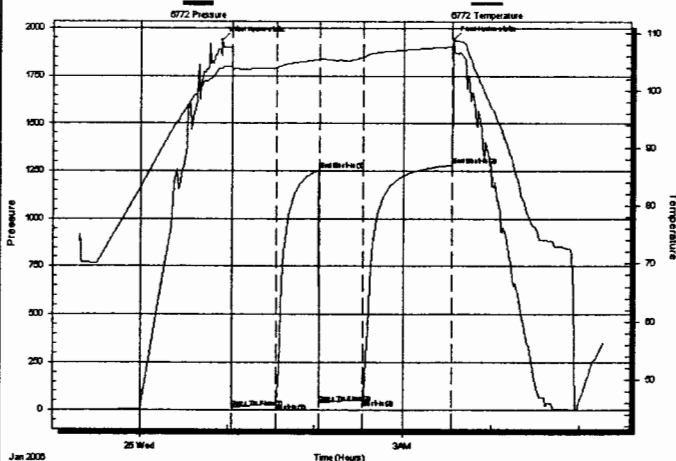

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1936.46	103.89	Initial Hydro-static
7	13.27	103.66	Open To Flow (1)
38	36.38	103.97	Shut-In(1)
67	1254.44	105.36	End Shut-In(1)
67	38.66	105.21	Open To Flow (2)
97	56.90	105.77	Shut-In(2)
157	1281.50	107.65	End Shut-In(2)
158	1941.26	108.85	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
60.00	mud some oil spots 100% m	0.30

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

TOOL DIAGRAM

Dark Horse Oil Company

34861 Forest Park Drive
Elizabeth, CO 80107

ATTN: Paul Gunzelman

Robison 1-36

36-4s-30w Decatur

Job Ticket: 23178

DST#: 1

Test Start: 2006.01.24 @ 23:18:24

Tool Information

Drill Pipe:	Length: 3757.00 ft	Diameter: 3.80 inches	Volume: 52.70 bbl	Tool Weight: 1500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 30000.00 lb
Drill Collar:	Length: 122.00 ft	Diameter: 2.25 inches	Volume: 0.60 bbl	Weight to Pull Loose: 60000.00 lb
		Total Volume: 53.30 bbl		Tool Chased 0.00 ft
Drill Pipe Above KB:	5.00 ft			String Weight: Initial 43000.00 lb
Depth to Top Packer:	3896.00 ft			Final 43000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	68.00 ft			
Tool Length:	90.00 ft			
Number of Packers:	2	Diameter: 6.75 inches		

Tool Comments:

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
------------------	-------------	------------	----------	------------	----------------

Stubb	1.00			3875.00	
Shut In Tool	5.00			3880.00	
Hydraulic tool	5.00			3885.00	
Safety Joint	2.00			3887.00	
Packer	5.00			3892.00	22.00 Bottom Of Top Packer
Packer	4.00			3896.00	
Stubb	1.00			3897.00	
Recorder	0.00	6772	Inside	3897.00	
Perforations	29.00			3926.00	
Change Over Sub	1.00			3927.00	
Drill Pipe	31.00			3958.00	
Change Over Sub	1.00			3959.00	
Recorder	0.00	7437	Outside	3959.00	
Bullnose	5.00			3964.00	68.00 Bottom Packers & Anchor

Total Tool Length: 90.00



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

FLUID SUMMARY

Dark Horse Oil Company

Robison 1-36

34861 Forest Park Drive
Elizabeth, CO 80107

36-4s-30w Decatur

Job Ticket: 23178

DST#: 1

ATTN: Paul Gunzelman

Test Start: 2006.01.24 @ 23:18:24

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

0 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

0 ppm

Viscosity: 50.00 sec/qt

Cushion Volume:

bbl

Water Loss: 6.37 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 800.00 ppm

Filter Cake: 2.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
60.00	mud some oil spots 100% m	0.295

Total Length: 60.00 ft

Total Volume: 0.295 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

DST Test Number: 1


36-4s-30w Decatur


Dark Horse Oil Company

Inside

Serial #: 6772

Pressure vs. Time

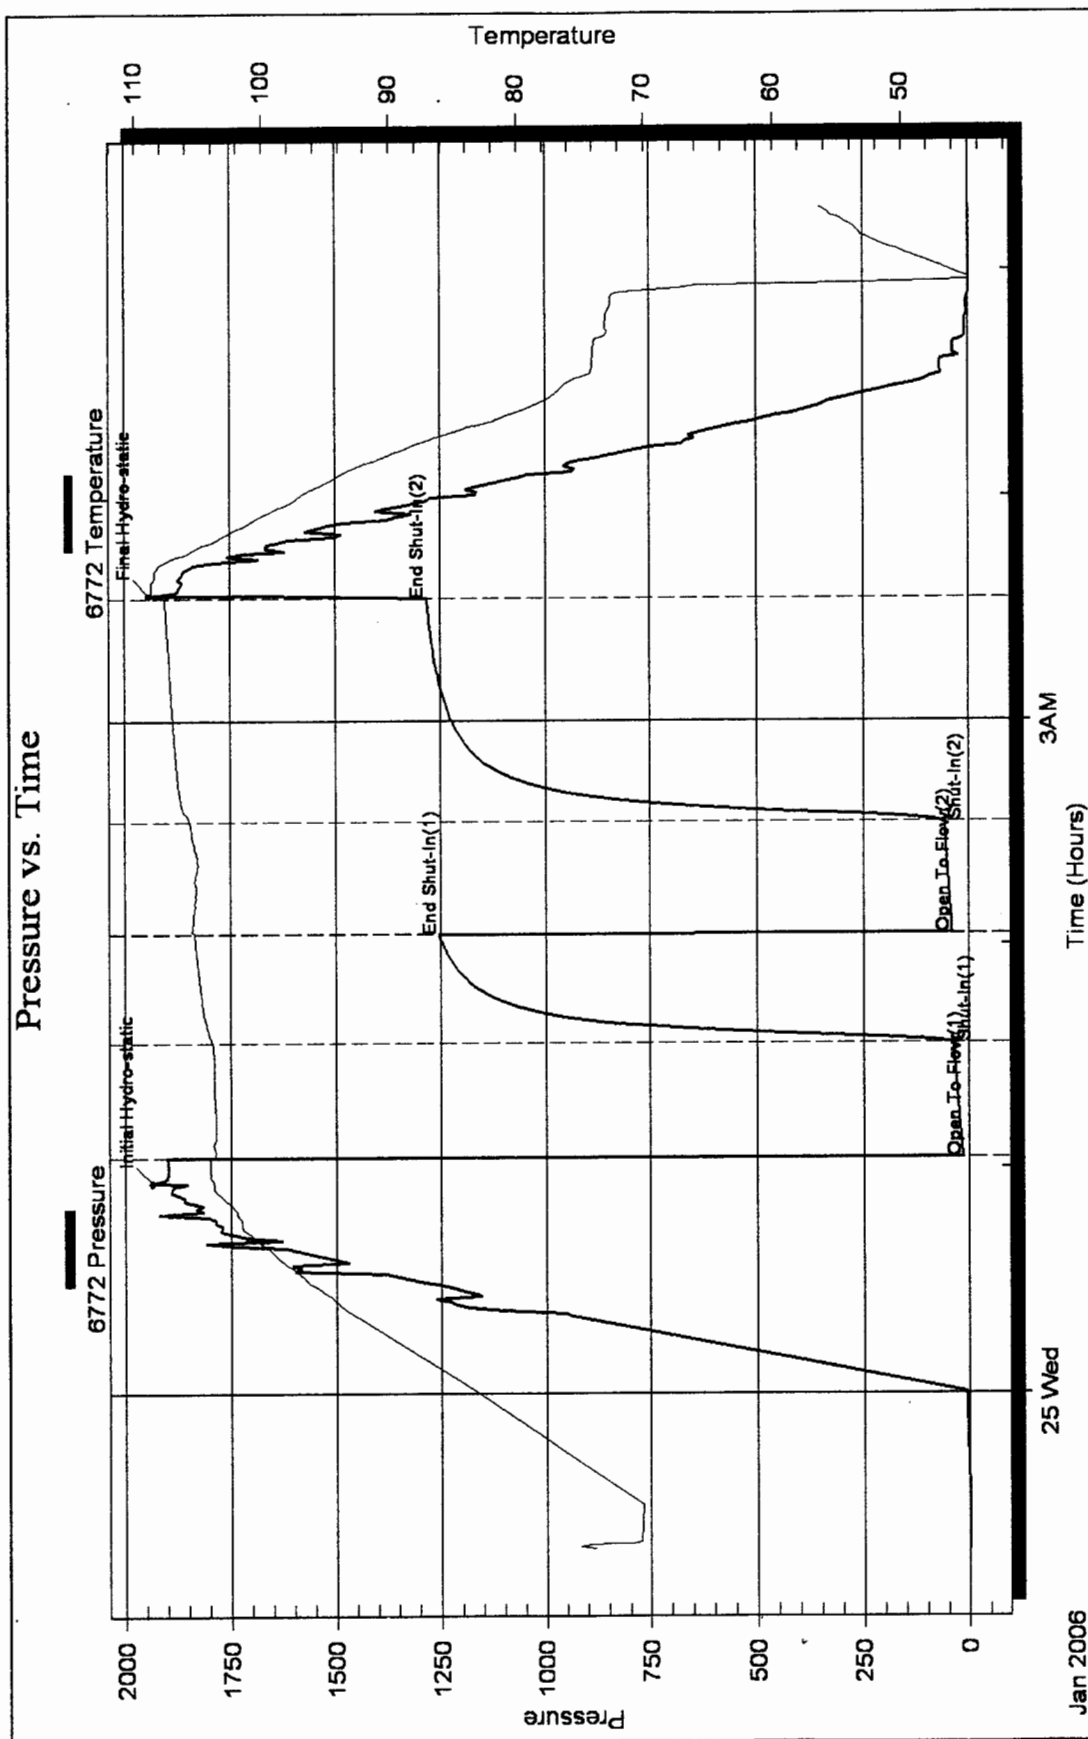



DRILL STEM TEST REPORT

Prepared For: **Dark Horse Oil Company**

34861 Forest Park Drive
Elizabeth, CO 80107

ATTN: Paul Gunzelman

36-4s-30w Decatur

Robison 1-36

Start Date: 2006.01.25 @ 17:42:24

End Date: 2006.01.26 @ 02:33:19

Job Ticket #: 23179 DST #: 2

Trilobite Testing, Inc

PO Box 362 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Dark Horse Oil Company

34861 Forest Park Drive
Elizabeth, CO 80107

ATTN: Paul Gunzelman

Robison 1-36

36-4s-30w Decatur

Job Ticket: 23179

DST#: 2

Test Start: 2006.01.25 @ 17:42:24

GENERAL INFORMATION:

Formation: **LKC G&H**

Deviated: **No** Whipstock: **ft (KB)**

Time Tool Opened: 19:41:34

Time Test Ended: 02:33:19

Test Type: **Conventional Bottom Hole**

Tester: **Brandon Turley**

Unit No: **35**

Interval: **4000.00 ft (KB) To 4074.00 ft (KB) (TVD)**

Total Depth: **4074.00 ft (KB) (TVD)**

Hole Diameter: **7.88 inches** Hole Condition: **Good**

Reference Elevations: **2851.00 ft (KB)**

2846.00 ft (CF)

KB to GR/CF: **5.00 ft**

Serial #: 6772

Inside

Press@RunDepth: **455.99 psig @ 4001.00 ft (KB)**

Start Date: **2006.01.25**

End Date:

2006.01.26

Start Time: **17:42:24**

End Time:

02:33:19


Capacity: **7000.00 psig**

Last Calib.: **1899.12.30**

Time On Btm: **2006.01.25 @ 19:32:49**

Time Off Btm: **2006.01.25 @ 23:26:18**

TEST COMMENT: IF: 1/4 blow BOB in 3 min.
IS: 1/4 blow BOB in 12 min.
FF: 1/4 blow BOB in 5 min.
FS: 1/4 blow BOB in 14 min.

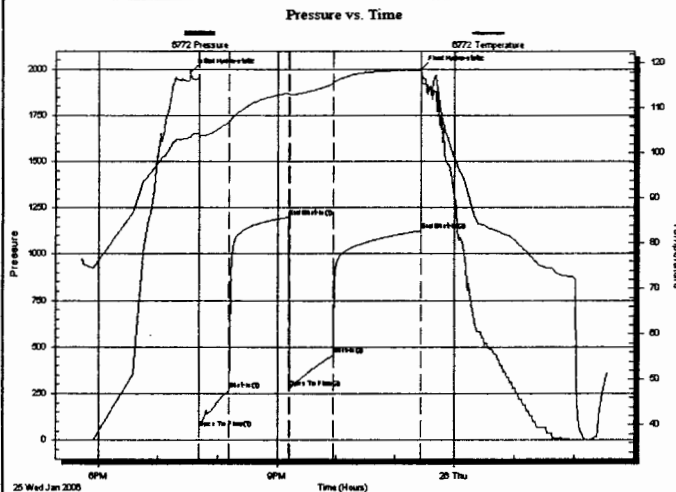

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1981.16	103.43	Initial Hydro-static
9	61.62	103.85	Open To Flow (1)
39	269.29	106.99	Shut-In(1)
99	1200.50	113.34	End Shut-In(1)
100	279.27	113.10	Open To Flow (2)
144	455.99	115.48	Shut-In(2)
233	1125.36	118.38	End Shut-In(2)
234	1999.19	118.62	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
184.00	w mco 50%o 20%w 30%m	1.47
186.00	mcgp 20%g 50%o 30%m	2.61
496.00	go 20%g 80%o	6.96
236.00	go 40%g 60%o	3.31

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

TOOL DIAGRAM

Dark Horse Oil Company

Robison 1-36

34861 Forest Park Drive
Elizabeth, CO 80107

36-4s-30w Decatur

Job Ticket: 23179

DST#: 2

ATTN: Paul Gunzelman

Test Start: 2006.01.25 @ 17:42:24

Tool Information

Drill Pipe:	Length: 3887.00 ft	Diameter: 3.80 inches	Volume: 54.52 bbl	Tool Weight: 1500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 30000.00 lb
Drill Collar:	Length: 122.00 ft	Diameter: 2.25 inches	Volume: 0.60 bbl	Weight to Pull Loose: 90000.00 lb
		Total Volume: 55.12 bbl		Tool Chased 0.00 ft
Drill Pipe Above KB:	31.00 ft			String Weight: Initial 44000.00 lb
Depth to Top Packer:	4000.00 ft			Final 48000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	74.00 ft			
Tool Length:	96.00 ft			
Number of Packers:	2	Diameter: 6.75 inches		
Tool Comments:				

Tool Description

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Stubb	1.00			3979.00	
Shut In Tool	5.00			3984.00	
Hydraulic tool	5.00			3989.00	
Safety Joint	2.00			3991.00	
Packer	5.00			3996.00	22.00 Bottom Of Top Packer
Packer	4.00			4000.00	
Stubb	1.00			4001.00	
Recorder	0.00	6772	Inside	4001.00	
Perforations	5.00			4006.00	
Change Over Sub	1.00			4007.00	
Drill Pipe	61.00			4068.00	
Change Over Sub	1.00			4069.00	
Recorder	0.00	7437	Outside	4069.00	
Bullnose	5.00			4074.00	74.00 Bottom Packers & Anchor

Total Tool Length: 96.00



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

FLUID SUMMARY

Dark Horse Oil Company

Robison 1-36

34861 Forest Park Drive
Elizabeth, CO 80107

36-4s-30w Decatur

Job Ticket: 23179

DST#: 2

ATTN: Paul Gunzelman

Test Start: 2006.01.25 @ 17:42:24

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

32 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

0 ppm

Viscosity: 50.00 sec/qt

Cushion Volume:

bbl

Water Loss: 5.98 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 800.00 ppm

Filter Cake: 2.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
184.00	w mco 50%o 20%w 30%m	1.470
186.00	mcgp 20%g 50%o 30%m	2.609
496.00	go 20%g 80%o	6.958
236.00	go 40%g 60%o	3.310

Total Length: 1102.00 ft

Total Volume: 14.347 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

DST Test Number: 2


36-4s-30w Decatur


Dark Horse Oil Company

Inside

Serial #: 6772

Pressure vs. Time

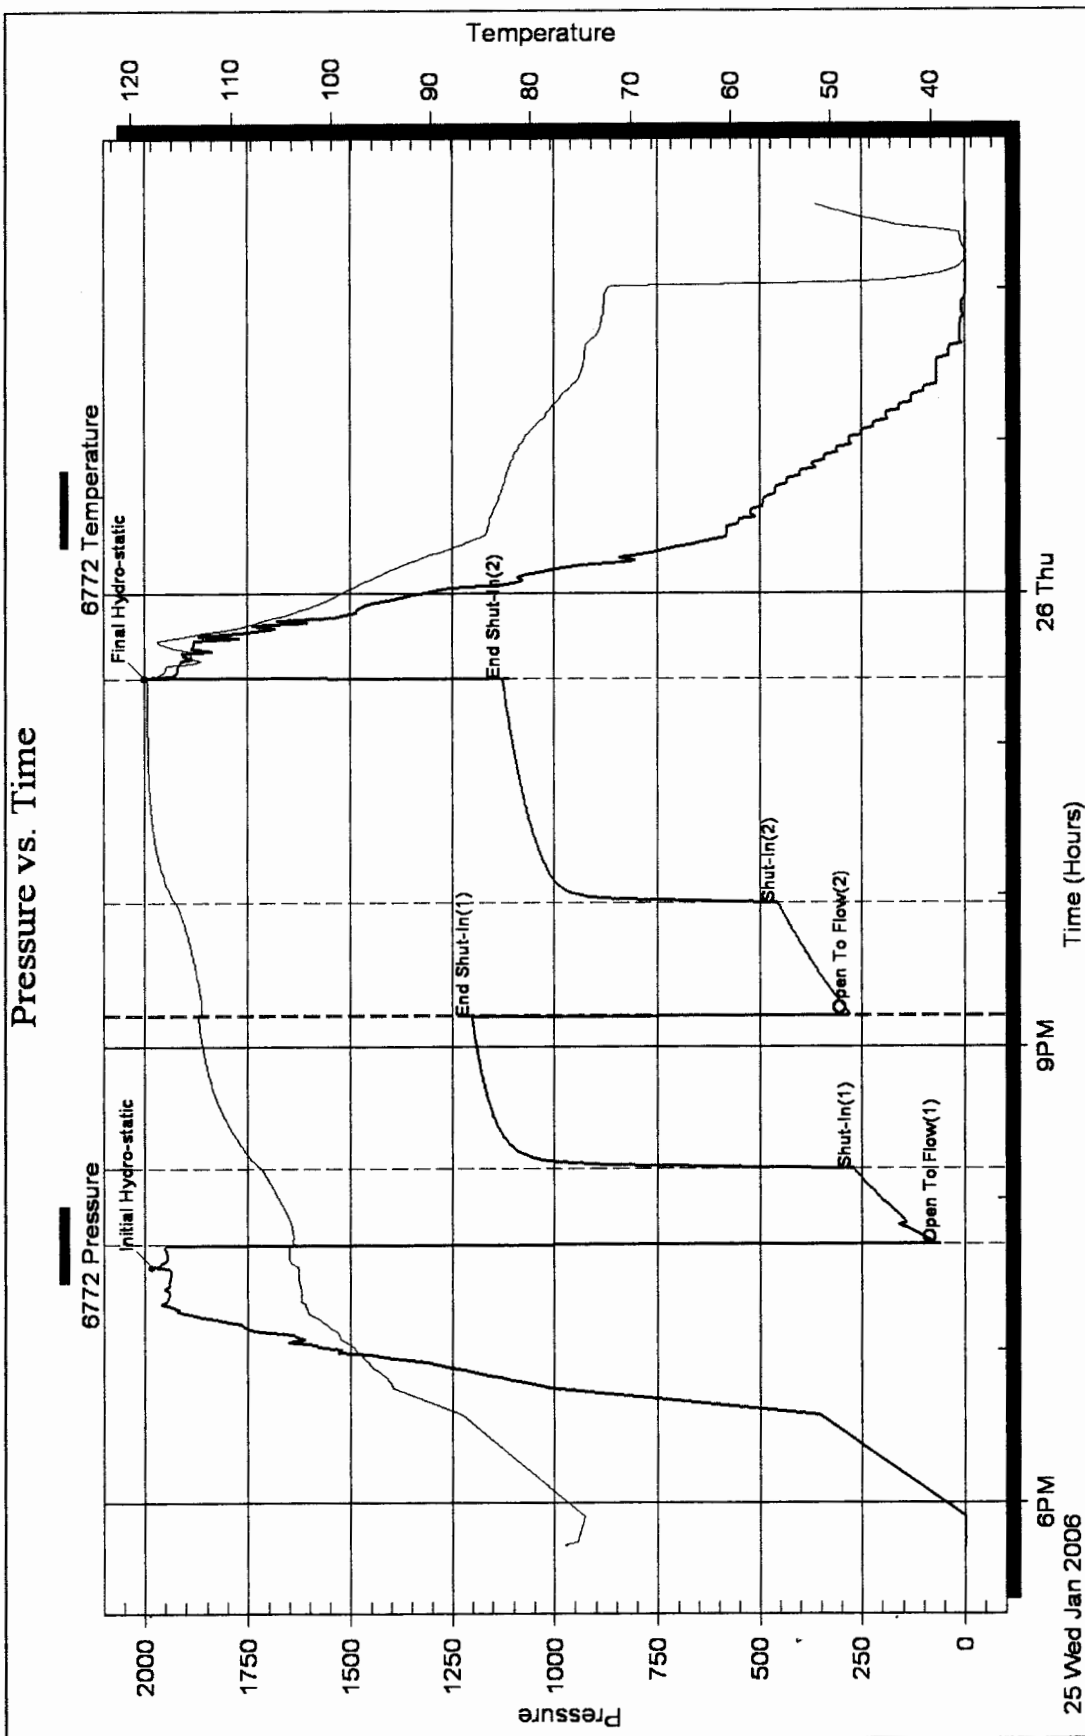



DRILL STEM TEST REPORT

Prepared For: **Dark Horse Oil Company**

34861 Forest Park Drive
Elizabeth, CO 80107

ATTN: Paul Gunzelman

36-4s-30w Decatur

Robison 1-36

Start Date: 2006.01.26 @ 11:48:14

End Date: 2006.01.26 @ 16:01:09

Job Ticket #: 32180 DST #: 3

Trilobite Testing, Inc
PO Box 362 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Dark Horse Oil Company

34861 Forest Park Drive
Elizabeth, CO 80107

ATTN: Paul Gunzelman

Robison 1-36

36-4s-30w Decatur

Job Ticket: 32180

DST#: 3

Test Start: 2006.01.26 @ 11:48:14

GENERAL INFORMATION:

Formation: **KC J-K-L**

Deviated: **No** Whipstock: **ft (KB)**

Time Tool Opened: 14:01:54

Time Test Ended: 16:01:09

Test Type: **Conventional Bottom Hole**

Tester: **Brandon Turley**

Unit No: **35**

Interval: **4074.00 ft (KB) To 4148.00 ft (KB) (TVD)**

Total Depth: **4148.00 ft (KB) (TVD)**

Hole Diameter: **7.88 inches** Hole Condition: **Good**

Reference Elevations: **2851.00 ft (KB)**

2846.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: 6772 **Inside**

Press@RunDepth: **psig @ 4075.00 ft (KB)**

Start Date: **2006.01.26**

End Date: **2006.01.26**

Start Time: **11:48:14**

End Time: **16:01:09**


Capacity: **7000.00 psig**

Last Calib.: **1899.12.30**

Time On Btm: **2006.01.26 @ 13:58:24**

Time Off Btm: **2006.01.26 @ 14:04:54**

TEST COMMENT: Packers failed at open.

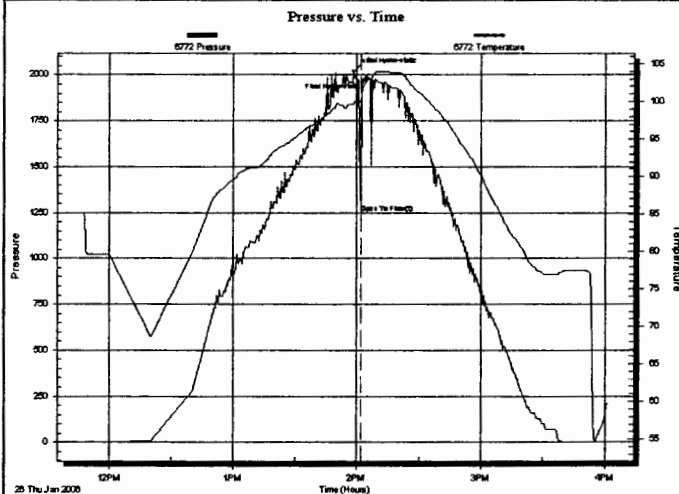

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2018.67	99.63	Initial Hydro-static
4	1246.63	100.30	Open To Flow (1)
7	1995.98	102.68	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
370.00	mud 100% m	4.08

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TOOL DIAGRAM

Dark Horse Oil Company

Robison 1-36

34861 Forest Park Drive
Elizabeth, CO 80107

36-4s-30w Decatur

Job Ticket: 32180

DST#: 3

ATTN: Paul Gunzelman

Test Start: 2006.01.26 @ 11:48:14

Tool Information

Drill Pipe:	Length: 3944.00 ft	Diameter: 3.80 inches	Volume: 55.32 bbl	Tool Weight:	1500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer:	30000.00 lb
Drill Collar:	Length: 122.00 ft	Diameter: 2.25 inches	Volume: 0.60 bbl	Weight to Pull Loose:	50000.00 lb
		Total Volume:	55.92 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	14.00 ft			String Weight: Initial	48000.00 lb
Depth to Top Packer:	4074.00 ft			Final	50000.00 lb
Depth to Bottom Packer:	ft				
Interval between Packers:	74.00 ft				
Tool Length:	96.00 ft				
Number of Packers:	2	Diameter:	6.75 inches		
Tool Comments:					

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Stubb	1.00			4053.00	
Shut In Tool	5.00			4058.00	
Hydraulic tool	5.00			4063.00	
Safety Joint	2.00			4065.00	
Packer	5.00			4070.00	22.00 Bottom Of Top Packer
Packer	4.00			4074.00	
Stubb	1.00			4075.00	
Recorder	0.00	6772	Inside	4075.00	
Perforations	5.00			4080.00	
Change Over Sub	1.00			4081.00	
Drill Pipe	61.00			4142.00	
Change Over Sub	1.00			4143.00	
Recorder	0.00	7437	Outside	4143.00	
Bullnose	5.00			4148.00	74.00 Bottom Packers & Anchor

Total Tool Length: 96.00



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

FLUID SUMMARY

Dark Horse Oil Company

Robison 1-36

34861 Forest Park Drive
Elizabeth, CO 80107

36-4s-30w Decatur

Job Ticket: 32180

DST#: 3

ATTN: Paul Gunzelman

Test Start: 2006.01.26 @ 11:48:14

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

0 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

0 ppm

Viscosity: 47.00 sec/qt

Cushion Volume:

bbl

Water Loss: 6.38 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 1200.00 ppm

Filter Cake: 2.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
370.00	mud 100%m	4.079

Total Length: 370.00 ft

Total Volume: 4.079 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:


DST Test Number: 3


36-4s-30w Decatur

Inside Dark Horse Oil Company

Serial #: 6772

Pressure vs. Time

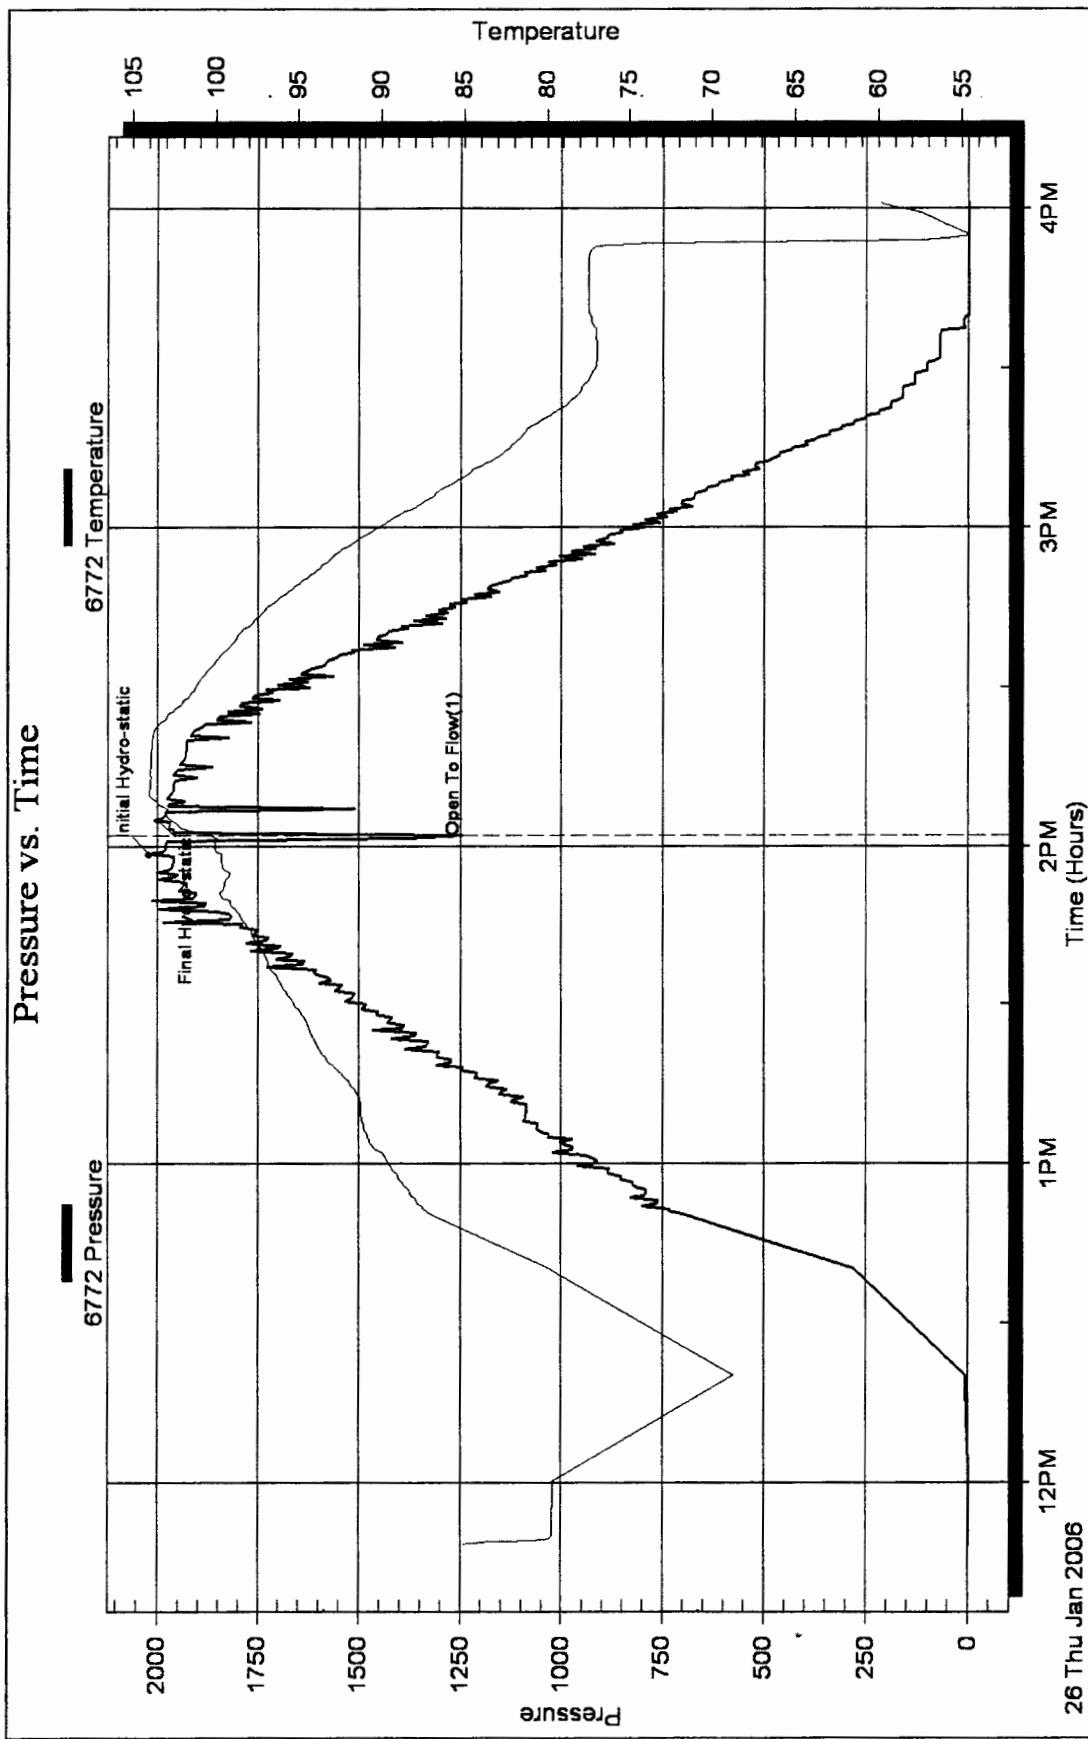



DRILL STEM TEST REPORT

Prepared For: **Dark Horse Oil Company**

34861 Forest Park Drive
Elizabeth, CO 80107

ATTN: Paul Gunzelman

36-4s-30w Decatur

Robison 1-36

Start Date: 2006.01.26 @ 16:08:53

End Date: 2006.01.26 @ 22:19:47

Job Ticket #: 23181 DST #: 4

Trilobite Testing, Inc
PO Box 362 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Dark Horse Oil Company

34861 Forest Park Drive
Elizabeth, CO 80107

ATTN: Paul Gunzelman

Robison 1-36

36-4s-30w Decatur

Job Ticket: 23181

DST#: 4

Test Start: 2006.01.26 @ 16:08:53

GENERAL INFORMATION:

Formation: KC J-K-L

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 18:12:18

Time Test Ended: 22:19:47

Test Type: Conventional Bottom Hole

Tester: Brandon Turley

Unit No: 35

Interval: 4066.00 ft (KB) To 4148.00 ft (KB) (TVD)

Total Depth: 4148.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Good

Reference Elevations: 2851.00 ft (KB)

2846.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: 6772 Inside

Press@RunDepth: 17.94 psig @ 4067.00 ft (KB)

Start Date: 2006.01.26

End Date:

2006.01.26

Start Time: 16:08:53

End Time:

22:19:47

Capacity: 7000.00 psig

Last Calib.: 1899.12.30

Time On Btm: 2006.01.26 @ 18:09:18


Time Off Btm: 2006.01.26 @ 20:29:47

TEST COMMENT: IF: 1/4 blow died in 7 min.

IS: No return.

FF: No blow.

FS: No return.

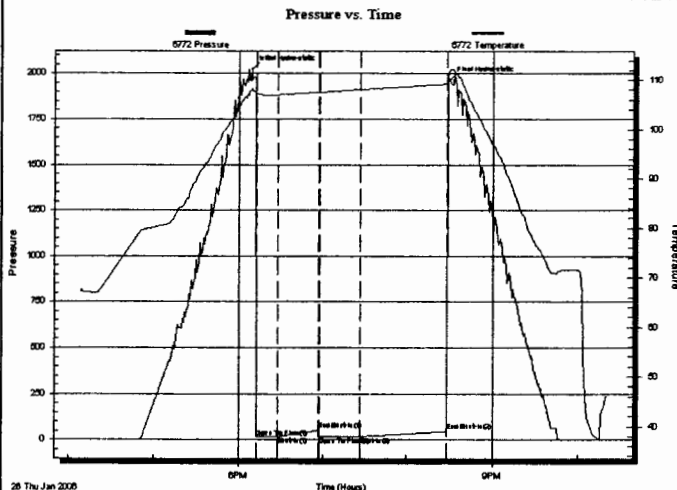

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2023.64	108.18	Initial Hydro-static
3	14.52	107.28	Open To Flow (1)
18	16.19	106.98	Shut-In(1)
48	51.90	107.56	End Shut-In(1)
49	16.90	107.54	Open To Flow (2)
78	17.94	108.07	Shut-In(2)
139	46.57	109.20	End Shut-In(2)
141	1965.11	112.10	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
5.00	mud 100%rn	0.02

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TOOL DIAGRAM

Dark Horse Oil Company

Robison 1-36

34861 Forest Park Drive
Elizabeth, CO 80107

36-4s-30w Decatur

Job Ticket: 23181

DST#: 4

ATTN: Paul Gunzelman

Test Start: 2006.01.26 @ 16:08:53

Tool Information

Drill Pipe:	Length: 3944.00 ft	Diameter: 3.80 inches	Volume: 55.32 bbl	Tool Weight: 1500.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 30000.00 lb
Drill Collar:	Length: 122.00 ft	Diameter: 2.25 inches	Volume: 0.60 bbl	Weight to Pull Loose: 60000.00 lb
		Total Volume:	55.92 bbl	Tool Chased 0.00 ft
Drill Pipe Above KB:	22.00 ft			String Weight: Initial 48000.00 lb
Depth to Top Packer:	4066.00 ft			Final 48000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	82.00 ft			
Tool Length:	104.00 ft			
Number of Packers:	2	Diameter: 6.75 inches		
Tool Comments:				

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Stubb	1.00			4045.00	
Shut In Tool	5.00			4050.00	
Hydraulic tool	5.00			4055.00	
Safety Joint	2.00			4057.00	
Packer	5.00			4062.00	22.00 Bottom Of Top Packer
Packer	4.00			4066.00	
Stubb	1.00			4067.00	
Recorder	0.00	6772	Inside	4067.00	
Perforations	13.00			4080.00	
Change Over Sub	1.00			4081.00	
Drill Pipe	61.00			4142.00	
Change Over Sub	1.00			4143.00	
Recorder	0.00	7437	Outside	4143.00	
Bullnose	5.00			4148.00	82.00 Bottom Packers & Anchor

Total Tool Length: 104.00



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

FLUID SUMMARY

Dark Horse Oil Company

Robison 1-36

34861 Forest Park Drive
Elizabeth, CO 80107

36-4s-30w Decatur

Job Ticket: 23181

DST#: 4

ATTN: Paul Gunzelman

Test Start: 2006.01.26 @ 16:08:53

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

0 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

0 ppm

Viscosity: 47.00 sec/qt

Cushion Volume:

bbl

Water Loss: 6.37 in³

Gas Cushion Type:

Resistivity: 0.00 ohm.m

Gas Cushion Pressure:

psig

Salinity: 1200.00 ppm

Filter Cake: 2.00 inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
5.00	mud 100%r	0.025

Total Length: 5.00 ft

Total Volume: 0.025 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

DST Test Number: 4

36-4s-30w Decatur

Dark Horse Oil Company

Inside

Serial #: 6772

Pressure vs. Time

