


15-065-23135-00-00
Stevenson-Lucky 3

27-7s-22w



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Werth Exploration Trust

Stevenson@Luckt #3

Hays KS 67601
1308 Schwaller Ave

27-7s-22w Graham

Job Ticket: 23029 DST#: 1

ATTN: Andy Werth

Test Start: 2006.02.11 @ 18:49:11

GENERAL INFORMATION:


Formation: LKC H-L
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 20:28:40
Time Test Ended: 00:33:10
Interval: 3557.00 ft (KB) To 3681.00 ft (KB) (TVD)
Total Depth: 3681.00 ft (KB) (TVD)
Hole Diameter: 7.85 inches Hole Condition: Fair

Test Type: Conventional Bottom Hole
Tester: Ray Schwager
Unit No: 28

Reference Elevations: 2218.00 ft (KB)
2213.00 ft (CF)
KB to GRVCF: 5.00 ft

Serial #: 8167 Inside
Press@RunDepth: 37.30 psig @ 3562.01 ft (KB) Capacity: 7000.00 psig
Start Date: 2006.02.11 End Date: 2006.02.12 Last Calib.: 2006.02.12
Start Time: 18:49:11 End Time: 00:33:10 Time On Strt: 2006.02.11 @ 20:23:10
Time Off Strt: 2006.02.11 @ 22:35:40

TEST COMMENT: FFP-wk bl thru-out 1"bl
FFP-no bl
Times 30-30-30-30

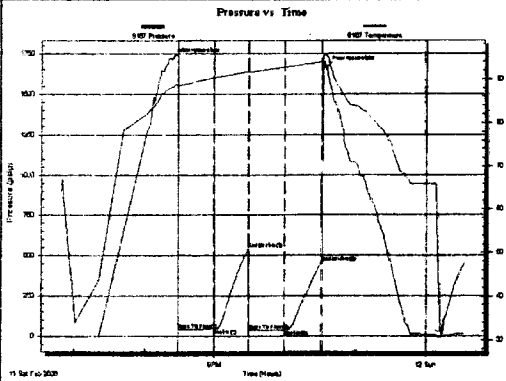

PRESSURE SUMMARY			
Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1716.19	88.19	Initial Hydro-static
6	39.83	88.51	Open To Flow (1)
36	43.18	90.23	Shut-in (1)
66	539.07	91.69	End Shut-in (1)
66	35.30	91.81	Open To Flow (2)
96	37.30	92.74	Shut-in (2)
128	452.88	94.01	End Shut-in (2)
133	1657.44	95.30	Final Hydro-static

Recovery		
Length (ft)	Description	Volume (bbl)
10.00	mud	0.14

Gas Rates			
	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)

RECEIVED

MAR 02 2006

KCC WICHITA

22-7-22w
