

DRILL STEM TEST REPORT

Prepared For: **Tengasco Inc**

Po Box 458
Hays KS 67601

ATTN: Rod Tremblay

3-9s-18w Rooks KS

McElhaney A #3


Start Date: 2011.03.31 @ 17:18:14

End Date: 2011.03.31 @ 23:17:14

Job Ticket #: 042875 DST #: 1

RECEIVED
JUL 01 2011
KCC WICHITA

Trilobite Testing, Inc
PO Box 1733 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Tengasco Inc

Po Box 458
Hays KS 67601

ATTN: Rod Tremblay

McElhaney A #3

3-9s-18w Rooks KS

Job Ticket: 042875

DST#: 1

Test Start: 2011.03.31 @ 17:18:14

GENERAL INFORMATION:

Formation: **Topeka**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 18:49:14

Time Test Ended: 23:17:14

Interval: **3071.00 ft (KB) To 3095.00 ft (KB) (TVD)**

Total Depth: **3095.00 ft (KB) (TVD)**

Hole Diameter: **7.88 inches** Hole Condition: Good

Test Type: Conventional Bottom Hole

Tester: Jeff Brown

Unit No: 44

Reference Elevations: 2008.00 ft (KB)

2003.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: **6672**

Inside

Press@RunDepth: 21.46 psig @ 3072.00 ft (KB)

Start Date: 2011.03.31

End Date: 2011.03.31

Start Time: 17:18:15

End Time: 23:17:14

Capacity: 8000.00 psig


Last Calib.: 2011.03.31

Time On Btm: 2011.03.31 @ 18:48:44

Time Off Btm: 2011.03.31 @ 21:54:14

TEST COMMENT: IFP-Weak blow built to 1 1/8 in
ISI-Dead no blow back
FFP-Weak blow built to 3/4 in
FSI-Dead no blow back

Pressure vs. Time

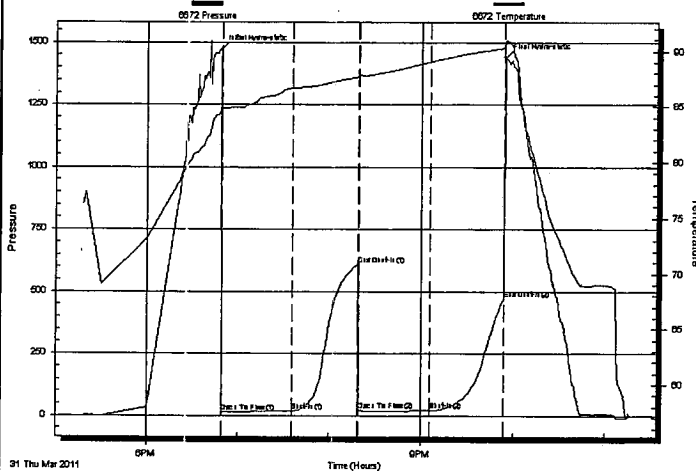

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1472.97	84.95	Initial Hydro-static
1	14.51	84.63	Open To Flow (1)
47	18.28	86.68	Shut-In (1)
91	611.12	87.66	End Shut-In (1)
91	23.21	87.64	Open To Flow (2)
137	21.46	89.05	Shut-In (2)
185	471.53	90.30	End Shut-In (2)
186	1441.24	90.88	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
10.00	HOCM 25%O75%M	0.14

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
----------------	-----------------	------------------



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

TOOL DIAGRAM

Tengasco Inc

McElhaney A #3

Po Box 458
Hays KS 67601

3-9s-18w Rooks KS

Job Ticket: 042875

DST#: 1

ATTN: Rod Tremblay

Test Start: 2011.03.31 @ 17:18:14


Tool Information

Drill Pipe:	Length:	3066.00 ft	Diameter:	3.80 inches	Volume:	43.01 bbl	Tool Weight:	2000.00 lb	
Heavy Wt. Pipe:	Length:	0.00 ft	Diameter:	2.70 inches	Volume:	0.00 bbl	Weight set on Packer:	20000.00 lb	
Drill Collar:	Length:	0.00 ft	Diameter:	2.25 inches	Volume:	0.00 bbl	Weight to Pull Loose:	42000.00 lb	
					Total Volume:	43.01 bbl	Tool Chased	0.00 ft	
Drill Pipe Above KB:	15.00 ft							String Weight: Initial	34000.00 lb
Depth to Top Packer:	3071.00 ft							Final	35000.00 lb
Depth to Bottom Packer:	ft								
Interval between Packers:	24.00 ft								
Tool Length:	44.00 ft								
Number of Packers:	2		Diameter:	6.75 inches					
Tool Comments:									

Tool Description

Length (ft) Serial No. Position Depth (ft) Accum. Lengths

Change Over Sub	1.00			3052.00		
Shut In Tool	5.00			3057.00		
Hydraulic tool	5.00			3062.00		
Packer	4.00			3066.00	20.00	Bottom Of Top Packer
Packer	5.00			3071.00		
Stubb	1.00			3072.00		
Recorder	0.00	6672	Inside	3072.00		
Recorder	0.00	8321	Outside	3072.00		
Perforations	20.00			3092.00		
Bullnose	3.00			3095.00	24.00	Bottom Packers & Anchor
Total Tool Length:	44.00					



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Tengasco Inc

McElhaney A #3

Po Box 458
Hays KS 67601

3-9s-18w Rooks KS

Job Ticket: 042875

DST#: 1

ATTN: Rod Tremblay

Test Start: 2011.03.31 @ 17:18:14

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

ppm

Viscosity: 61.00 sec/qt

Cushion Volume:

bbl

Water Loss: 7.18 in³

Gas Cushion Type:

Resistivity: ohm.m

Gas Cushion Pressure:

psig

Salinity: 2700.00 ppm

Filter Cake: inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
10.00	HOCM 25% O75%M	0.140

Total Length: 10.00 ft

Total Volume: 0.140 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:


Recovery Comments:


Serial #: 6672

Inside Tengasco Inc

3-9s-18w Rooks KS

DST Test Number: 1

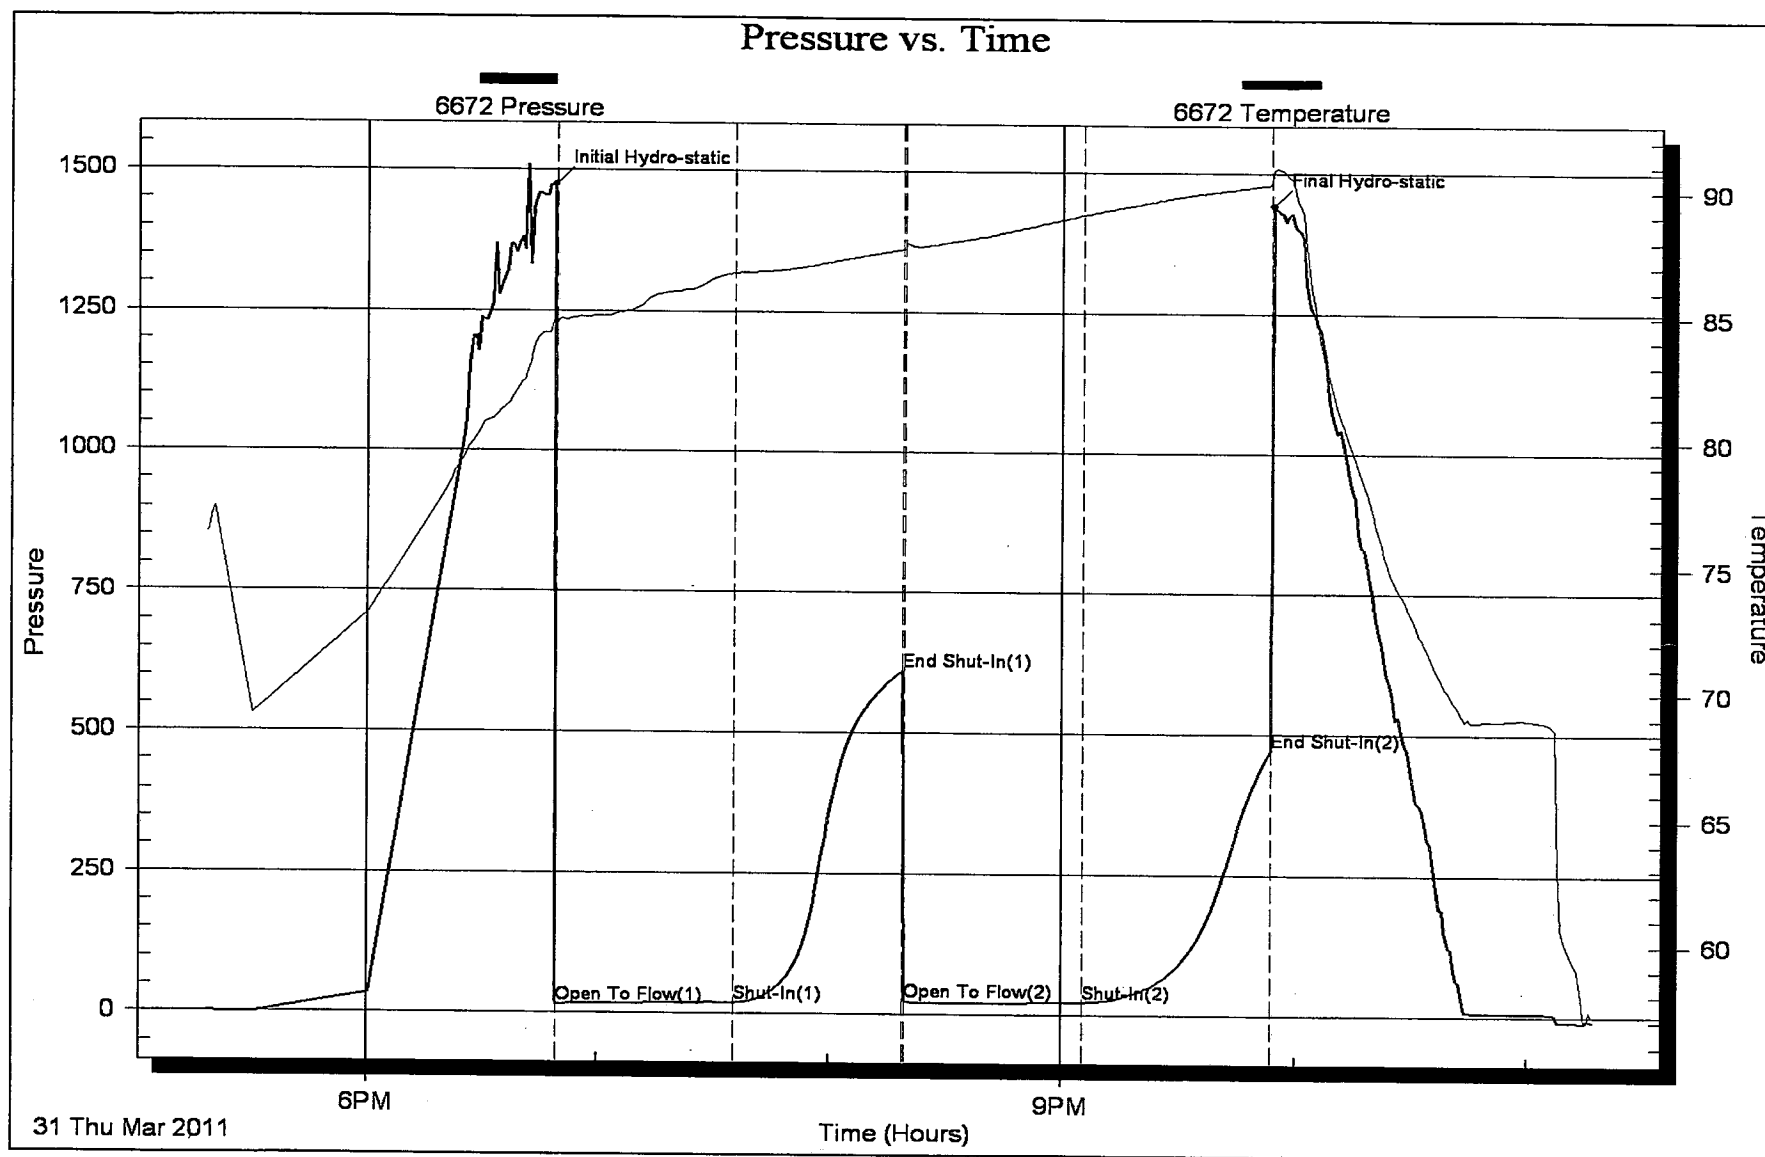



DRILL STEM TEST REPORT

Prepared For: **Tengasco Inc**

Po Box 458
Hays KS 67601

ATTN: Rod Tremblay

3-9s-18w Rooks KS

McElhaney A #3

Start Date: 2011.04.01 @ 13:16:39


End Date: 2011.04.01 @ 18:26:24

Job Ticket #: 042601 DST #: 2

Trilobite Testing, Inc

PO Box 1733 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



**TRILOBITE
TESTING, INC**

DRILL STEM TEST REPORT

Tengasco Inc

Po Box 458
Hays KS 67601

ATTN: Rod Tremblay

McElhaney A #3

3-9s-18w Rooks KS

Job Ticket: 042601

DST#: 2

Test Start: 2011.04.01 @ 13:16:39

GENERAL INFORMATION:

Formation: **LKC-C**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 14:43:24

Time Test Ended: 18:26:24

Test Type: Conventional Bottom Hole

Tester: Jeff Brown

Unit No: 44

Interval: **3196.00 ft (KB) To 3224.00 ft (KB) (TVD)**

Total Depth: 3224.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Good

Reference Elevations: 2008.00 ft (KB)

2003.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: 6672

Inside

Press@RunDepth: 20.59 psig @ 3201.00 ft (KB)

Start Date: 2011.04.01

End Date:

2011.04.01

Start Time: 13:16:40

End Time:

18:26:24

Capacity: 8000.00 psig


Last Calib.: 2011.04.01

Time On Btm: 2011.04.01 @ 14:43:09

Time Off Btm: 2011.04.01 @ 17:17:24

TEST COMMENT: IFP-Weak blow built to 1/4 in
ISI-Dead no blow back
FFP-Weak surface blow died out in 12 min
FSI-Dead no blow back

Pressure vs. Time

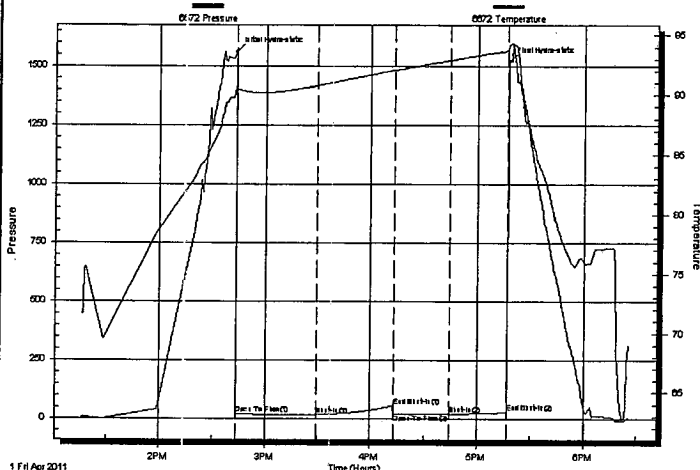

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1560.31	90.69	Initial Hydro-static
1	19.92	90.25	Open To Flow (1)
47	18.94	90.78	Shut-In(1)
90	56.60	92.07	End Shut-In(1)
91	22.81	92.06	Open To Flow (2)
122	20.59	92.92	Shut-In(2)
154	29.39	93.71	End Shut-In(2)
155	1519.56	94.15	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
3.00	SOCM 5% O95%M	0.04

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

TOOL DIAGRAM

Tengasco Inc

McElhaney A #3

Po Box 458
Hays KS 67601

3-9s-18w Rooks KS

Job Ticket: 042601

DST#: 2

ATTN: Rod Tremblay

Test Start: 2011.04.01 @ 13:16:39

Tool Information


Drill Pipe:	Length: 3191.00 ft	Diameter: 3.80 inches	Volume: 44.76 bbl	Tool Weight:	2000.00 lb	
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 2.70 inches	Volume: 0.00 bbl	Weight set on Packer:	20000.00 lb	
Drill Collar:	Length: 0.00 ft	Diameter: 2.25 inches	Volume: 0.00 bbl	Weight to Pull Loose:	39000.00 lb	
			Total Volume:	44.76 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	15.00 ft			String Weight: Initial	35000.00 lb	
Depth to Top Packer:	3196.00 ft			Final	35000.00 lb	
Depth to Bottom Packer:	ft					
Interval between Packers:	28.00 ft					
Tool Length:	48.00 ft					
Number of Packers:	2	Diameter:	6.75 inches			

Tool Comments:

Tool Description

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	1.00			3177.00	
Shut In Tool	5.00			3182.00	
Hydraulic tool	5.00			3187.00	
Packer	4.00			3191.00	20.00 Bottom Of Top Packer
Packer	5.00			3196.00	
Stubb	1.00			3197.00	
Perforations	4.00			3201.00	
Recorder	0.00	6672	Inside	3201.00	
Recorder	0.00	8321	Outside	3201.00	
Perforations	20.00			3221.00	
Bullnose	3.00			3224.00	28.00 Bottom Packers & Anchor

Total Tool Length: 48.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Tengasco Inc

McElhaney A #3

Po Box 458
Hays KS 67601

3-9s-18w Rooks KS

Job Ticket: 042601

DST#: 2

ATTN: Rod Tremblay

Test Start: 2011.04.01 @ 13:16:39

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

ppm

Viscosity: 52.00 sec/qt

Cushion Volume:

bbl

Water Loss: 9.58 in³

Gas Cushion Type:

Resistivity: ohm.m

Gas Cushion Pressure:

psig

Salinity: 2400.00 ppm

Filter Cake: inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
3.00	SOCM 5%O95%M	0.042

Total Length:

3.00 ft

Total Volume:

0.042 bbl

Num Fluid Samples: 0


Num Gas Bombs: 0


Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

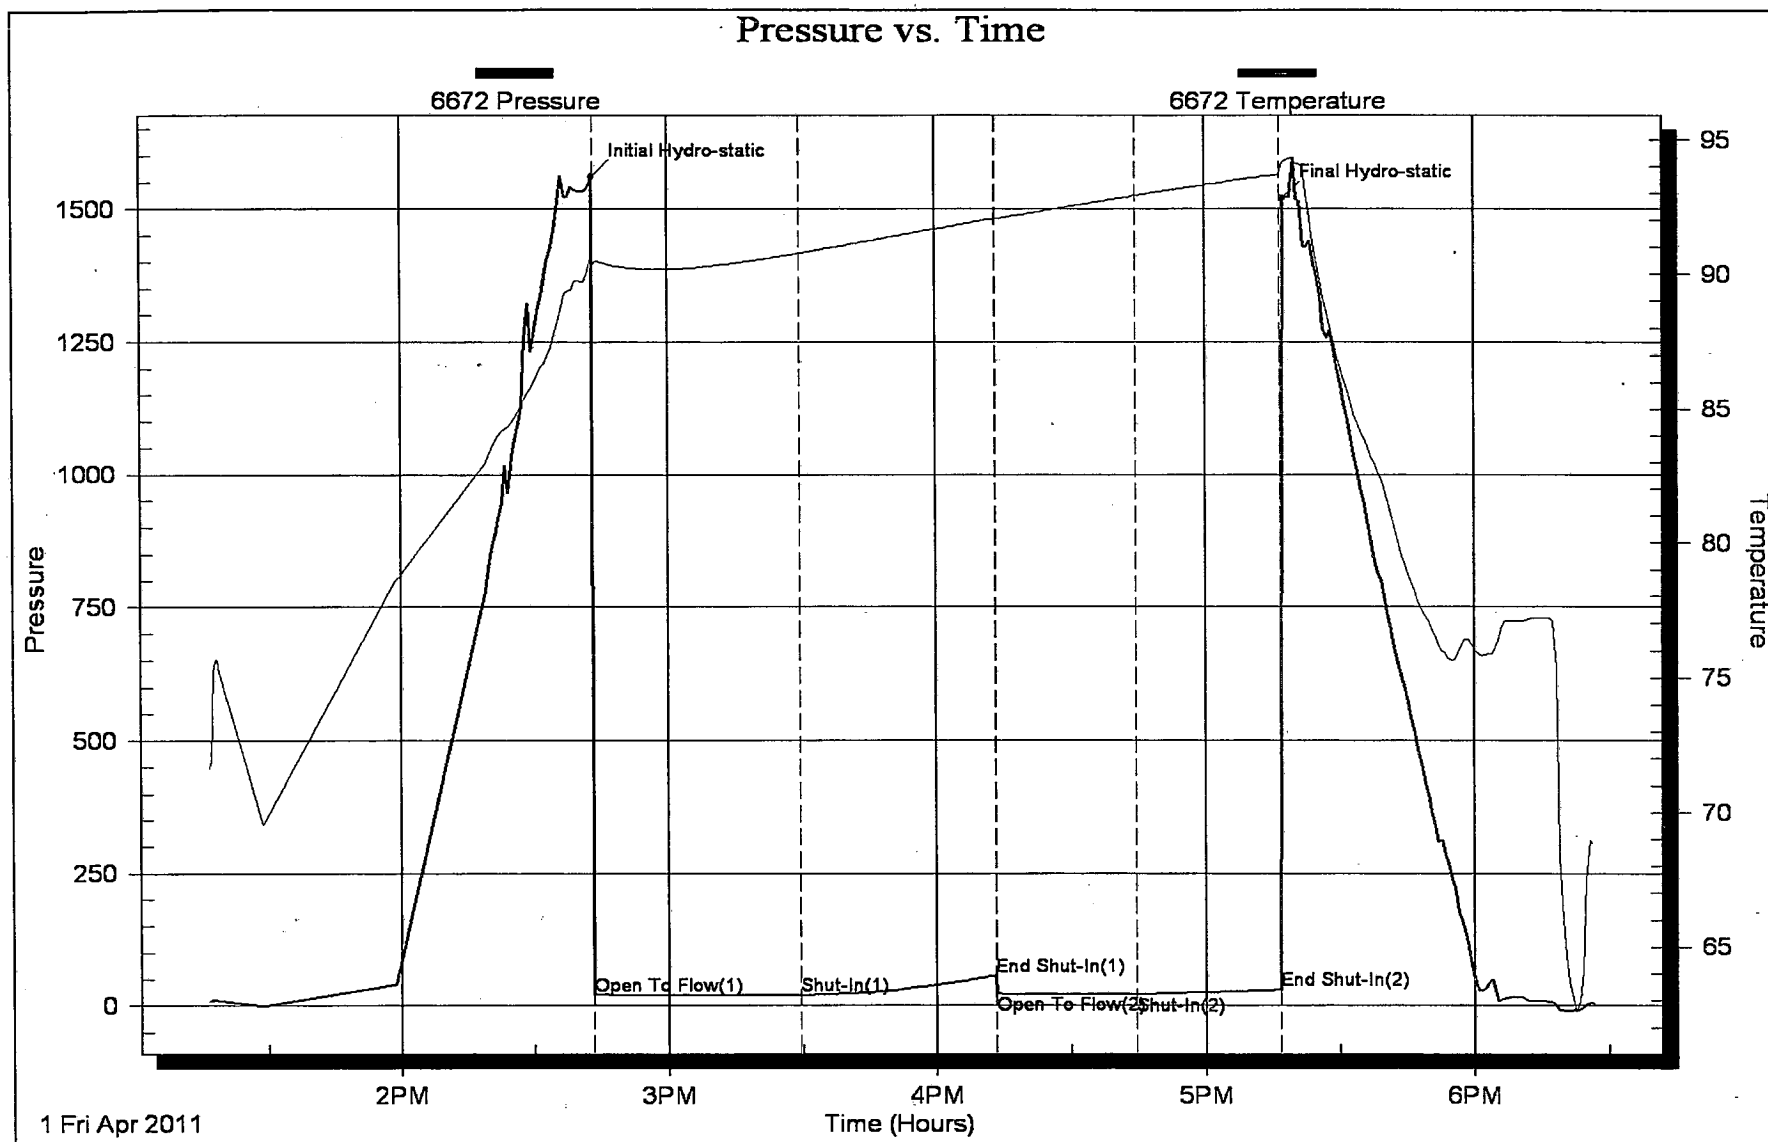



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Prepared For: **Tengasco Inc**

Po Box 458
Hays KS 67601

ATTN: Rod Tremblay

3-9s-18w Rooks KS

McElhaney A #3

Start Date: 2011.04.02 @ 02:12:39

End Date: 2011.04.02 @ 09:50:39


Job Ticket #: 042602

DST #: 3

Trilobite Testing, Inc

PO Box 1733 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

Tengasco Inc

Po Box 458
Hays KS 67601

ATTN: Rod Tremblay

McElhaney A #3

3-9s-18w Rooks KS

Job Ticket: 042602

DST#: 3

Test Start: 2011.04.02 @ 02:12:39

GENERAL INFORMATION:

Formation: **LKC-D-E-F-G**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 04:07:39

Time Test Ended: 09:50:39

Test Type: Conventional Bottom Hole

Tester: Jeff Brown

Unit No: 44

Interval: **3230.00 ft (KB) To 3268.00 ft (KB) (TVD)**

Total Depth: **3268.00 ft (KB) (TVD)**

Hole Diameter: 7.88 inches Hole Condition: Good

Reference Elevations: 2008.00 ft (KB)

2003.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: **6672** Inside

Press@RunDepth: 476.87 psig @ 3237.00 ft (KB)

Start Date: 2011.04.02

End Date: 2011.04.02

Start Time: 02:12:40

End Time: 09:50:39

Capacity: 8000.00 psig


Last Calib.: 2011.04.02

Time On Btm: 2011.04.02 @ 04:07:24

Time Off Btm: 2011.04.02 @ 07:10:09

TEST COMMENT: IFP-Strong blow BOB in 1 1/4 min
ISI-Good blow back BOB in 12 1/2 min
FFP-Strong blow BOB in 3 1/2 min
FSI-Good blow back BOB in 18 1/2 min

Pressure vs. Time

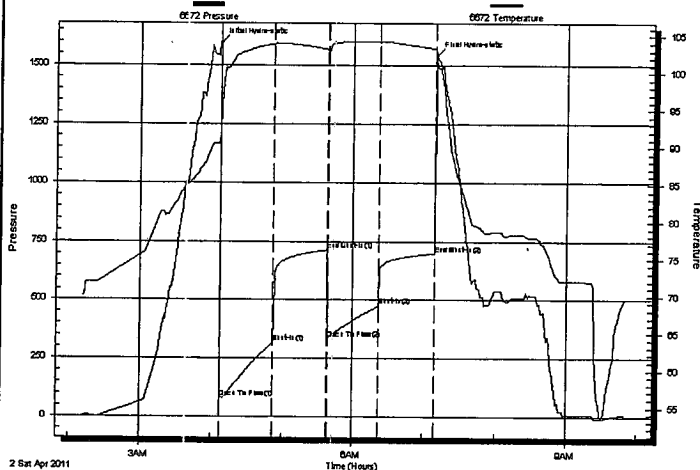

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1595.04	91.48	Initial Hydro-static
1	80.22	91.61	Open To Flow (1)
45	317.15	103.89	Shut-In(1)
91	712.87	103.25	End Shut-In(1)
91	334.27	102.86	Open To Flow (2)
136	476.87	104.17	Shut-In(2)
182	698.91	103.32	End Shut-In(2)
183	1541.84	102.64	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
315.00	MCXGO 10%N50%G40%O	4.42
1008.00	Gassy Oil 30%G70%O	14.14
0.00	1450 Gip	0.00

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

TOOL DIAGRAM

Tengasco Inc

McElhaney A #3

Po Box 458
Hays KS 67601

3-9s-18w Rooks KS

Job Ticket: 042602

DST#: 3

ATTN: Rod Tremblay

Test Start: 2011.04.02 @ 02:12:39


Tool Information

Drill Pipe:	Length: 3221.00 ft	Diameter: 3.80 inches	Volume: 45.18 bbl	Tool Weight:	2000.00 lb	
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 2.70 inches	Volume: 0.00 bbl	Weight set on Packer:	20000.00 lb	
Drill Collar:	Length: 0.00 ft	Diameter: 2.25 inches	Volume: 0.00 bbl	Weight to Pull Loose:	45000.00 lb	
			Total Volume:	45.18 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	11.00 ft			String Weight: Initial	35000.00 lb	
Depth to Top Packer:	3230.00 ft			Final	41000.00 lb	
Depth to Bottom Packer:	ft					
Interval between Packers:	38.00 ft					
Tool Length:	58.00 ft					
Number of Packers:	2	Diameter:	6.75 inches			
Tool Comments:						

Tool Description

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	1.00			3211.00	
Shut In Tool	5.00			3216.00	
Hydraulic tool	5.00			3221.00	
Packer	4.00			3225.00	20.00 Bottom Of Top Packer
Packer	5.00			3230.00	
Perforations	6.00			3236.00	
Stubb	1.00			3237.00	
Recorder	0.00	6672	Inside	3237.00	
Recorder	0.00	8321	Outside	3237.00	
Perforations	28.00			3265.00	
Bullnose	3.00			3268.00	38.00 Bottom Packers & Anchor

Total Tool Length: 58.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Tengasco Inc

McElhaney A #3

Po Box 458
Hays KS 67601

3-9s-18w Rooks KS

Job Ticket: 042602

DST#: 3

ATTN: Rod Tremblay

Test Start: 2011.04.02 @ 02:12:39

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

38 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

ppm

Viscosity: 52.00 sec/qt

Cushion Volume:

bbl

Water Loss: 9.59 in³

Gas Cushion Type:

Resistivity: ohm.m

Gas Cushion Pressure:

psig

Salinity: 2400.00 ppm

Filter Cake: inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
315.00	MCGO 10%M50%G40%O	4.419
1008.00	Gassy Oil 30%G70%O	14.140
0.00	1450 Gip	0.000

Total Length: 1323.00 ft

Total Volume: 18.559 bbl

Num Fluid Samples: 0


Num Gas Bombs: 0


Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

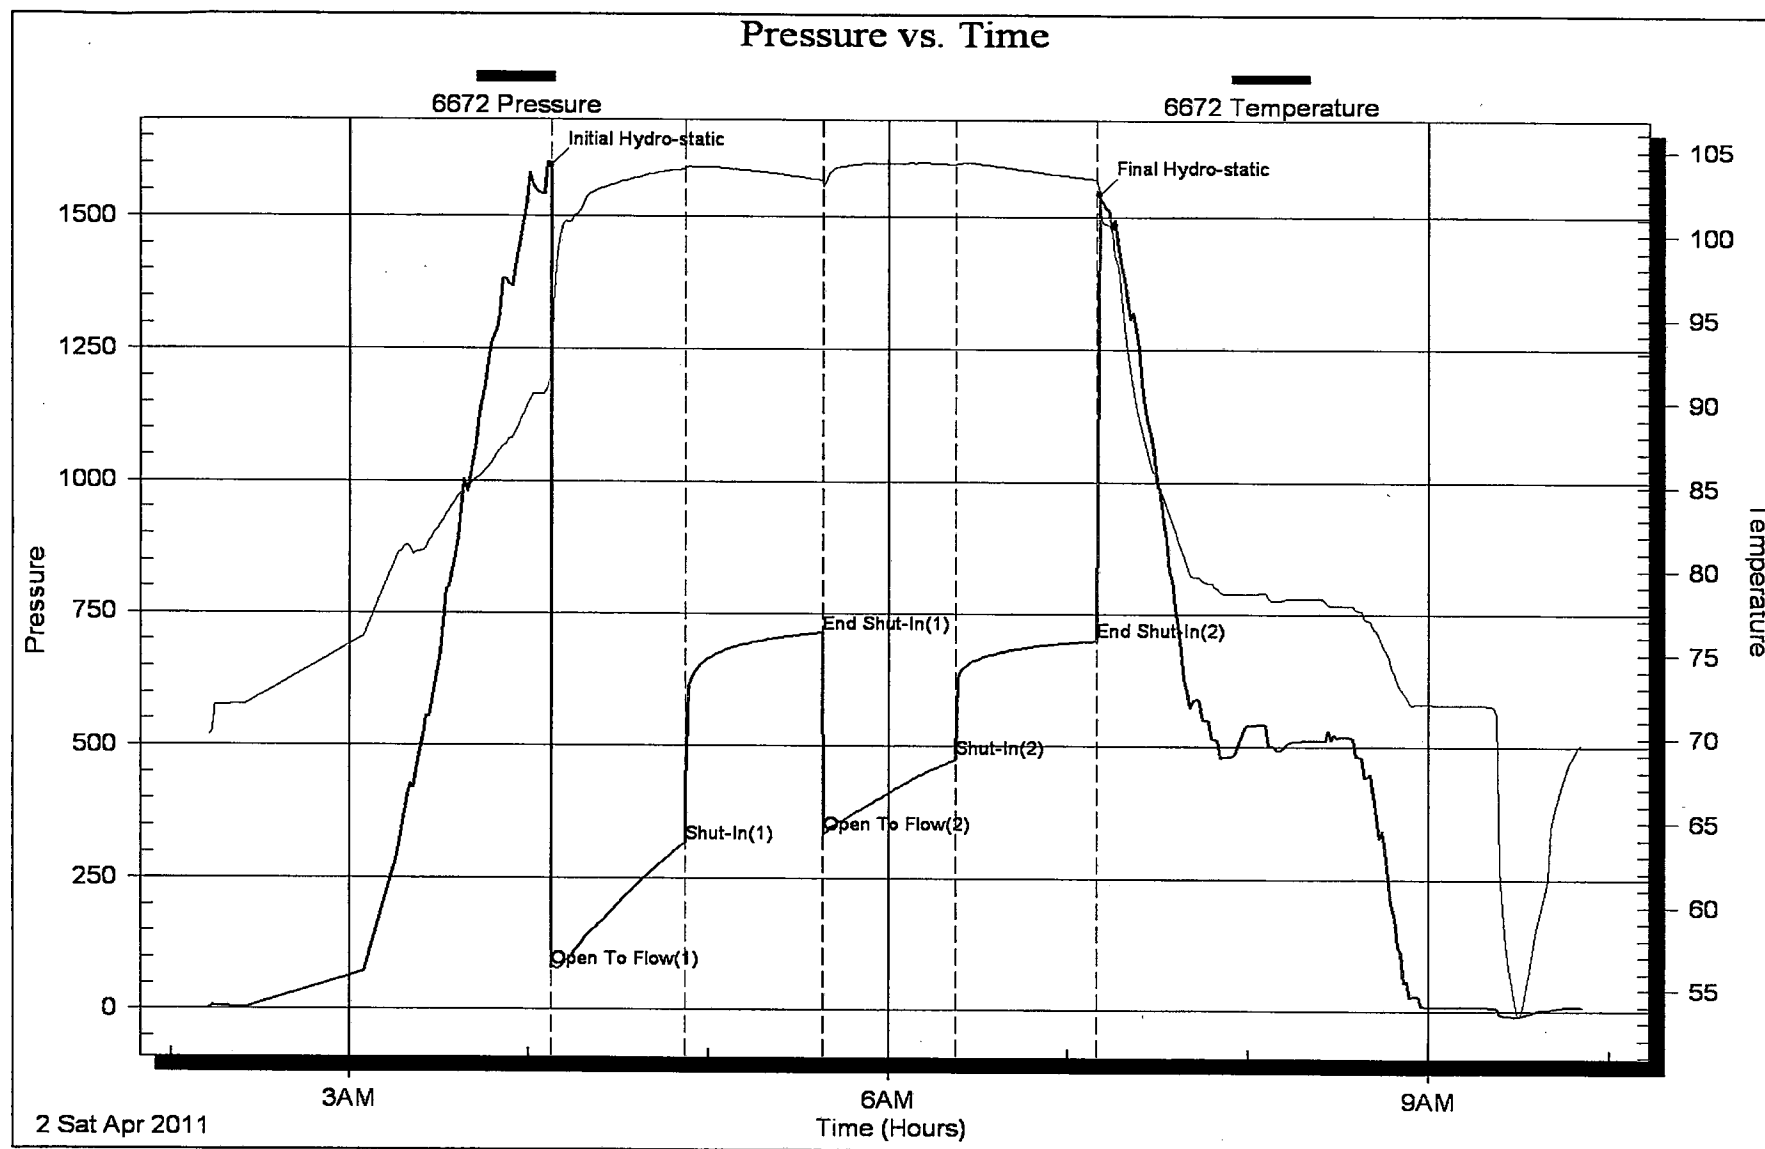



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Prepared For: **Tengasco Inc**

Po Box 458
Hays KS 67601

ATTN: Rod Tremblay

3-9s-18w Rooks KS

McElhaney A #3

Start Date: 2011.04.02 @ 18:05:46

End Date: 2011.04.03 @ 00:46:31


Job Ticket #: 04203

DST #: 4

Trilobite Testing, Inc

PO Box 1733 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

Tengasco Inc

Po Box 458
Hays KS 67601

ATTN: Rod Tremblay

McElhaney A #3

3-9s-18w Rooks KS

Job Ticket: 04203

DST#: 4

Test Start: 2011.04.02 @ 18:05:46

GENERAL INFORMATION:

Formation: LKC-H-I

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 19:41:46

Time Test Ended: 00:46:31

Test Type: Conventional Bottom Hole

Tester: Jeff Brown

Unit No: 44

Interval: 3306.00 ft (KB) To 3336.00 ft (KB) (TVD)

Total Depth: 3336.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Good

Reference Elevations: 2008.00 ft (KB)

2003.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: 6672 Inside

Press@RunDepth: 54.05 psig @ 3308.00 ft (KB)

Start Date: 2011.04.02

End Date:

2011.04.03

Start Time: 18:05:47

End Time:

00:46:31

Capacity: 8000.00 psig


Last Calib.: 2011.04.03

Time On Btm: 2011.04.02 @ 19:41:31

Time Off Btm: 2011.04.02 @ 22:45:31

TEST COMMENT: IFP-Good blow BOB in 34 1/2 min
ISI-Dead no blow back
FFP-Good blow BOB in 42 min
FSI-Dead no blow back

Pressure vs. Time

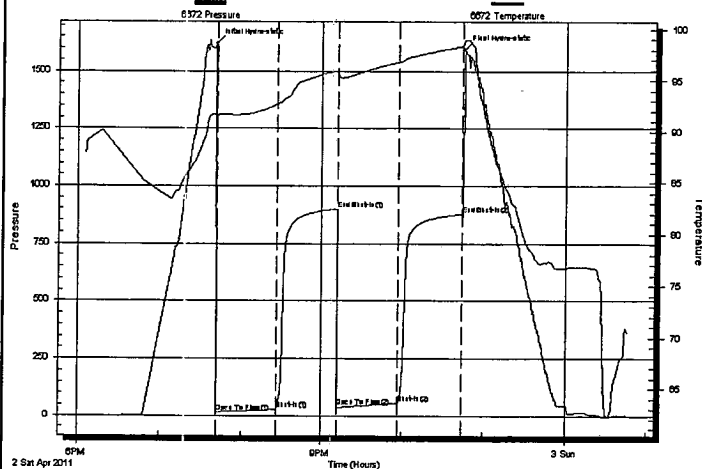

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1621.25	91.95	Initial Hydro-static
1	16.54	91.41	Open To Flow (1)
46	28.57	92.72	Shut-In(1)
90	898.58	95.90	End Shut-In(1)
91	40.15	95.55	Open To Flow (2)
136	54.05	96.81	Shut-In(2)
183	877.30	98.36	End Shut-In(2)
184	1595.76	98.97	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
63.00	HOCWM 35%O5%W65%M	0.88
25.00	Gassy Oil 25%G75%O	0.35

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

TOOL DIAGRAM

Tengasco Inc

McElhaney A #3

Po Box 458
Hays KS 67601

3-9s-18w Rooks KS

Job Ticket: 04203

DST#: 4

ATTN: Rod Tremblay

Test Start: 2011.04.02 @ 18:05:46

Tool Information


Drill Pipe:	Length: 3314.00 ft	Diameter: 3.80 inches	Volume: 46.49 bbl	Tool Weight:	2000.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 2.70 inches	Volume: 0.00 bbl	Weight set on Packer:	20000.00 lb
Drill Collar:	Length: 0.00 ft	Diameter: 2.25 inches	Volume: 0.00 bbl	Weight to Pull Loose:	40000.00 lb
		Total Volume:	46.49 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	28.00 ft			String Weight: Initial	34000.00 lb
Depth to Top Packer:	3306.00 ft			Final	37000.00 lb
Depth to Bottom Packer:	ft				
Interval between Packers:	30.00 ft				
Tool Length:	50.00 ft				
Number of Packers:	2	Diameter:	6.75 inches		

Tool Comments:

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
------------------	-------------	------------	----------	------------	----------------

Change Over Sub	1.00			3287.00	
Shut In Tool	5.00			3292.00	
Hydraulic tool	5.00			3297.00	
Packer	4.00			3301.00	20.00 Bottom Of Top Packer
Packer	5.00			3306.00	
Perforations	1.00			3307.00	
Stubb	1.00			3308.00	
Recorder	0.00	6672	Inside	3308.00	
Recorder	0.00	8321	Outside	3308.00	
Perforations	25.00			3333.00	
Bullnose	3.00			3336.00	30.00 Bottom Packers & Anchor

Total Tool Length: 50.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Tengasco Inc

McElhaney A #3

Po Box 458
Hays KS 67601

3-9s-18w Rooks KS

Job Ticket: 04203

DST#: 4

ATTN: Rod Tremblay

Test Start: 2011.04.02 @ 18:05:46

Mud and Cushion Information

Mud Type: Gel Chem

Cushion Type:

Oil API:

38 deg API

Mud Weight: 9.00 lb/gal

Cushion Length:

ft

Water Salinity:

ppm

Viscosity: 52.00 sec/qt

Cushion Volume:

bbl

Water Loss: 9.59 in³

Gas Cushion Type:

Resistivity: ohm.m

Gas Cushion Pressure:

psig

Salinity: 2400.00 ppm

Filter Cake: inches

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
63.00	HOCWM 35%O5%W65%M	0.884
25.00	Gassy Oil 25%G75%O	0.351

Total Length:

88.00 ft

Total Volume:

1.235 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

Serial #: 6672

Inside Tengasco Inc

3-9s-18w Rocks KS

DST Test Number: 4

