


ORIGINAL



DRILL STEM TEST REPORT

Prepared For: **Coral Prod. Corp.**

1600 Stout St.
Suite 1500
Denver, Co. 80202

ATTN: Jerry Green

19-9s-21w

Wasinger #1

Start Date: 2001.01.17 @ 15:45:00

End Date: 2001.01.18 @ 01:30:00

Job Ticket #: 13970

DST #: 1

15-065-22811

NE

910 FNL 2270 FEL

Trilobite Testing Inc.
Box 362 Hays KS 67601
785.625.4778 trilobite@eaglecom.net

15-065-22811

Coral Prod. Corp.


Wasinger #1

19-9s-21w

DST #: 1

KC.

2001.01.17



DRILL STEM TEST REPORT

Coral Prod. Corp.

Wasinger #1

1600 Stout St.
Suite 1500
Denver, Co. 80202
ATTN: Jerry Green

19-9s-21w

Job Ticket: 13970

DST#: 1

Test Start: 2001.01.17 @ 15:45:00

GENERAL INFORMATION:

Formation: KC.

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 18:44:27

Time Test Ended: 01:30:00

Test Type: Conventional Bottom Hole

Tester: John Schmidt

Unit No: 18

Interval: 3633.00 ft (KB) To 3658.00 ft (KB) (TVD)

Total Depth: 3658.00 ft (KB)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2346.00 ft (KB)

2341.00 ft (CF)

KB to GR/CF: 5.00 ft

Serial #: 3227 Inside

Press@RunDepth: 42.40 psig @ 3635.01 ft (KB)

Start Date: 2001.01.17

End Date:

2001.01.18

Start Time: 17:11:32

End Time:

00:40:56


Capacity: 7000.00 psig

Last Calib.: 2001.01.17

Time On Btm: 2001.01.17 @ 18:37:27

Time Off Btm: 2001.01.17 @ 22:44:57

TEST COMMENT: IF- Weak 2" in 45 Min.
FF-Weak 1" in 60 Min.

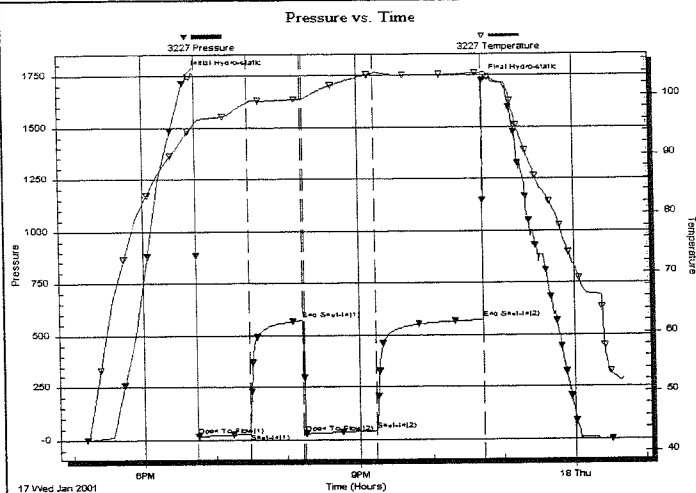

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
86	1752.99	93.61	Initial Hydro-static
93	16.39	95.27	Open To Flow (1)
137	27.52	98.71	Shut-In(1)
182	571.62	99.38	End Shut-In(1)
184	27.94	99.38	Open To Flow (2)
242	42.40	103.65	Shut-In(2)
332	571.78	103.68	End Shut-In(2)
334	1727.45	103.81	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
55.00	Mud Cut Water W/ Oil Specks	0.77

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
----------------	-----------------	------------------


Serial #: 3227

Inside

Coral Prod. Corp.

19-9s-21w

Pressure vs. Time

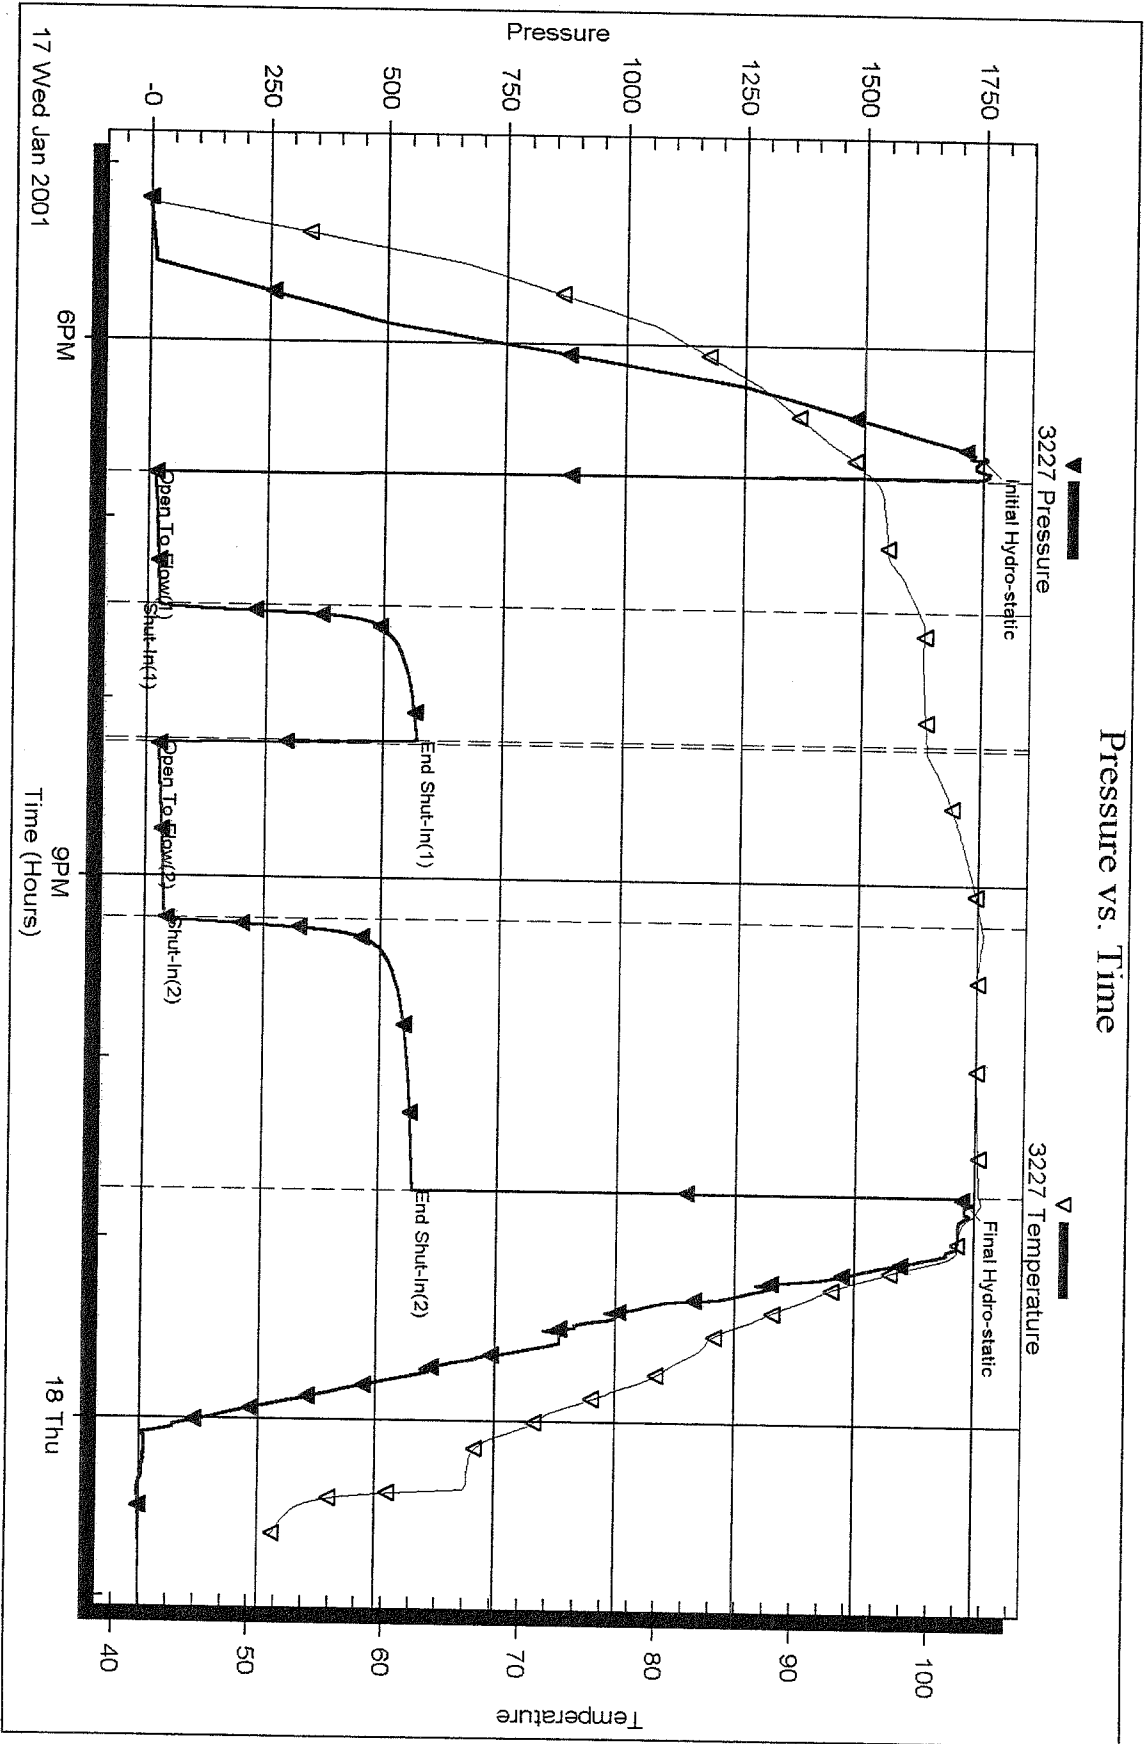



DRILL STEM TEST REPORT

Prepared For: **Coral Prod. Corp.**

1600 Stout St.
Suite 1500
Denver, Co. 80202

ATTN: Jerry Green

19-9s-21w

Wasinger #1

Start Date: 2001.01.18 @ 22:30:00

End Date: 2001.01.19 @ 12:00:00

Job Ticket #: 13971 DST #: 2

Trilobite Testing Inc.
Box 362 Hays KS 67601
785.625.4778 trilobite@eaglecom.net

Coral Prod. Corp.


Wasinger #1

19-9s-21w

DST #: 2

Arb.

2001.01.18



DRILL STEM TEST REPORT

Coral Prod. Corp.
1600 Stout St.
Suite 1500
Denver, Co. 80202
ATTN: Jerry Green

Wasinger #1

19-9s-21w

Job Ticket: 13971

DST#: 2

Test Start: 2001.01.18 @ 22:30:00

GENERAL INFORMATION:

Formation: Arb.
Deviated: No Whipstock: ft (KB)
Time Tool Opened: 02:22:08
Time Test Ended: 12:00:00

Test Type: Conventional Bottom Hole
Tester: John Schmidt
Unit No: 18


Interval: 3818.00 ft (KB) To 3882.00 ft (KB) (TVD)
Total Depth: 3658.00 ft (KB)
Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 2346.00 ft (KB)
2341.00 ft (CF)
KB to GR/CF: 5.00 ft

Serial #: 3227 Inside
Press@RunDepth: 1117.41 psig @ 3820.01 ft (KB)
Start Date: 2001.01.19 End Date: 2001.01.19
Start Time: 00:25:43 End Time: 11:22:08

Capacity: 7000.00 psig
Last Calib.: 2001.01.19
Time On Btm: 2001.01.19 @ 02:13:38
Time Off Btm: 2001.01.19 @ 06:25:38

TEST COMMENT: IF-Strong Bot.1 Min.
FF-Strong Bot.1 Min.

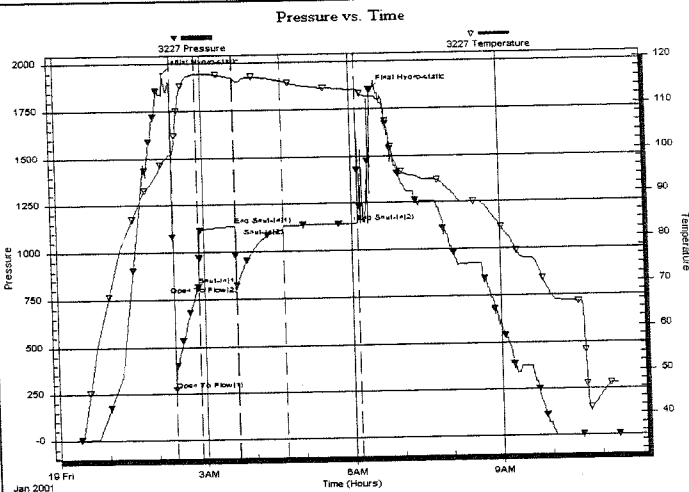

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
108	1944.97	98.03	Initial Hydro-static
117	264.57	99.36	Open To Flow (1)
147	822.98	117.11	Shut-In(1)
193	1136.03	116.24	End Shut-In(1)
193	816.42	116.20	Open To Flow (2)
251	1117.41	115.53	Shut-In(2)
342	1142.72	113.29	End Shut-In(2)
360	1846.04	111.94	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
2750.00	Oil	38.58

Gas Rates

Choke(inches)	Pressure (psig)	Gas Rate (Mcf/d)



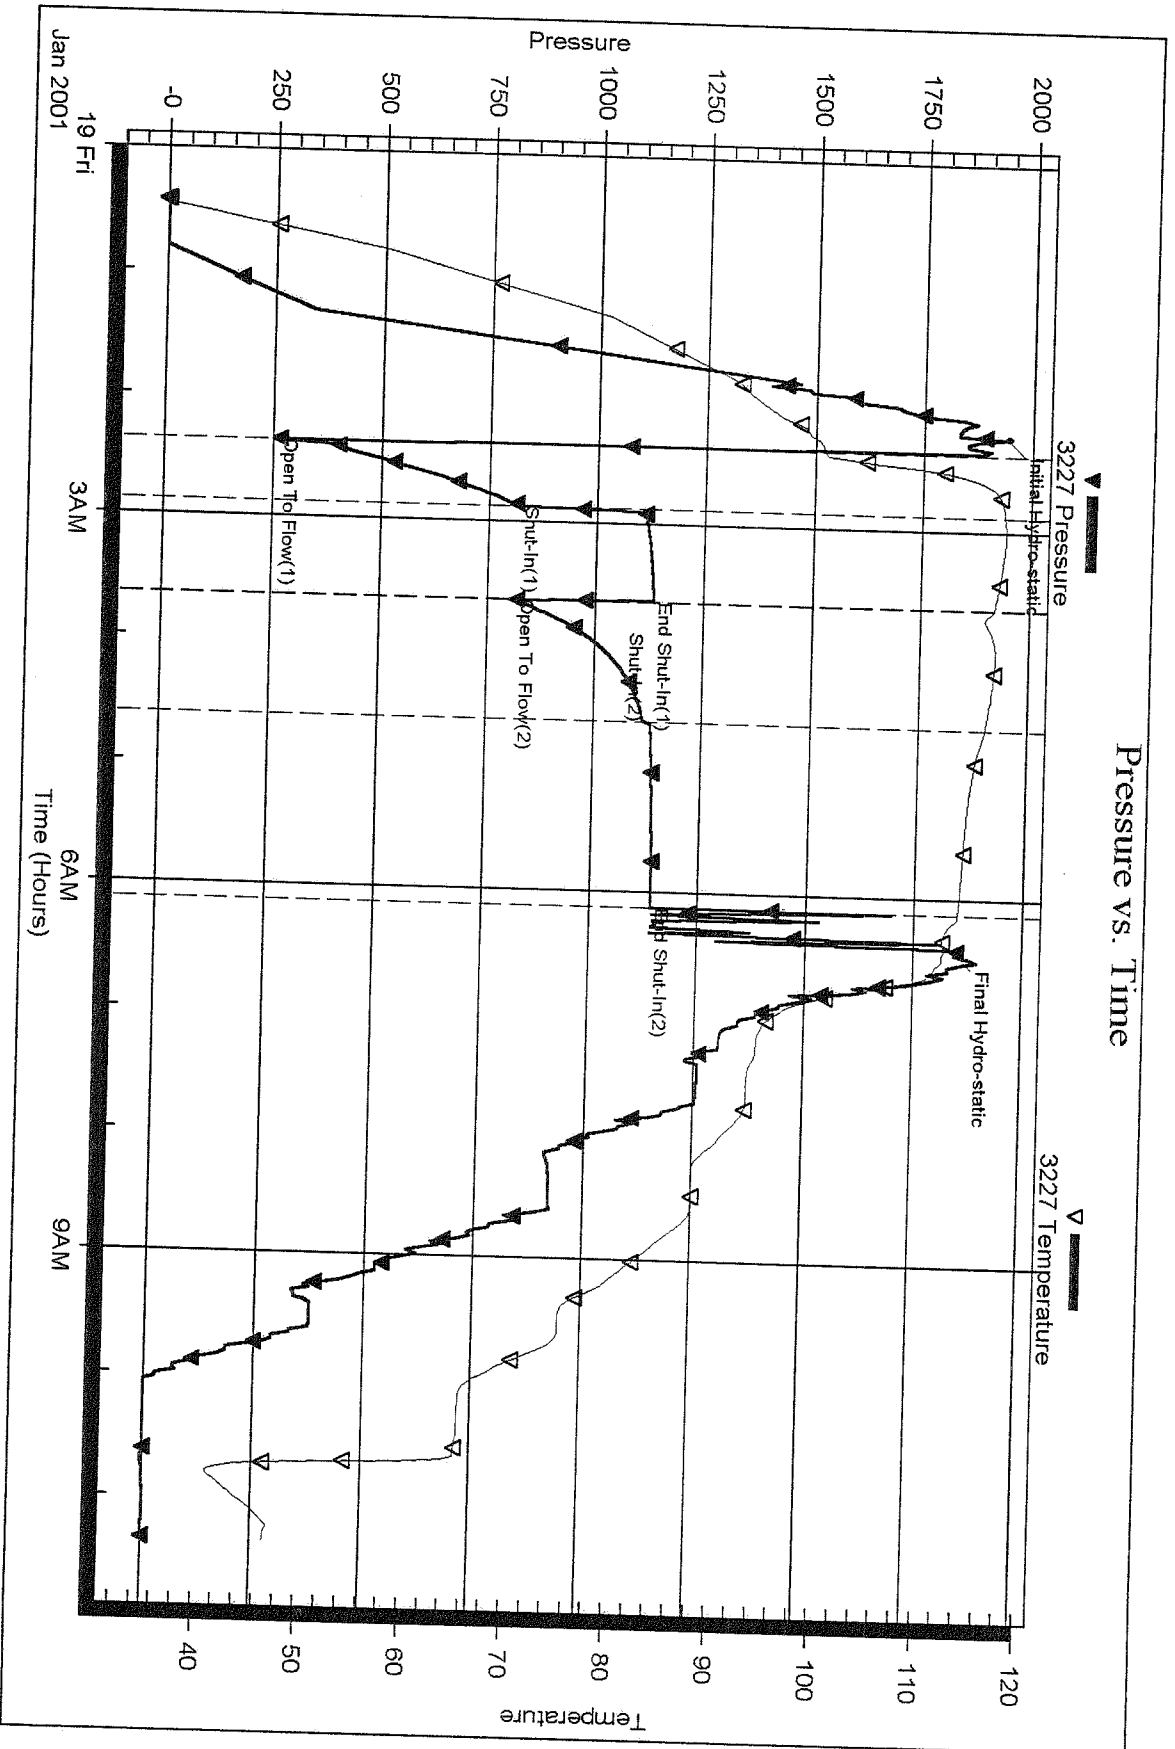


CHART PAGE

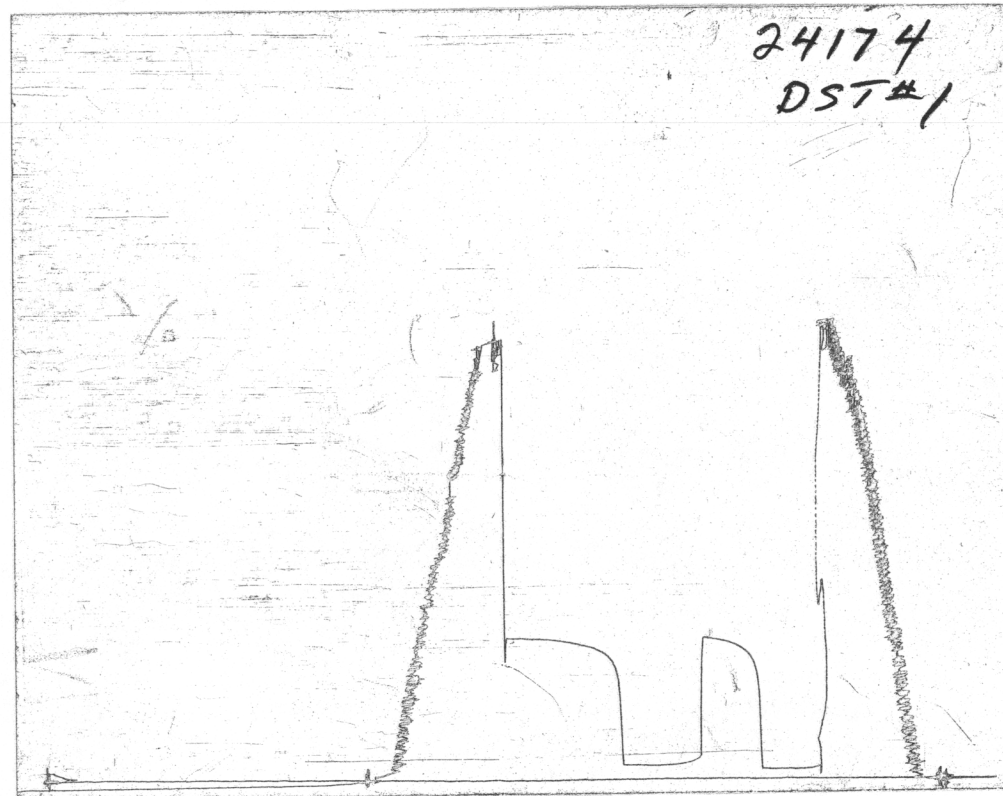

This is a photocopy of the actual AK-1 recorder chart

CHART PAGE

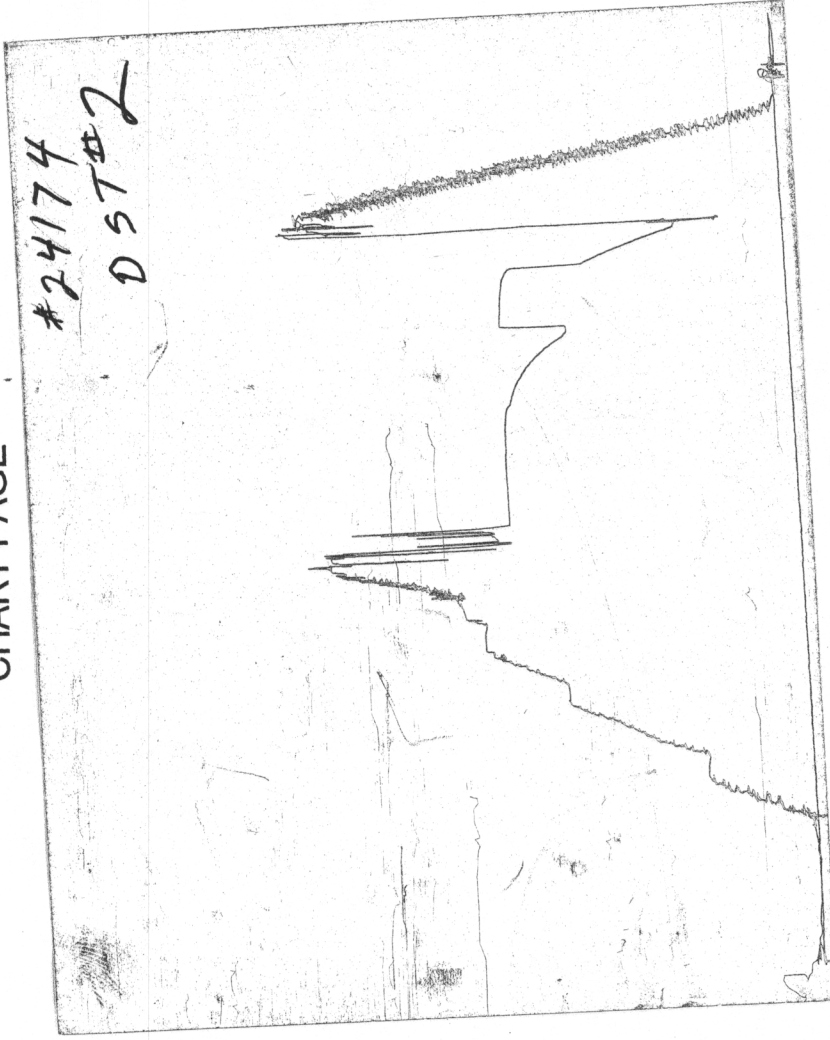

This is a photocopy of the actual AK-1 recorder chart

TRILOBITE TESTING L.L.C.

P.O. Box 362 • Hays, Kansas 67601

N^o 13970

Test Ticket

Well Name & No. <u>WASINGER #1</u>	Test No. <u>#1</u>	Date <u>1-17-01</u>
Company <u>CORAL PROD. CORP.</u>	Zone Tested <u>KC.</u>	
Address <u>1600 STOUT ST. SUITE 1500 DENVER, CO. 80202</u>		Elevation <u>2346</u> KB <u>2341</u> GL
Co. Rep / Geo. <u>JERRY GREEN</u>	Cont. <u>VONFELDT</u>	Est. Ft. of Pay <u> </u> Por. <u> </u> %
Location: Sec. <u>19</u>	Twp. <u>9S</u>	Rge. <u>21W</u> Co. <u>GRAHAM</u> State <u>KS</u>
No. of Copies <u> </u>	Distribution Sheet (Y, N) <u> </u>	Turnkey (Y, N) <u> </u> Evaluation (Y, N) <u> </u>

Interval Tested <u>3633-3658</u>	Initial Str Wt./Lbs. <u>38,000</u>	Unseated Str Wt./Lbs. <u>38,000</u>
Anchor Length <u>25'</u>	Wt. Set Lbs. <u>20,000</u>	Wt. Pulled Loose/Lbs. <u>54,000</u>
Top Packer Depth <u>3628</u>	Tool Weight <u>2,500</u>	
Bottom Packer Depth <u>3633</u>	Hole Size — 7 7/8" <u>✓</u>	Rubber Size — 6 3/4" <u>✓</u>
Total Depth <u>3658</u>	Wt. Pipe Run <u>0</u>	Drill Collar Run <u>0</u>
Mud Wt. <u>9.1</u> LCM <u>TR</u> Vis. <u>52</u> WL <u>8.0</u>	Drill Pipe Size <u>4 1/2 XH</u>	Ft. Run <u>3620</u>
Blow Description <u>IF-WEAK 2" IN-45 MIN.</u>		
<u>F.F.-WEAK 1" IN-60 MIN.</u>		

Recovery — Total Feet <u>55'</u>	GIP <u> </u>	Ft. in DC <u> </u>	Ft. in DP <u> </u>
Rec. <u>55'</u>	Feet Of <u>MUD. C/WATER W/OIL SPEC</u>	%gas <u> </u> %oil <u> </u>	%water <u> </u> %mud <u> </u>
Rec. <u> </u>	Feet Of <u> </u>	%gas <u> </u> %oil <u> </u>	%water <u> </u> %mud <u> </u>
Rec. <u> </u>	Feet Of <u> </u>	%gas <u> </u> %oil <u> </u>	%water <u> </u> %mud <u> </u>
Rec. <u> </u>	Feet Of <u> </u>	%gas <u> </u> %oil <u> </u>	%water <u> </u> %mud <u> </u>
Rec. <u> </u>	Feet Of <u> </u>	%gas <u> </u> %oil <u> </u>	%water <u> </u> %mud <u> </u>
BHT <u>103</u>	°F Gravity <u> </u>	°API D@ <u> </u>	°F Corrected Gravity <u> </u> °API <u> </u>
RW <u>1.27</u>	@ <u>62</u> °F	Chlorides <u>30,000</u> ppm	Recovery <u> </u> Chlorides <u> </u> ppm System <u> </u>

	AK-1	Alpine			
(A) Initial Hydrostatic Mud	<u>1752</u>	PSI	Recorder No. <u>3227</u>	T-On Location <u>15:45</u>	1:36
(B) First Initial Flow Pressure	<u>16</u>	PSI	(depth) <u>3635</u>	T-Started <u>17:15</u>	1:15
(C) First Final Flow Pressure	<u>27</u>	PSI	Recorder No. <u>24174</u>	T-Open <u>18:45</u>	
(D) Initial Shut-In Pressure	<u>571</u>	PSI	(depth) <u>3655</u>	T-Pulled <u>22:45</u>	
(E) Second Initial Flow Pressure	<u>27</u>	PSI	Recorder No. <u> </u>	T-Out <u>24:30</u>	
(F) Second Final Flow Pressure	<u>42</u>	PSI	(depth) <u> </u>	T-Off Location <u> </u>	
(G) Final Shut-in Pressure	<u>571</u>	PSI	Initial Opening <u>45</u>	Test <u>BOTTOM HOLE</u>	700
(Q) Final Hydrostatic Mud	<u>1727</u>	PSI	Initial Shut-in <u>45</u>	Jars <u> </u>	
			Final Flow <u>60</u>	Safety Joint <u>✓ 50</u>	
			Final Shut-in <u>90</u>	Straddle <u> </u>	

TRILOBITE TESTING L.L.C. SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND OF THE PROPERTY OR PERSONNEL OF THE ONE FOR WHOM A TEST IS MADE, OR FOR ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH THE USE OF ITS EQUIPMENT, OR ITS STATEMENTS OR OPINION CONCERNING THE RESULTS OF ANY TEST. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT COST BY THE PARTY FOR WHOM THE TEST IS MADE.

Approved By Jerry Green

Our Representative John J. Schmidt

Elec. Rec. ✓ 150
Mileage 4.5
Other 1 hr 30
TOTAL PRICE \$ 975

TRILOBITE TESTING L.L.C.

P.O. Box 362 • Hays, Kansas 67601

N^o 13971

Test Ticket

Well Name & No. <u>WASINGER #1</u>	Test No. <u>#2</u>	Date <u>1-19-01</u>
Company <u>CORAL PROD. CORP.</u>	Zone Tested <u>ARB.</u>	
Address <u>1600 STOUT ST. SUITE 1500 DENVER, CO. 80202</u>		Elevation <u>2346</u> KB <u>2341</u> GL
Co. Rep / Geo. <u>JERRY GREEN</u>	Cont. <u>VONFELDT</u>	Est. Ft. of Pay <u> </u> Por. <u> </u> %
Location: Sec. <u>19</u>	Twp. <u>9S</u>	Rge. <u>21W</u> Co. <u>GRAHAM</u> State <u>KS</u>
No. of Copies <u> </u>	Distribution Sheet (Y, N) <u> </u>	Turnkey (Y, N) <u> </u> Evaluation (Y, N) <u> </u>

Interval Tested <u>3818-3882</u>	Initial Str Wt./Lbs. <u>40,000</u>	Unseated Str Wt./Lbs. <u>54,000</u>
Anchor Length <u>64'</u>	Wt. Set Lbs. <u>20,000</u>	Wt. Pulled Loose/Lbs. <u>85,000</u>
Top Packer Depth <u>3813</u>	Tool Weight <u>3,000</u>	
Bottom Packer Depth <u>3818</u>	Hole Size — 7 7/8" <u>✓</u>	Rubber Size — 6 3/4" <u>✓</u>
Total Depth <u>3882</u>	Wt. Pipe Run <u>0</u>	Drill Collar Run <u>0</u>
Mud Wt. <u>9.4</u> LCM <u>TR.</u> Vis. <u>53</u> WL <u>8.8</u>	Drill Pipe Size <u>4 1/2 XH</u>	Ft. Run <u>3805</u>
Blow Description <u>I.F. - STRONG BLOW BOTTOM IN 1-MIN.</u>		
<u>F.F. - STRONG BLOW BOTTOM IN 1-MIN</u>		

Recovery — Total Feet <u>2750'</u>	GIP <u>120'</u>	Ft. in DC <u> </u>	Ft. in DP <u> </u>
Rec. <u>2750</u>	Feet Of <u>01L</u>	%gas <u> </u> %oil <u> </u>	%water <u> </u> %mud <u> </u>
Rec. <u> </u>	Feet Of <u> </u>	%gas <u> </u> %oil <u> </u>	%water <u> </u> %mud <u> </u>
Rec. <u> </u>	Feet Of <u> </u>	%gas <u> </u> %oil <u> </u>	%water <u> </u> %mud <u> </u>
Rec. <u> </u>	Feet Of <u> </u>	%gas <u> </u> %oil <u> </u>	%water <u> </u> %mud <u> </u>
Rec. <u> </u>	Feet Of <u> </u>	%gas <u> </u> %oil <u> </u>	%water <u> </u> %mud <u> </u>
BHT <u> </u>	°F Gravity <u> </u>	°API D@ <u>24</u>	°F Corrected Gravity <u>26</u> °API <u> </u>
RW <u> </u>	@ <u> </u>	°F Chlorides <u> </u> ppm Recovery	Chlorides <u> </u> ppm System

(A) Initial Hydrostatic Mud	AK-1 <u>1944</u>	Alpine <u>1944</u>	PSI Recorder No. <u>3227</u>	T-On Location <u>22:30</u>
(B) First Initial Flow Pressure	<u>264</u>	PSI (depth) <u>3820</u>	T-Started <u>13:00</u>	<u>125</u>
(C) First Final Flow Pressure	<u>822</u>	PSI Recorder No. <u>24174</u>	T-Open <u>02:20</u>	<u>10:20</u>
(D) Initial Shut-In Pressure	<u>1136</u>	PSI (depth) <u>3879</u>	T-Pulled <u>06:05</u>	
(E) Second Initial Flow Pressure	<u>816</u>	PSI Recorder No. <u> </u>	T-Out <u>10:45</u>	
(F) Second Final Flow Pressure	<u>1117</u>	PSI (depth) <u> </u>	T-Off Location <u> </u>	
(G) Final Shut-in Pressure	<u>1142</u>	PSI Initial Opening <u>30</u>	Test <u>BOTTOM HOLE</u>	<u>700</u>
(Q) Final Hydrostatic Mud	<u>1846</u>	PSI Initial Shut-in <u>45</u>	Jars <u> </u>	
		Final Flow <u>60</u>	Safety Joint <u>✓ 50</u>	
		Final Shut-in <u>90</u>	Straddle <u> </u>	
			Circ. Sub <u> </u>	
			Sampler <u> </u>	
			Extra Packer <u> </u>	
			Elec. Rec. <u>✓ 150</u>	
			Mileage <u>45</u>	
			Other <u>4hrs 150</u>	
			TOTAL PRICE \$ <u>1095</u>	

TRILOBITE TESTING L.L.C. SHALL NOT BE LIABLE FOR DAMAGE OF ANY KIND OF THE PROPERTY OR PERSONNEL OF THE ONE FOR WHOM A TEST IS MADE, OR FOR ANY LOSS SUFFERED OR SUSTAINED, DIRECTLY OR INDIRECTLY, THROUGH THE USE OF ITS EQUIPMENT, OR ITS STATEMENTS OR OPINION CONCERNING THE RESULTS OF ANY TEST. TOOLS LOST OR DAMAGED IN THE HOLE SHALL BE PAID FOR AT COST BY THE PARTY FOR WHOM THE TEST IS MADE.

Approved By [Signature]
Our Representative John J. Schmidt

4hrs
90
60
150
