

DATE 3-9-61

TICKET NO. 282

COMPANY Davis Bros. CONTRACTOR Transit Corp.

WELL NO. 1 'C' LEASE Osborne COUNTY Rooks SEC. 30 RG. 9 TWP. 17

TEST NO. 1 HOLE SIZE 7 7/8" PACKER SIZE 6 3/4" TOOL JOINT 4" FH

ANCHOR LENGTH 30' AIR CHAMBER LENGTH --- SIZE CHOKE 1/2"

FORMATION Toronto INTERVAL TESTED 3270'-3300' ELEVATION 2114' DF T. D. 3300'

MUD WEIGHT 9.9 VISCOSITY 40 WATER LOSS 15cc

TOOL OPEN 2 hrs. IBHP SHUT IN TIME 20 min. FBHP SHUT IN TIME 30 min.

BLOW Strong through out test.

RECOVERY 1100' of muddy water.

REMARKS _____


APPROVED BY J. R. Green TESTER R. A. Dickey

APPROVED BY

J. R. Green

TESTER

R. A. Dickey

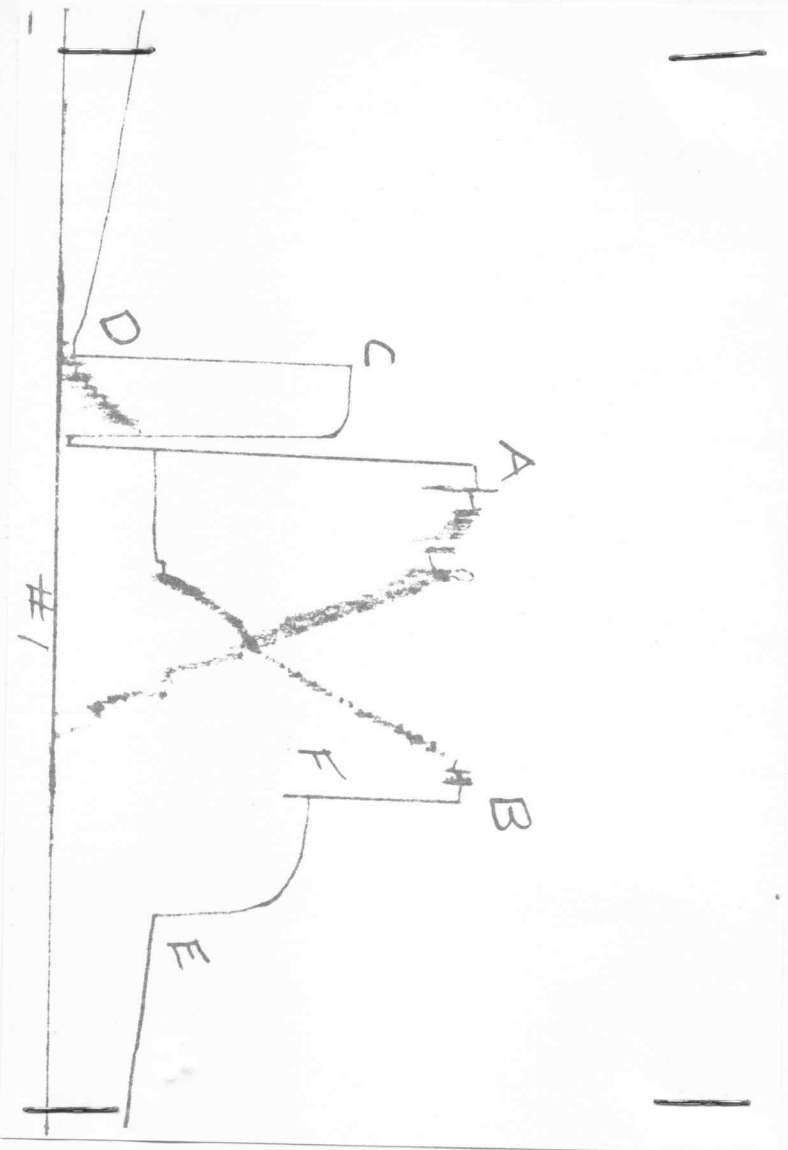

PRESSURE READINGS

A. Initial Hyd. Pressure	1780
B. Final Hyd. Pressure	1780
C. Initial BHP	1190
D. Initial Flow Pressure	80
E. Final Flow Pressure	450
F. Final BHP	1060

DATE 3-10-61

TICKET NO. 283

COMPANY Davis Bros. CONTRACTOR Transit Corp.

WELL NO. 1 'C' LEASE Osborne COUNTY Rooks SEC. 30 RG. 9 TWP. 17

TEST NO. 2 HOLE SIZE 7 7/8" PACKER SIZE 6 3/4" TOOL JOINT 4" FH

ANCHOR LENGTH 85' AIR CHAMBER LENGTH --- SIZE CHOKER 1/2"

FORMATION K.C. INTERVAL TESTED 3295'-3380' ELEVATION 2114' DF T. D. 3380'

MUD WEIGHT 9.9 VISCOSITY 41 WATER LOSS 14cc

TOOL OPEN 2 hrs. IBHP SHUT IN TIME 20 min. FBHP SHUT IN TIME 30 min.

BLOW Strong through out test.

RECOVERY 900' of muddy water.

REMARKS


APPROVED BY J. R. Green TESTER R. A. Dickey

APPROVED BY

J. R. Green

TESTER

R. A. Dickey

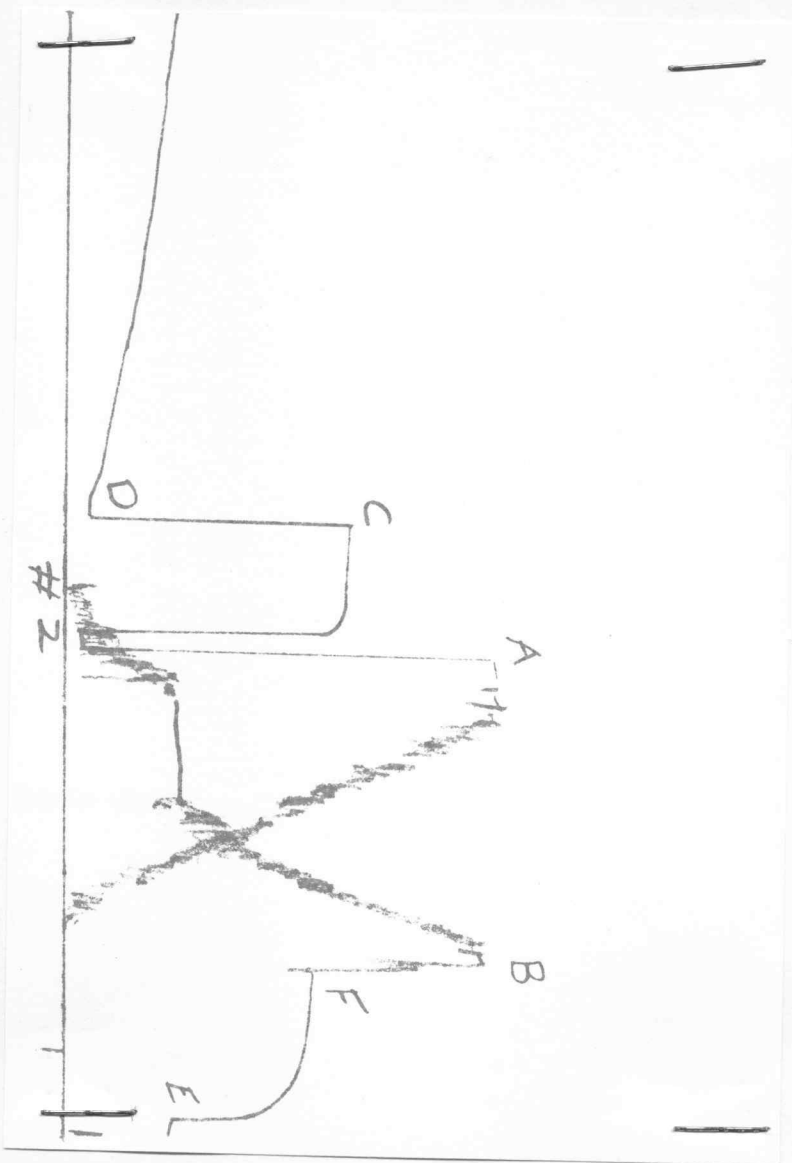

PRESSURE READINGS	
A. Initial Hyd. Pressure	1840
B. Final Hyd. Pressure	1830
C. Initial BHP	1200
D. Initial Flow Pressure	120
E. Final Flow Pressure	470
F. Final BHP	1040
