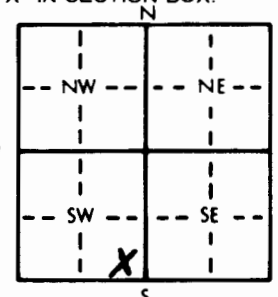


1 LOCATION OF WATER WELL: County: Dickinson Fraction: SE 1/4 SE 1/4 SW 1/4 Section Number: 32 Township Number: T 12 S Range Number: R 4 E

Distance and direction from nearest town or city street address of well if located within city? 1/2 mile East of Chapman on Highway 40

2 WATER WELL OWNER: Hankins Construction Co. + J.R. Gibbons RR#, St. Address, Box #: Box 632 City, State, ZIP Code: Chapman, KS 61431 Application Number: Temporary Permit *Copy Attached*

3 LOCATE WELL'S LOCATION WITH AN "X" IN SECTION BOX:  4 DEPTH OF COMPLETED WELL: 58 ft. ELEVATION: _____ ft. Depth(s) Groundwater Encountered: 1. 30 ft. 2. _____ ft. 3. _____ ft. WELL'S STATIC WATER LEVEL: 30 ft. below land surface measured on mo/day/yr Pump test data: Well water was _____ ft. after _____ hours pumping _____ gpm Est. Yield: 800 gpm: Well water was _____ ft. after _____ hours pumping _____ gpm Bore Hole Diameter: 15 in. to 60 in. to _____ ft. and _____ in. to _____ ft. WELL WATER TO BE USED AS: 5 Public water supply 8 Air conditioning 11 Injection well 1 Domestic 3 Feedlot 6 Oil field water supply 9 Dewatering 12 Other (Specify below) 2 Irrigation 4 Industrial 7 Lawn and garden only 10 Monitoring well Was a chemical/bacteriological sample submitted to Department? Yes _____ No _____ If yes, mo/day/yr sample was submitted Water Well Disinfected? Yes No

5 TYPE OF BLANK CASING USED: 1 Steel 3 RMP (SR) 5 Wrought iron 8 Concrete tile CASING JOINTS: Glued Clamped _____ 2 PVC 4 ABS 6 Asbestos-Cement 9 Other (specify below) Welded _____ Threaded _____ Blank casing diameter: 8 in. to 30 in. Dia _____ in. to _____ in. Dia _____ in. to _____ in. Dia Casing height above land surface: 2 in., weight Sch 40 lbs./ft. Wall thickness or gauge No. _____ TYPE OF SCREEN OR PERFORATION MATERIAL: 1 Steel 3 Stainless steel 5 Fiberglass 7 PVC 10 Asbestos-cement 2 Brass 4 Galvanized steel 6 Concrete tile 8 RMP (SR) 11 Other (specify) _____ 12 None used (open hole) SCREEN OR PERFORATION OPENINGS ARE: 1 Continuous slot 3 Mill slot 40/1000 5 Gauzed wrapped 8 Saw cut 11 None (open hole) 2 Louvered shutter 4 Key punched 6 Wire wrapped 9 Drilled holes 10 Other (specify) _____ SCREEN-PERFORATED INTERVALS: From 30 ft. to 58 ft. From _____ ft. to _____ ft. From _____ ft. to _____ ft. GRAVEL PACK INTERVALS: From 25 ft. to 58 ft. From _____ ft. to _____ ft. From _____ ft. to _____ ft.

6 GROUT MATERIAL: 1 Neat cement 2 Cement grout 3 Bentonite 4 Other _____ Grout Intervals: From 0 ft. to 25 ft. From _____ ft. to _____ ft. From _____ ft. to _____ ft. What is the nearest source of possible contamination: 1 Septic tank 4 Lateral lines None Close 7 Pit privy 10 Livestock pens 14 Abandoned water well 2 Sewer lines 5 Cess pool 8 Sewage lagoon 11 Fuel storage 15 Oil well/Gas well 3 Watertight sewer lines 6 Seepage pit 9 Feedyard 12 Fertilizer storage 16 Other (specify below) 13 Insecticide storage _____ Direction from well? _____ How many feet? _____

FROM	TO	LITHOLOGIC LOG	FROM	TO	PLUGGING INTERVALS
0	4	Top Soil			
4	15	Brown Clay			
15	28	Sandy Clay			
28	32	Fine Sand			
32	60'	Coarse Sand (Water) & Fine Gravel			

7 CONTRACTOR'S OR LANDOWNER'S CERTIFICATION: This water well was (1) constructed (2) reconstructed, or (3) plugged under my jurisdiction and was completed on (mo/day/year) 4/2/92 and this record is true to the best of my knowledge and belief. Kansas Water Well Contractor's License No. 451 This Water Well Record was completed on (mo/day/yr) 4/27/92 under the business name of Haldeman Well Drilling by (signature) Craig

OFFICE USE ONLY
T
R
EW
SEC.
