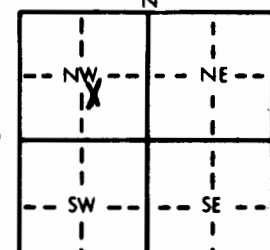


1 LOCATION OF WATER WELL: County: SEDGWICK		Fraction NW 1/4 SE 1/4 NW 1/4	Section Number 34	Township Number T 28 S	Range Number R 2 E
Distance and direction from nearest town or city street address of well if located within city? 6633 South Bedford Ct. Fairway Meadows Wichita, KS.					
2 WATER WELL OWNER: RR#, St. Address, Box # : City, State, ZIP Code :		Beckham Construction 2006 North Forestpark Derby, KS. Board of Agriculture, Division of Water Resources Application Number:			
3 LOCATE WELL'S LOCATION WITH AN "X" IN SECTION BOX: 		4 DEPTH OF COMPLETED WELL: 80 ft. ELEVATION: Depth(s) Groundwater Encountered 1. 41 ft. 2. ft. 3. ft. WELL'S STATIC WATER LEVEL 41 ft. below land surface measured on mo/day/yr 6-21-88 Pump test data: Well water was ft. after hours pumping gpm Est. Yield gpm Well water was ft. after hours pumping gpm Bore Hole Diameter 11 in. to ft., and in. to ft. WELL WATER TO BE USED AS: 1 Domestic 3 Feedlot 5 Public water supply 8 Air conditioning 11 Injection well 2 Irrigation 4 Industrial 6 Oil field water supply 9 Dewatering 12 Other (Specify below) 7 Lawn and garden only 10 Monitoring well Was a chemical/bacteriological sample submitted to Department? Yes No X ; If yes, mo/day/yr sample was submitted Water Well Disinfected? Yes X No			
5 TYPE OF BLANK CASING USED: 1 Steel 3 RMP (SR) 2 PVC 4 ABS Blank casing diameter 5 in. to 45 ft., Dia. in. to ft., Dia. in. to ft. Casing height above land surface 12 in., weight 1.59 lbs./ft. Wall thickness or gauge No. 203		CASING JOINTS: Glued X Clamped Welded Threaded Cer-Mac styrene SDR-26			
TYPE OF SCREEN OR PERFORATION MATERIAL: 1 Steel 3 Stainless steel 5 Fiberglass 2 Brass 4 Galvanized steel 6 Concrete tile SCREEN OR PERFORATION OPENINGS ARE: 1 Continuous slot 3 Mill slot 5 Gauzed wrapped 8 Saw cut 11 None (open hole) 2 Louvered shutter 4 Key punched 6 Wire wrapped 9 Drilled holes 7 Torch cut 10 Other (specify)		7 PVC 10 Asbestos-cement 8 RMP (SR) 11 Other (specify) 9 ABS 12 None used (open hole)			
SCREEN-PERFORATED INTERVALS: From 45 ft. to 80 ft., From ft. to ft. From ft. to ft., From ft. to ft.		GRAVEL PACK INTERVALS: From 24 ft. to 80 ft., From ft. to ft. From ft. to ft., From ft. to ft.			
6 GROUT MATERIAL: 1 Neat cement 2 Cement grout 3 Bentonite 4 Other Grout Intervals: From 4 ft. to 24 ft., From ft. to ft., From ft. to ft.		What is the nearest source of possible contamination: Septic system not installed at this time. 14 Abandoned water well 1 Septic tank 4 Lateral lines 7 Pit privy 11 Fuel storage 15 Oil well/Gas well 2 Sewer lines 5 Cess pool 8 Sewage lagoon 12 Fertilizer storage 16 Other (specify below) 3 Watertight sewer lines 6 Seepage pit 9 Feedyard 13 Insecticide storage None apparent Direction from well? How many feet?			
FROM TO LITHOLOGIC LOG		FROM TO PLUGGING INTERVALS			
0	3	Topsoil			
3	18	Clay			
18	58	Brown Sahle			
58	80	Gray Shale			
7 CONTRACTOR'S OR LANDOWNER'S CERTIFICATION: This water well was (1) constructed, (2) reconstructed, or (3) plugged under my jurisdiction and was completed on (mo/day/year) 6-21-88 and this record is true to the best of my knowledge and belief. Kansas Water Well Contractor's License No. 236 This Water Well Record was completed on (mo/day/yr) 4-1-89 under the business name of Harp Well & Pump Service, Inc. by (signature) <i>Mark Arnold</i>					
