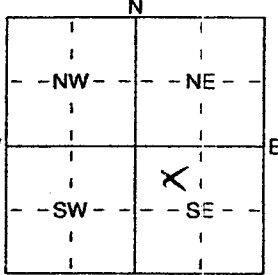


1 LOCATION OF WATER WELL: Fraction 1/4 NW 1/4 SE 1/4 Section Number 20 Township Number T 6 S Range Number R 20  
 County: Atchison

Distance and direction from nearest town or city street address of well if located within city?  
4 miles southwest of Atchison, KS

2 WATER WELL OWNER: ContiGroup Companies  
 RR#, St. Address, Box #: U.S. Highway 59 West Board of Agriculture, Division of Water Resources  
 City, State, ZIP Code: Atchison, KS 66002 Application Number:

3 LOCATE WELL'S LOCATION WITH AN "X" IN SECTION BOX:  4 DEPTH OF COMPLETED WELL 62 ft. ELEVATION: 1060.12 (GRAVIM)  
 Depth(s) Groundwater Encountered 1 21-37.5 ft. 2 57-61 ft. 3 71.5-77 ft.  
 WELL'S STATIC WATER LEVEL 21.9 ft. below land surface measured on mo/day/yr AUGUST 2006  
 Pump test data: Well water was \_\_\_\_\_ ft. after \_\_\_\_\_ hours pumping \_\_\_\_\_ gp  
 Est. Yield UNK gpm: Well water was \_\_\_\_\_ ft. after \_\_\_\_\_ hours pumping \_\_\_\_\_ gp  
 WELL WATER TO BE USED AS: 5 Public water supply 8 Air conditioning 11 Injection well  
 1 Domestic 3 Feedlot 6 Oil field water supply 9 Dewatering 12 Other (Specify below)  
 2 Irrigation 4 Industrial 7 Domestic (lawn & garden) 10 Monitoring well  
 Was a chemical/bacteriological sample submitted to Department? Yes No; If yes, mo/day/yr sample was submitted  
 Water Well Disinfected? Yes No

5 TYPE OF BLANK CASING USED: 1 Steel 2 PVC 3 RMP (SR) 4 ABS 5 Wrought iron 6 Asbestos-Cement 7 Fiberglass 8 Concrete tile 9 Other (specify below) CASING JOINTS: Glued \_\_\_\_\_ Clamped \_\_\_\_\_  
 Blank casing diameter Steel 8" in. to 0-49 ft. Dia 2" PVC in. to 0-57 ft. Dia \_\_\_\_\_ in. to \_\_\_\_\_  
 Casing height above land surface -6 in., weight \_\_\_\_\_ lbs./ft. Wall thickness or gauge No. \_\_\_\_\_  
 TYPE OF SCREEN OR PERFORATION MATERIAL: 1 Steel 2 Brass 3 Stainless Steel 4 Galvanized Steel 5 Fiberglass 6 Concrete tile 7 PVC 7 PVC 8 RMP (SR) 9 ABS 10 Asbestos-Cement 11 Other (Specify) 12 None used (open hole)  
 SCREEN OR PERFORATION OPENINGS ARE: 1 Continuous slot 2 Louvered shutter 3 Mill slot 3 Mill slot 4 Key punched 5 Gauzed wrapped 6 Wire wrapped 7 Torch cut 8 Saw cut 9 Drilled holes 10 Other (specify) 0.01 slot 11 None (open hole)  
 SCREEN-PERFORATED INTERVALS: From 57 ft. to 62 ft. From \_\_\_\_\_ ft. to \_\_\_\_\_ ft.  
 GRAVEL PACK INTERVALS: From 55.5 ft. to 62 ft. From \_\_\_\_\_ ft. to \_\_\_\_\_ ft.  
Bentonite From 50 ft. to 55.5 ft. From \_\_\_\_\_ ft. to \_\_\_\_\_ ft.

6 GROUT MATERIAL: 1 Neat cement 2 Cement grout 2 Cement grout 3 Bentonite 4 Other \_\_\_\_\_  
 Grout Intervals: From -0.2 ft. to 50 ft. From \_\_\_\_\_ ft. to \_\_\_\_\_ ft. From \_\_\_\_\_ ft. to \_\_\_\_\_ ft.  
 What is the nearest source of possible contamination: 1 Septic tank 2 Sewer lines 3 Watertight sewer lines 4 Lateral lines 5 Cess pool 6 Seepage pit 7 Pit privy 8 Sewage lagoon 9 Feedyard 10 Livestock pens 11 Fuel storage 12 Fertilizer storage 13 Insecticide storage 14 Abandoned water well 15 Oil well/Gas well 16 Other (specify below)  
 Direction from well? \_\_\_\_\_ How many feet? \_\_\_\_\_

FROM	TO	LITHOLOGIC LOG	FROM	TO	PLUGGING INTERVALS
0	15	Brown and grey silty clay			
15	17	Bentonite			
17	19.21	Brown silty clay			
21.9	37.5	Brown silty clay, soft wet			
37.5	39	Brown silty clay, stiff			
39	43	Brown silty clay, soft wet			
43	57	Grey silty clay, stiff			
57	61	Fine grained sand wet			
61	67	Grey silt dense, moist to dry			
67	67.5	Fine grained sand, wet			
67.5	71.5	Grey silt, dense moist to dry			
71.5	77	Fine grained sands wet			
77	97	Grey silty clay, stiff			

RECEIVED  
 MAY 11 2007  
 BUREAU OF WATER

7 CONTRACTOR'S OR LANDOWNER'S CERTIFICATION: This water well was (1) constructed (2) reconstructed, or (3) plugged under my jurisdiction and was completed on (mo/day/year) 8/4/06 and this record is true to the best of my knowledge and belief. Kans.  
 Water Well Contractor's Licence No 597 This Water Well Record was completed on (mo/day/yr) MARCH 27, 2007  
 under the business name of Prosonic Corp. by (signature) Jenny Boudreau
