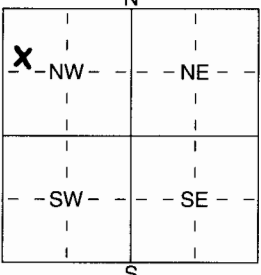


1 LOCATION OF WATER WELL:		Fraction	Section Number	Township Number	Range Number
County: <u>Hodgeman</u>		<u>SW 1/4 NW 1/4 NW 1/4</u>	<u>8</u>	<u>T 23</u>	<u>S R 24 E/W</u>
Distance and direction from nearest town or city street address of well if located within city? <u>BPS 380 04.268' N</u> <u>990 59.406' W</u>					
2 WATER WELL OWNER: <u>Richard Snodgrass</u>					
RR#, St. Address, Box # <u>Box 200</u>			Board of Agriculture, Division of Water Resources		
City, State, ZIP Code <u>Jetmore KS 67854</u>			Application Number:		
3 LOCATE WELL'S LOCATION WITH 4 DEPTH OF COMPLETED WELL <u>200</u> ft. ELEVATION: <u>2340</u>					
AN "X" IN SECTION BOX:		Depth(s) Groundwater Encountered 1 ft. 2 ft. 3 ft.			
		WELL'S STATIC WATER LEVEL ft. below land surface measured on mo/day/yr			
		Pump test data: Well water was ft. after hours pumping gpm			
		Est. Yield gpm: Well water was ft. after hours pumping gpm			
		WELL WATER TO BE USED AS: 5 Public water supply 8 Air conditioning 11 Injection well			
		1 Domestic 3 Feedlot 6 Oil field water supply 9 Dewatering 12 Other (Specify below)			
		2 Irrigation 4 Industrial 7 Domestic (lawn & garden) 10 Monitoring well			
		<u>closed loop heat pump well</u>			
		Was a chemical/bacteriological sample submitted to Department? Yes No <u>X</u> ; If yes, mo/day/yr sample was submitted			
		Water Well Disinfected? Yes No			
5 TYPE OF BLANK CASING USED:					
1 Steel 3 RMP (SR)		5 Wrought iron		8 Concrete tile	
2 PVC 4 ABS		6 Asbestos-Cement		9 Other (specify below)	
		7 Fiberglass		CASING JOINTS: Glued Clamped	
				Welded	
				Threaded	
Blank casing diameter in. to ft., Dia in. to ft., Dia in. to ft.					
Casing height above land surface in., weight lbs./ft. Wall thickness or gauge No.					
TYPE OF SCREEN OR PERFORATION MATERIAL:					
1 Steel 3 Stainless Steel		5 Fiberglass		7 PVC	
2 Brass 4 Galvanized Steel		6 Concrete tile		8 RMP (SR)	
				10 Asbestos-Cement	
				11 Other (Specify)	
				12 None used (open hole)	
SCREEN OR PERFORATION OPENINGS ARE:					
1 Continuous slot 3 Mill slot		5 Guazed wrapped		8 Saw cut	
2 Louvered shutter 4 Key punched		6 Wire wrapped		9 Drilled holes	
		7 Torch cut		10 Other (specify) ft.	
SCREEN-PERFORATED INTERVALS: From ft. to ft., From ft. to ft.					
GRAVEL PACK INTERVALS: From ft. to ft., From ft. to ft.					
6 GROUT MATERIAL: 1 Neat cement 2 Cement grout 3 Bentonite 4 Other					
Grout Intervals: From <u>200</u> ft. to <u>0</u> ft., From ft. to ft., From ft. to ft.					
What is the nearest source of possible contamination:					
1 Septic tank 4 Lateral lines		7 Pit privy		10 Livestock pens	
2 Sewer lines 5 Cess pool		8 Sewage lagoon		11 Fuel storage	
3 Watertight sewer lines 6 Seepage pit		9 Feedyard		12 Fertilizer storage	
				13 Insecticide storage	
				14 Abandoned water well	
				15 Oil well/Gas well	
				16 Other (specify below)	
Direction from well? <u>S</u> How many feet? <u>24</u>					
FROM TO		LITHOLOGIC LOG		FROM TO	
<u>0 10</u>		<u>sandy loam</u>		<u>200 0</u>	
<u>10 35</u>		<u>gravel w/ sand</u>		<u>high solids bentonite</u>	
<u>35 100</u>		<u>limestone w/ clay layers</u>		<u>13.4 #/gal</u>	
<u>100 130</u>		<u>clay</u>			
<u>130 170</u>		<u>limestone</u>			
<u>170 200</u>		<u>clay</u>			
7 CONTRACTOR'S OR LANDOWNER'S CERTIFICATION: This water well was (1) constructed, (2) reconstructed, or (3) plugged under my jurisdiction and was completed on (mo/day/year) <u>12/31/07</u> and this record is true to the best of my knowledge and belief. Kansas Water Well Contractor's Licence No <u>733</u> This Water Well Record was completed on (mo/day/yr) <u>01/10/08</u> under the business name of <u>CYC Loop Drillids</u> by (signature) <u>RC</u>					
INSTRUCTIONS: Use typewriter or ball point pen. PLEASE PRESS FIRMLY and PRINT clearly. Please fill in blanks, underline or circle the correct answers. Send top three copies to Kansas Department of Health and Environment, Bureau of Water, Geology Section, 1000 SW Jackson St., Suite 420, Topeka, Kansas 66612-1367. Telephone 785-296-5522. Send one to WATER WELL OWNER and retain one for your records. Fee of \$5.00 for each constructed well.					
