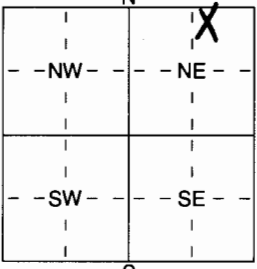


1 LOCATION OF WATER WELL: County: <u>Sedgwick</u> Fraction: <u>1/4</u> <u>1/4</u> <u>1/4</u> <u>1/4</u> Section Number: <u>4</u> Township Number: <u>T 27 S</u> Range Number: <u>R 1 E/W</u>	
Distance and direction from nearest town or city street address of well if located within city? <u>7918 Meadow Park Ct.</u>	
2 WATER WELL OWNER: <u>River City Construction</u> RR#, St. Address, Box # : City, State, ZIP Code : Board of Agriculture, Division of Water Resources Application Number:	
3 LOCATE WELL'S LOCATION WITH AN "X" IN SECTION BOX: 	4 DEPTH OF COMPLETED WELL <u>48</u> ft. ELEVATION: Depth(s) Groundwater Encountered 1 ft. 2 ft. 3 ft. WELL'S STATIC WATER LEVEL <u>17</u> ft. below land surface measured on mo/day/yr <u>4-1-04</u> Pump test data: Well water was ft. after hours pumping gpm Est. Yield <u>30</u> gpm: Well water was ft. after hours pumping gpm WELL WATER TO BE USED AS: 1 Domestic 3 Feedlot 5 Public water supply 8 Air conditioning 11 Injection well 2 Irrigation 4 Industrial 7 Domestic (lawn & garden) 10 Monitoring well 12 Other (Specify below) Was a chemical/bacteriological sample submitted to Department? Yes No <u>X</u> ; If yes, mo/day/yr sample was submitted Water Well Disinfected? Yes <u>X</u> No
5 TYPE OF BLANK CASING USED: 1 Steel 3 RMP (SR) 5 Wrought iron 8 Concrete tile CASING JOINTS: Glued <u>X</u> Clamped 2 PVC 4 ABS 6 Asbestos-Cement 9 Other (specify below) Welded Blank casing diameter <u>5</u> in. to <u>40</u> ft. Dia in. to ft. Dia in. to ft. Casing height above land surface <u>12</u> in., weight <u>2 40</u> lbs./ft. Wall thickness or gauge No. <u>160 psi</u> TYPE OF SCREEN OR PERFORATION MATERIAL: 1 Steel 3 Stainless Steel 5 Fiberglass 7 PVC 10 Asbestos-Cement 2 Brass 4 Galvanized Steel 6 Concrete tile 9 ABS 11 Other (Specify) 12 None used (open hole) SCREEN OR PERFORATION OPENINGS ARE: 1 Continuous slot 3 Mill slot 5 Gauzed wrapped 8 Saw cut 11 None (open hole) 2 Louvered shutter 4 Key punched 6 Wire wrapped 9 Drilled holes 7 Torch cut 10 Other (specify) ft. SCREEN-PERFORATED INTERVALS: From ft. to <u>48</u> ft., From ft. to ft. GRAVEL PACK INTERVALS: From <u>17</u> ft. to <u>48</u> ft., From ft. to ft. From ft. to ft., From ft. to ft.	
6 GROUT MATERIAL: 1 Neat cement 2 Cement grout 3 Bentonite 4 Other Grout Intervals: From <u>3</u> ft. to ft., From ft. to ft., From ft. to ft. What is the nearest source of possible contamination: 1 Septic tank 4 Lateral lines 7 Pit privy 10 Livestock pens 14 Abandoned water well 2 Sewer lines 5 Cess pool 8 Sewage lagoon 11 Fuel storage 15 Oil well/Gas well 3 Watertight sewer lines 6 Seepage pit 9 Feedyard 12 Fertilizer storage 16 Other (specify below) Direction from well? <u>north</u> 13 Insecticide storage How many feet? <u>30</u>	
FROM TO LITHOLOGIC LOG	FROM TO PLUGGING INTERVALS
0 3 top soil	
3 18 clay	
18 30 gravel	
30 32 clay	
32 48 med sand	
7 CONTRACTOR'S OR LANDOWNER'S CERTIFICATION: This water well was (1) constructed, (2) reconstructed, or (3) plugged under my jurisdiction and was completed on (mo/day/year) <u>4-1-04</u> and this record is true to the best of my knowledge and belief. Kansas Water Well Contractor's Licence No. <u>318</u> This Water Well Record was completed on (mo/day/yr) <u>4-1-04</u> under the business name of <u>Weninger Drilling Inc</u> by (signature) <u>[Signature]</u>	
