

1 LOCATION OF WATER WELL:		Fraction	Section Number	Township Number	Range Number
County:	<i>Sedgwick</i>	<i>SW</i> $\frac{1}{4}$ <i>NW</i> $\frac{1}{4}$ <i>NW</i> $\frac{1}{4}$	<i>25</i>	T <i>27</i> S	R <i>1</i> E <i>(W)</i>

Distance and direction from nearest town or city street address of well if located within city?

2	WATER WELL OWNER:
---	-------------------


RR#, St. Address, Box # :
City, State, ZIP Code :

CMI 9/109
2 North Nevada
Colorado Springs CO 80903

Board of Agriculture, Division of Water Resource
Application Number:

3 LOCATE WELL'S LOCATION WITH AN "X" IN SECTION BOX:

AN "X" IN SECTION BOX:

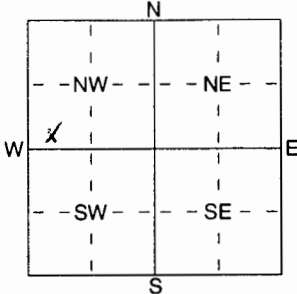

4 DEPTH OF COMPLETED WELL 59' ft. ELEVATION:

Depth(s) Groundwater Encountered 1 13.75 ft. 2 _____ ft. 3 _____ ft.
WELL'S STATIC WATER LEVEL 13.75 ft. below land surface measured on mo/day/yr _____

Pump test data: Well water was ft. after hours pumping gpr
 Est. Yield gpm: Well water was ft. after hours pumping gpr

WELL WATER TO BE USED AS:

1 Domestic	3 Feedlot	5 Public water supply	8 Air conditioning	11 Injection well
2 Irrigation	4 Industrial	6 Oil field water supply	9 Dewatering	12 Other (Specify below)
		7 Domestic (lawn & garden)	10 Monitoring well	MW-17

Was a chemical/bacteriological sample submitted to Department? Yes No X ; If yes, mo/day/yrs sample was submitted
Water Well Disinfected? Yes No (No)

5	TYPE OF BLANK CASING USED:
---	----------------------------

1 Steel
2 PVC
3 RMP (SR)
4 ABS

5 Wrought iron
6 Asbestos-Cement
7 Fiberglass

8 Concrete tile
9 Other (specify below)

CASING JOINTS: Glued Clamped
Welded
Threaded

Blank casing diameter 2 in. to 39 ft., Dia in. to ft., Dia in. to ft.

Casing height above land surface Flush in., weight 10.6 lbs./ft. Wall thickness or gauge No. 10

TYPE OF SCREEN OR PERFORATION MATERIAL:

1 Steel
2 Brass
3 Stainless Steel
4 Galvanized Steel

5 Fiberglass
6 Concrete tile

7 PVC
8 RMP (SR)
9 ABS

10 Asbestos-Cement
11 Other (Specify)
12 None used (open hole)

SCREEN OR PERFORATION OPENINGS ARE:

1 Continuous slot
2 Louvered shutter
3 Mill slot
4 Key punched

5 Guazed wrapped
6 Wire wrapped
7 Torch cut

8 Saw cut
9 Drilled holes
10 Other (specify) ft

SCREEN-PERFORATED INTERVALS: From 44' ft. to 39' ft., From _____ ft. to _____ ft.

From ft. to ft., From ft. to ft.

GRAVEL PACK INTERVALS: From 0 ft. to 44 ft., From _____ ft. to _____ ft.
From _____ ft. to _____ ft., From _____ ft. to _____ ft.

6	GROUT MATERIAL:	1 Neat cement	2 Cement grout	3 Bentonite	4 Other
---	-----------------	---------------	----------------	-------------	---------------

Grout Intervals: From 2 2 ft. to 42 ft., From ft. to ft., From ft. to ft.

What is the nearest source of possible contamination:

1 Septic tank	4 Lateral lines	7 Pit privy	11 Fuel storage	15 Oil well/Gas well
2 Sewer lines	5 Cess pool	8 Sewage lagoon	12 Fertilizer storage	16 Other (specify below)
3 Watertight sewer lines	6 Seepage pit	9 Feedyard	13 Insecticide storage	

Direction from well?

How many feet?

[illegible]

7. CONTRACTOR'S OR LANDOWNER'S CERTIFICATION: This water well was (1) constructed, (2) reconstructed, or (3) plugged under my jurisdiction and was completed on (mo/day/year) 6/14/04 and this record is true to the best of my knowledge and belief. Kansas

Water Well Contractor's Licence No. 705 This Water Well Record was completed on (mo/day/yr)
under the business name of 4440 EX by (signature)
