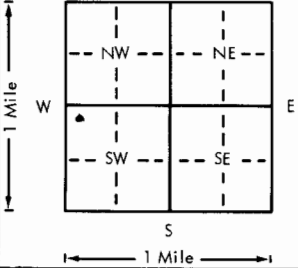


USE TYPEWRITER OR BALL POINT PEN-PRESS FIRMLY, PRINT CLEARLY.

WATER WELL RECORD
KSA 82a-1201-1215

Kansas Department of Health and Environment-Division of Environment
(Water well Contractors)
Topeka, Kansas 66620

1. Location of well: County Kingman Fraction NW 1/4 NW 1/4 SW 1/4 Section number 14 Township number T 28 S R 7 Range number EW																																																									
2. Distance and direction from nearest town or city: 3 1/2 S. of Kingman Street address of well location if in city: Kingman Kansas																																																									
3. Owner of well: Patrick Goff R.R. or street: Kingman Kansas City, state, zip code: Kingman Kansas																																																									
4. Locate with "X" in section below: Sketch map: 																																																									
<table border="1" style="width:100%; border-collapse: collapse;"> <tr> <td rowspan="8" style="width:50%; vertical-align: top;"> 5. Type and color of material <table border="1" style="width:100%; border-collapse: collapse;"> <thead> <tr> <th style="width:80%;"></th> <th style="width:10%;">From</th> <th style="width:10%;">To</th> </tr> </thead> <tbody> <tr><td>Topsail</td><td>0</td><td>4</td></tr> <tr><td>Sand</td><td>4</td><td>9</td></tr> <tr><td>Clay</td><td>9</td><td>23</td></tr> <tr><td>Sand</td><td>23</td><td>39</td></tr> <tr><td>Clay</td><td>39</td><td>41</td></tr> <tr><td>Gravel</td><td>41</td><td>48</td></tr> <tr><td>Red Bed</td><td>48</td><td>50</td></tr> </tbody> </table> </td> <td style="width:50%; vertical-align: top;"> <table border="1" style="width:100%; border-collapse: collapse;"> <tr> <td>6. Bore hole <input checked="" type="checkbox"/> Well depth: 3-22-75</td> <td>Completion date: 3-22-75</td> </tr> <tr> <td>7. Cable tool <input type="checkbox"/> Rotary <input checked="" type="checkbox"/> Driven <input type="checkbox"/> Dug <input type="checkbox"/> Hollow rod <input type="checkbox"/> Jetted <input type="checkbox"/> Bored <input type="checkbox"/> Reverse rotary <input type="checkbox"/></td> <td></td> </tr> <tr> <td colspan="2">8. Use: <input checked="" type="checkbox"/> Domestic <input type="checkbox"/> Public supply <input type="checkbox"/> Industry <input type="checkbox"/> Irrigation <input type="checkbox"/> Air conditioning <input type="checkbox"/> Stock <input type="checkbox"/> Lawn <input type="checkbox"/> Oil field water <input type="checkbox"/> Other</td> </tr> <tr> <td colspan="2">9. Casing: Material PL Height: Above or below 12 in. Threaded <input type="checkbox"/> Welded <input checked="" type="checkbox"/> Surface 1.5 lbs./ft. RMP <input checked="" type="checkbox"/> PVC <input type="checkbox"/> Weight 1.5 lbs./ft. Dia. 5 in. to 50 ft. depth Wall Thickness: inches or 200 Dia. <input type="checkbox"/> in. to <input type="checkbox"/> ft. depth gage No.</td> </tr> <tr> <td colspan="2">10. Screen: Manufacturer's name Sunflower Plastics Type RMP Dia. 5" Slot/gauze 1/8 Length 20' Set between 30 ft. and 50 ft. ft. and <input type="checkbox"/> ft. Gravel pack? Yes Size range of material 4 X 5</td> </tr> <tr> <td colspan="2">11. Static water level: 32 ft. below land surface Date 3-22-75 mo./day/yr.</td> </tr> <tr> <td colspan="2">12. Pumping level below land surfaces: 98 ft. after 1 hrs. pumping 10 g.p.m. <input type="checkbox"/> ft. after <input type="checkbox"/> hrs. pumping <input type="checkbox"/> g.p.m. Estimated maximum yield 10 g.p.m.</td> </tr> <tr> <td colspan="2">13. Water sample submitted: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No Date</td> </tr> <tr> <td colspan="2">14. Well head completion: <input checked="" type="checkbox"/> Pitless adapter 14 Inches above grade</td> </tr> <tr> <td colspan="2">15. Well grouted? Yes With: <input checked="" type="checkbox"/> Neat cement <input type="checkbox"/> Bentonite <input type="checkbox"/> Concrete Depth: From 4 ft. to 24 ft.</td> </tr> <tr> <td colspan="2">16. Nearest source of possible contamination: 180 ft. Direction SW Type Septic Well disinfected upon completion? <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No</td> </tr> <tr> <td colspan="2">17. Pump: Not installed Manufacturer's name Aer motor Model number SD-50 HP 1/2 Volt 230 Length of drop pipe 38 ft. capacity 10 g.p.m. Type: <input checked="" type="checkbox"/> Submersible <input type="checkbox"/> Turbine <input type="checkbox"/> Jet <input type="checkbox"/> Reciprocating <input type="checkbox"/> Centrifugal <input type="checkbox"/> Other</td> </tr> </table> </td> </tr> <tr> <td colspan="2">(Use a second sheet if needed)</td> </tr> <tr> <td>18. Elevation: Topography: <input type="checkbox"/> Hill <input type="checkbox"/> Slope <input checked="" type="checkbox"/> Upland <input type="checkbox"/> Valley</td> <td>19. Remarks:</td> </tr> <tr> <td colspan="2">20. Water well contractor's certification: This well was drilled under my jurisdiction and this report is true to the best of my knowledge and belief. Carl Hayes Water Well Serv. 224 Business Office License No. 02386 Address: Maple Shoals, Mo. Signed: Carl Hayes Date: 3-22-75 Authorized representative</td> </tr> </table>		5. Type and color of material <table border="1" style="width:100%; border-collapse: collapse;"> <thead> <tr> <th style="width:80%;"></th> <th style="width:10%;">From</th> <th style="width:10%;">To</th> </tr> </thead> <tbody> <tr><td>Topsail</td><td>0</td><td>4</td></tr> <tr><td>Sand</td><td>4</td><td>9</td></tr> <tr><td>Clay</td><td>9</td><td>23</td></tr> <tr><td>Sand</td><td>23</td><td>39</td></tr> <tr><td>Clay</td><td>39</td><td>41</td></tr> <tr><td>Gravel</td><td>41</td><td>48</td></tr> <tr><td>Red Bed</td><td>48</td><td>50</td></tr> </tbody> </table>		From	To	Topsail	0	4	Sand	4	9	Clay	9	23	Sand	23	39	Clay	39	41	Gravel	41	48	Red Bed	48	50	<table border="1" style="width:100%; border-collapse: collapse;"> <tr> <td>6. Bore hole <input checked="" type="checkbox"/> Well depth: 3-22-75</td> <td>Completion date: 3-22-75</td> </tr> <tr> <td>7. Cable tool <input type="checkbox"/> Rotary <input checked="" type="checkbox"/> Driven <input type="checkbox"/> Dug <input type="checkbox"/> Hollow rod <input type="checkbox"/> Jetted <input type="checkbox"/> Bored <input type="checkbox"/> Reverse rotary <input type="checkbox"/></td> <td></td> </tr> <tr> <td colspan="2">8. Use: <input checked="" type="checkbox"/> Domestic <input type="checkbox"/> Public supply <input type="checkbox"/> Industry <input type="checkbox"/> Irrigation <input type="checkbox"/> Air conditioning <input type="checkbox"/> Stock <input type="checkbox"/> Lawn <input type="checkbox"/> Oil field water <input type="checkbox"/> Other</td> </tr> <tr> <td colspan="2">9. Casing: Material PL Height: Above or below 12 in. Threaded <input type="checkbox"/> Welded <input checked="" type="checkbox"/> Surface 1.5 lbs./ft. RMP <input checked="" type="checkbox"/> PVC <input type="checkbox"/> Weight 1.5 lbs./ft. Dia. 5 in. to 50 ft. depth Wall Thickness: inches or 200 Dia. <input type="checkbox"/> in. to <input type="checkbox"/> ft. depth gage No.</td> </tr> <tr> <td colspan="2">10. Screen: Manufacturer's name Sunflower Plastics Type RMP Dia. 5" Slot/gauze 1/8 Length 20' Set between 30 ft. and 50 ft. ft. and <input type="checkbox"/> ft. Gravel pack? Yes Size range of material 4 X 5</td> </tr> <tr> <td colspan="2">11. Static water level: 32 ft. below land surface Date 3-22-75 mo./day/yr.</td> </tr> <tr> <td colspan="2">12. Pumping level below land surfaces: 98 ft. after 1 hrs. pumping 10 g.p.m. <input type="checkbox"/> ft. after <input type="checkbox"/> hrs. pumping <input type="checkbox"/> g.p.m. Estimated maximum yield 10 g.p.m.</td> </tr> <tr> <td colspan="2">13. Water sample submitted: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No Date</td> </tr> <tr> <td colspan="2">14. Well head completion: <input checked="" type="checkbox"/> Pitless adapter 14 Inches above grade</td> </tr> <tr> <td colspan="2">15. Well grouted? Yes With: <input checked="" type="checkbox"/> Neat cement <input type="checkbox"/> Bentonite <input type="checkbox"/> Concrete Depth: From 4 ft. to 24 ft.</td> </tr> <tr> <td colspan="2">16. Nearest source of possible contamination: 180 ft. Direction SW Type Septic Well disinfected upon completion? <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No</td> </tr> <tr> <td colspan="2">17. Pump: Not installed Manufacturer's name Aer motor Model number SD-50 HP 1/2 Volt 230 Length of drop pipe 38 ft. capacity 10 g.p.m. Type: <input checked="" type="checkbox"/> Submersible <input type="checkbox"/> Turbine <input type="checkbox"/> Jet <input type="checkbox"/> Reciprocating <input type="checkbox"/> Centrifugal <input type="checkbox"/> Other</td> </tr> </table>	6. Bore hole <input checked="" type="checkbox"/> Well depth: 3-22-75	Completion date: 3-22-75	7. Cable tool <input type="checkbox"/> Rotary <input checked="" type="checkbox"/> Driven <input type="checkbox"/> Dug <input type="checkbox"/> Hollow rod <input type="checkbox"/> Jetted <input type="checkbox"/> Bored <input type="checkbox"/> Reverse rotary <input type="checkbox"/>		8. Use: <input checked="" type="checkbox"/> Domestic <input type="checkbox"/> Public supply <input type="checkbox"/> Industry <input type="checkbox"/> Irrigation <input type="checkbox"/> Air conditioning <input type="checkbox"/> Stock <input type="checkbox"/> Lawn <input type="checkbox"/> Oil field water <input type="checkbox"/> Other		9. Casing: Material PL Height: Above or below 12 in. Threaded <input type="checkbox"/> Welded <input checked="" type="checkbox"/> Surface 1.5 lbs./ft. RMP <input checked="" type="checkbox"/> PVC <input type="checkbox"/> Weight 1.5 lbs./ft. Dia. 5 in. to 50 ft. depth Wall Thickness: inches or 200 Dia. <input type="checkbox"/> in. to <input type="checkbox"/> ft. depth gage No.		10. Screen: Manufacturer's name Sunflower Plastics Type RMP Dia. 5" Slot/gauze 1/8 Length 20' Set between 30 ft. and 50 ft. ft. and <input type="checkbox"/> ft. Gravel pack? Yes Size range of material 4 X 5		11. Static water level: 32 ft. below land surface Date 3-22-75 mo./day/yr.		12. Pumping level below land surfaces: 98 ft. after 1 hrs. pumping 10 g.p.m. <input type="checkbox"/> ft. after <input type="checkbox"/> hrs. pumping <input type="checkbox"/> g.p.m. Estimated maximum yield 10 g.p.m.		13. Water sample submitted: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No Date		14. Well head completion: <input checked="" type="checkbox"/> Pitless adapter 14 Inches above grade		15. Well grouted? Yes With: <input checked="" type="checkbox"/> Neat cement <input type="checkbox"/> Bentonite <input type="checkbox"/> Concrete Depth: From 4 ft. to 24 ft.		16. Nearest source of possible contamination: 180 ft. Direction SW Type Septic Well disinfected upon completion? <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No		17. Pump: Not installed Manufacturer's name Aer motor Model number SD-50 HP 1/2 Volt 230 Length of drop pipe 38 ft. capacity 10 g.p.m. Type: <input checked="" type="checkbox"/> Submersible <input type="checkbox"/> Turbine <input type="checkbox"/> Jet <input type="checkbox"/> Reciprocating <input type="checkbox"/> Centrifugal <input type="checkbox"/> Other		(Use a second sheet if needed)		18. Elevation: Topography: <input type="checkbox"/> Hill <input type="checkbox"/> Slope <input checked="" type="checkbox"/> Upland <input type="checkbox"/> Valley	19. Remarks:	20. Water well contractor's certification: This well was drilled under my jurisdiction and this report is true to the best of my knowledge and belief. Carl Hayes Water Well Serv. 224 Business Office License No. 02386 Address: Maple Shoals, Mo. Signed: Carl Hayes Date: 3-22-75 Authorized representative	
5. Type and color of material <table border="1" style="width:100%; border-collapse: collapse;"> <thead> <tr> <th style="width:80%;"></th> <th style="width:10%;">From</th> <th style="width:10%;">To</th> </tr> </thead> <tbody> <tr><td>Topsail</td><td>0</td><td>4</td></tr> <tr><td>Sand</td><td>4</td><td>9</td></tr> <tr><td>Clay</td><td>9</td><td>23</td></tr> <tr><td>Sand</td><td>23</td><td>39</td></tr> <tr><td>Clay</td><td>39</td><td>41</td></tr> <tr><td>Gravel</td><td>41</td><td>48</td></tr> <tr><td>Red Bed</td><td>48</td><td>50</td></tr> </tbody> </table>			From	To	Topsail	0	4	Sand	4	9	Clay	9	23	Sand	23	39	Clay	39	41	Gravel	41	48	Red Bed	48	50	<table border="1" style="width:100%; border-collapse: collapse;"> <tr> <td>6. Bore hole <input checked="" type="checkbox"/> Well depth: 3-22-75</td> <td>Completion date: 3-22-75</td> </tr> <tr> <td>7. Cable tool <input type="checkbox"/> Rotary <input checked="" type="checkbox"/> Driven <input type="checkbox"/> Dug <input type="checkbox"/> Hollow rod <input type="checkbox"/> Jetted <input type="checkbox"/> Bored <input type="checkbox"/> Reverse rotary <input type="checkbox"/></td> <td></td> </tr> <tr> <td colspan="2">8. Use: <input checked="" type="checkbox"/> Domestic <input type="checkbox"/> Public supply <input type="checkbox"/> Industry <input type="checkbox"/> Irrigation <input type="checkbox"/> Air conditioning <input type="checkbox"/> Stock <input type="checkbox"/> Lawn <input type="checkbox"/> Oil field water <input type="checkbox"/> Other</td> </tr> <tr> <td colspan="2">9. Casing: Material PL Height: Above or below 12 in. Threaded <input type="checkbox"/> Welded <input checked="" type="checkbox"/> Surface 1.5 lbs./ft. RMP <input checked="" type="checkbox"/> PVC <input type="checkbox"/> Weight 1.5 lbs./ft. Dia. 5 in. to 50 ft. depth Wall Thickness: inches or 200 Dia. <input type="checkbox"/> in. to <input type="checkbox"/> ft. depth gage No.</td> </tr> <tr> <td colspan="2">10. Screen: Manufacturer's name Sunflower Plastics Type RMP Dia. 5" Slot/gauze 1/8 Length 20' Set between 30 ft. and 50 ft. ft. and <input type="checkbox"/> ft. Gravel pack? Yes Size range of material 4 X 5</td> </tr> <tr> <td colspan="2">11. Static water level: 32 ft. below land surface Date 3-22-75 mo./day/yr.</td> </tr> <tr> <td colspan="2">12. Pumping level below land surfaces: 98 ft. after 1 hrs. pumping 10 g.p.m. <input type="checkbox"/> ft. after <input type="checkbox"/> hrs. pumping <input type="checkbox"/> g.p.m. Estimated maximum yield 10 g.p.m.</td> </tr> <tr> <td colspan="2">13. Water sample submitted: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No Date</td> </tr> <tr> <td colspan="2">14. Well head completion: <input checked="" type="checkbox"/> Pitless adapter 14 Inches above grade</td> </tr> <tr> <td colspan="2">15. Well grouted? Yes With: <input checked="" type="checkbox"/> Neat cement <input type="checkbox"/> Bentonite <input type="checkbox"/> Concrete Depth: From 4 ft. to 24 ft.</td> </tr> <tr> <td colspan="2">16. Nearest source of possible contamination: 180 ft. Direction SW Type Septic Well disinfected upon completion? <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No</td> </tr> <tr> <td colspan="2">17. Pump: Not installed Manufacturer's name Aer motor Model number SD-50 HP 1/2 Volt 230 Length of drop pipe 38 ft. capacity 10 g.p.m. Type: <input checked="" type="checkbox"/> Submersible <input type="checkbox"/> Turbine <input type="checkbox"/> Jet <input type="checkbox"/> Reciprocating <input type="checkbox"/> Centrifugal <input type="checkbox"/> Other</td> </tr> </table>	6. Bore hole <input checked="" type="checkbox"/> Well depth: 3-22-75	Completion date: 3-22-75	7. Cable tool <input type="checkbox"/> Rotary <input checked="" type="checkbox"/> Driven <input type="checkbox"/> Dug <input type="checkbox"/> Hollow rod <input type="checkbox"/> Jetted <input type="checkbox"/> Bored <input type="checkbox"/> Reverse rotary <input type="checkbox"/>		8. Use: <input checked="" type="checkbox"/> Domestic <input type="checkbox"/> Public supply <input type="checkbox"/> Industry <input type="checkbox"/> Irrigation <input type="checkbox"/> Air conditioning <input type="checkbox"/> Stock <input type="checkbox"/> Lawn <input type="checkbox"/> Oil field water <input type="checkbox"/> Other		9. Casing: Material PL Height: Above or below 12 in. Threaded <input type="checkbox"/> Welded <input checked="" type="checkbox"/> Surface 1.5 lbs./ft. RMP <input checked="" type="checkbox"/> PVC <input type="checkbox"/> Weight 1.5 lbs./ft. Dia. 5 in. to 50 ft. depth Wall Thickness: inches or 200 Dia. <input type="checkbox"/> in. to <input type="checkbox"/> ft. depth gage No.		10. Screen: Manufacturer's name Sunflower Plastics Type RMP Dia. 5" Slot/gauze 1/8 Length 20' Set between 30 ft. and 50 ft. ft. and <input type="checkbox"/> ft. Gravel pack? Yes Size range of material 4 X 5		11. Static water level: 32 ft. below land surface Date 3-22-75 mo./day/yr.		12. Pumping level below land surfaces: 98 ft. after 1 hrs. pumping 10 g.p.m. <input type="checkbox"/> ft. after <input type="checkbox"/> hrs. pumping <input type="checkbox"/> g.p.m. Estimated maximum yield 10 g.p.m.		13. Water sample submitted: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No Date		14. Well head completion: <input checked="" type="checkbox"/> Pitless adapter 14 Inches above grade		15. Well grouted? Yes With: <input checked="" type="checkbox"/> Neat cement <input type="checkbox"/> Bentonite <input type="checkbox"/> Concrete Depth: From 4 ft. to 24 ft.		16. Nearest source of possible contamination: 180 ft. Direction SW Type Septic Well disinfected upon completion? <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No		17. Pump: Not installed Manufacturer's name Aer motor Model number SD-50 HP 1/2 Volt 230 Length of drop pipe 38 ft. capacity 10 g.p.m. Type: <input checked="" type="checkbox"/> Submersible <input type="checkbox"/> Turbine <input type="checkbox"/> Jet <input type="checkbox"/> Reciprocating <input type="checkbox"/> Centrifugal <input type="checkbox"/> Other								
			From	To																																																					
	Topsail		0	4																																																					
	Sand		4	9																																																					
	Clay		9	23																																																					
	Sand		23	39																																																					
	Clay		39	41																																																					
	Gravel	41	48																																																						
Red Bed	48	50																																																							
6. Bore hole <input checked="" type="checkbox"/> Well depth: 3-22-75	Completion date: 3-22-75																																																								
7. Cable tool <input type="checkbox"/> Rotary <input checked="" type="checkbox"/> Driven <input type="checkbox"/> Dug <input type="checkbox"/> Hollow rod <input type="checkbox"/> Jetted <input type="checkbox"/> Bored <input type="checkbox"/> Reverse rotary <input type="checkbox"/>																																																									
8. Use: <input checked="" type="checkbox"/> Domestic <input type="checkbox"/> Public supply <input type="checkbox"/> Industry <input type="checkbox"/> Irrigation <input type="checkbox"/> Air conditioning <input type="checkbox"/> Stock <input type="checkbox"/> Lawn <input type="checkbox"/> Oil field water <input type="checkbox"/> Other																																																									
9. Casing: Material PL Height: Above or below 12 in. Threaded <input type="checkbox"/> Welded <input checked="" type="checkbox"/> Surface 1.5 lbs./ft. RMP <input checked="" type="checkbox"/> PVC <input type="checkbox"/> Weight 1.5 lbs./ft. Dia. 5 in. to 50 ft. depth Wall Thickness: inches or 200 Dia. <input type="checkbox"/> in. to <input type="checkbox"/> ft. depth gage No.																																																									
10. Screen: Manufacturer's name Sunflower Plastics Type RMP Dia. 5" Slot/gauze 1/8 Length 20' Set between 30 ft. and 50 ft. ft. and <input type="checkbox"/> ft. Gravel pack? Yes Size range of material 4 X 5																																																									
11. Static water level: 32 ft. below land surface Date 3-22-75 mo./day/yr.																																																									
12. Pumping level below land surfaces: 98 ft. after 1 hrs. pumping 10 g.p.m. <input type="checkbox"/> ft. after <input type="checkbox"/> hrs. pumping <input type="checkbox"/> g.p.m. Estimated maximum yield 10 g.p.m.																																																									
13. Water sample submitted: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No Date																																																									
14. Well head completion: <input checked="" type="checkbox"/> Pitless adapter 14 Inches above grade																																																									
15. Well grouted? Yes With: <input checked="" type="checkbox"/> Neat cement <input type="checkbox"/> Bentonite <input type="checkbox"/> Concrete Depth: From 4 ft. to 24 ft.																																																									
16. Nearest source of possible contamination: 180 ft. Direction SW Type Septic Well disinfected upon completion? <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No																																																									
17. Pump: Not installed Manufacturer's name Aer motor Model number SD-50 HP 1/2 Volt 230 Length of drop pipe 38 ft. capacity 10 g.p.m. Type: <input checked="" type="checkbox"/> Submersible <input type="checkbox"/> Turbine <input type="checkbox"/> Jet <input type="checkbox"/> Reciprocating <input type="checkbox"/> Centrifugal <input type="checkbox"/> Other																																																									
(Use a second sheet if needed)																																																									
18. Elevation: Topography: <input type="checkbox"/> Hill <input type="checkbox"/> Slope <input checked="" type="checkbox"/> Upland <input type="checkbox"/> Valley	19. Remarks:																																																								
20. Water well contractor's certification: This well was drilled under my jurisdiction and this report is true to the best of my knowledge and belief. Carl Hayes Water Well Serv. 224 Business Office License No. 02386 Address: Maple Shoals, Mo. Signed: Carl Hayes Date: 3-22-75 Authorized representative																																																									

28 - 70 - 14 NW 1/4 SW
 T R Sec 1/4 1/4 1/4
