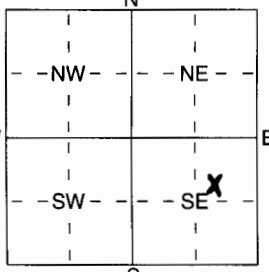


1 LOCATION OF WATER WELL: Fraction SW 1/4 NE 1/4 SE 1/4 Section Number 35 Township Number T 3 S Range Number R 18 EW  
 County: Phillips

Distance and direction from nearest town or city street address of well if located within city? 166 4th St Phillipsburg Ks, 67661

2 WATER WELL OWNER: DARRELL REDINGER  
 RR#, St. Address, Box # : 184 4th St Board of Agriculture, Division of Water Resources  
 City, State, ZIP Code : Phillipsburg Ks 67661 55 Application Number:

3 LOCATE WELL'S LOCATION WITH AN "X" IN SECTION BOX: 55' DEPTH OF COMPLETED WELL ..... ft. ELEVATION: ..... ft.  
  
 Depth(s) Groundwater Encountered 43 ft. 2 ..... ft. 3 ..... ft.  
 WELL'S STATIC WATER LEVEL 42 ft. below land surface measured on mo/day/yr 10-30-05  
 Pump test data: Well water was 14 ft. after 1 hours pumping 10 gpm  
 Est. Yield 12 gpm: Well water was ..... ft. after ..... hours pumping ..... gpm  
 WELL WATER TO BE USED AS: 5 Public water supply 8 Air conditioning 11 Injection well  
 1 Domestic 3 Feedlot 6 Oil field water supply 9 Dewatering 12 Other (Specify below)  
 2 Irrigation 4 Industrial 7 Domestic (lawn & garden) 10 Monitoring well  
 Was a chemical/bacteriological sample submitted to Department? Yes ..... No ; If yes, mo/day/yr sample was submitted  
 Water Well Disinfected?  Yes No

5 TYPE OF BLANK CASING USED: 5 Wrought iron 8 Concrete tile CASING JOINTS: Glued  Clamped .....  
 1 Steel 3 RMP (SR) 6 Asbestos-Cement 9 Other (specify below) Welded .....  
2 PVC 4 ABS 7 Fiberglass ..... Threaded .....  
 Blank casing diameter 4 in. to 35 ft., Dia ..... in. to ..... ft., Dia ..... in. to ..... ft.  
 Casing height above land surface 24 in., weight 160 lbs./ft. Wall thickness or gauge No. ....  
 TYPE OF SCREEN OR PERFORATION MATERIAL: PVC 10 Asbestos-Cement  
 1 Steel 3 Stainless Steel 5 Fiberglass 8 RMP (SR) 11 Other (Specify) .....  
 2 Brass 4 Galvanized Steel 6 Concrete tile 9 ABS 12 None used (open hole)  
 SCREEN OR PERFORATION OPENINGS ARE: 5 Gauzed wrapped 8 Saw cut 11 None (open hole)  
 1 Continuous slot 3 Mill slot 6 Wire wrapped 9 Drilled holes  
 2 Louvered shutter 4 Key punched 7 Torch cut 10 Other (specify) ..... ft.  
 SCREEN-PERFORATED INTERVALS: From 55 ft. to 35 ft., From ..... ft. to ..... ft.  
 GRAVEL PACK INTERVALS: From ..... ft. to ..... ft., From ..... ft. to ..... ft.  
 From ..... ft. to ..... ft., From ..... ft. to ..... ft.

6 GROUT MATERIAL: 1 Neat cement 2 Cement grout 3 Bentonite 4 Other .....  
 Grout Intervals: From 0-20 ft. to 0 ft., From ..... ft. to ..... ft., From ..... ft. to ..... ft.  
 What is the nearest source of possible contamination: 10 Livestock pens 14 Abandoned water well  
 1 Septic tank 4 Lateral lines 7 Pit privy 11 Fuel storage 15 Oil well/Gas well  
 2 Sewer lines 5 Cess pool 8 Sewage lagoon 12 Fertilizer storage 16 Other (specify below)  
 3 Watertight sewer lines 6 Seepage pit 9 Feedyard 13 Insecticide storage NONE  
 Direction from well? How many feet?

FROM	TO	LITHOLOGIC LOG	FROM	TO	PLUGGING INTERVALS
<u>0</u>	<u>15</u>	<u>TOPSOIL - brown clay</u>			
<u>15</u>	<u>43</u>	<u>yellow clay, loose white rock</u>			
<u>43</u>	<u>53</u>	<u>white rock, sand, gravel</u>			
<u>53</u>	<u>55</u>	<u>shale</u>			

7 CONTRACTOR'S OR LANDOWNER'S CERTIFICATION: This water well was (1) constructed, (2) reconstructed, or (3) plugged under my jurisdiction and was completed on (mo/day/year) 10-29-03 and this record is true to the best of my knowledge and belief. Kansas Water Well Contractor's License No. 738 This Water Well Record was completed on (mo/day/yr) 10-30-05 under the business name of Redinger Well Service by (signature) Darrell Redinger
