


REVISION:	DESCRIPTION:
-----------	--------------

WELL No: 2

REV.

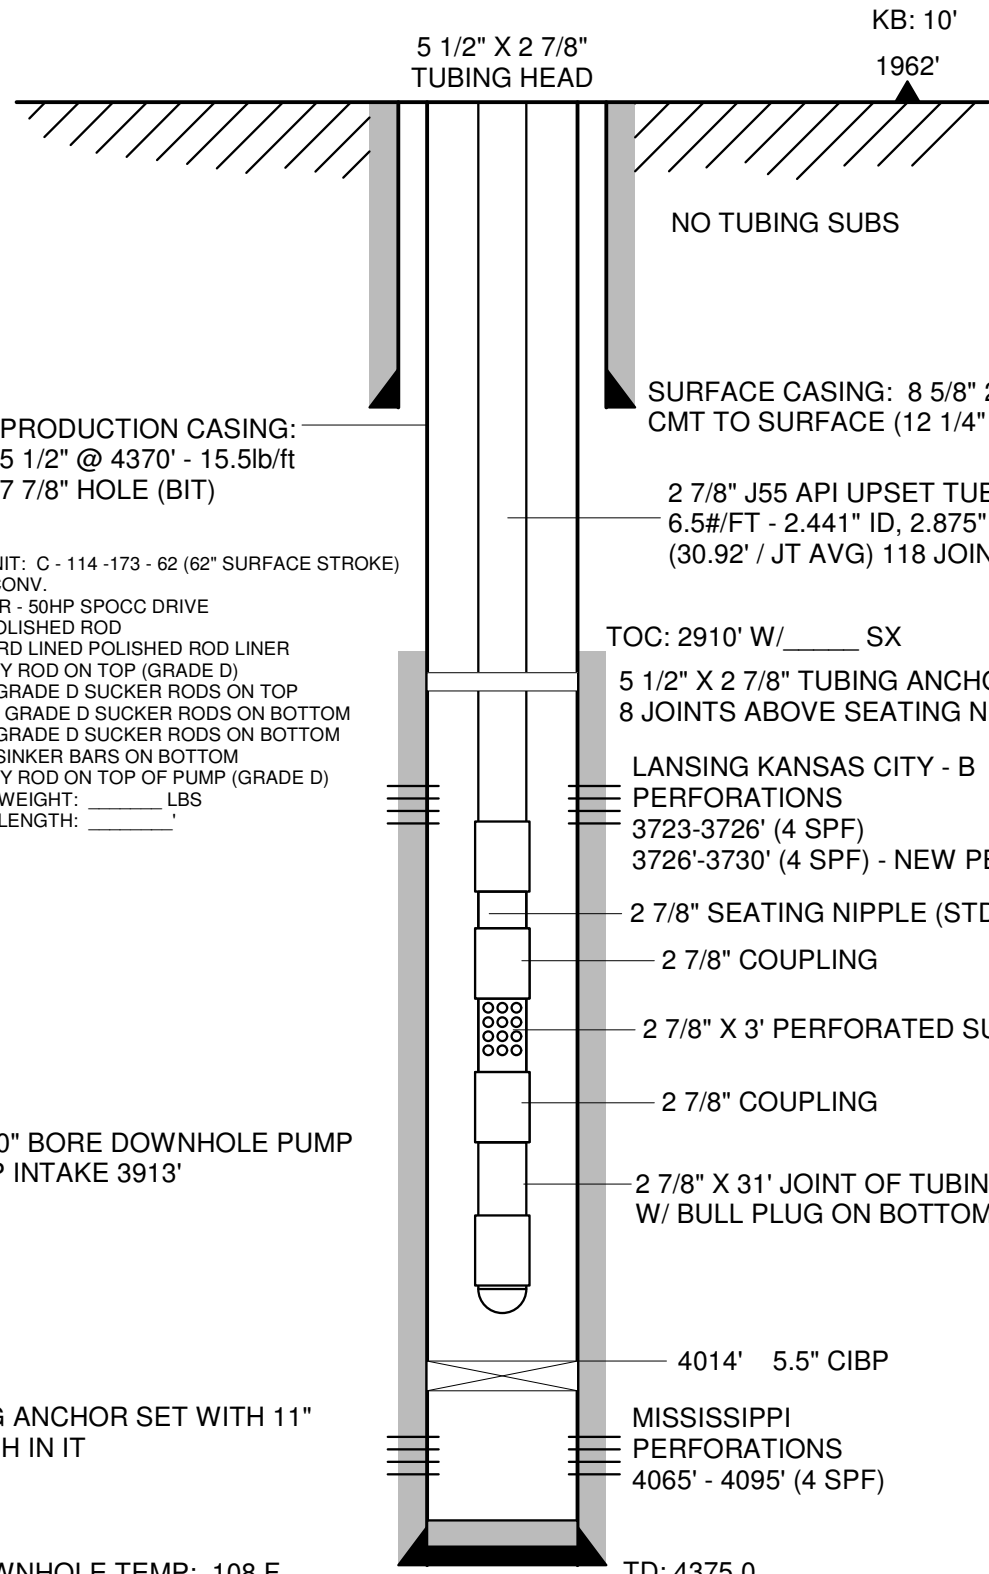

PUMPING UNIT: C - 114 -173 - 62 (62" SURFACE STROKE)
 AMERICAN CONV.
 30 HP MOTOR - 50HP SPOCC DRIVE
 1.25" X 18' POLISHED ROD
 1.50" X 8' HARD LINED POLISHED ROD LINER
 7/8" X 6' PONY ROD ON TOP (GRADE D)
 500' OF 7/8" GRADE D SUCKER RODS ON TOP
 3025' OF 3/4" GRADE D SUCKER RODS ON BOTTOM
 225' OF 7/8" GRADE D SUCKER RODS ON BOTTOM
 50' OF 1.50" SINKER BARS ON BOTTOM
 7/8" X 2' PONY ROD ON TOP OF PUMP (GRADE D)
 TOTAL ROD WEIGHT: _____ LBS
 TOTAL ROD LENGTH: _____'

SURFACE CASING: 8 5/8" 23#/FT @ 861' ____ SX
 CMT TO SURFACE (12 1/4" HOLE)

2 7/8" J55 API UPSET TUBING
 6.5#/FT - 2.441" ID, 2.875" OD
 (30.92' / JT AVG) 118 JOINTS

TOC: 2910' W/ ____ SX
 5 1/2" X 2 7/8" TUBING ANCHOR (11" STRETCH)
 8 JOINTS ABOVE SEATING NIPPLE

LANSING KANSAS CITY - B
 PERFORATIONS
 3723-3726' (4 SPF)
 3726'-3730' (4 SPF) - NEW PERFS.

2 7/8" SEATING NIPPLE (STD)
 2 7/8" COUPLING

2 7/8" X 3' PERFORATED SUB

2 7/8" COUPLING

2 7/8" X 31' JOINT OF TUBING
 W/ BULL PLUG ON BOTTOM

4014' 5.5" CIBP

MISSISSIPPI
 PERFORATIONS
 4065' - 4095' (4 SPF)

2.0000" BORE DOWNHOLE PUMP
 PUMP INTAKE 3913'

*TUBING ANCHOR SET WITH 11"
 STRETCH IN IT

DOWNHOLE TEMP: 108 F

TD: 4375.0
 PBDT: 4344.0

5,000 PSIG CIBP WAS SET AT 3794'
 NOW DROVE DOWN TO 4160'

DRAWN: BK 09/01/11	APPROVED:	LEASE: FOX #2	WELL No: 2	REV.
--------------------	-----------	---------------	------------	------

LassoEnergy LLC

TOLERANCES (Unless Otherwise Specified)	LOCATION: 13-25S-14W - STAFFORD CO.
Fractional..... ± 1/32"	SCALE: N/A
2 Place Decimal..... ± .030	
3 Place Decimal..... ± .005	
4 Place Decimal..... ± .001	
