


Cathodic Protection Installation Request
Coffeyville to Caney 10"
AC Mitigation Deep Well #6

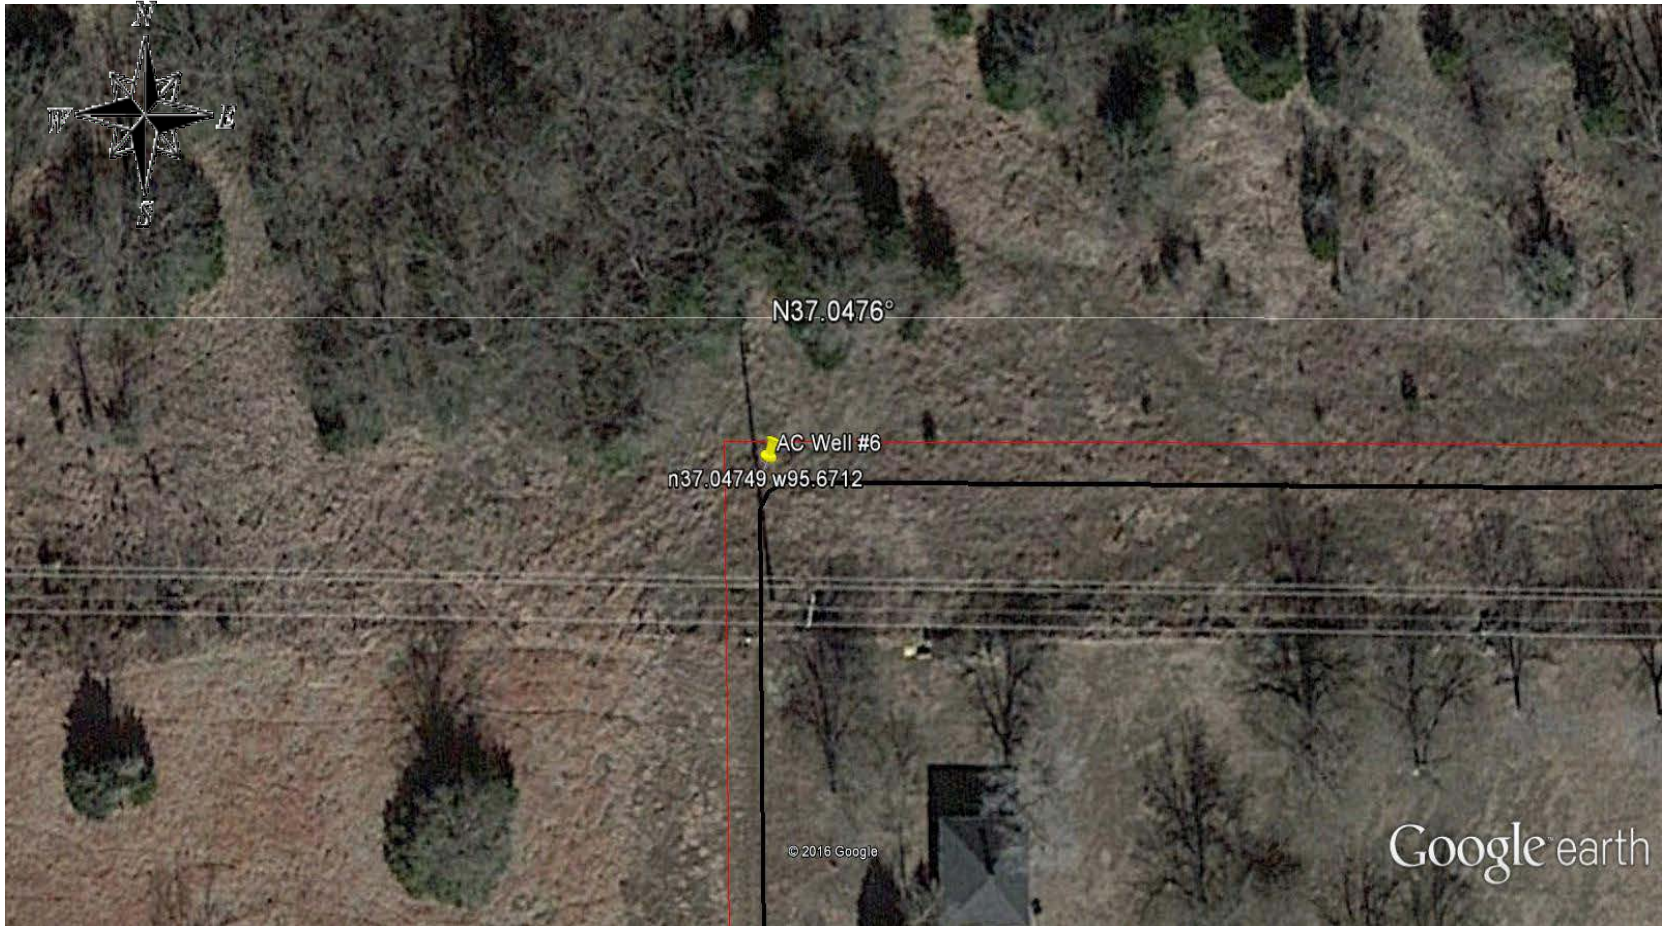

Region: <u>CENTRAL</u>	Area: <u>COFFEYVILLE</u>	Pipeline: <u>Coffeyville to Caney 10"</u>	
Alignment Sheet: _____	Tract: <u>6561-MG-39</u>	Mile Post: <u>3.81 miles</u>	Survey Station: <u>201+60</u>
State : <u>Kansas</u>	County: <u>Montgomery</u>	Longitude: <u>-95.671236°</u>	Latitude: <u>37.047486°</u>
Section: <u>33</u>	1/4 Sec.of 1/4: <u>SW/SE/NW/SE</u>	Township: <u>T34S</u>	Range: <u>R16E</u>
Location: _____			
Property Owner <u>Donald and Joan White 918 254-7637</u>			
Contact & Information: _____			
Power Company Contact and Information: <u>N/A</u>			
Groundbed Type: <u>AC MITIGATION</u>	Current Required: <u>NA</u>	Soil Resistance: <u>13.82094 ohm meters</u>	
Anode Type: <u>ANOTEC HSCI 2660</u>	Number of Anodes: <u>25</u>	Type of Backfill: <u>LORESCO SC3</u>	
Amount of Backfill: <u>9,300LBS</u>	Type of Cable: <u>2/0 HMWPE</u>	Amount of Cable: <u>175'</u>	
New Rectifier Required: (yes/no): <u>N/A</u>	Rectifier Type: <u>N/A</u>	Anode Depth: <u>255'</u>	
Anode Spacing: <u>10'</u>	Anode Hole Specs: <u>420 X 10</u>	Design Life: <u>20 YEARS</u>	
Required Installation Date: _____		Construction Company: <u>Pipeline Controls and Services</u>	
Driving Directions	From the intersection of West 1st and N. Inglewood Ave. travel North 1315ft North go East 995 West to GPS coordinates. From North line 65ft South. From East survey line 340ft West.		
Details:	GROUND BED TO BE COMPLETED BELOW GRADE AND ANODE WIRES WILL BE TERMINATED AT PCR BOX		
Requested By: <u>TVANGOOR</u>		Date: <u>01/04/16</u>	
