



Company: Trans Pacific Oil Corporation
Lease: Fritzler "A" Unit #1-6

SEC: 6 TWN: 18S RNG: 24W
 County: NESS
 State: Kansas
 Drilling Contractor: Duke Drilling Company, Inc - Rig 2
 Elevation: 2384 GL
 Field Name: Dex North
 Pool: WILDCAT
 Job Number: 350
 API #: 3526068

Operation:
 Tripping out of hole with test tool

DATE
 June
07
 2019

DST #2 **Formation: Mississippian** **Test Interval: 4316 - 4375'** **Total Depth: 4375'**
 Time On: 15:20 06/07 Time Off: 23:50 06/08
 Time On Bottom: 17:37 06/07 Time Off Bottom: 21:52 06/07

Electronic Volume Estimate:
 50'


1st Open
 Minutes: 30
 Current Reading: 2.4" at 30 min
 Max Reading: 2.5"

1st Close
 Minutes: 75
 Current Reading: 0" at 75 min
 Max Reading: 0"

2nd Open
 Minutes: 60
 Current Reading: 1.4" at 60 min
 Max Reading: 1.8"

2nd Close
 Minutes: 90
 Current Reading: 0" at 90 min
 Max Reading: 0"

Inside Recorder

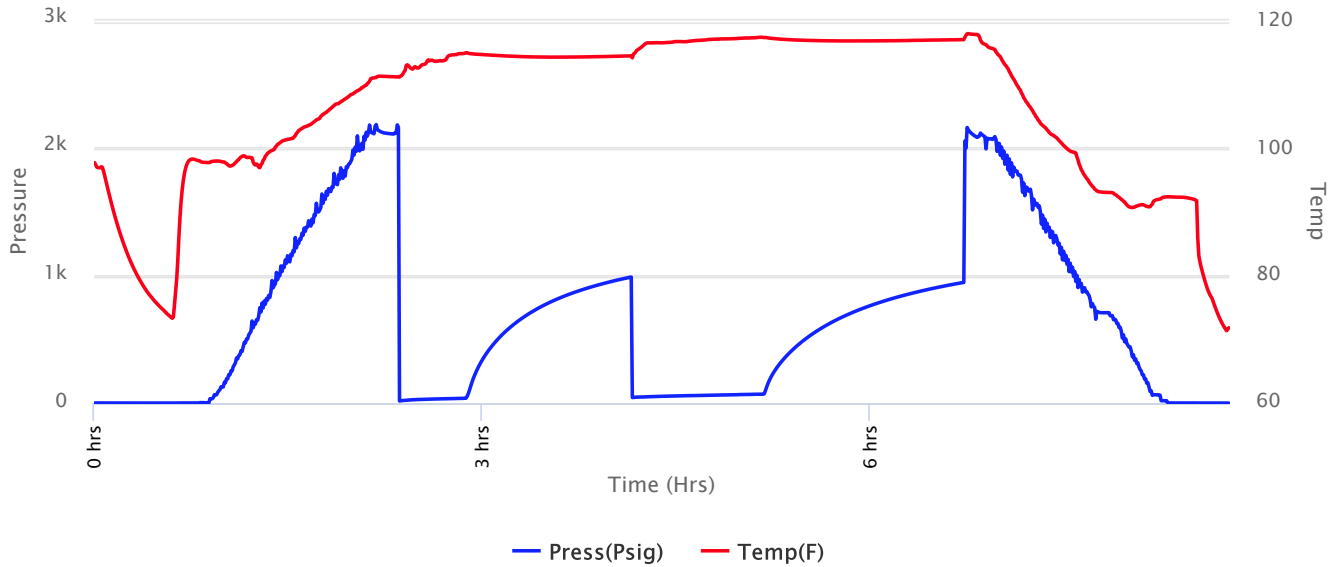



Company: Trans Pacific Oil Corporation
Lease: Fritzler "A" Unit #1-6

SEC: 6 TWN: 18S RNG: 24W
 County: NESS
 State: Kansas
 Drilling Contractor: Duke Drilling Company, Inc - Rig 2
 Elevation: 2384 GL
 Field Name: Dex North
 Pool: WILDCAT
 Job Number: 350
 API #: 3526068

Operation:
 Tripping out of hole with test tool

DATE
 June
07
 2019

DST #2 **Formation: Mississippian** **Test Interval: 4316 - 4375'** **Total Depth: 4375'**
 Time On: 15:20 06/07 Time Off: 23:50 06/08
 Time On Bottom: 17:37 06/07 Time Off Bottom: 21:52 06/07


Recovered		Description of Fluid	Gas %	Oil %	Water %	Mud %
Foot	BBLs					
30	0.387	O	0	100	0	0
40	0.516	HMCO	0	50	0	50
65	0.8385	SLOCM	0	10	0	90

Total Recovered: 135 ft
 Total Barrels Recovered: 1.7415

Reversed Out
 NO

Initial Hydrostatic Pressure	2109	PSI
Initial Flow	17 to 39	PSI
Initial Closed in Pressure	985	PSI
Final Flow Pressure	44 to 70	PSI
Final Closed in Pressure	943	PSI
Final Hydrostatic Pressure	2105	PSI
Temperature	118	°F
Pressure Change Initial Close / Final Close	4.2	%

Recovery at a glance

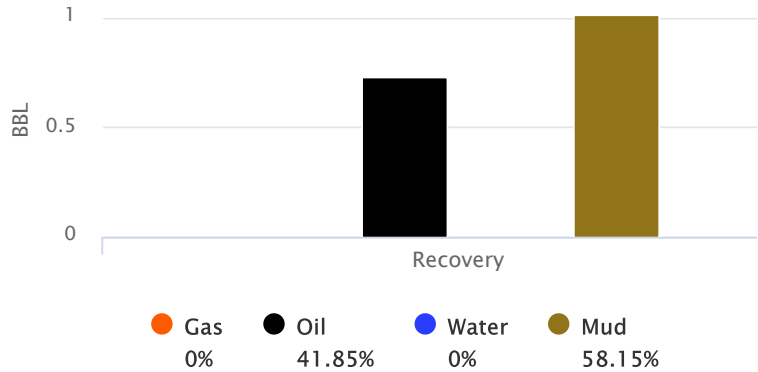

GIP cubic foot volume: 0



Company: Trans Pacific Oil Corporation

Lease: Fritzler "A" Unit #1-6

SEC: 6 TWN: 18S RNG: 24W
County: NESS
State: Kansas
Drilling Contractor: Duke Drilling Company, Inc - Rig 2
Elevation: 2384 GL
Field Name: Dex North
Pool: WILDCAT
Job Number: 350
API #: 3526068

Operation:
Tripping out of hole with test tool

DATE
June
07
2019

DST #2 **Formation: Mississippian** **Test Interval: 4316 - 4375'** **Total Depth: 4375'**
Time On: 15:20 06/07 Time Off: 23:50 06/08
Time On Bottom: 17:37 06/07 Time Off Bottom: 21:52 06/07

BUCKET MEASUREMENT:

1st Open: 1/4" blow building to 2 1/2"
1st Close: No BB
2nd Open: Surface blow building to 1 1/4"
2nd Close: No BB

REMARKS:

Tool Sample: 0% Gas 18% Oil 4% Water 78% Mud
Gravity: 39 @ 60 °F



Company: Trans Pacific Oil Corporation
Lease: Fritzler "A" Unit #1-6

SEC: 6 TWN: 18S RNG: 24W
 County: NESS
 State: Kansas
 Drilling Contractor: Duke Drilling Company, Inc - Rig 2
 Elevation: 2384 GL
 Field Name: Dex North
 Pool: WILDCAT
 Job Number: 350
 API #: 3526068

Operation:
 Tripping out of hole with test tool

DATE
 June
07
 2019

DST #2 **Formation: Mississippian** **Test Interval: 4316 - 4375'** **Total Depth: 4375'**
 Time On: 15:20 06/07 Time Off: 23:50 06/08
 Time On Bottom: 17:37 06/07 Time Off Bottom: 21:52 06/07

Down Hole Makeup

Heads Up: 34.01 FT	Packer 1: 4310.63 FT
Drill Pipe: 4321.9 FT <i>ID-3.640</i>	Packer 2: 4315.63 FT
Weight Pipe: 0 FT <i>ID-2 7/8</i>	Top Recorder: 4300.05 FT
Collars: 0 FT <i>ID-2 1/4</i>	Bottom Recorder: 4354 FT
Test Tool: 28.74 FT <i>ID-3 1/2-FH</i> <i>Safety Joint</i>	Well Bore Size: 7 7/8
Total Anchor: 59.37	Surface Choke: 1"
<u>Anchor Makeup</u>	Bottom Choke: 5/8"
Packer Sub: 1 FT	
Perforations: (top): 3 FT <i>4 1/2-FH</i>	
Change Over: 1 FT	
Drill Pipe: (in anchor): 31.37 FT <i>ID-3.640</i>	
Change Over: 1 FT	
Perforations: (below): 22 FT <i>4 1/2-FH</i>	



Company: Trans Pacific Oil Corporation

Lease: Fritzler "A" Unit #1-6

SEC: 6 TWN: 18S RNG: 24W
County: NESS
State: Kansas
Drilling Contractor: Duke Drilling Company, Inc - Rig 2
Elevation: 2384 GL
Field Name: Dex North
Pool: WILDCAT
Job Number: 350
API #: 3526068

Operation:
Tripping out of hole with test tool

DATE
June
07
2019

DST #2 **Formation: Mississippian** **Test Interval: 4316 - 4375'** **Total Depth: 4375'**
Time On: 15:20 06/07 Time Off: 23:50 06/08
Time On Bottom: 17:37 06/07 Time Off Bottom: 21:52 06/07

Mud Properties

Mud Type: Chemical **Weight:** 9.35 **Viscosity:** 58 **Filtrate:** 8.0 **Chlorides:** 4,600 ppm



Company: Trans Pacific Oil Corporation

Lease: Fritzler "A" Unit #1-6

SEC: 6 TWN: 18S RNG: 24W
County: NESS
State: Kansas
Drilling Contractor: Duke Drilling Company, Inc - Rig 2
Elevation: 2384 GL
Field Name: Dex North
Pool: WILDCAT
Job Number: 350
API #: 3526068

Operation:
Tripping out of hole with test tool

DATE
June
07
2019

DST #2 **Formation: Mississippian** **Test Interval: 4316 - 4375'** **Total Depth: 4375'**
Time On: 15:20 06/07 Time Off: 23:50 06/08
Time On Bottom: 17:37 06/07 Time Off Bottom: 21:52 06/07

Gas Volume Report

1st Open			
Time	Orifice	PSI	MCF/D

2nd Open			
Time	Orifice	PSI	MCF/D
