

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company CITIES SERVICE OIL COMPANY

Lease and Well No. ZVOLANEK # C-1

County ELLSWORTH

State KANSAS

Date APRIL 21, 1963

Formation Test No.	<u>1</u>	Total Depth	<u>2762</u>
Interval Tested	<u>2737</u>	To	<u>2762</u>
		Anchor Length	<u>25'</u>
Size Hole	<u>7 7/8</u>	Size Drill Pipe	<u>4 1/2 ACME</u>
		Size Packer	<u>6 3/4</u>
Mud Weight	<u>10</u>	Viscosity	<u>38</u>
		Bottom Hole Temp.	<u>98</u> ° F
Chokes: Top	<u>1/2</u>	Bottom	<u>1/2</u>
		Ticket No.	<u>6590</u>

RECOVERY

INITIAL OPENING 2 MINUTES

GOOD BLOW THROUGHOUT TEST

945 FEET SALT WATER

Lease and Well No. ZVOLANEK # C-1 33 15 10 SE NW NW
Formation Test No. 1

COMPANY CITIES SERVICE OIL COMPANY DATE APRIL 21, 1963
 LEASE ZVOLANEK WELL NO. C-1 TEST NO. 1 TICKET NO. 6590

	TIME	PSI
INITIAL HYDRO MUD PRESSURE	----	1535
INITIAL CLOSED IN PRESSURE	30 MINUTES	1069
INITIAL FLOW	----	90
FINAL FLOW	62 MINUTES	442
FINAL CLOSED IN PRESSURE	30 MINUTES	1065
FINAL HYDRO MUD PRESSURE	----	1490

TOTAL DEPTH 2762
 PACKER DEPTH 2737
 BT. NO. 1049 DEPTH 2757

	1ST FLOW PRESSURE		INITIAL CIP		2ND FLOW PRESSURE		FINAL CIP	
	TIME DEFL. ".000"	PSI TEMP. CORR.	TIME DEFL. ".000"	PSI TEMP. CORR.	TIME DEFL. ".000"	PSI TEMP. CORR.	TIME DEFL. ".000"	PSI TEMP. CORR.
P0	.000	55	.000	55	.000	90	.000	442
P1			.042	1065	.083	160	.042	1055
P2			.083	1065	.167	235	.083	1055
P3			.125	1065	.250	295	.125	1060
P4			.167	1065	.333	345	.167	1065
P5			.209	1069	.416	390	.209	1065
P6			.250	1069	.500	442	.250	1065
P7								
P8								
P9								
P10								
	2	MINUTE INTERVAL	5	MINUTE INTERVAL	10	MINUTE INTERVAL	5	MINUTE INTERVAL


REMARKS

INITIAL OPENING 2 MINUTES

SPECIAL PRESSURE DATA

33-155-10 W

Pressure: Each Square _____ psi

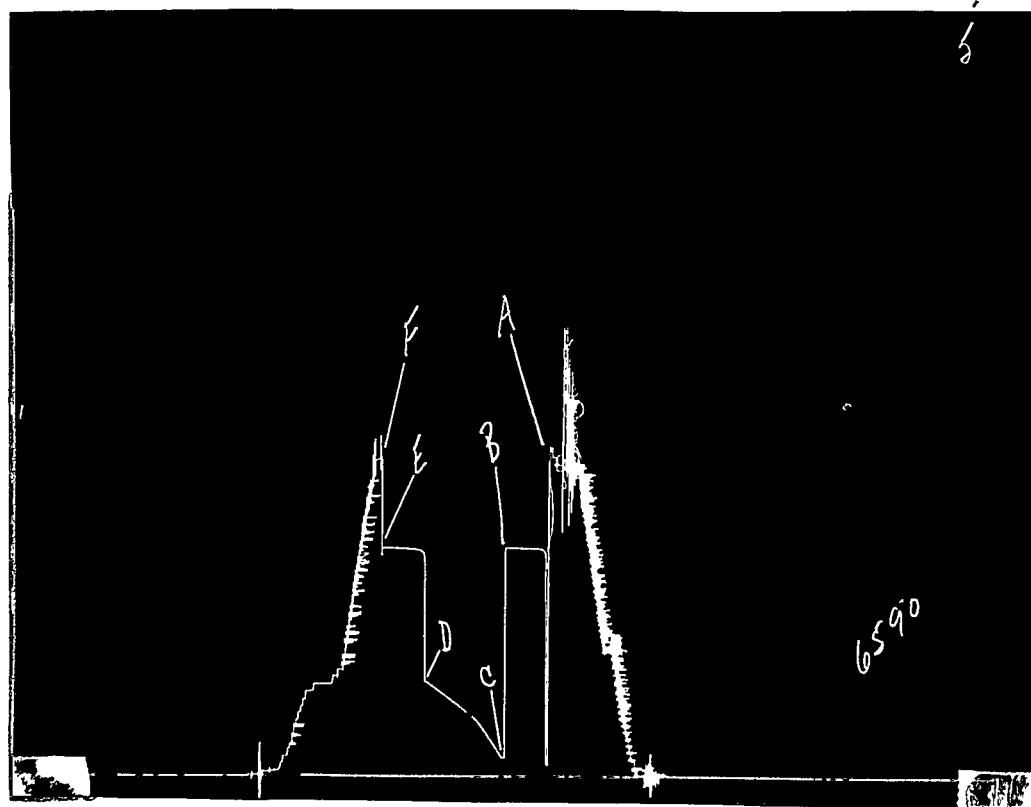

Tool Open 1 hr. _____ mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>1480</u>	<u>1535</u>
(B) Initial Shut-in Pressure	<u>1055</u>	<u>1069</u>
(C) Initial Flow Pressure	<u>85</u>	<u>90</u>
(D) Final Flow Pressure	<u>450</u>	<u>442</u>
(E) Final Shut-in Pressure	<u>990</u>	<u>1065</u>
(F) Final Hydrostatic Pressure	<u>1465</u>	<u>1490</u>

6590

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company CITIES SERVICE OIL COMPANY

Lease and Well No. ZVOLANEK # C-1

County ELLSWORTH

State KANSAS

Date APRIL 22, 1963

Formation Test No. 2 Total Depth 2945
Interval Tested 2932 To 2945 Anchor Length 13'
Size Hole 7 7/8 Size Drill Pipe 4 1/2 ACME Size Packer 6 3/4
Mud Weight 9.7 Viscosity 40 Bottom Hole Temp. 123 ° F
Chokes: Top 1/2 Bottom 1/2 Ticket No. 6591

RECOVERY

INITIAL OPENING 2 MINUTES

STRONG BLOW DECREASING TO
GOOD BY END OF TEST

1360 FEET GAS IN DRILL PIPE
63 FEET OIL AND GAS CUT MUD

Lease and Well No.

ZVOLANEK # C-1

33 15 10

SE NW NW

Formation Test No.

2

33

COMPANY CITIES SERVICE OIL COMPANY

DATE APRIL 22, 1963

LEASE ZVOLANEK WELL NO. C-1 TEST NO. 2 TICKET NO. 6591

	TIME	PSI
INITIAL HYDRO MUD PRESSURE	-----	1617
INITIAL CLOSED IN PRESSURE	30 MINUTES	570
INITIAL FLOW	-----	40
FINAL FLOW	62 MINUTES	40
FINAL CLOSED IN PRESSURE	30 MINUTES	305
FINAL HYDRO MUD PRESSURE	-----	1617

TOTAL DEPTH 2945

PACKER DEPTH 2932

BT. NO. 1049 DEPTH 2940


	1ST FLOW PRESSURE		INITIAL CIP		2ND FLOW PRESSURE		FINAL CIP	
	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.
P0	.000	40	.000	40	.000	40	.000	40
P1			.042	40	.083	40	.042	55
P2			.083	55	.167	40	.083	90
P3			.125	90	.250	40	.125	160
P4			.167	225	.333	40	.167	242
P5			.209	410	.416	40	.209	285
P6			.250	570	.500	40	.250	305
P7								
P8								
P9								
P10								
	2 MINUTE INTERVAL		5 MINUTE INTERVAL		10 MINUTE INTERVAL		5 MINUTE INTERVAL	

REMARKS

INITIAL OPENING 2 MINUTES

SPECIAL PRESSURE DATA

155-10W

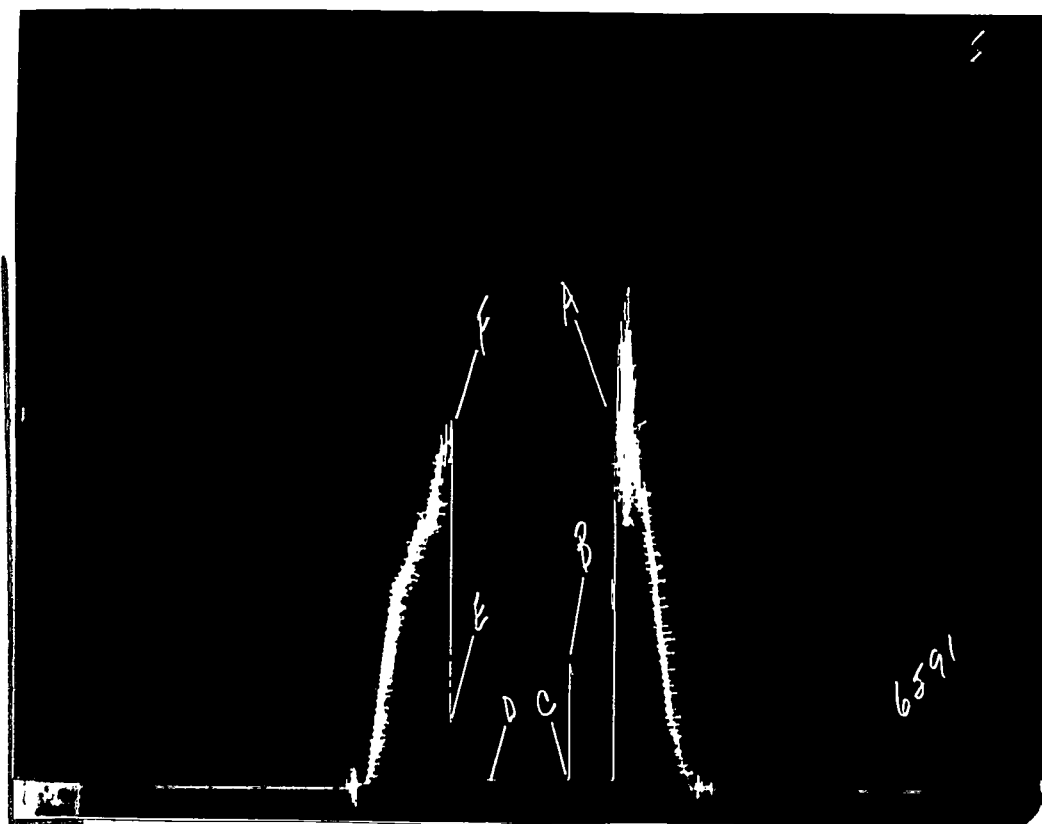

Tool Open 1 hr. _____ mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>1585</u>	<u>1617</u>
(B) Initial Shut-in Pressure	<u>575</u>	<u>570</u>
(C) Initial Flow Pressure	<u>45</u>	<u>40</u>
(D) Final Flow Pressure	<u>45</u>	<u>40</u>
(E) Final Shut-in Pressure	<u>315</u>	<u>305</u>
(F) Final Hydrostatic Pressure	<u>1580</u>	<u>1617</u>

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company CITIES SERVICE OIL COMPANY

Lease and Well No. ZVOLANEK # C-1

County ELLSWORTH State KANSAS

Date APRIL 23, 1963

Formation Test No. 3 Total Depth 2986
Interval Tested 2950 To 2986 Anchor Length 36'
Size Hole 7 7/8 Size Drill Pipe 4 1/2 ACME Size Packer 6 3/4
Mud Weight 9.7 Viscosity 46 Bottom Hole Temp 99 ° F
Chokes: Top 1/2 Bottom 1/2 Ticket No. 6592

RECOVERY

INITIAL OPENING 2 MINUTES

WEAK BLOW FOR 2 MINUTES
FLUSHED TOOL AFTER 30 MINUTES
NO BLOW

10 FEET DRILLING MUD

Lease and Well No. ZVOLANEK # C-1 33 15 10 SE NW NW

Formation Test No. 3

COMPANY CITIES SERVICE OIL COMPANYDATE APRIL 23, 1963LEASE ZVOLANEKWELL NO. C-1TEST NO. 3TICKET NO. 6592

	TIME	PSI
INITIAL HYDRO MUD PRESSURE	----	1610
INITIAL CLOSED IN PRESSURE	30 MINUTES	615
INITIAL FLOW	----	47
FINAL FLOW	62 MINUTES	47
FINAL CLOSED IN PRESSURE	30 MINUTES	57
FINAL HYDRO MUD PRESSURE	----	1610

TOTAL DEPTH 2986PACKER DEPTH 2950BT. NO. 1049 DEPTH 2981

	1ST FLOW PRESSURE		INITIAL CIP		2ND FLOW PRESSURE		FINAL CIP	
	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.
P0	.000	40	.000	40	.000	47	.000	47
P1			.042	125	.083	47	.042	47
P2			.083	225	.167	47	.083	47
P3			.125	360	.250	47	.125	47
P4			.167	470	.333	47	.167	55
P5			.209	545	.416	47	.209	55
P6			.250	615	.500	47	.250	57
P7								
P8								
P9								
P10								
	2	MINUTE INTERVAL	5	MINUTE INTERVAL	10	MINUTE INTERVAL	5	MINUTE INTERVAL


REMARKS _____

INITIAL OPENING 2 MINUTES

SPECIAL PRESSURE DATA

33-155-10W

Pressure: Each Square _____ psi

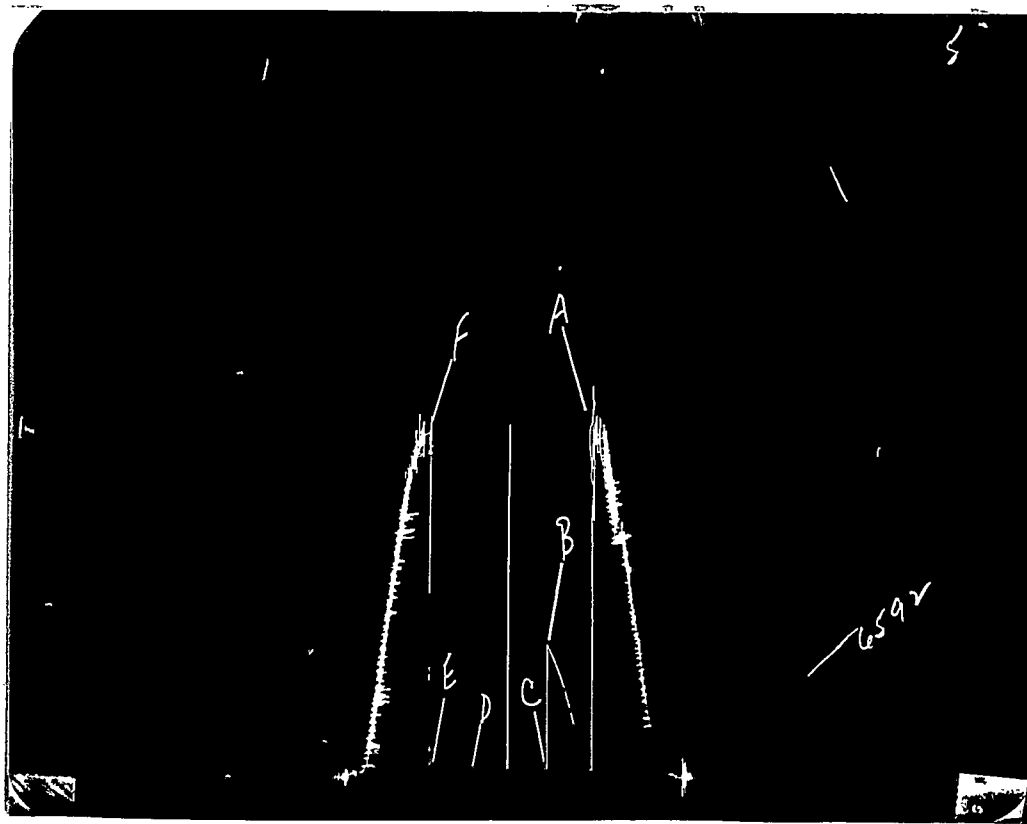

Tool Open — 1 hr. _____ mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>1610</u>	<u>1610</u>
(B) Initial Shut-in Pressure	<u>695</u>	<u>615</u>
(C) Initial Flow Pressure	<u>35</u>	<u>47</u>
(D) Final Flow Pressure	<u>35</u>	<u>47</u>
(E) Final Shut-in Pressure	<u>60</u>	<u>57</u>
(F) Final Hydrostatic Pressure	<u>1590</u>	<u>1610</u>

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company CITIES SERVICE OIL COMPANY

Lease and Well No. ZVOLANEK # C-1

County ELLSWORTH

State KANSAS

Date APRIL 23, 1963

Formation Test No. 4 Total Depth 3007
Interval Tested 2996 To 3007 Anchor Length 11'
Size Hole 7 7/8 Size Drill Pipe 4 1/2 ACME Size Packer 6 3/4
Mud Weight 9.7 Viscosity 46 Bottom Hole Temp. 106 ° F
Chokes: Top 1/2 Bottom 1/2 Ticket No. 6593

RECOVERY

INITIAL OPENING 2 MINUTES

WEAK STEADY BLOW THROUGHOUT TEST

217 FEET MUD CUT WATER WITH FEW
SPECKS OF OIL IN TOP STAND

Lease and Well No. ZVOLANEK # C-1 33 15 10 SE NW NW

Formation Test No. 4

COMPANY CITIES SERVICE OIL COMPANYDATE APRIL 23, 1963LEASE ZVOLANEKWELL NO. C-1TEST NO. 4TICKET NO. 6593

	TIME	PSI
INITIAL HYDRO MUD PRESSURE	----	1625
INITIAL CLOSED IN PRESSURE	30 MINUTES	1127
INITIAL FLOW	----	47
FINAL FLOW	62 MINUTES	117
FINAL CLOSED IN PRESSURE	30 MINUTES	1088
FINAL HYDRO MUD PRESSURE	----	1625

TOTAL DEPTH 3007PACKER DEPTH 2996BT. NO. 1049 DEPTH 3002

	1ST FLOW PRESSURE		INITIAL CIP		2ND FLOW PRESSURE		FINAL CIP	
	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.
P0	.000	40	.000	40	.000	47	.000	117
P1			.042	1085	.083	47	.042	1017
P2			.083	1110	.167	55	.083	1055
P3			.125	1120	.250	75	.125	1065
P4			.167	1120	.333	90	.167	1075
P5			.209	1127	.416	100	.209	1085
P6			.250	1127	.500	117	.250	1088
P7								
P8								
P9								
P10								
	2	MINUTE INTERVAL	5	MINUTE INTERVAL	10	MINUTE INTERVAL	5	MINUTE INTERVAL


REMARKS

INITIAL OPENING 2 MINUTES

SPECIAL PRESSURE DATA

33-155-10W

Pressure: Each Square _____ psi

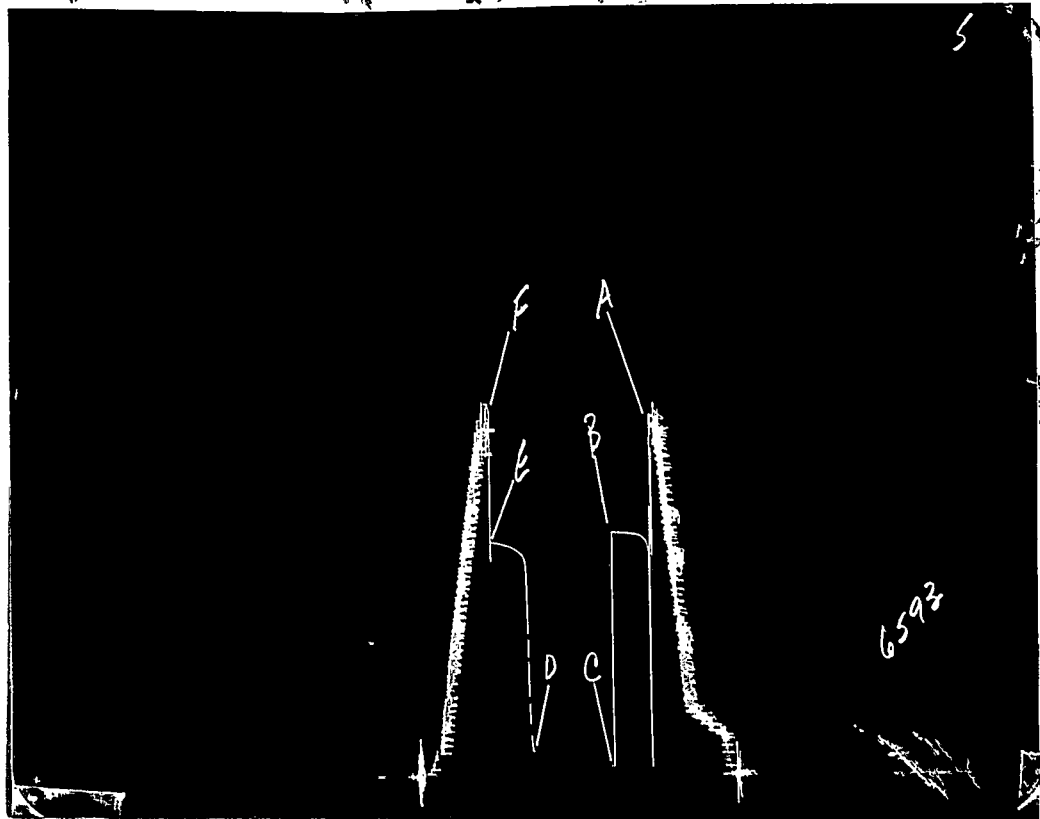

Tool Open 1 hr. 2 mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>1605</u>	<u>1625</u>
(B) Initial Shut-in Pressure	<u>1125</u>	<u>1127</u>
(C) Initial Flow Pressure	<u>50</u>	<u>47</u>
(D) Final Flow Pressure	<u>115</u>	<u>117</u>
(E) Final Shut-in Pressure	<u>1070</u>	<u>1088</u>
(F) Final Hydrostatic Pressure	<u>1595</u>	<u>1625</u>

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company CITIES SERVICE OIL COMPANY

Lease and Well No. ZVOLANEK # C-1

County ELLSWORTH

State KANSAS

Date APRIL 25, 1963

Formation Test No. 5 Total Depth 3259
Interval Tested 3252 To 3259 Anchor Length 7'
Size Hole 7 7/8 Size Drill Pipe 4 1/2 ACME Size Packer 6 3/4
Mud Weight 9.9 Viscosity 41 Bottom Hole Temp. 99 ° F
Chokes: Top 1/2 Bottom 1/2 Ticket No. 6594

RECOVERY

INITIAL OPENING 2 MINUTES

WEAK BLOW FOR 2 MINUTES
FLUSHED TOOL AFTER 8 MINUTES
AND 32 MINUTES NO BLOW

12 FEET DRILLING MUD WITH FEW
OIL SPECKS

INITIAL SHUT-IN PRESSURE AND 32
MINUTES OF OPEN FLOW PLUGGED.
TOOL OPEN TOTAL OF 28 MINUTES.

Lease and Well No. ZVOLANEK # C-1 33 15 10 SE NW NW Formation Test No. 5

COMPANY CITIES SERVICE OIL COMPANY DATE APRIL 25, 1963
 LEASE ZVOLANEK WELL NO. C-1 TEST NO. 5 TICKET NO. 6594

	TIME	PSI
INITIAL HYDRO MUD PRESSURE	-----	1655
INITIAL CLOSED IN PRESSURE	30 MINUTES	-----
INITIAL FLOW	-----	30
FINAL FLOW	62 MINUTES	30
FINAL CLOSED IN PRESSURE	30 MINUTES	420
FINAL HYDRO MUD PRESSURE	-----	1650

TOTAL DEPTH 3259
 PACKER DEPTH 3252
 BT. NO. 1049 DEPTH 3254


	1ST FLOW PRESSURE		INITIAL CIP		2ND FLOW PRESSURE		FINAL CIP	
	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.
P0	.000				.000	30	.000	30
P1					.042	30	.042	82
P2					.083	30	.083	170
P3					.125	30	.125	285
P4					.167	30	.167	360
P5					.209	30	.209	400
P6							.250	420
P7								
P8								
P9								
P10								
	MINUTE INTERVAL		MINUTE INTERVAL		5	MINUTE INTERVAL	5	MINUTE INTERVAL

REMARKS INITIAL SHUT-IN PRESSURE AND 32 MINUTES OF
OPEN FLOW PLUGGED. TOOL OPEN TOTAL OF 28 MINUTES

SPECIAL PRESSURE DATA

33-155-10W

Pressure: Each Square _____ psi

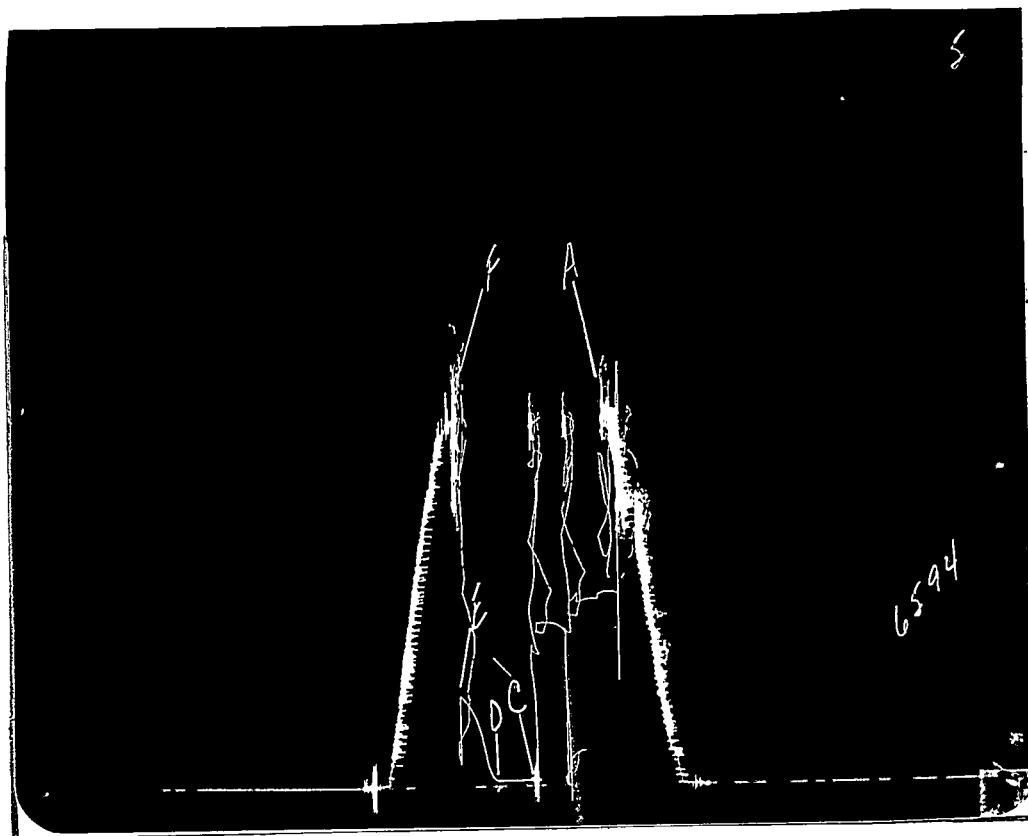

Tool Open 1 hr. 2 mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>1655</u>	<u>1655</u>
(B) Initial Shut-in Pressure	_____	_____
(C) Initial Flow Pressure	<u>20</u>	<u>30</u>
(D) Final Flow Pressure	<u>20</u>	<u>30</u>
(E) Final Shut-in Pressure	<u>420</u>	<u>420</u>
(F) Final Hydrostatic Pressure	<u>1650</u>	<u>1650</u>

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company CITIES SERVICE OIL COMPANY

Lease and Well No. ZVOLANEK # C-1

County ELLSWORTH State KANSAS Date APRIL 26, 1963

Formation Test No. 6 Total Depth 3263
Interval Tested 3254 To 3263 Anchor Length 9'
Size Hole 7 7/8 Size Drill Pipe 4 1/2 ACME Size Packer 6 3/4
Mud Weight 9.9 Viscosity 41 Bottom Hole Temp 98 ° F
Chokes: Top 1/2 Bottom 1/2 Ticket No. 6595

RECOVERY

INITIAL OPENING 2 MINUTES

WEAK BLOW FOR 2 MINUTES
FLUSHED TOOL AFTER 10 MINUTES
AND 30 MINUTES, NO BLOW

15 FEET DRILLING MUD

Lease and Well No. ZVOLANEK # C-1 33 15 10 SE NW NW Formation Test No. 6

COMPANY CITIES SERVICE OIL COMPANYDATE A PRIL 26, 1963LEASE ZVOLANEKWELL
NO.C-1TEST
NO.6TICKET NO. 6595

	TIME	PSI
INITIAL HYDRO MUD PRESSURE	-----	1670
INITIAL CLOSED IN PRESSURE	30 MINUTES	650
INITIAL FLOW	-----	40
FINAL FLOW	62 MINUTES	40
FINAL CLOSED IN PRESSURE	30 MINUTES	380
FINAL HYDRO MUD PRESSURE	-----	1652

TOTAL DEPTH 3263PACKER DEPTH 3254DT. NO. 1049 DEPTH 3259

	1ST FLOW PRESSURE		INITIAL CIP		2ND FLOW PRESSURE		FINAL CIP	
	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.
P0	.000	40	.000	40	.000	40	.000	40
P1			.042	315	.083	40	.042	82
P2			.083	490	.167	40	.083	160
P3			.125	560	.250	40	.125	250
P4			.167	607	.333	40	.167	315
P5			.209	635	.416	40	.209	360
P6			.250	650	.500	40	.250	380
P7								
P8								
P9								
P10								
	2 MINUTE INTERVAL		5 MINUTE INTERVAL		10 MINUTE INTERVAL		5 MINUTE INTERVAL	


REMARKS

INITIAL OPENING 2 MINUTES

SPECIAL PRESSURE DATA

33-155-10 W

Pressure: Each Square _____ psi

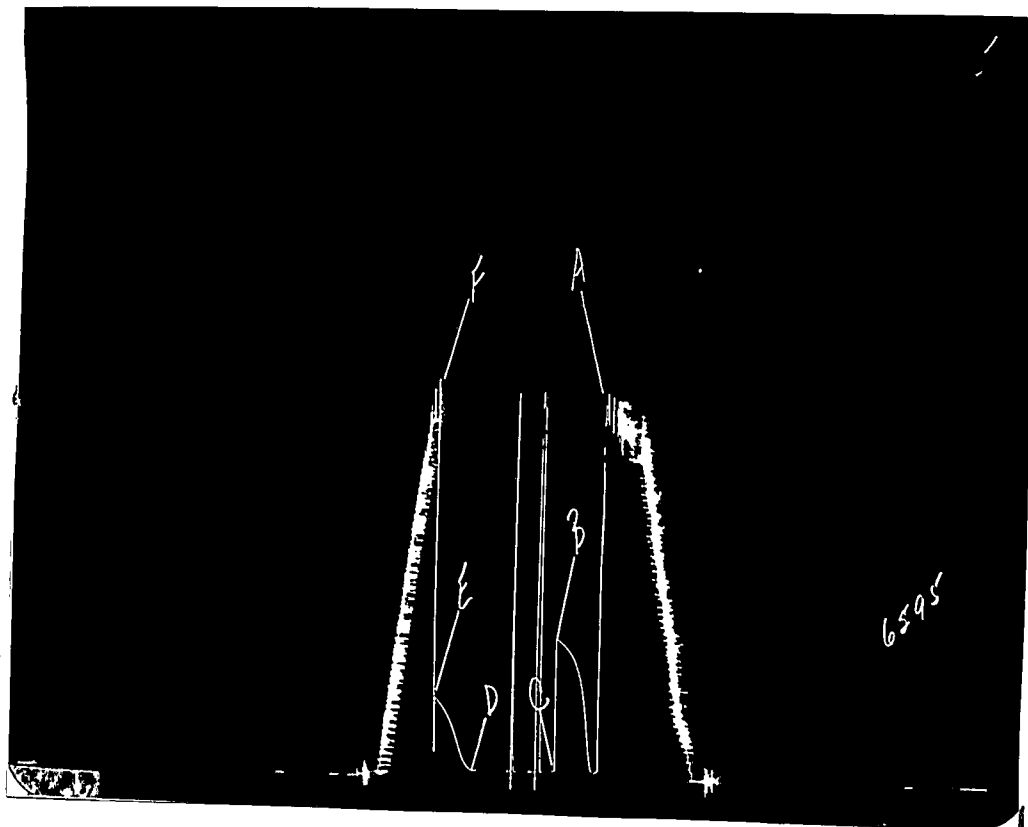

Tool Open -- 1 hr. 2 mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>1690</u>	<u>1670</u>
(B) Initial Shut-in Pressure	<u>655</u>	<u>650</u>
(C) Initial Flow Pressure	<u>40</u>	<u>40</u>
(D) Final Flow Pressure	<u>40</u>	<u>40</u>
(E) Final Shut-in Pressure	<u>375</u>	<u>380</u>
(F) Final Hydrostatic Pressure	<u>1685</u>	<u>1652</u>

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company CITIES SERVICE OIL COMPANY

Lease and Well No. ZVOLANEK # C-1

County ELLSWORTH State KANSAS Date APRIL 27, 1963

Formation Test No. 7 Total Depth 3279
Interval Tested 3271 To 3279 Anchor Length 8'
Size Hole 7 7/8 Size Drill Pipe 4 1/2 ACME Size Packer 6 3/4
Mud Weight 9.6 Viscosity 45 Bottom Hole Temp. 103 ° F
Chokes: Top 1/2 Bottom 1/2 Ticket No. 6596

RECOVERY

INITIAL OPENING 2 MINUTES

WEAK BLOW FOR 22 MINUTES
FLUSHED TOOL AFTER 25 MINUTES
AND 35 MINUTES, NO BLOW.

95 FEET MUDDY WATER

Lease and Well No. ZVOLANEK # C-1 33 15 10 SE NW NW Formation Test No. 7

COMPANY CITIES SERVICE OIL COMPANY DATE APRIL 27, 1963
 LEASE ZVOLANEK WELL NO. C-1 TEST NO. 7 TICKET NO. 6596

	TIME	PSI
INITIAL HYDRO MUD PRESSURE	-----	1755
INITIAL CLOSED IN PRESSURE	30 MINUTES	47
INITIAL FLOW	-----	47
FINAL FLOW	62 MINUTES	62
FINAL CLOSED IN PRESSURE	30 MINUTES	62
FINAL HYDRO MUD PRESSURE	-----	1740

TOTAL DEPTH 3279
 PACKER DEPTH 3271
 ST. NO. 1049 DEPTH 3274


	1ST FLOW PRESSURE		INITIAL CIP		2ND FLOW PRESSURE		FINAL CIP	
	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.
P0	.000	40	.000	40	.000	47	.000	62
P1			.042	47	.083	47	.042	62
P2			.083	47	.167	47	.083	62
P3			.125	47	.250	55	.125	62
P4			.167	47	.333	55	.167	62
P5			.209	47	.416	62	.209	62
P6			.250	47	.500	62	.250	62
P7								
P8								
P9								
P10								
	2	MINUTE INTERVAL	5	MINUTE INTERVAL	10	MINUTE INTERVAL	5	MINUTE INTERVAL

REMARKS _____
 INITIAL OPENING 2 MINUTES

SPECIAL PRESSURE DATA

83-155-10W

Pressure: Each Square _____ psi

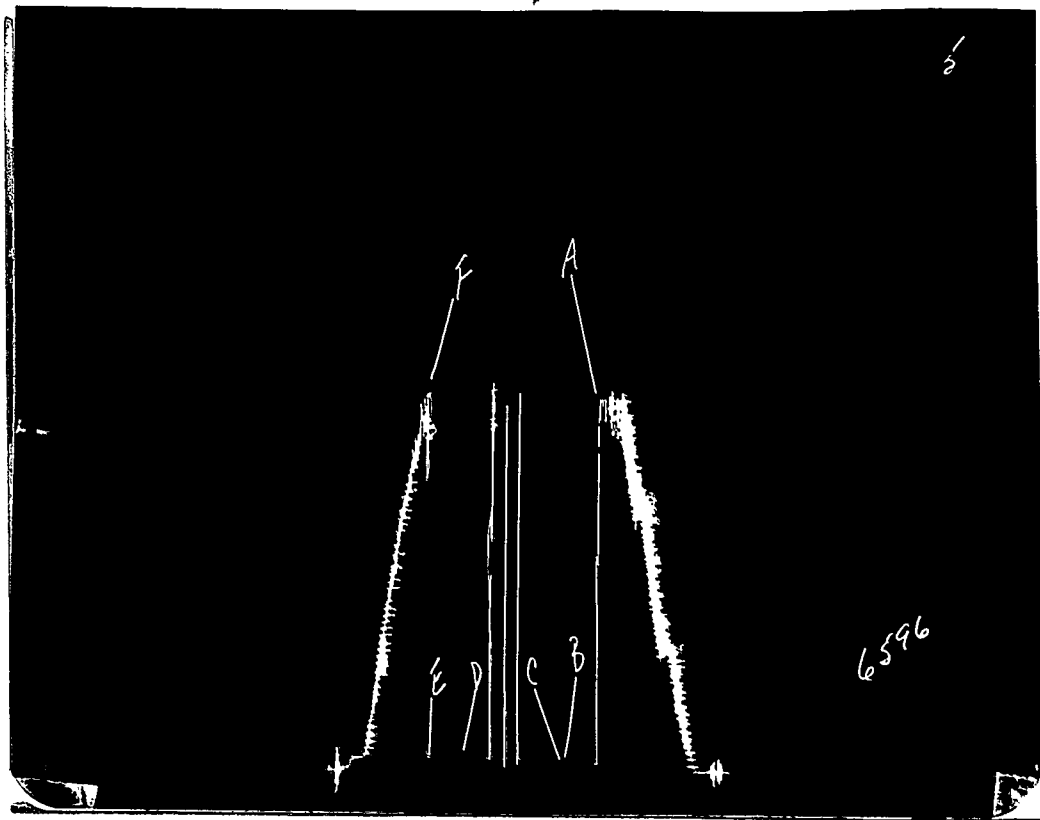

Tool Open 1 hr. 2 mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>1700</u>	<u>1755</u>
(B) Initial Shut-in Pressure	<u>55</u>	<u>47</u>
(C) Initial Flow Pressure	<u>50</u>	<u>47</u>
(D) Final Flow Pressure	<u>50</u>	<u>62</u>
(E) Final Shut-in Pressure	<u>105</u>	<u>62</u>
(F) Final Hydrostatic Pressure	<u>1695</u>	<u>1740</u>

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company CITIES SERVICE OIL COMPANY

Lease and Well No. ZVOLANEK # C-1

County ELLSWORTH State KANSAS Date APRIL 27, 1963

Formation Test No. 8 Total Depth 3305
Interval Tested 3295 To • 3305 Anchor Length 10'
Size Hole 7 7/8 Size Drill Pipe 4 1/2 ACME Size Packer 6 3/4
Mud Weight 9.6 Viscosity 47 Bottom Hole Temp. 123 ° F
Chokes: Top 1/2 Bottom 1/2 Ticket No. 6597

RECOVERY

INITIAL OPENING 2 MINUTES

GOOD BLOW, DECREASING TO FAIR
BY END OF TEST

2350 FEET OF SALT WATER

Lease and Well No. ZVOLANEK # C-1 33 15 10 SE NW NW
Formation Test No. 8

COMPANY CITIES SERVICE OIL COMPANYDATE APRIL 27, 1963LEASE ZVOLANEKWELL NO. C-1TEST NO. 8TICKET NO. 6597

	TIME	PSI
INITIAL HYDRO MUD PRESSURE	-----	1755
INITIAL CLOSED IN PRESSURE	30 MINUTES	1092
INITIAL FLOW	----	145
FINAL FLOW	92 MINUTES	880
FINAL CLOSED IN PRESSURE	30 MINUTES	1092
FINAL HYDRO MUD PRESSURE	-----	1730

TOTAL DEPTH 3305PACKER DEPTH 3295BT. NO. 1049 DEPTH 3300


	1ST FLOW PRESSURE		IAL CIP		2ND FLOW PRESSURE		FINAL CIP	
	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.	TIME DEFL. .000"	PSI TEMP. CORR.
P0	.000	82	.000	82	.000	145	.000	880
P1			.042	1075	.083	260	.042	1085
P2			.083	1085	.167	380	.083	1092
P3			.125	1089	.250	497	.125	1092
P4			.167	1092	.333	580	.167	1092
P5			.209	1092	.416	650	.209	1092
P6			.250	1092	.500	712	.250	1092
P7					.583	785		
P8					.667	830		
P9					.750	880		
P10								
	2	MINUTE INTERVAL	5	MINUTE INTERVAL	10	MINUTE INTERVAL	5	MINUTE INTERVAL

REMARKS

INITIAL OPENING 2 MINUTES

SPECIAL PRESSURE DATA

Pressure: Each Square _____ psi

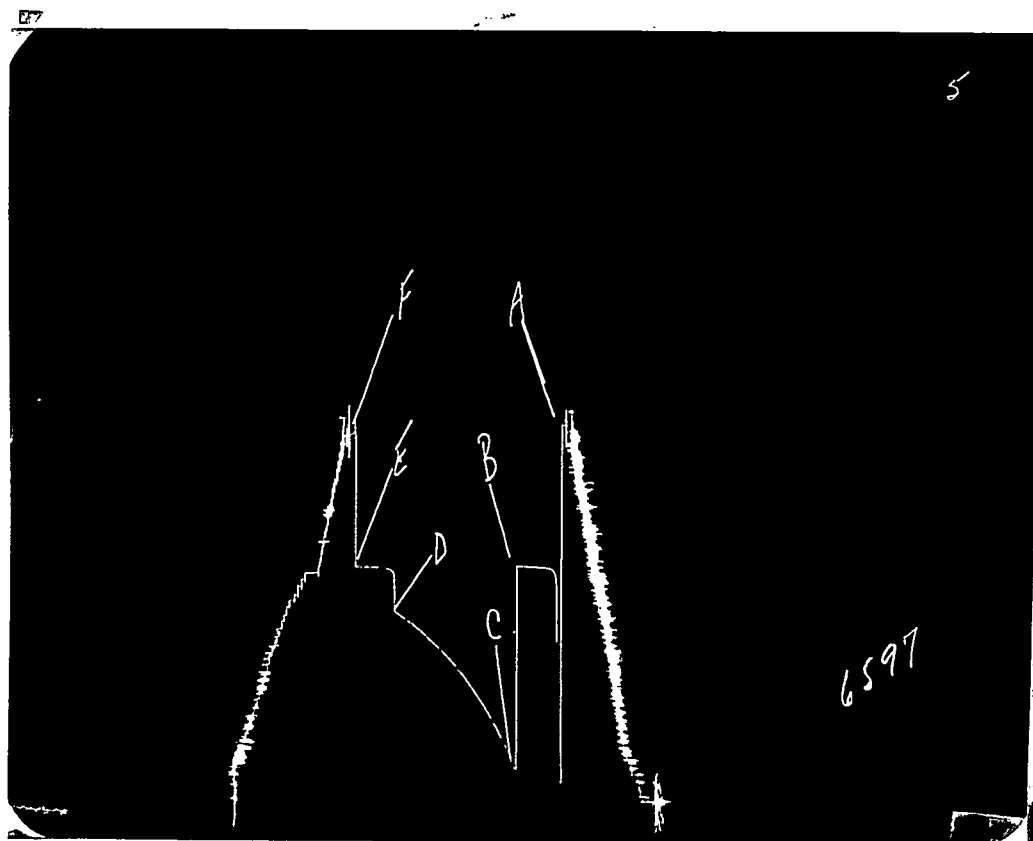

Tool Open 1 hr. 32 mins: Shut-in: Initial _____ hr. 30 mins: Final _____ hr. 30 mins.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	<u>1725</u>	<u>1755</u>
(B) Initial Shut-in Pressure	<u>1090</u>	<u>1092</u>
(C) Initial Flow Pressure	<u>195</u>	<u>145</u>
(D) Final Flow Pressure	<u>840</u>	<u>880</u>
(E) Final Shut-in Pressure	<u>1065</u>	<u>1092</u>
(F) Final Hydrostatic Pressure	<u>1720</u>	<u>1730</u>
