

DATE 8-2-59

TICKET NO. 137

COMPANY Davis Bros. CONTRACTOR Transit Corp.

WELL NO. C 1 LEASE Yohe COUNTY Rooks SEC. 24 RG. 10 TWP. 18

TEST NO. 1 HOLE SIZE 7 7/8" PACKER SIZE 6 3/4" TOOL JOINT 4 1/2" FH

ANCHOR LENGTH 59' AIR CHAMBER LENGTH --- SIZE CHOKE 1/2"

FORMATION Topeka INTERNAL TESTED 3208'-3267' ELEVATION 2087' RB T. D. 3267'

MUD WEIGHT 10.2 VISCOSITY 40 WATER LOSS 15


TOOL OPEN 2 hrs. IBHP SHUT IN TIME 20 min. FBHP SHUT IN TIME 30 min.

BLOW Strong through out test.

RECOVERY 720' of muddy water.

REMARKS |

APPROVED BY J. R. Green TESTER R. A. Dickey

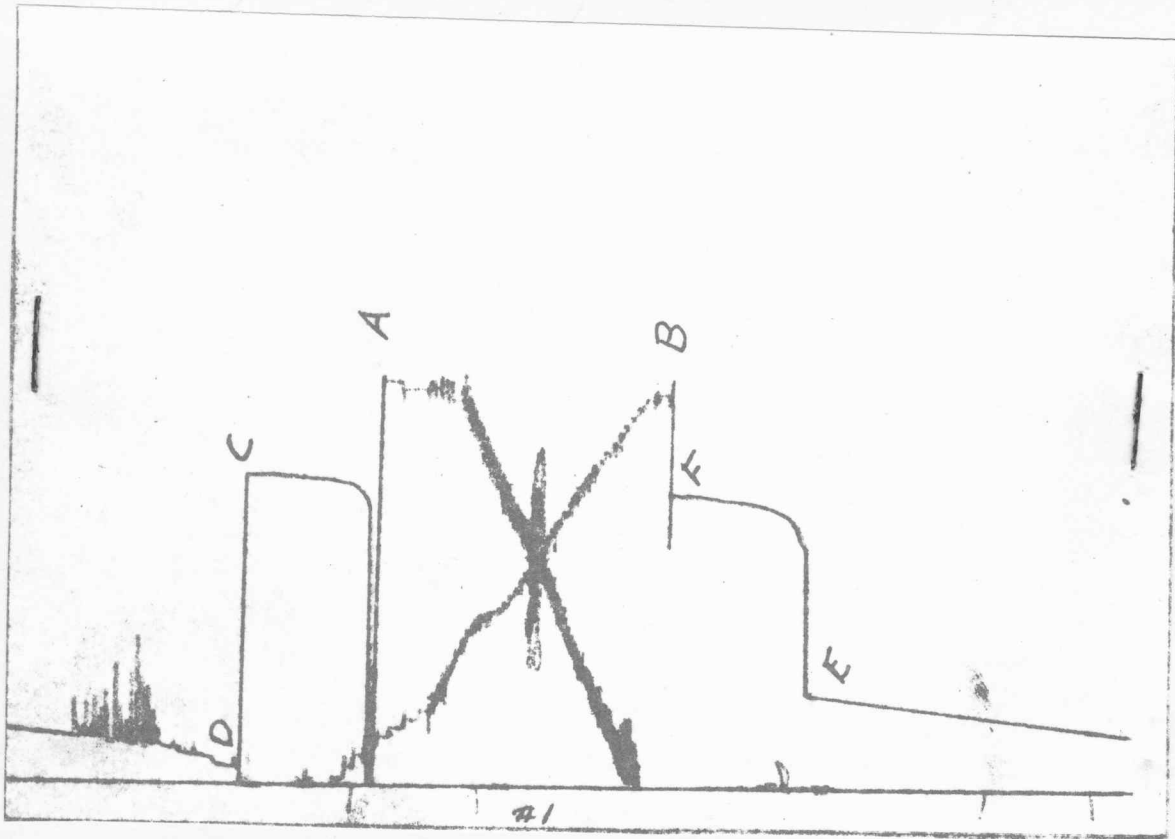

PRESSURE READINGS	Field	Office Corrected
A. Initial Hyd. Pressure	1790	1710
B. Final Hyd. Pressure	1790	1700
C. Initial BHP	1300	1312
D. Initial Flow Pressure	80	83
E. Final Flow Pressure	420	400
F. Final BHP	1230	1240

DATE 8-3-59

TICKET NO. 138

COMPANY Davis Bros. CONTRACTOR Transit Corp.

WELL NO. C 1 LEASE Yohe COUNTY Rooks SEC. 24 RG. 10 TWP. 18

TEST NO. 2 HOLE SIZE 7 7/8" PACKER SIZE 6 3/4" TOOL JOINT 4 1/2" FH

ANCHOR LENGTH 113' AIR CHAMBER LENGTH --- SIZE CHOKE 1/2"

FORMATION TESTED K.C. INTERNAL TESTED 3257'-3370' ELEVATION 2087' RB T. D. 3370'

MUD WEIGHT 9.9 VISCOSITY 41 WATER LOSS 16cc

TOOL OPEN 2 hrs. IBHP SHUT IN TIME 20 min. FBHP SHUT IN TIME 30 min.


BLOW Strong through out test.

RECOVERY 420' of heavily gas cut muddy water with a few specks of oil,

120' of gas, 60' of this was very slightly oil & gas cut mud.

REMARKS _____

APPROVED BY J. R. Green TESTER R. A. Dickey

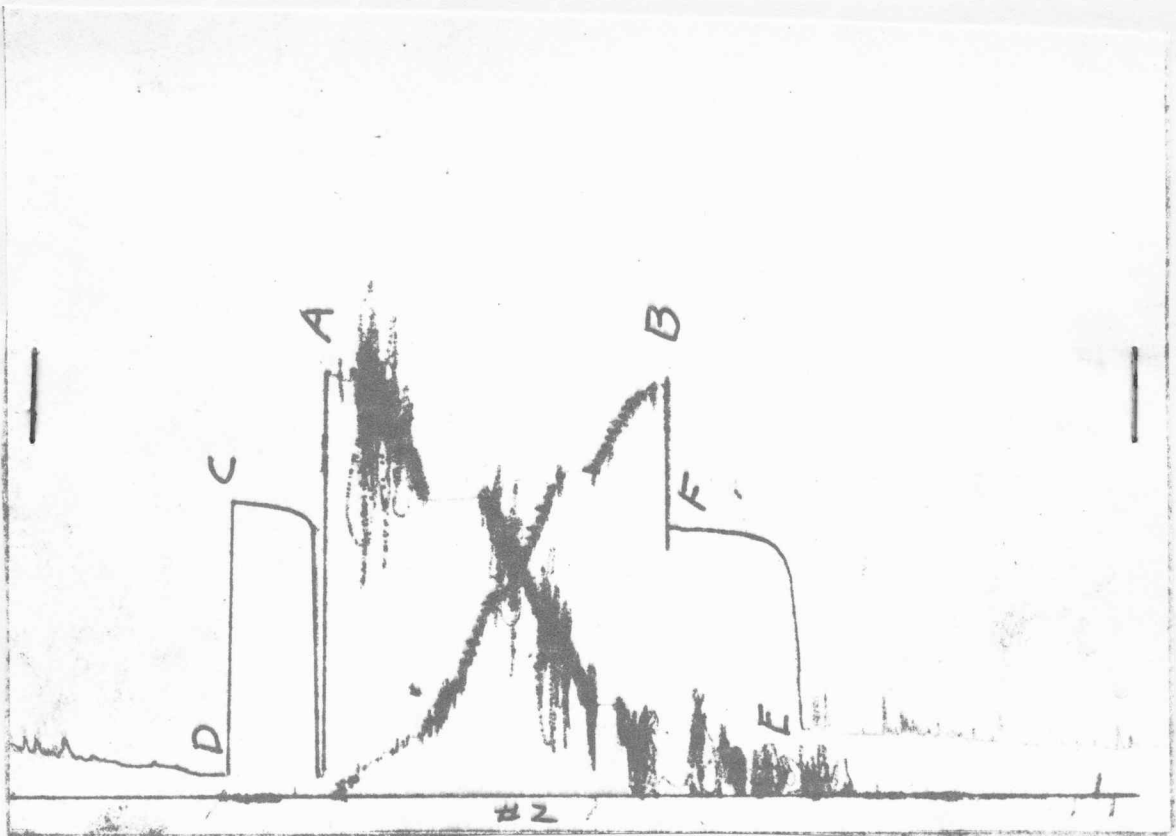

PRESSURE READINGS	Field	Office Corrected
A. Initial Hyd. Pressure	1800	1800
B. Final Hyd. Pressure	1800	1800
C. Initial BHP	1280	1276
D. Initial Flow Pressure	100	96
E. Final Flow Pressure	390	290
F. Final BHP	1140	1138

DATE 8-5-59

TICKET NO. 139

COMPANY Davis Bros. CONTRACTOR Transit Corp.

WELL NO. 'C' 1 LEASE Yohe COUNTY Rooks SEC. 24 RG. 10 TWP. 18

TEST NO. 3 HOLE SIZE 7 7/8" PACKER SIZE 6 3/4" TOOL JOINT 4 1/2" FH

ANCHOR LENGTH 60' AIR CHAMBER LENGTH --- SIZE CHOKE 1/2"

FORMATION K.C. INTERNAL TESTED 3366'-3426' ELEVATION 2087' RB T. D. 3426'

MUD WEIGHT 10 VISCOSITY 42 WATER LOSS 12cc


TOOL OPEN 2 hrs. IBHP SHUT IN TIME 20 min. FBHP SHUT IN TIME 30 min.

BLOW Strong through out test.

RECOVERY 1560' of muddy water.

REMARKS |

APPROVED BY J. R. Green TESTER R. A. Dickey

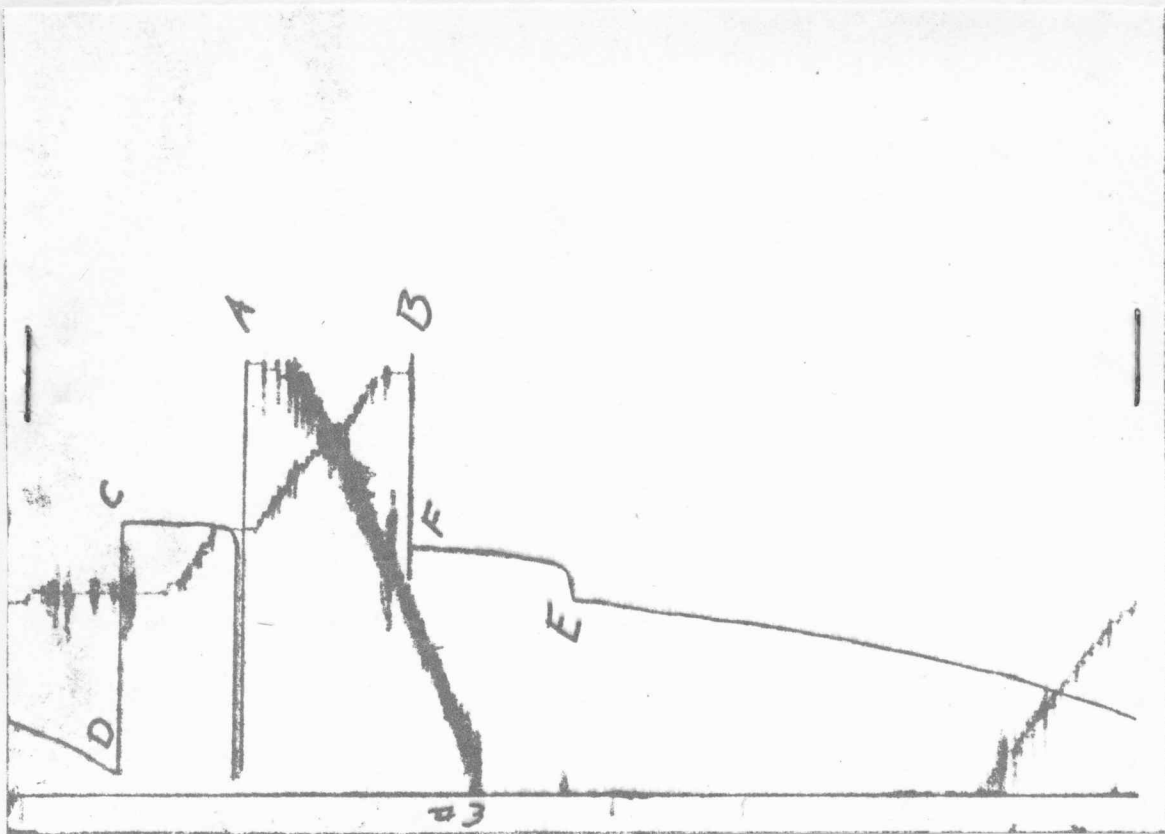

PRESSURE READINGS	Field	Office Corrected
A. Initial Hyd. Pressure	1830	1825
B. Final Hyd. Pressure	1830	1800
C. Initial BHP	1180	1176
D. Initial Flow Pressure	100	98
E. Final Flow Pressure	820	825
F. Final BHP	1090	1052

DATE 8-5-59

TICKET NO. 140

COMPANY Davis Bros. CONTRACTOR Transit Corp.

WELL NO. 'C' 1 LEASE Yohe COUNTY Rooks SEC. 24 RG. 10 TWP. 18

TEST NO. 4 HOLE SIZE 7 7/8" PACKER SIZE 6 3/4" TOOL JOINT 4 1/2" FH

ANCHOR LENGTH 113' AIR CHAMBER LENGTH --- SIZE CHOKE 1/2"

FORMATION K.C. INTERNAL TESTED 3422'-3535' ELEVATION 2087' RB T. D. 3535'

MUD WEIGHT 10 VISCOSITY 40 WATER LOSS 17cc


TOOL OPEN 2 hrs. IBHP SHUT IN TIME 20 min. FBHP SHUT IN TIME 30 min.

BLOW Weak through out test.

RECOVERY 180' of gas, 120' of very heavy oil & gas cut mud, (est. 75% oil)

REMARKS |

APPROVED BY J. R. Green TESTER R. A. Dickey

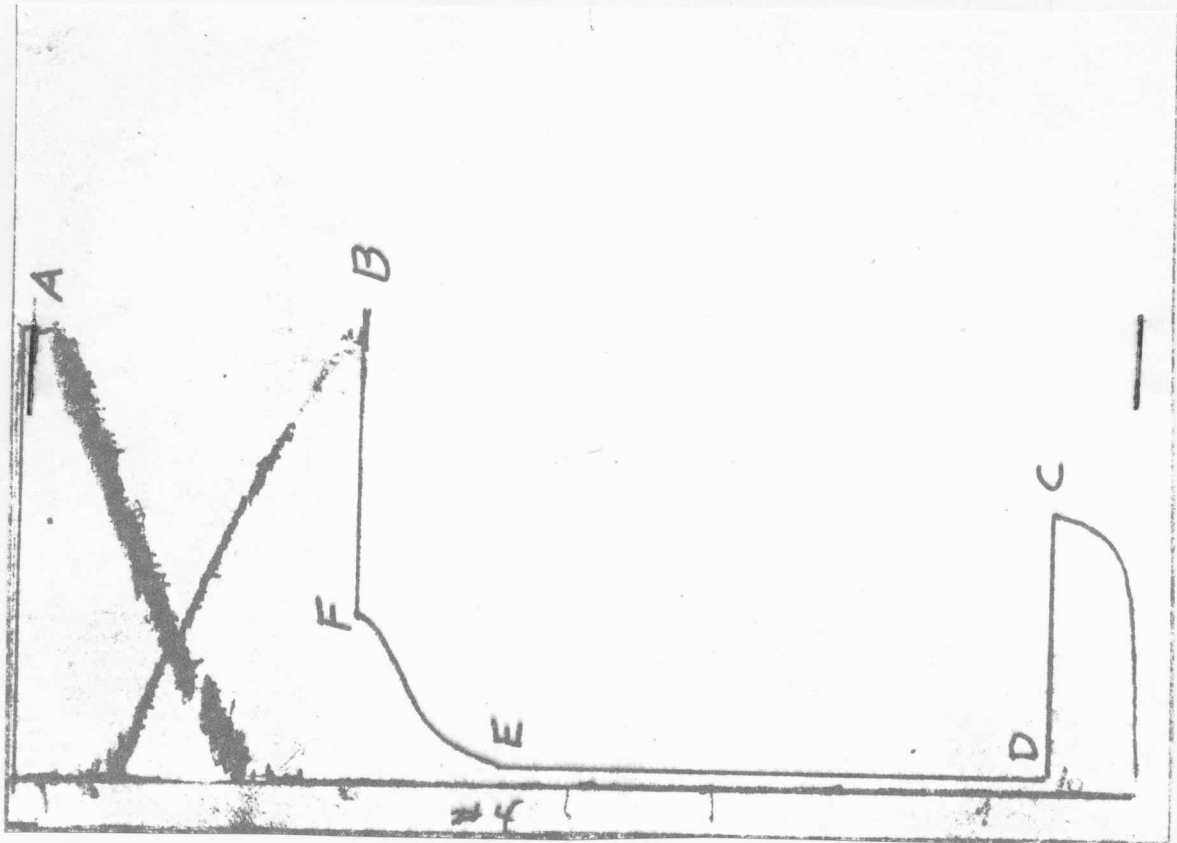

PRESSURE READINGS	Field	Office Corrected
A. Initial Hyd. Pressure	1950	1950
B. Final Hyd. Pressure	1942	1942
C. Initial BHP	1190	1180
D. Initial Flow Pressure	90	90
E. Final Flow Pressure	100	100
F. Final BHP	720	721
