

DATE 7-24-61

TICKET NO. 300

COMPANY Robinowitz Oil Co. CONTRACTOR Triangle Drlg.

WELL NO. 1 LEASE Landaner COUNTY Ellis SEC. 30 RG. 12 TWP. 20

TEST NO. 1 HOLE SIZE 7 7/8" PACKER SIZE 6 3/4" TOOL JOINT 4 1/2" FH

ANCHOR LENGTH 66' AIR CHAMBER LENGTH --- SIZE CHOKE 1/2"

FORMATION Arbuckle INTERVAL TESTED 3837'-3903' ELEVATION 2215' DF T. D. 3903'

MUD WEIGHT 10.6 VISCOSITY 46 WATER LOSS 15cc


TOOL OPEN 45 min. IBHP SHUT IN TIME --- FBHP SHUT IN TIME 30 min.

BLOW Very weak blow for 26 min.

RECOVERY 15' of rotary mud.

REMARKS By passed tool.

APPROVED BY J. R. Green TESTER R. A. Dickey

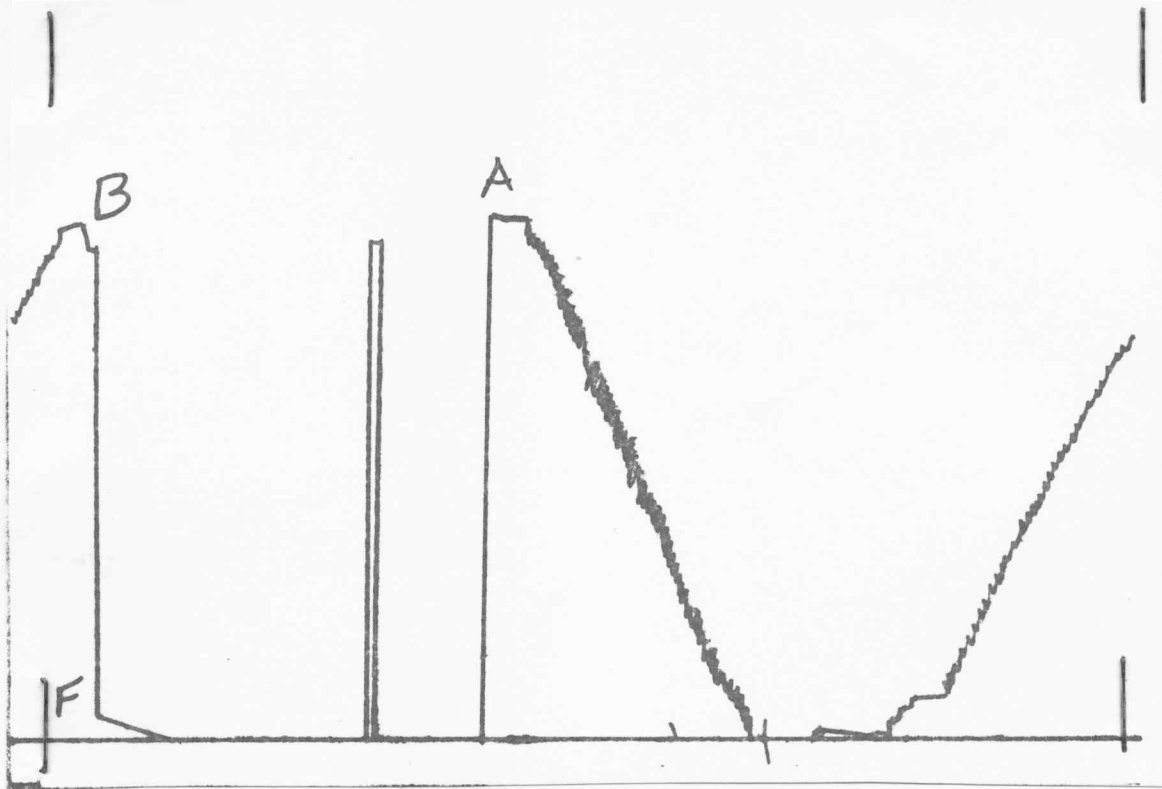

PRESSURE READINGS	
A. Initial Hyd. Pressure	2260
B. Final Hyd. Pressure	2260
C. Initial BHP	----
D. Initial Flow Pressure	0
E. Final Flow Pressure	0
F. Final BHP	100
