

MILLER TESTING COMPANY

Box 547

GREAT BEND, KANSAS

Company CAMERON REED

Lease and Well No. STORM #3

County ELLIS State KANSAS

Date NOVEMBER 3, 1967

Formation Test No. 2 Total Depth 3838 Elev. 2208 DF
 Interval Tested 3807 To 3838 Anchor Length 31'
 Size Hole 7 7/8 Size Drill Pipe 4 1/2 FH Size Packer 6 3/4
 Mud Weight 10 Viscosity 40 Water Loss 10.4 c.c. Bottom Hole Temp. 106 °F
 Chokes: Top 1/2 Bottom 1/2 Ticket No. 8778

RECOVERY

FAIR BLOW THROUGHOUT TEST.

30 FEET OF SLIGHTLY OIL CUT MUD.
 60 FEET OF HEAVY OIL CUT MUD.
 60 FEET OF FROGGY OILY MUD.
 60 FEET OF FROGGY MUDDY OIL.

Lease and Well No. STORM #3 35 13S 20W NW SW NW

Formation Test No. 2

COMPANY CAMERON REED

DATE NOVEMBER 3, 1967

LEASE STORM

WELL NO. 3

TEST NO. 2

TEST NO. 2

TICKET NO. 8778

	TIME	PSI
INITIAL HYDRO MUD PRESSURE		2093
INITIAL CLOSED IN PRESSURE	30 mins.	1138
INITIAL FLOW	30 mins.	48 to 74
FINAL FLOW	30 mins.	100 to 118
FINAL CLOSED IN PRESSURE	30 mins.	1130
FINAL HYDRO MUD PRESSURE		2067

TOTAL DEPTH 3838


PACKER DEPTH 3807

BT. NO. 2162 DEPTH 3833

[illegible]

SPECIAL PRESSURE DATA

6

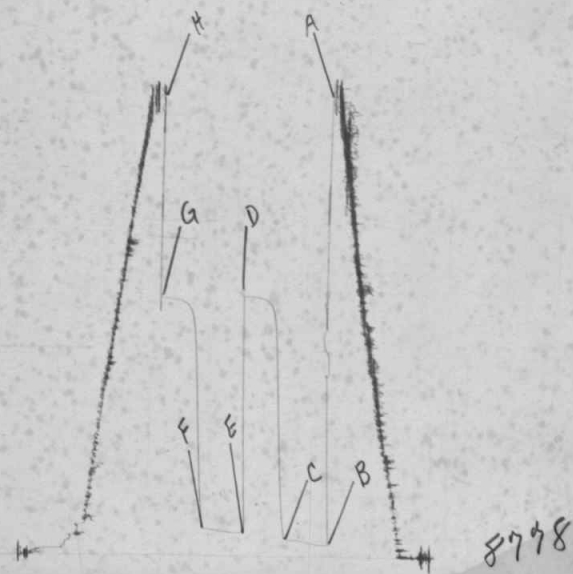

Tool Open: 1st Flow hr. 30 mins: Shut-in Initial hr. 30 min: 2nd Flow hr. 30 min: Shut-in Final hr. 30 min.

	Field Reading	Corrected Reading
(A) Initial Hydrostatic Pressure	2084	2093
(B) Initial 1st Flow Pressure	43	48
(C) Final 1st Flow Pressure	69	74
(D) Initial Shut-in Pressure	1133	1138
(E) Initial 2nd Flow Pressure	99	100
(F) Final 2nd Flow Pressure	112	118
(G) Final Shut-in Pressure	1125	1130
(H) Final Hydrostatic Pressure	2066	2067

8778
