

SUPERIOR TESTERS, INC.

433 SOUTH WESTVIEW, DERBY, KANSAS

Date 8/3/71 Ticket No. 2342 Elevation _____

Total Depth 3356 Tested From 3334 To 3356 Formation Tested Topeka

Blow Fair blow through out test

Mud Wt. 9.5 Viscosity 35 Bottom Hole Temp 108

Size Bottom Choke 1/2" Size Top Choke 1/2"

Size Drill Pipe 4 1/8" FH Size Hole 7 7/8" Length Air Chamber - Ft.

Initial Shut in Time 45 Min Tool Open 2 Hr 30 Min Final Shut in Time 45 Min

Recovery 1020' of salt water

Office Corrected Pressure Reading

Initial Shut in Pressure 1118 Lbs

Initial Flow Pressure 23 Lbs

Final Flow Pressure 514 Lbs

Final Shut in Pressure 1102 Lbs

Initial Hydrostatic Pressure 1757 Lbs

Final Hydrostatic Pressure 1741 Lbs

Remarks _____

Witnessed By H. E. Schwerdtfeger

Tool Operator R. L. Budig

Location SE 1/4, SE 32-135-20W

Name of Lease Boos

Well No. A-1

Test No. 1


Company Larry G. Stephenson, Et Al.

County Ellis

State Kansas

#2342

D.S.T. #1

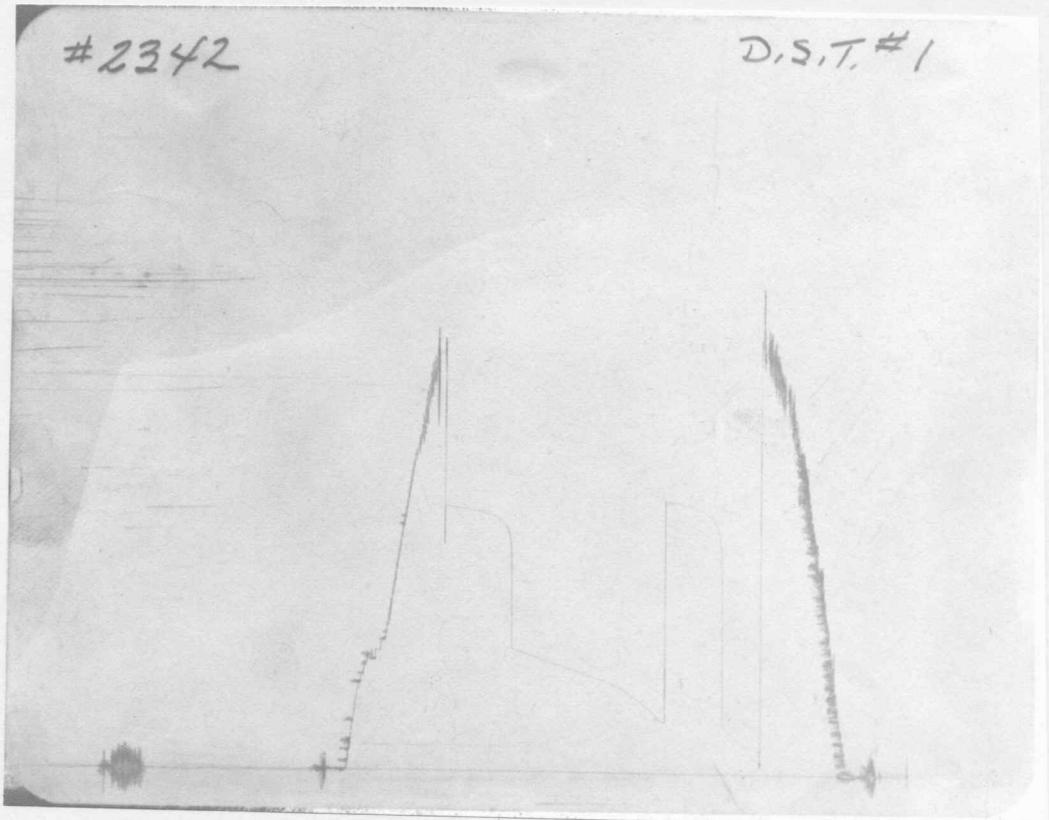

SUPERIOR TESTERS, INC.

433 SOUTH WESTVIEW, DERBY, KANSAS

Date 8/5/71 Ticket No. 2343 Elevation _____

Total Depth 3630 Tested From 3574 To 3630 Formation Tested Kansas City

Blow Fair blow through out test

Mud Wt. 9.6 Viscosity 40 Bottom Hole Temp 111

Size Bottom Choke 1/2" Size Top Choke 1/2"

Size Drill Pipe 4 1/2" FH Size Hole 7 7/8" Length Air Chamber - Ft.

Initial Shut in Time 45 Min Tool Open 2 Hr 30 Min Final Shut in Time 45 Min

| | |
|--|--|
| Recovery <u>60' of gas, 5' of oil, 75' of oil cut mud, 120' of slightly oil cut watery mud</u> | Office Corrected Pressure Reading Initial Shut in Pressure <u>458</u> Lbs Initial Flow Pressure <u>63</u> Lbs Final Flow Pressure <u>158</u> Lbs Final Shut in Pressure <u>347</u> Lbs Initial Hydrostatic Pressure <u>1986</u> Lbs Final Hydrostatic Pressure <u>1971</u> Lbs |
|--|--|

Remarks _____

Witnessed By H. E. Schwerdtfeger


Tool Operator R. L. Budig

Location SE, NW, SE 32-135-30W County Ellis State Kansas

Name of Lease Boos Well No. A-1 Test No. 2 Company Larry G. Stephenson, Et Al

2343

D.S.T. # 2

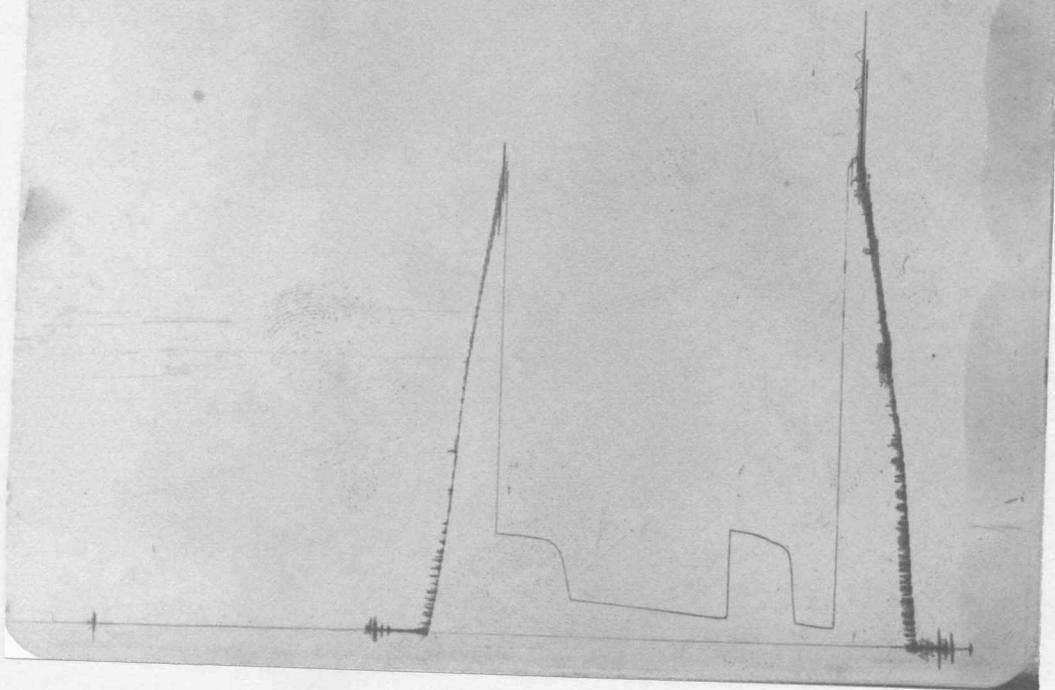

SUPERIOR TESTERS, INC.

433 SOUTH WESTVIEW, DERBY, KANSAS

Date 8/6/71 Ticket No. 2438 Elevation _____

Total Depth 3775 Tested From 3756 To 3775 Formation Tested Kansas City

Blow Weak blow through out test

Mud Wt. 9.9 Viscosity 41 Bottom Hole Temp 128

Size Bottom Choke 1/2" Size Top Choke 1/2"

Size Drill Pipe 4 1/8" PH Size Hole 7 7/8" Length Air Chamber - Ft.

Initial Shut in Time 45 Min Tool Open 2 Hr 30 Min Final Shut in Time 45 Min

Recovery 180' of muddy water

Office Corrected Pressure Reading

Initial Shut in Pressure 304 Lbs

Initial Flow Pressure 40 Lbs

Final Flow Pressure 128 Lbs

Final Shut in Pressure 296 Lbs

Initial Hydrostatic Pressure 1984 Lbs

Final Hydrostatic Pressure 1976 Lbs

Remarks _____

Witnessed By H. E. Schwerdtfeger

Tool Operator Art Budig

Location SE, NW, SE 32-13S-20W

Boos
Name of Lease

A-1
Well No. 5

County Ellis
Company Jerry G. Stephenson Et Al

State Kansas

8438

DST
#3

