

# SUPERIOR TESTERS, INC.

433 SOUTH WESTVIEW, DERBY, KANSAS

Date 7/17/71 Ticket No. 2432 Elevation \_\_\_\_\_

Total Depth 2460 Tested From 2432 To 2460 Formation Tested Topoka

Blow Strong and steady

Mud Wt. 10 Viscosity 39 Bottom Hole Temp 94

Size Bottom Choke 1/2" Size Top Choke 1/2"

Size Drill Pipe 4 1/8" FH Size Hole 7 7/8 Length Air Chamber - Ft.

Initial Shut in Time 60 Min Tool Open 2 Hr 30 Min Final Shut in Time 60 Min

Recovery 60' gassy mud

### Office Corrected Pressure Reading

Initial Shut in Pressure 232 Lbs

Initial Flow Pressure 56 Lbs

Final Flow Pressure 56 Lbs

Final Shut in Pressure 656 Lbs

Initial Hydrostatic Pressure 1515 Lbs

Final Hydrostatic Pressure 1496 Lbs

Remarks \_\_\_\_\_

Witnessed By Richard M. Foley

Tool Operator Art Budg

Location SEC. 16, T17N, R16E, S10W

County Ellsworth

State KANSAS

Baker  
Name of Lease


4  
Well No.

1  
Test No.

International Resources Corp.  
Company

2432

DST  
#1

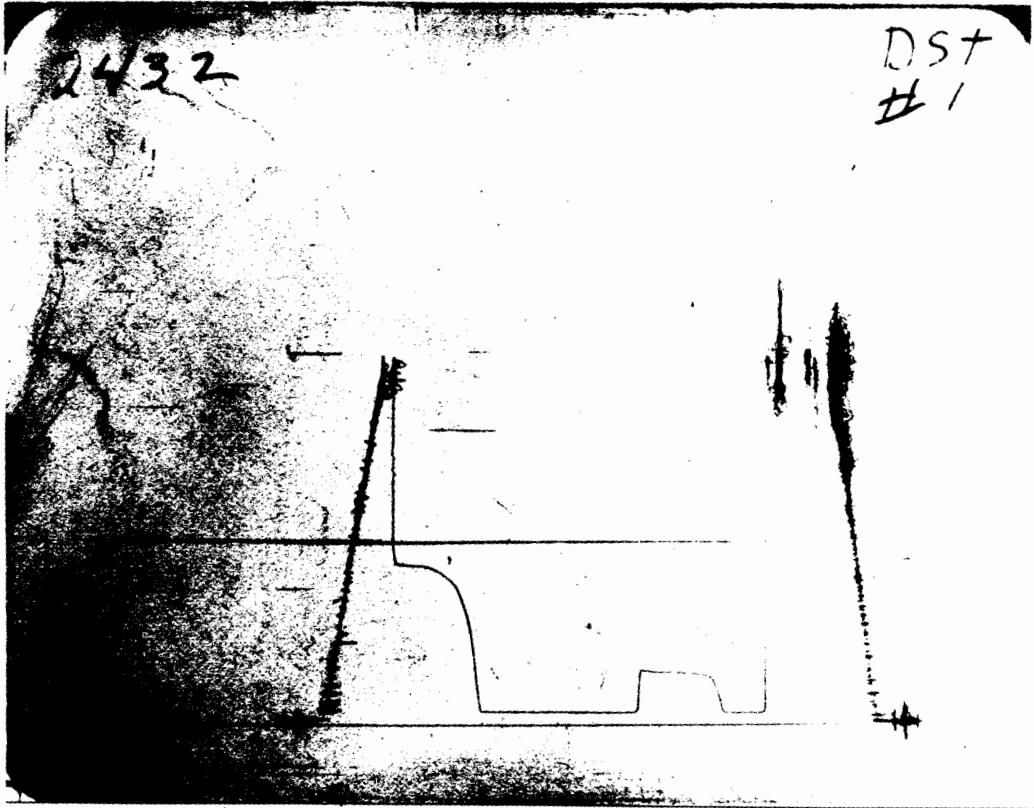

# SUPERIOR TESTERS, INC.

433 SOUTH WESTVIEW, DERBY, KANSAS

Date 7/18/71 Ticket No. 2433 Elevation \_\_\_\_\_

Total Depth 2853 Tested From 2825 To 2853 Formation Tested Kansas City

Blow Fair blow

Mud Wt. 10 Viscosity 41 Bottom Hole Temp 102

Size Bottom Choke 1/2" Size Top Choke 1/2"

Size Drill Pipe 4 1/2" FH Size Hole 7 7/8" Length Air Chamber \_\_\_\_\_ Ft.

Initial Shut in Time 60 Min Tool Open 3 Hr \_\_\_\_\_ Min Final Shut in Time 60 Min

Recovery 120' gas in drill pipe,

45' Oil cut mud

### Office Corrected Pressure Reading

Initial Shut in Pressure 208 Lbs

Initial Flow Pressure 48 Lbs

Final Flow Pressure 56 Lbs

Final Shut in Pressure 120 Lbs

Initial Hydrostatic Pressure 1536 Lbs

Final Hydrostatic Pressure 1500 Lbs

Remarks \_\_\_\_\_

Witnessed By Richard M. Foley

Tool Operator Art Budig

Location SE. NW, SW 16-14S-10W

Name of Lease Baker


Well No. 4

Test No. 2

County Ellsworth

State Kansas

Company International Resources Corp.

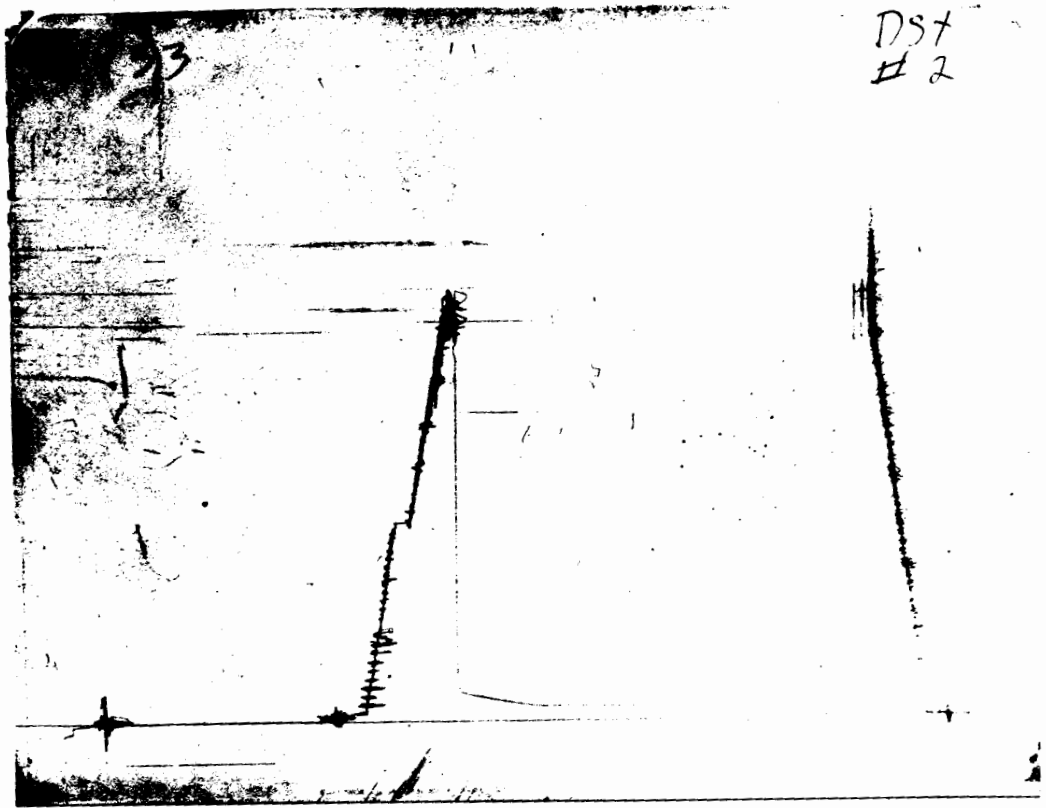

DST  
# 2
