




OIL WELL CEMENTING INC.

Date 5-17-69

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6249

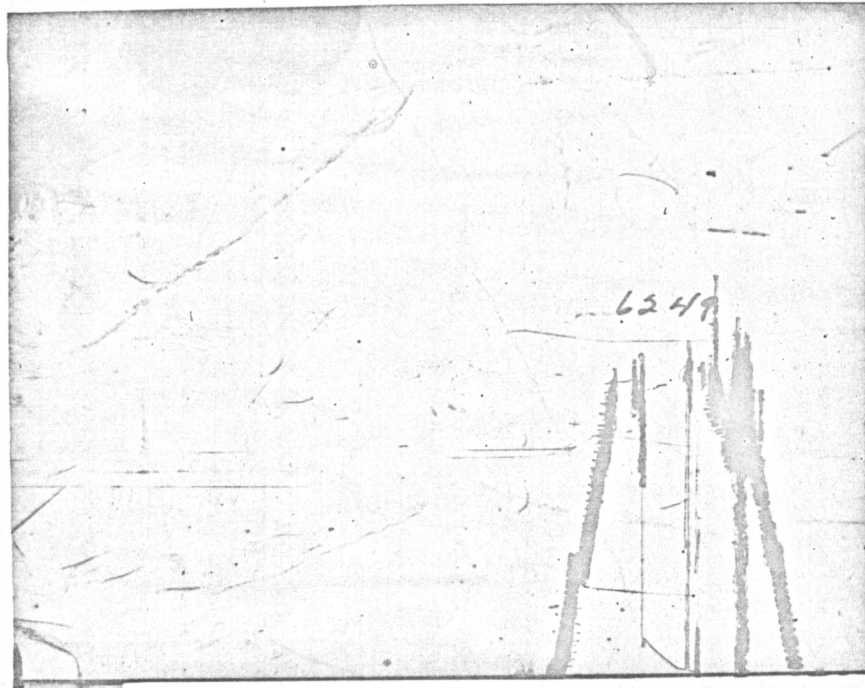

Company WILL P. ASH & AMERICAN DRIG. CO. Contractor AMERICAN DRIG. CO.

Well No. 1 Lease PRINCE County RUSSELL Sec. Twp Rng

Test No. 1 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 5/8

Interval Tested From 2425 To 2455 Depth of Well 2455 Size Choke 5/8

Fluid Recovered In Temp. 90 Elev. 1663 KB.

Initial Hyd. 1415 P.S.I. Final Hyd. 1415 P.S.I.

First Initial Flow Pressure P.S.I. Opened Tool 2:01 ~~###~~ P.M.

First Final Flow Pressure P.S.I. First Flow Pres. Min.

Initial Closed-in Pressure P.S.I. Initial Closed-in Pres. Min.

Second Initial Flow Pressure 25 P.S.I. Second Flow Pres. 15 Min.

Second Final Flow Pressure 25 P.S.I. Final Closed-in Pres. 30 Min.

Final Closed-in Pressure 162 P.S.I. ALL PRESSURES CORRECTED ON
MICROMETER CHART SCANNER.

Blow VERY WEAK . DEAD IN 5 MIN.

Recovery 5 FT. MUD.

Remarks

Approved By DENT Tester BOWMAN



OIL WELL CEMENTING INC.

Date 5-18-69

DRILL STEM TEST RECOVERY REPORT

Ticket No. 6250



Company WILL P. ASH & AMERICAN DRIG. Contractor AMERICAN DRIG. CO.

Well No. 1 Lease PRINCE County RUSSELL Sec. Twp Rng

Test No. 2 Size Hole 7 7/8 Packer Size 6 3/4 Drill Pipe Size 4 1/2 XH.

Interval Tested From 2808 To 2830 Depth of Well 2830 Size Choke 5/8

Fluid Recovered In FLEXWEIGHT Temp. 104 Elev. 1663 KB.

Initial Hyd. 1949 P.S.I. Final Hyd. 1949 P.S.I.

First Initial Flow Pressure 10 P.S.I. Opened Tool 9:05 ~~###~~ P.M.

First Final Flow Pressure 38 P.S.I. First Flow Pres. 15 Min.

Initial Closed-in Pressure 680 P.S.I. Initial Closed-in Pres. 45 Min.

Second Initial Flow Pressure 60 P.S.I. Second Flow Pres. 120 Min.

Second Final Flow Pressure 216 P.S.I. Final Closed-in Pres. 45 Min.

Final Closed-in Pressure 662 P.S.I. ALL PRESSURES CORRECTED ON
MICROMETER CHART SCANNER.

Blow STRONG BLOW THRU-OUT TEST. 750 FT. GAS IN PIPE.

Recovery 15 FT. OIL & GAS CUT MUD. 220 FT. FROGGY MUD CUT OIL.

610 FT. CLEAN OIL. 80 FT. OILY MUDDY WATER.

Remarks

Approved By FOLEY Tester BOWMAN
