

15-167-21334

Telephone
(316) 793-6347Mobil — (316) 793-7859
Unit 7076

33-145-12w

P. O. Box 1424
GREAT BEND, KANSAS 67530NE NE1 NW1 Sec 33-145-124
Russell Co., Ks.

Company ICER ADDIS Date 7-20-79

Address 5307 E. CENTRAL WICHITA, KANSAS 67207

Drilling Contractor DUKE DRILLING COMPANY Rig No. 2

Lease, Well No. KEPKA #1 County RUSSELL Sec. 33 Twp. 14 Rng. 12

Size Hole 7 7/8 Size Pipe 4 1/2 F.H. - 4 1/2 E.X.H. Size Tool 3 1/2

Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 F.H.

Interval Tested 2203' to 2230' Total Depth 2230'

Test No. 1 Successful No. 1 Misrun No. 0

Formation Tested TARKIO Time Packer Set 7:35 A.M. Time Tool Opened 7:40 A.M.

Tool Open 30-30 Min. Initial Shut-in-Time 30 Min. Final Shut-in-Time 30 Min.

Blow FIRST OPENING: WEAK BLOW.

SECOND OPENING: VERY WEAK BLOW.

Recovery 80 FEET OF MUD, 60 FEET OF SLIGHTLY OIL CUT MUD. GAS SLIGHTLY OILY IN TOOL.

Remarks: TOOL SLID APPROXIMATELY 10 FEET.


TEMPERATURE 90 DEGREES. A-27'

Initial BHP 741# IFP 106# - 106# FFP 117# - 117# Final BHP 730#

Hydrastatic Press. 1263# - 1211# Mud Wt. Vis. Water Loss

Extra Equipment Jars Straddle Packer Safety Joint

Tester Carl Skinner Approved By Richard M. Foley Ticket No. 2381

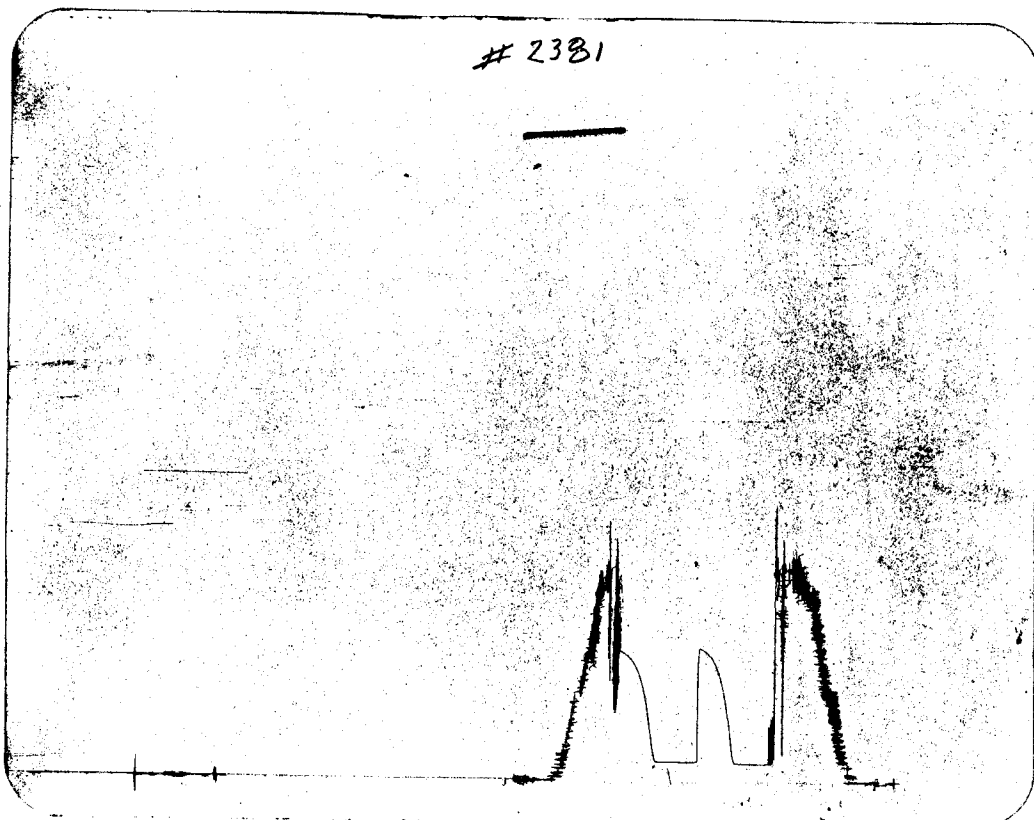

Telephone
(316) 793-6347


Mobil — (316) 793-7859
Unit 7076



P. O. Box 1424
GREAT BEND, KANSAS 67530

NE NW NW Sec. 33-14s-12₄
Russell Co., *Ks*

Company ICER ADDIS Date 7-20-79
Address 5307 E. CENTRAL WICHITA, KANSAS 67207
Drilling Contractor DUKE DRILLING COMPANY Rig No. 2
Lease, Well No. KEPKA #1 County RUSSELL Sec. 33 Twp. 14 Rng. 12
Size Hole 7 7/8 Size Pipe 4 1/2 F.H. - 4 1/2 E.X.H. Size Tool 3 1/2
Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 F.H.
Interval Tested 2229' to 2278' Total Depth 2278'
Test No. 2 Successful No. _____ Misrun No. _____
Formation Tested TARKIO #2 Time Packer Set _____ Time Tool Opened _____
Tool Open _____ Min. Initial Shut-in-Time _____ Min. Final Shut-in-Time _____ Min.
Blow PACKER FAILURE
Recovery _____
Remarks: _____
Initial BHP _____ IFP _____ FFP _____ Final BHP _____
Hydrastatic Press. _____ Mud Wt. _____ Vis. _____ Water Loss _____
Extra Equipment _____ Jars _____ Straddle Packer _____ Safety Joint _____
Tester Carl Skinner Approved By _____ Ticket No. 2382

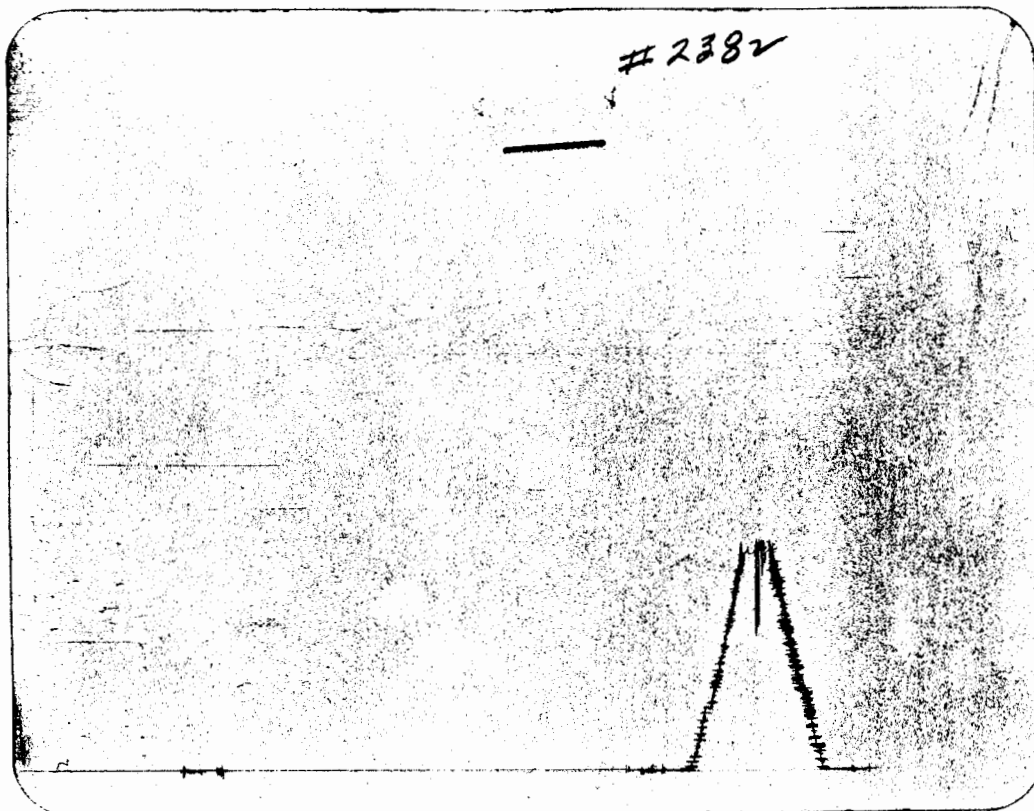

Telephone
(316) 793-6347


Mobil — (316) 793-7859
Unit 7076



P. O. Box 1424
GREAT BEND, KANSAS 67530

NE NW NW Sec. 33-14-12
Russell Co., Ks

Company ICER ADDIS Date 7-20-79
Address 5307 E. CENTRAL WICHITA, KANSAS 67207
Drilling Contractor DUKE DRILLING COMPANY Rig No. 2
Lease, Well No. KEPKA #1 County RUSSELL Sec. 33 Twp. 14 Rng. 12
Size Hole 7 7/8 Size Pipe 4 1/2 F.H. - 4 1/2 E. X.H. Size Tool 3 1/2
Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 F.H.
Interval Tested 2209' to 2278' Total Depth 2278'
Test No. 3 Successful No. _____ Misrun No. _____
Formation Tested TARKIO Time Packer Set 1:55 A.M. Time Tool Opened 2:00 A.M.
Tool Open 30-30 Min. Initial Shut-in-Time 30 Min. Final Shut-in-Time 30 Min.
Blow FIRST OPENING: WEAK BLOW.
SECOND OPENING: WEAK BLOW.
Recovery 80 FEET OF OIL CUT MUD.
Remarks: TOOL SLID APPROXIMATELY 6 FEET.
TEMPERATURE 90 DEGREES. A-69'
Initial BHP 730# IFP 53# - 74# FFP 106# - 106# Final BHP 531 #
Hydrastatic Press. 1243# - 1200# Mud Wt. 9.7 Vis. 39 Water Loss 6 c c
Extra Equipment _____ Jars _____ Straddle Packer _____ Safety Joint _____
Tester Carl Skinner Approved By Richard M. Foley Ticket No. 2383

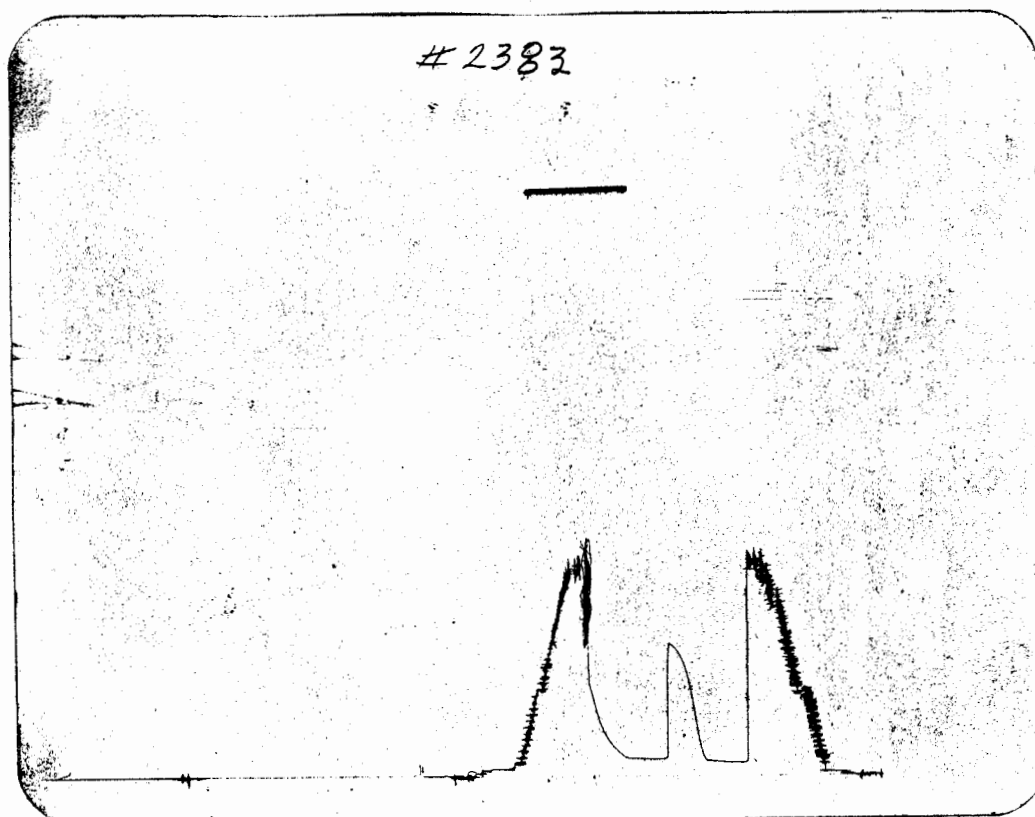

Telephone
(316) 793-6347


Mobil — (316) 793-7859
Unit 7076



P. O. Box 1424
GREAT BEND, KANSAS 67530

NE NW NW Sec. 33-14s-12W
Russell Co., KS

Company ICER ADDIS Date 7-22-79
Address 5307 E. CENTRAL WICHITA, KANSAS 67207
Drilling Contractor DUKE DRILLING COMPANY Rig No. 2
Lease, Well No. KEPKA #1 County RUSSELL Sec. 33 Twp. 14 Rng. 12
Size Hole 7 7/8 Size Pipe 4 1/2 E.X.H. - 4 1/2 F.H. Size Tool 3 1/2
Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 F.H.
Interval Tested 2897' to 2920' Total Depth 2920'
Test No. 4 Successful No. 3 Misrun No. -
Formation Tested KC Time Packer Set 10:25 P.M. Time Tool Opened 10:30 P.M.
Tool Open 30-30 Min. Initial Shut-in-Time 30 Min. Final Shut-in-Time 30 Min.
Blow FIRST OPENING: VERY WEAK INTERMITTENT 20 MINUTE BLOW.
SECOND OPENING: DID NOT BLOW.
Recovery APPROXIMATELY 15 FEET OF MUD, APPROXIMATELY 1 FOOT OF FREE OIL.
Remarks: TEMPERATURE 96 DEGREES.
A-23'
Initial BHP 53# IFP 10# - 10# FFP 21# - 21# Final BHP 43#
Hydrastatic Press. 1724# - 1682# Mud Wt. 10 Vis. 63 Water Loss 11 cc
Extra Equipment _____ Jars _____ Straddle Packer _____ Safety Joint _____
Tester Carl Skinner Approved By Richard M. Foley Ticket No. 2384

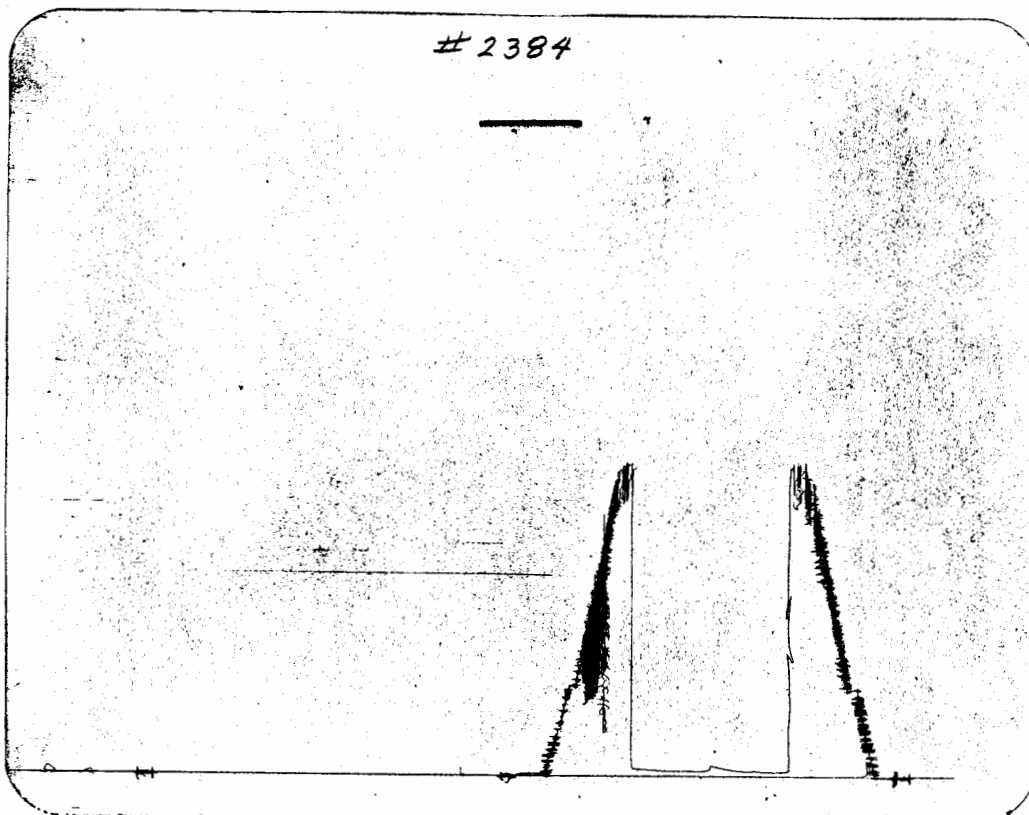

Telephone
(316) 793-6347


Mobil — (316) 793-7859
Unit 7076



P. O. Box 1424
GREAT BEND, KANSAS 67530

NE NW1 NW1 Sec. 33-14s-12w
Russell Co., Ks

Company ICER ADDIS Date 7-23-79
Address 5307 E. CENTRAL WICHITA, KANSAS 67207
Drilling Contractor DUKE DRILLING COMPANY Rig No. 2
Lease, Well No. KEPKA #1 County RUSSELL Sec. 33 Twp. 14 Rng. 12
Size Hole 7 7/8 Size Pipe 4 1/2 E.X.H. - 4 1/2 F.H. Size Tool 3 1/2
Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 F.H.
Interval Tested 2962' to 2980' Total Depth 2980'
Test No. 5 Successful No. 4 Misrun No.
Formation Tested KC Time Packer Set 2:50 P.M. Time Tool Opened 2:55 P.M.
Tool Open 30-30 Min. Initial Shut-in-Time 30 Min. Final Shut-in-Time 30 Min.
Blow FIRST OPENING: STRONG BLOW OFF BOTTOM OF BUCKET IN 1 MINUTE.
SECOND OPENING: STRONG BLOW.
Recovery 330 FEET OF CLEAN OIL, 180 FEET OF MUDDY OIL, 180 FEET OF MUDDY WATER.
Remarks: GAS TO SURFACE IN 55 MINUTES. TOO SMALL TO MEASURE. 37 GRAVITY @ 86 DEGREES,
CARR. 35.1 A-18'
Initial BHP 877# IFP 53# - 160# FFP 212# - 266# Final BHP 866#
Hydrastatic Press. 1787# - 1734# Mud Wt. 10 Vis. 42 Water Loss 14.8 cc
Extra Equipment Jars Straddle Packer Safety Joint
Tester Carl Skinner Approved By Richard M. Foley Ticket No. 2385

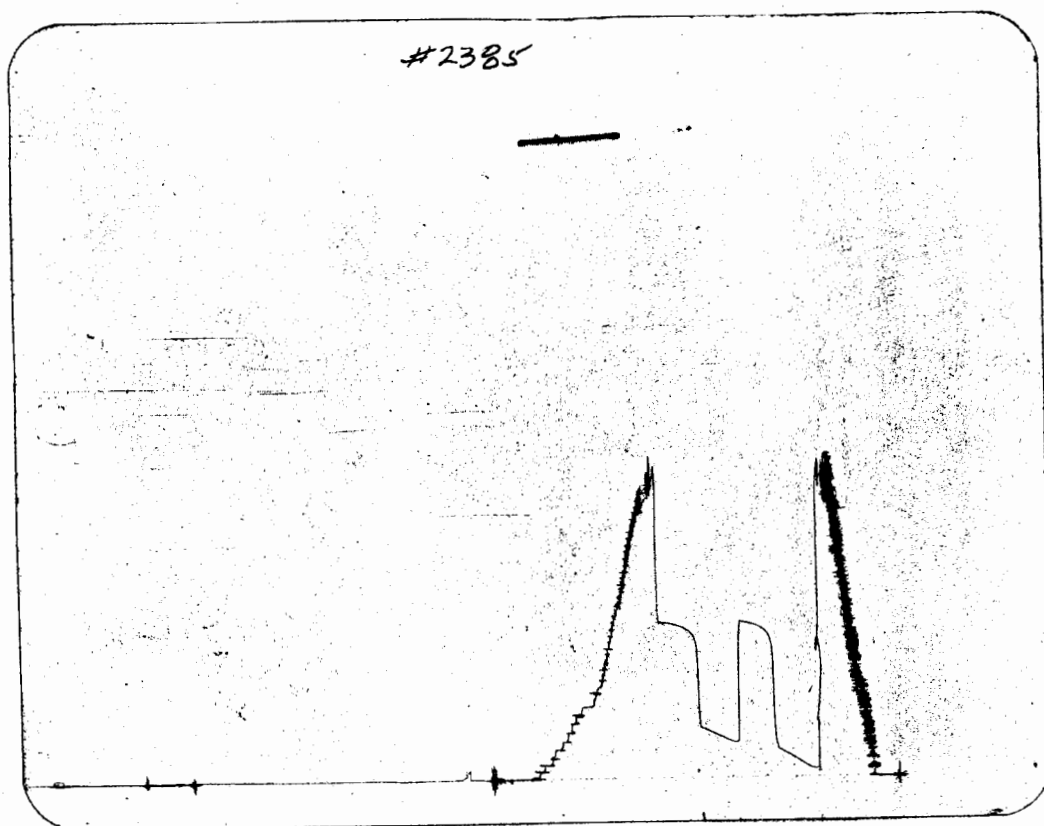

Telephone
(316) 793-6347

Mobil — (316) 793-7859
Unit 7076



P. O. Box 1424
GREAT BEND, KANSAS 67530

NE NW NW Sec. 33-14s-124
Russell Co., Ks

Company ICER ADDIS Date 7-24-79
Address 5307 E. CENTRAL WICHITA, KANSAS 67207
Drilling Contractor DUKE DRILLING COMPANY Rig No. 2
Lease, Well No. KEPKA #1 County RUSSELL Sec. 33 Twp. 14 Rng. 12
Size Hole 7 7/8 Size Pipe 4 1/2 E.X.H. - 4 1/2 F.H. Size Tool 3 1/2
Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 F.H.
Interval Tested 3151' to 3170' Total Depth 3170'
Test No. 6 Successful No. 6 Misrun No. 0
Formation Tested MARM. Time Packer Set 8:45 P.M. Time Tool Opened 8:50 P.M.
Tool Open 30-20 Min. Initial Shut-in-Time 20 Min. Final Shut-in-Time 20 Min.
Blow FIRST OPENING: WEAK 20 MINUTE BLOW.
SECOND OPENING: NO BLOW.
Recovery APPROXIMATELY 10 FEET OF MUD WITH A FEW SPECKS OF OIL.
Remarks:

Initial BHP 43 PSI IFP 32-32 PSI FFP 32-32 PSI Final BHP 43 PSI
Hydrastatic Press. 1891-1828 PSI Mud Wt. 10.2 Vis. 42 Water Loss 16.4 cc
Extra Equipment _____ Jars _____ Straddle Packer _____ Safety Joint _____
Tester Donald Scott Approved By Richard Foley Ticket No. 2386

