


FORMATION TEST REPORT



Home Office:

Wichita, Kansas 67201

P.O. Box 1599

Phone (316) 262-5861

COMPANY BALCRON OIL COMPANY LEASE & WELL NO. 36-16-20W SEC. 36 TWP. 16s RGE. 20 TEST NO. 1 DATE 9/5/89

28661

WESTERN TESTING CO. INC.
SUBSURFACE PRESSURE SURVEY

DATE	:	9/5/89	TICKET	:	14712
CUSTOMER	:	BALCRON OIL COMPANY	LEASE	:	BALDWIN
WELL	:	4-36	TEST:	:	1
ELEVATION	:		GEOLOGIST	:	JAY D. S.
SECTION	:	36	FORMATION	:	LANSING
RANGE	:	20W	TOWNSHIP	:	16S
GAUGE SN#	:	13629	COUNTY	:	RUSH
			STATE	:	KANSAS
			RANGE	:	4425
			CLOCK	:	12

INTERVAL FROM	:	3478	TO	:	3503	TOTAL DEPTH	:	3503
DEPTH OF SELECTIVE ZONE	:							
PACKER DEPTH	:	3473	SIZE	:	6.75			
PACKER DEPTH	:	3478	SIZE	:	6.75			
PACKER DEPTH	:		SIZE	:				
PACKER DEPTH	:		SIZE	:				

DRILLING CON.	:	DUKE DRILLING RIG #4			
MUD TYPE	:	CHEMICAL	VISCOSITY	:	61
WEIGHT	:	9.	WATER LOSS (CC)	:	10.
CHLORIDES (PPM)	:	11000			
JARS-MAKE	:	WTC	SERIAL NUMBER	:	408
DID WELL FLOW ?	:	NO	REVERSED OUT ?	:	NO

DRILL COLLAR LENGTH	:	220	FT	I.D. inch	:	2.20
WEIGHT PIPE LENGTH	:	0	FT	I.D. inch	:	0.00
DRILL PIPE LENGTH	:	3229	FT	I.D. inch	:	3.80
TEST TOOL LENGTH	:	29	FT	TOOL SIZE	:	5.50
ANCHOR LENGTH	:	25	FT	ANCHOR SIZE	:	5.50
SURFACE CHOKE SIZE	:	.75	IN	BOTTOM CHOKE SIZE	:	.75
MAIN HOLE SIZE	:	7.875	IN	TOOL JOINT SIZE	:	4.5 XH

BLOW COMMENT #1	:	INITIAL FLOW PERIOD-STRONG-BOTTOM OF BUCKET
BLOW COMMENT #2	:	IN 30 MINUTES.
BLOW COMMENT #3	:	FINAL FLOW PERIOD-STRONG-12" IN BUCKET
BLOW COMMENT #4	:	

WESTERN TESTING CO. INC.
WICHITA-KANSAS

Pressure Transient Report

COMPANY : BALCRON OIL COMPANY
RIG : RUSH-KANSAS
FIELD : BALDWIN
WELL : 4-36
DATE : 9/5/89
GAUGE NO : 13629

OPERATIONAL COMMENTS

RECOVERED : 310 FT OF: MUDDY SALT WATER W/ SHOW
RECOVERED : 0 FT OF: OF OIL ON TOP
RECOVERED : 0 FT OF: CHLORIDES 58000 PPM

Total Barrels Fluid = 2.30
Total Fluid Prod Rate = 54.22 BFPD
Indicated Wtr Rate = 27.11 BWPD

REMARK 1 :
REMARK 2 :
REMARK 3 :
REMARK 4 :

SET PACKER(S) : 2:10 PM

TIME STARTED OFF BOTTOM : 5:10 PM

WELL TEMPERATURE : 112

INITIAL HYDROSTATIC PRESSURE

(A) 1693

INITIAL FLOW PERIOD MIN: 31

(B) 65 PSI TO (C) : 109

INITIAL CLOSED IN PERIOD MIN: 65

(D) 653

FINAL FLOW PERIOD MIN: 30

(E) 178 PSI TO (F) : 178

FINAL CLOSED IN PERIOD MIN: 65

(G) 644

FINAL HYDROSTATIC PRESSURE

(H) 1649

RELEASED

1002 8 1991

FROM CONFIDENTIAL

COMPANY : BALCRON OIL COMPANY
WELL : 4-36
GAUGE # : 13629
DATE : 5/ 9/98

FIELD : BALDWIN
JOB # : 14712
DEPTH : 3503
TEST :

DATA No.	REAL TIME HR:MN:SS	ELAPSE TIME DELTA HOURS	PRESSURE PSIG	TEMP DEG F	DELTA P P1-P(1-1)

INITIAL FLOW PERIOD					
2	2:10: 0	0.000	65.000	112.00	0.000
3	2:11: 0	0.017	65.000	112.00	0.000
4	2:11:59	0.033	65.000	112.00	0.000
5	2:13: 0	0.050	65.000	112.00	0.000
6	2:14: 0	0.067	65.000	112.00	0.000
7	2:14:59	0.083	65.000	112.00	0.000
8	2:16: 0	0.100	65.000	112.00	0.000
9	2:17: 0	0.117	65.000	112.00	0.000
10	2:17:59	0.133	65.000	112.00	0.000
11	2:19: 0	0.150	65.000	112.00	0.000
12	2:20: 0	0.167	65.000	112.00	0.000
13	2:20:59	0.183	65.000	112.00	0.000
14	2:22: 0	0.200	65.000	112.00	0.000
15	2:23: 0	0.217	65.000	112.00	0.000
16	2:23:59	0.233	65.000	112.00	0.000
17	2:25: 0	0.250	69.000	112.00	4.000
18	2:26: 0	0.267	73.000	112.00	4.000
19	2:26:59	0.283	76.000	112.00	3.000
20	2:28: 0	0.300	78.000	112.00	2.000
21	2:29: 0	0.317	80.000	112.00	2.000
22	2:29:59	0.333	83.000	112.00	3.000
23	2:31: 0	0.350	86.000	112.00	3.000
24	2:32: 0	0.367	89.000	112.00	3.000
25	2:32:59	0.383	93.000	112.00	4.000
26	2:34: 0	0.400	95.000	112.00	2.000
27	2:35: 0	0.417	97.000	112.00	2.000
28	2:35:59	0.433	99.000	112.00	2.000
29	2:37: 0	0.450	101.000	112.00	2.000
30	2:38: 0	0.467	103.000	112.00	2.000
31	2:38:59	0.483	105.000	112.00	2.000
32	2:40: 0	0.500	107.000	112.00	2.000
33	2:41: 0	0.517	109.000	112.00	2.000
INITIAL SHUT-IN PERIOD					
34	2:42: 0	0.533	145.000	112.00	36.000
35	2:43: 0	0.550	216.000	112.00	71.000
36	2:44: 0	0.567	272.000	112.00	56.000
37	2:45: 0	0.583	379.000	112.00	107.000
38	2:46: 0	0.600	438.000	112.00	59.000
39	2:47: 0	0.617	475.000	112.00	37.000
40	2:48: 0	0.633	503.000	112.00	28.000
41	2:49: 0	0.650	527.000	112.00	24.000
42	2:50: 0	0.667	542.000	112.00	15.000
43	2:51: 0	0.683	551.000	112.00	9.000
44	2:52: 0	0.700	560.000	112.00	9.000
45	2:53: 0	0.717	568.000	112.00	8.000
46	2:54: 0	0.733	575.000	112.00	7.000
47	2:55: 0	0.750	581.000	112.00	6.000
48	2:56: 0	0.767	588.000	112.00	7.000
49	2:57: 0	0.783	592.000	112.00	4.000
50	2:58: 0	0.800	596.000	112.00	4.000

COMPANY : BALCRON OIL COMPANY
WELL : 4-36
GAUGE # : 13629
DATE : 5/ 9/98

FIELD : BALDWIN
JOB # : 14712
DEPTH : 3503
TEST :

DATA No.	REAL TIME HR:MN:SS	ELAPSE TIME DELTA HOURS	PRESSURE PSIG	TEMP DEG F	DELTA P P1-P(1-1)
51	2:59: 0	0.817	600.000	112.00	4.000
52	3: 0: 0	0.833	601.000	112.00	1.000
53	3: 1: 0	0.850	604.000	112.00	3.000
54	3: 2: 0	0.867	607.000	112.00	3.000
55	3: 3: 0	0.883	609.000	112.00	2.000
56	3: 4: 0	0.900	611.000	112.00	2.000
57	3: 5: 0	0.917	615.000	112.00	4.000
58	3: 6: 0	0.933	617.000	112.00	2.000
59	3: 7: 0	0.950	619.000	112.00	2.000
60	3: 8: 0	0.967	621.000	112.00	2.000
61	3: 9: 0	0.983	623.000	112.00	2.000
62	3:10: 0	1.000	625.000	112.00	2.000
63	3:11: 0	1.017	627.000	112.00	2.000
64	3:12: 0	1.033	629.000	112.00	2.000
65	3:13: 0	1.050	631.000	112.00	2.000
66	3:14: 0	1.067	632.000	112.00	1.000
67	3:15: 0	1.083	633.000	112.00	1.000
68	3:16: 0	1.100	634.000	112.00	1.000
69	3:17: 0	1.117	635.000	112.00	1.000
70	3:18: 0	1.133	636.000	112.00	1.000
71	3:19: 0	1.150	637.000	112.00	1.000
72	3:20: 0	1.167	638.000	112.00	1.000
73	3:21: 0	1.183	639.000	112.00	1.000
74	3:22: 0	1.200	640.000	112.00	1.000
75	3:23: 0	1.217	641.000	112.00	1.000
76	3:24: 0	1.233	642.000	112.00	1.000
77	3:25: 0	1.250	643.000	112.00	1.000
78	3:26: 0	1.267	644.000	112.00	1.000
79	3:27: 0	1.283	645.000	112.00	1.000
80	3:28: 0	1.300	646.000	112.00	1.000
81	3:29: 0	1.317	647.000	112.00	1.000
82	3:30: 0	1.333	648.000	112.00	1.000
83	3:31: 0	1.350	649.000	112.00	1.000
84	3:32: 0	1.367	650.000	112.00	1.000
85	3:33: 0	1.383	651.000	112.00	1.000
86	3:34: 0	1.400	652.000	112.00	1.000
87	3:35: 0	1.417	652.000	112.00	0.000
88	3:36: 0	1.433	652.000	112.00	0.000
89	3:37: 0	1.450	652.000	112.00	0.000
90	3:38: 0	1.467	652.000	112.00	0.000
91	3:39: 0	1.483	652.000	112.00	0.000
92	3:40: 0	1.500	652.000	112.00	0.000
93	3:41: 0	1.517	652.000	112.00	0.000
94	3:42: 0	1.533	653.000	112.00	1.000
95	3:43: 0	1.550	653.000	112.00	0.000
96	3:44: 0	1.567	653.000	112.00	0.000
97	3:45: 0	1.583	653.000	112.00	0.000
98	3:46: 0	1.600	653.000	112.00	0.000
FINAL FLOW PERIOD					
99	3:47: 0	1.617	178.000	112.00	-475.000
100	3:47: 0	1.617	178.000	112.00	0.000
101	3:47:59	1.633	178.000	112.00	0.000

COMPANY : BALCRON OIL COMPANY
WELL : 4-36
GAUGE # : 13629
DATE : 5/ 9/98

FIELD : BALDWIN
JOB # : 14712
DEPTH : 3503
TEST :

DATA No.	REAL TIME HR:MN:SS	ELAPSE TIME DELTA HOURS	PRESSURE PSIG	TEMP DEG F	DELTA P P1-P(1-1)
102	3:49: 0	1.650	178.000	112.00	0.000
103	3:50: 0	1.667	178.000	112.00	0.000
104	3:50:59	1.883	178.000	112.00	0.000
105	3:52: 0	1.700	178.000	112.00	0.000
106	3:53: 0	1.717	178.000	112.00	0.000
107	3:53:59	1.733	178.000	112.00	0.000
108	3:55: 0	1.750	178.000	112.00	0.000
109	3:56: 0	1.767	178.000	112.00	0.000
110	3:56:59	1.783	178.000	112.00	0.000
111	3:58: 0	1.800	178.000	112.00	0.000
112	3:59: 0	1.817	178.000	112.00	0.000
113	3:59:59	1.833	178.000	112.00	0.000
114	4: 1: 0	1.850	178.000	112.00	0.000
115	4: 2: 0	1.867	178.000	112.00	0.000
116	4: 2:59	1.883	178.000	112.00	0.000
117	4: 4: 0	1.900	178.000	112.00	0.000
118	4: 5: 0	1.917	178.000	112.00	0.000
119	4: 5:59	1.933	178.000	112.00	0.000
120	4: 7: 0	1.950	178.000	112.00	0.000
121	4: 8: 0	1.967	178.000	112.00	0.000
122	4: 8:59	1.983	178.000	112.00	0.000
123	4:10: 0	2.000	178.000	112.00	0.000
124	4:11: 0	2.017	178.000	112.00	0.000
125	4:11:59	2.033	178.000	112.00	0.000
126	4:13: 0	2.050	178.000	112.00	0.000
127	4:14: 0	2.067	178.000	112.00	0.000
128	4:14:59	2.083	178.000	112.00	0.000
129	4:16: 0	2.100	178.000	112.00	0.000
FINAL SHUT-IN PERIOD					
130	4:17: 0	2.117	219.000	112.00	41.000
131	4:17:59	2.133	270.000	112.00	51.000
132	4:18:59	2.150	341.000	112.00	71.000
133	4:20: 0	2.167	402.000	112.00	61.000
134	4:20:59	2.183	449.000	112.00	47.000
135	4:21:59	2.200	487.000	112.00	38.000
136	4:23: 0	2.217	508.000	112.00	21.000
137	4:23:59	2.233	527.000	112.00	19.000
138	4:25: 0	2.250	538.000	112.00	11.000
139	4:26: 0	2.267	548.000	112.00	10.000
140	4:26:59	2.283	557.000	112.00	9.000
141	4:28: 0	2.300	562.000	112.00	5.000
142	4:29: 0	2.317	569.000	112.00	7.000
143	4:29:59	2.333	575.000	112.00	6.000
144	4:31: 0	2.350	580.000	112.00	5.000
145	4:32: 0	2.367	583.000	112.00	3.000
146	4:32:59	2.383	587.000	112.00	4.000
147	4:33:59	2.400	589.000	112.00	2.000
148	4:35: 0	2.417	593.000	112.00	4.000
149	4:35:59	2.433	597.000	112.00	4.000
150	4:36:59	2.450	599.000	112.00	2.000
151	4:38: 0	2.467	601.000	112.00	2.000
152	4:38:59	2.483	604.000	112.00	3.000

COMPANY : BALCRON OIL COMPANY
WELL : 4-36
GAUGE # : 13629
DATE : 5/ 9/98

FIELD : BALDWIN
JOB # : 14712
DEPTH : 3503
TEST :

DATA No.	REAL TIME HR:MN:SS	ELAPSE TIME DELTA HOURS	PRESSURE PSIG	TEMP DEG F	DELTA P P1-P(1-1)
153	4:40: 0	2.500	607.000	112.00	3.000
154	4:41: 0	2.517	610.000	112.00	3.000
155	4:41:59	2.533	613.000	112.00	3.000
156	4:43: 0	2.550	615.000	112.00	2.000
157	4:44: 0	2.567	617.000	112.00	2.000
158	4:44:59	2.583	619.000	112.00	2.000
159	4:46: 0	2.600	321.000	112.00	-298.000
160	4:47: 0	2.617	623.000	112.00	302.000
161	4:47:59	2.633	624.000	112.00	1.000
162	4:48:59	2.650	626.000	112.00	2.000
163	4:50: 0	2.667	627.000	112.00	1.000
164	4:50:59	2.683	628.000	112.00	1.000
165	4:51:59	2.700	629.000	112.00	1.000
166	4:53: 0	2.717	630.000	112.00	1.000
167	4:53:59	2.733	631.000	112.00	1.000
168	4:55: 0	2.750	632.000	112.00	1.000
169	4:56: 0	2.767	633.000	112.00	1.000
170	4:58:59	2.783	634.000	112.00	1.000
171	4:58: 0	2.800	635.000	112.00	1.000
172	4:59: 0	2.817	635.000	112.00	0.000
173	4:59:59	2.833	635.000	112.00	0.000
174	5: 1: 0	2.850	636.000	112.00	1.000
175	5: 2: 0	2.867	636.000	112.00	0.000
176	5: 2:59	2.883	636.000	112.00	0.000
177	5: 3:59	2.900	637.000	112.00	1.000
178	5: 5: 0	2.917	638.000	112.00	1.000
179	5: 5:59	2.933	638.000	112.00	0.000
180	5: 6:59	2.950	638.000	112.00	0.000
181	5: 8: 0	2.967	638.000	112.00	0.000
182	5: 8:59	2.983	639.000	112.00	1.000
183	5:10: 0	3.000	640.000	112.00	1.000
184	5:11: 0	3.017	641.000	112.00	1.000
185	5:11:59	3.033	642.000	112.00	1.000
186	5:13: 0	3.050	643.000	112.00	1.000
187	5:14: 0	3.067	644.000	112.00	1.000
188	5:14:59	3.083	644.000	112.00	0.000
189	5:16: 0	3.100	644.000	112.00	0.000
190	5:17: 0	3.117	644.000	112.00	0.000
191	5:17:59	3.133	644.000	112.00	0.000
192	5:18:59	3.150	644.000	112.00	0.000
193	5:20: 0	3.167	644.000	112.00	0.000
194	5:20:59	3.183	644.000	112.00	0.000

WESTERN-TESTING CO. INC.

BALCROW
DST 1

JKT 14712


13629

I

RELEASED

JUN 28

FROM CONFIDENTIAL

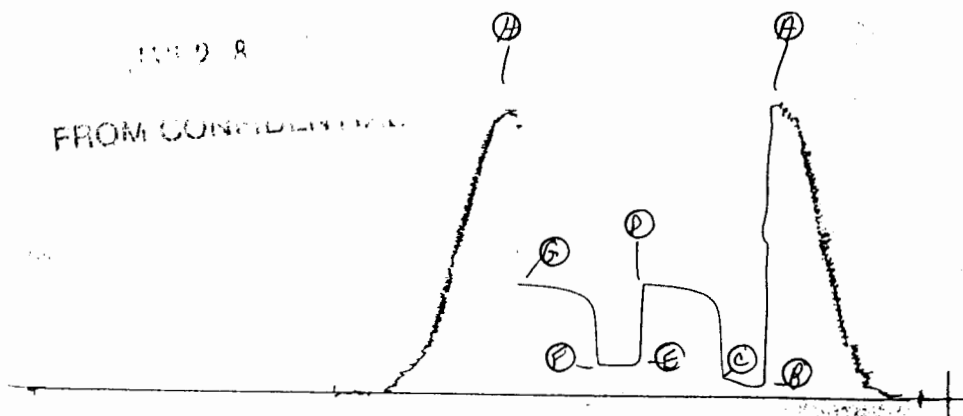

Inside Recorder

BALCROW
DST 1

JKT 14712


1566

O

RELEASED

JUN 28 1991

FROM CONFIDENTIAL

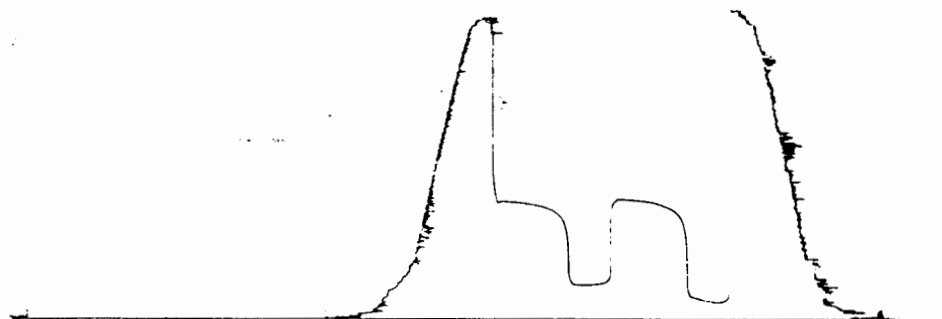

Outside Recorder

BALCROW
DST 1

1566


7KT 14712

O

RELEASED

JAN 28 1991

FROM CONFIDENTIAL

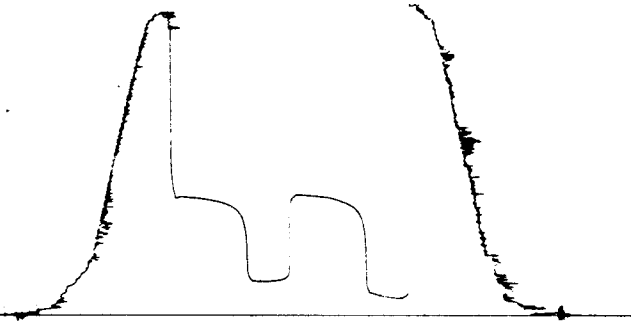

BALCROW
DST 1

13629


7KT 14712

I


RELEASED

JAN 28

FROM CONFIDENTIAL

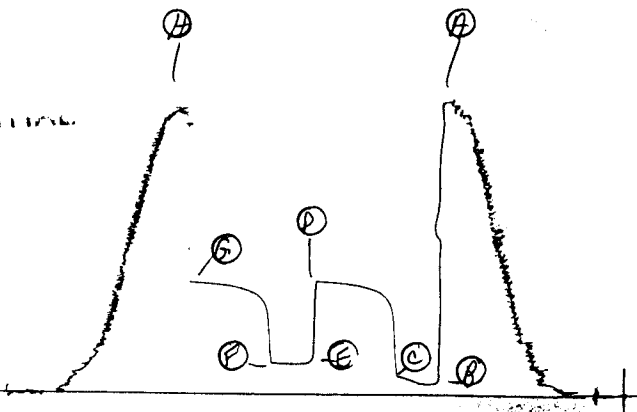

FORMATION TEST REPORT



Home Office:

Wichita, Kansas 67201

P.O. Box 1599

Phone (316) 262-5861

COMPANY BALCRON OIL COMPANY

LEASE & WELL NO.

BALDWIN #4-36

SEC. 36

TWP. 16S

RGE. 20W

TEST NO. 2

DATE 9/7/89

SW (NW) NE

WESTERN TESTING CO. INC.
SUBSURFACE PRESSURE SURVEY

DATE : 9/7/89	TICKET : 14713
CUSTOMER : BALCRON OIL COMPANY	LEASE : BALDWIN
WELL : #4-36 TEST: 2	GEOLOGIST : J. D. S.
ELEVATION :	FORMATION : ARBUCKLE
SECTION : 36	TOWNSHIP : 16S
RANGE : 20W	STATE : KANSAS
COUNTY : RUSH	CLOCK : 12
GAUGE SN# : 13629	RANGE : 4425

INTERVAL FROM : 3828	TO : 3870	TOTAL DEPTH : 3870
DEPTH OF SELECTIVE ZONE :		
PACKER DEPTH : 3823	SIZE : 6.75	
PACKER DEPTH : 3828	SIZE : 6.75	
PACKER DEPTH :	SIZE :	
PACKER DEPTH :	SIZE :	

DRILLING CON. : DUKE DRILLING RIG #4		
MUD TYPE : CHEMICAL	VISCOSITY : 52	
WEIGHT : 9.2	WATER LOSS (CC) : 11.4	
CHLORIDES (PPM) : 10000		
JARS-MAKE : WTC	SERIAL NUMBER : 408	
DID WELL FLOW ? : NO	REVERSED OUT ? : NO	

DRILL COLLAR LENGTH : 210 FT	I.D. inch : 2.20	
WEIGHT PIPE LENGTH : 0 FT	I.D. inch : 0.00	
DRILL PIPE LENGTH : 3589 FT	I.D. inch : 3.80	
TEST TOOL LENGTH : 29 FT	TOOL SIZE : 5.50	
ANCHOR LENGTH : 42 FT	ANCHOR SIZE : 5.50	
SURFACE CHOKE SIZE : .75 IN	BOTTOM CHOKE SIZE : .75	
MAIN HOLE SIZE : 7.875 IN	TOOL JOINT SIZE : 4.5 XH	

BLOW COMMENT #1 : INITIAL FLOW PERIOD-NONE-FLUSHED TOOL-BRIEF SURGE

BLOW COMMENT #2 :

BLOW COMMENT #3 :

BLOW COMMENT #4 :

RECOVERED : 5 FT OF: DRILLING MUD

Total Barrels Fluid = 0.02
Total Fluid Prod Rate = 2.26 BFPD
Indicated Wtr Rate = 0.23 BWPD

REMARK 1 : TIGHT HOLE
REMARK 2 :
REMARK 3 :
REMARK 4 :

SET PACKER(S) : 5:50 AM

TIME STARTED OFF BOTTOM : 6:35 AM

WELL TEMPERATURE : 116

INITIAL HYDROSTATIC PRESSURE

(A) 2010

INITIAL FLOW PERIOD MIN: 15

(B) 94 PSI TO (C) : 65

INITIAL CLOSED IN PERIOD MIN: 29

(D) 122

FINAL FLOW PERIOD MIN: 0

(E) 0 PSI TO (F) : 0

FINAL CLOSED IN PERIOD MIN: 0

(G) 0

FINAL HYDROSTATIC PRESSURE

(H) 1926

RELEASED

JAN 28 1991

FROM CONFIDENTIAL

WESTERN TESTING CO. INC.
WICHITA-KANSAS

Pressure Transient Report

COMPANY : BALCRON OIL COMPANY
RIG : RUSH-KANSAS
FIELD : BALDWIN
WELL : #4-36
DATE : 9/7/89
GAUGE NO : 13629

OPERATIONAL COMMENTS : TIGHT HOLE

COMPANY : BALCRON OIL COMPANY
WELL : #4-36
GAUGE # : 13629
DATE : 7/ 9/89

FIELD : BALDWIN
JOB # : 14713
DEPTH : 3870
TEST :

DATA No.	REAL TIME HR:MN:SS	ELAPSE TIME DELTA HOURS	PRESSURE PSIG	TEMP DEG F	DELTA P P _i -P _(i-1)
INITIAL FLOW PERIOD					
2	5:50: 0	0.000	94.000	116.00	0.000
3	5:51: 0	0.017	91.000	116.00	-3.000
4	5:51:59	0.033	83.000	116.00	-8.000
5	5:53: 0	0.050	74.000	116.00	-9.000
6	5:54: 0	0.067	67.000	116.00	-7.000
7	5:54:59	0.083	64.000	116.00	-3.000
8	5:56: 0	0.100	60.000	116.00	-4.000
9	5:57: 0	0.117	58.000	116.00	-2.000
10	5:57:59	0.133	106.000	116.00	48.000
11	5:59: 0	0.150	98.000	116.00	-8.000
12	6: 0: 0	0.167	84.000	116.00	-14.000
13	6: 0:59	0.183	77.000	116.00	-7.000
14	6: 2: 0	0.200	73.000	116.00	-4.000
15	6: 3: 0	0.217	70.000	116.00	-3.000
16	6: 3:59	0.233	67.000	116.00	-3.000
17	6: 5: 0	0.250	65.000	116.00	-2.000
INITIAL SHUT-IN PERIOD					
18	6: 6: 0	0.267	64.000	116.00	-1.000
19	6: 6:59	0.283	63.000	116.00	-1.000
20	6: 8: 0	0.300	62.000	116.00	-1.000
21	6: 9: 0	0.317	62.000	116.00	0.000
22	6: 9:59	0.333	62.000	116.00	0.000
23	6:11: 0	0.350	62.000	116.00	0.000
24	6:12: 0	0.367	62.000	116.00	0.000
25	6:12:59	0.383	62.000	116.00	0.000
26	6:14: 0	0.400	62.000	116.00	0.000
27	6:15: 0	0.417	62.000	116.00	0.000
28	6:15:59	0.433	62.000	116.00	0.000
29	6:17: 0	0.450	62.000	116.00	0.000
30	6:18: 0	0.467	64.000	116.00	2.000
31	6:18:59	0.483	66.000	116.00	2.000
32	6:20: 0	0.500	68.000	116.00	2.000
33	6:21: 0	0.517	70.000	116.00	2.000
34	6:21:59	0.533	74.000	116.00	4.000
35	6:23: 0	0.550	77.000	116.00	3.000
36	6:24: 0	0.567	79.000	116.00	2.000
37	6:24:59	0.583	82.000	116.00	3.000
38	6:26: 0	0.600	86.000	116.00	4.000
39	6:27: 0	0.617	89.000	116.00	3.000
40	6:27:59	0.633	92.000	116.00	3.000
41	6:29: 0	0.650	96.000	116.00	4.000
42	6:30: 0	0.667	102.000	116.00	6.000
43	6:30:59	0.683	105.000	116.00	3.000
44	6:32: 0	0.700	112.000	116.00	7.000
45	6:33: 0	0.717	115.000	116.00	3.000
46	6:33:59	0.733	122.000	116.00	7.000

WESTERN TESTING CO. INC.

13629

KT 14712

BALCROW
DST 2


7

10

RELEASED

JAN 28 1991

FROM CONFIDENTIAL

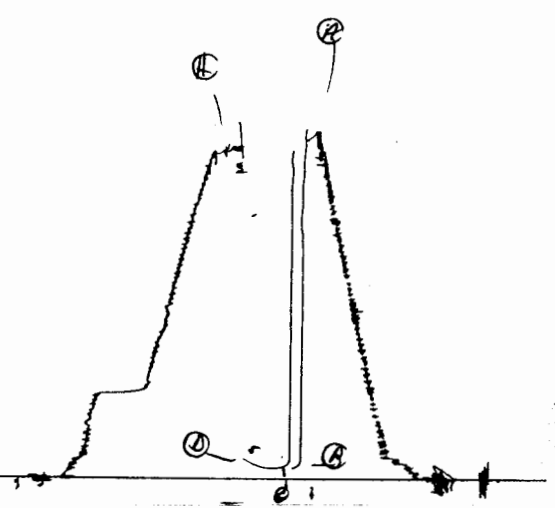

1566

KT 14712

BALCROW
DST 2

0

10

RELEASED

JAN 28 1991

FROM CONFIDENTIAL

