

Telephone
(316) 793-6347


Mobil — (316) 793-7859
Unit 7076



P. O. Box 1424
GREAT BEND, KANSAS 67530

Company PETROLEUM ENERGY, INC. Date 10-25-81
Address ONE TWENTY BLDG. - SUITE 710 WICHITA, KANSAS 67202
Drilling Contractor WHITE & ELLIS Rig No. 2
Lease, Well No. POPPELREITER # 1 County BARTON Sec. 8 Twp. 17 Rng. 11
Size Hole 7 7/8 Size Pipe 4 1/2 F.H. Size Tool 3 1/2 F.H.
Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 F.H.
Interval Tested 3209 to 3240 Total Depth 3240
Test No. 1 Successful No. 1 Misrun No. 0
Formation Tested KC Time Packer Set 10:35 P.M. Time Tool Opened 10:40 P.M.
Tool Open 30-30 Min. Initial Shut-in-Time 30 Min. Final Shut-in-Time 30 Min.
Blow VERY WEAK 11 MINUTE BLOW ON FIRST OPENING.
NO BLOW ON SECOND OPENING.
Recovery 15 FEET OF DRILLING MUD WITH A COUPLE OF SPECKS OF OIL ON TOP OF TOOL.
Remarks: FLUSHED TOOL ON SECOND OPENING
TEMPERATURE 104 DEGREES.
Initial BHP 399 # IFP 97 # - 97 # FFP 108 # - 97 # Final BHP 140 #
Hydrastatic Press. 1725 # - 1715 # Mud Wt. 9.8 Vis. 42 Water Loss 15 cc
Extra Equipment _____ Jars _____ Straddle Packer _____ Safety Joint _____
Tester GARY A. SHOOK Approved By JIM MUSGROVE Ticket No. 602

#602

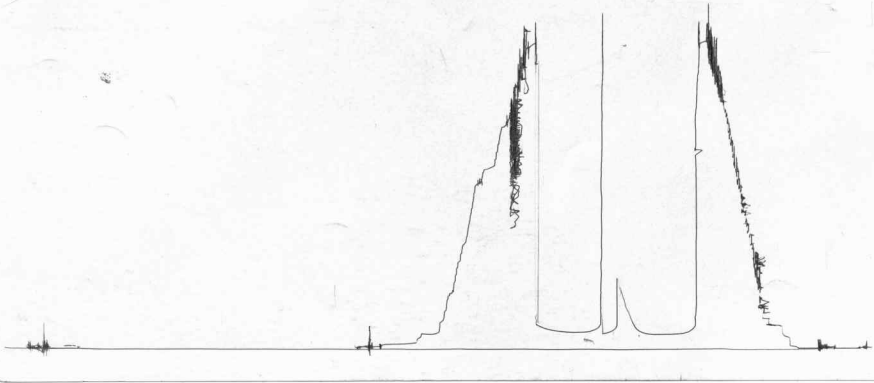

Telephone
(316) 793-6347

Mobil — (316) 793-7859
Unit 7076



P. O. Box 1424
GREAT BEND, KANSAS 67530

Company PETROLEUM ENERGY, INC. Date 10-26-81
Address ONE TWENTY BLDG. - SUITE 710 WICHITA, KANSAS 67202
Drilling Contractor WHITE & ELLIS Rig No. 2
Lease, Well No. POPPELREITER # 1 County BARTON Sec. 8 Twp. 17 Rng. 11
Size Hole 7 7/8 Size Pipe 4 1/2 F.H. Size Tool 3 1/2 F.H.
Size Packer 6 3/4 x 2 7/8 x 30 Size Choke 5/8 Size Anchor 4 1/2 F.H.
Interval Tested 3294 to 3306 Total Depth 3306
Test No. 2 Successful No. 2 Misrun No. 0
Formation Tested ARB Time Packer Set 5:25 P.M. Time Tool Opened 5:30 P.M.
Tool Open 45-45 Min. Initial Shut-in-Time 45 Min. Final Shut-in-Time 45 Min.
Blow OFF BOTTOM OF BUCKET IN 12 MINUTES ON FIRST OPENING.
STRONG BLOW ON SECOND OPENING.
Recovery 180 FEET OF GAS IN PIPE, 510 FEET OF CLEAN GASSY OIL, 270 FEET OF MUDDY
GASSY OIL. 780 FEET TOTAL.
Remarks: 40° GRAVITY.
TEMPERATURE 112 DEGREES
Initial BHP 1101 # IFP 119 # - 216 # FFP 269 # - 313 # Final BHP 1091 #
Hydrastatic Press. 1779 # - 1736 # Mud Wt. 9.7 Vis. 40 Water Loss 12.2 cc
Extra Equipment _____ Jars _____ Straddle Packer _____ Safety Joint _____
Tester GARY A. SHOOK Approved By JIM MUSGROVE Ticket No. 603

603

