

DATE 3-4-68

TICKET NO 1127

COMPANY American Oil Exploration Co. CONTRACTOR Co. tools

WELL NO. 1 LEASE Rathbum COUNTY Ellsworth SEC. 16 RG. 8 TWP. 17

TEST NO. 1 HOLE SIZE 7 7/8" PACKER SIZE 6 3/4" TOOL JOINT 4 1/2" PH

ANCHOR LENGTH 30' AIR CHAMBER LENGTH --- SIZE CHOKE 1/2"

FORMATION TESTED K.C. INTERVAL TESTED 2780'-2810' ELEVATION 1682' GL. T. D. 2810'

MUD WEIGHT 9.9 VISCOSITY 40 WATER LOSS 10.4cc


TOOL OPEN 75 min. IBHP SHUT IN TIME 45 min. FBHP SHUT IN TIME 45 min.

BLOW Very weak.

RECOVERY 30' of muddy water.

REMARKS _____

APPROVED BY Jack Maronde TESTER J. E. Parks

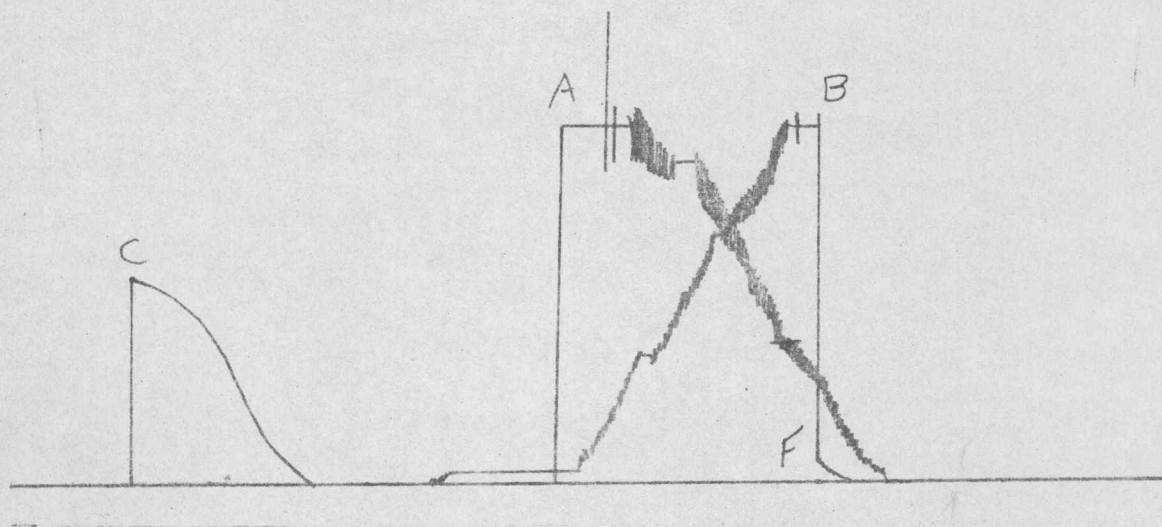

PRESSURE READINGS	
A. Initial Hyd. Pressure	1535
B. Final Hyd. Pressure	1535
C. Initial BHP	905
D. Initial Flow Pressure	0
E. Final Flow Pressure	0
F. Final BHP	98
