

SUPERIOR TESTERS ENTERPRISES L.L.C. 20-18s-26w

1(800)792-6902


15-135-24574

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: ROBERT F. HEMBREE Lease & Well No. PARKER#1 Test #: 1 Date: 12-8-06 SEC. 20 TWP. 18 RGE. 26

Temperature / Pressure Data

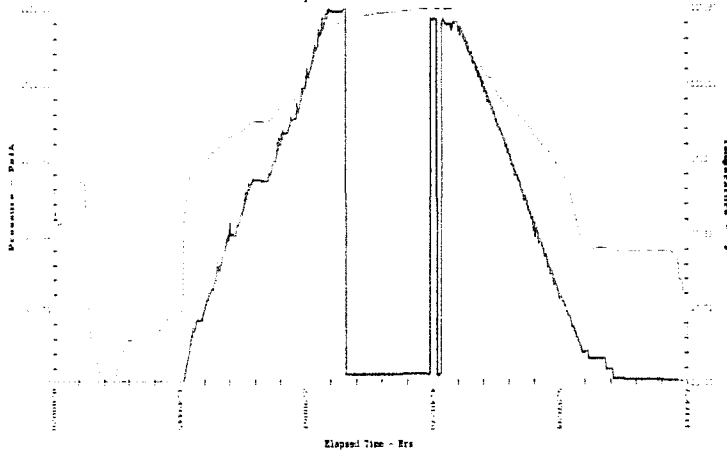

1	Initial Hydrostatic Pressure	2217
2	Initial Flow Pressure	72
3	Final Initial Flow Pressure	70
4	Initial Shut-In Pressure	76
5	Initial Final Flow Pressure	
6	Final Flow Pressure	
7	Final Shut-In Pressure	
8	Final Hydrostatic Pressure	2163

Maximum Temperature 119

GENERAL INFORMATION

COMPANY NAME ROBERT F. HEMBREE

TEST DATE 12/8/06

SECTION-TOWN-RANGE 20-18-26

STATE KANSAS

COUNTY NESS

ELEVATION GROUND LEVEL 2653

COMPANY REPRESENTATIVE KIM SHOEMAKER

LEASE AND WELL NUMBER PARKER#1

FORMATION TESTED MARM

DRILL STEM TEST NUMBER 1

REPORT NUMBER #####

ELEVATION KELLY BUSHINGS 2653

TESTING ENGINEER DAVID NICHOLS

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4416

TEST INTERVAL (to) 4453

ANCHOR LENGTH 37

TOTAL DEPTH (ft) 4453

TOP PACKER DEPTH 4411

BOTTOM PACKER DEPTH 4416

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

INITIAL OPEN

TOOL OPEN (from) 12:00

TOOL OPEN (to) 12:30

DURATION (min.) 30

FINAL OPEN

TOOL OPEN (from) 1:00

TOOL OPEN (to) 1:10

DURATION (min.) 10

INITIAL SHUT-IN

TOOL CLOSED (from) 12:30

TOOL CLOSED (to) 1:00

DURATION (min.) 30

FINAL SHUT-IN

TOOL CLOSED (from) 1:10

TOOL CLOSED (to)

DURATION (min.)

INITIAL FLOW

WEAK BLOW BUILT TO 1/2 INCH INTO WATER DIED

FINAL FLOW

NO BLOW FLUSH TOOL WEAK BLOW DIED AFTER 1 MIN

RECEIVED
KANSAS CORPORATION COMMISSION
JAN 24 2007
CONSERVATION DIVISION
WICHITA, KS


SUPERIOR TESTERS ENTERPRISES L.L.C.

DRILL STEM TEST REPORT

1(800)792-6902

GREAT BEND, KANSAS 67530

Temperature / Pressure Data

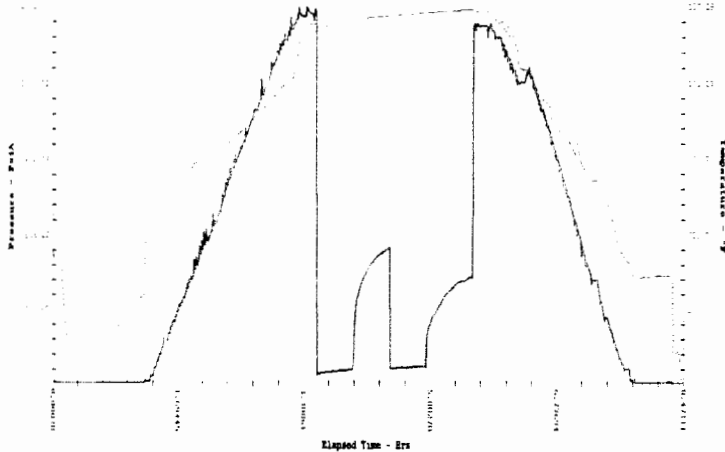

1	Initial Hydrostatic Pressure	2341
2	Initial Flow Pressure	81
3	Final Initial Flow Pressure	112
4	Initial Shut-In Pressure	871
5	Initial Final Flow Pressure	117
6	Final Flow Pressure	130
7	Final Shut-In Pressure	694
8	Final Hydrostatic Pressure	2257

Maximum Temperature 127

GENERAL INFORMATION

COMPANY NAME ROBERT F. HEMBREE

TEST DATE 12/10/06

SECTION-TOWN-RANGE 20-18-26

STATE KANSAS

COUNTY NESS

ELEVATION GROUND LEVEL 2635

COMPANY REPRESENTATIVE KIM SHOEMAKER

LEASE AND WELL NUMBER PARKER#1

FORMATION TESTED CHERKEESANDS MISS

DRILL STEM TEST NUMBER 2

REPORT NUMBER ####

ELEVATION KELLY BUSHINGS 2635

TESTING ENGINEER DAVID NICHOLS

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4595

TEST INTERVAL (to) 4648

ANCHOR LENGTH 53

TOTAL DEPTH (ft) 4648

TOP PACKER DEPTH 4590

BOTTOM PACKER DEPTH 4595

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

INITIAL OPEN

TOOL OPEN (from) 4:15

TOOL OPEN (to) 4:45

DURATION (min.) 30

FINAL OPEN

TOOL OPEN (from) 5:15

TOOL OPEN (to) 5:45

DURATION (min.) 30

INITIAL SHUT-IN

TOOL CLOSED (from) 4:45

TOOL CLOSED (to) 5:15

DURATION (min.) 30

FINAL SHUT-IN

TOOL CLOSED (from) 5:45

TOOL CLOSED (to) 6:15

DURATION (min.) 30

INITIAL FLOW

WEAK BLOW 1 INCH INTO WATER

FINAL FLOW

NO BLOW

RECEIVED
KANSAS CORPORATION COMMISSION

JAN 24 2007

CONSERVATION DIVISION
WICHITA, KS

26 Company: ROBERT F. HEMBREE Lease & Well No. PARKER#1 Test #: 2 Date: 12-10-06 SEC. 20 TWP. 18 RGE.
