

15-101-21905

35-185-28W

SUPERIOR TESTERS ENTERPRISES INC.


1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Company: SEDONA OIL & GAS CORP
SEC. 35 TWP. 18 RGE. 28

Lease & Well No: SHAPLAND LIVING TRUST #1 Test #: 1 Date: 5-16-06

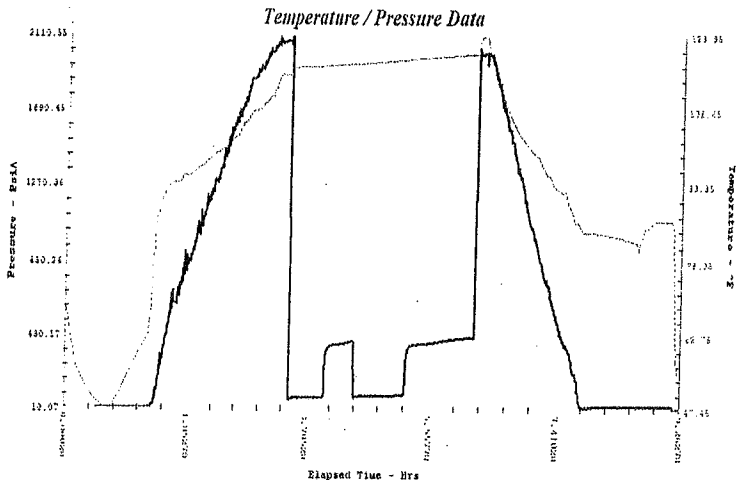

1	Initial Hydrostatic Pressure	2110
2	Initial Flow Pressure	66
3	Final Initial Flow Pressure	80
4	Initial Shut-In Pressure	400
5	Initial Final Flow Pressure	81
6	Final Flow Pressure	93
7	Final Shut-In Pressure	425
8	Final Hydrostatic Pressure	1949
	Maximum Temperature	123

GENERAL INFORMATION

COMPANY NAME SEDONA OIL & GAS	LEASE AND WELL NUMBER SHAPLAND LIVING
TEST DATE 5/16/06	FORMATION TESTED "K" ZONE
SECTION-TOWN-RANGE 35-18-28W	DRILL STEM TEST NUMBER 1
STATE KANSAS	REPORT NUMBER 14262
COUNTY LANE	ELEVATION KELLY BUSHINGS 2708
ELEVATION GROUND LEVEL 2703	TESTING ENGINEER JARED SCHECK
COMPANY REPRESENTATIVE		

TOOL SETTING INFORMATION

TEST INTERVAL (From) 4190	TOP PACKER DEPTH 4185
TEST INTERVAL (to) 4216	BOTTOM PACKER DEPTH 4190
ANCHOR LENGTH 26	NUMBER OF PACKERS 2
TOTAL DEPTH (ft) 4216	PACKER SIZE 6 3/4
		HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 5:04A	TOOL OPEN (from) 6:04
INITIAL OPEN TOOL OPEN (to) 5:34	FINAL OPEN TOOL OPEN (to) 6:49
DURATION (min.) 30	DURATION (min.) 45
TOOL CLOSED (from) 5:34	TOOL CLOSED (from) 6:49
INITIAL SHUT-IN TOOL CLOSED (to) 6:04	FINAL SHUT-IN TOOL CLOSED (to) 7:49
DURATION (min.) 30	DURATION (min.) 60

INITIAL FLOW

WEAK BUT BUILDING BLOW BUILT 1/12 INCHES INTO BUCKET IN 30 MIN

FINAL FLOW

WEAK BUT BUILDING BLOW BUILT 1 1/2 INCHES INTO BUCKET IN 45 MIN

FEET OF Recovery	RECOVERY DESCRIPTION	% GAS	% OIL	% MUD	% WATER
1) 60	OIL CUT MUDDY WATER		12	85	3
2) 60	WATER CUT MUD			30	70
3)					
4)					
5)					
6)					

RECEIVED
KANSAS CORPORATION COMMISSION
APR 09 2007
CONSERVATION DIVISION
WICHITA, KS

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND ,KANSAS 67530 (800)792-6902

GENERAL INFORMATION

COMPANY NAME SEDONA OIL & GAS CORP
TEST DATE 5/16/06
SECTION-TOWN-RANGE 35-18S-28W
STATE KANSAS
COUNTY LANE
ELEVATION GROUND LEVEL 2703
COMPANY REPRESENTATIVE

LEASE AND WELL NUMBER SHAPLAND LIVING TRUST #1
FORMATION TESTED "K" ZONE
DRILL STEM TEST NUMBER 1
REPORT NUMBER 14262
ELEVATION KELLY BUSHINGS 2708
TESTING ENGINEER JARED SCHECK

EXTRA EQUIPMENT

JARS NO
SAFETY JOINT YES
ELECTRONIC RECORDER YES
CIRCULATING SUB NO
TOP RECORDER DEPTH 4212
RECORDER NUMBER 91981

EXTRA PACKER (3RD) NO
EXTRA PACKER (4TH) NO
STRADDLE NO
HOOK WALL NO
SAMPLER NO
BOTTOM RECORDER DEPTH 4213
RECORDER NUMBER 5463

200 MILES ROUND TRIP FROM GREAT BEND

WELL INFORMATION

DRILLING CONTRACTOR WARREN DRILLING RIG #8
DRILL PIPE LENGTH 3895
DRILL PIPE I.D. 3.8
TOOL JOINT SIZE 4 1/2 X.H.

DRILL COLLAR LENGTH 274.99
DRILL COLLAR I.D. 2.25
TOOL JOINT SIZE 4 1/2 X.H.

WEIGHT PIPE LENGTH
WEIGHT PIPE I.D. 2.25
TOOL JOINT SIZE 4 1/2 X.H.
CHLORIDES-PITS 7,800


MUD WEIGHT #/GAL 9.2
VISCOSITY 43
WATER LOSS 8
CHLORIDES-DST 3,300
RESISTIVITY-DST @ 42,000

COMMENTS

RECEIVED
KANSAS CORPORATION COMMISSION

APR 09 2007

Temperature / Pressure Data

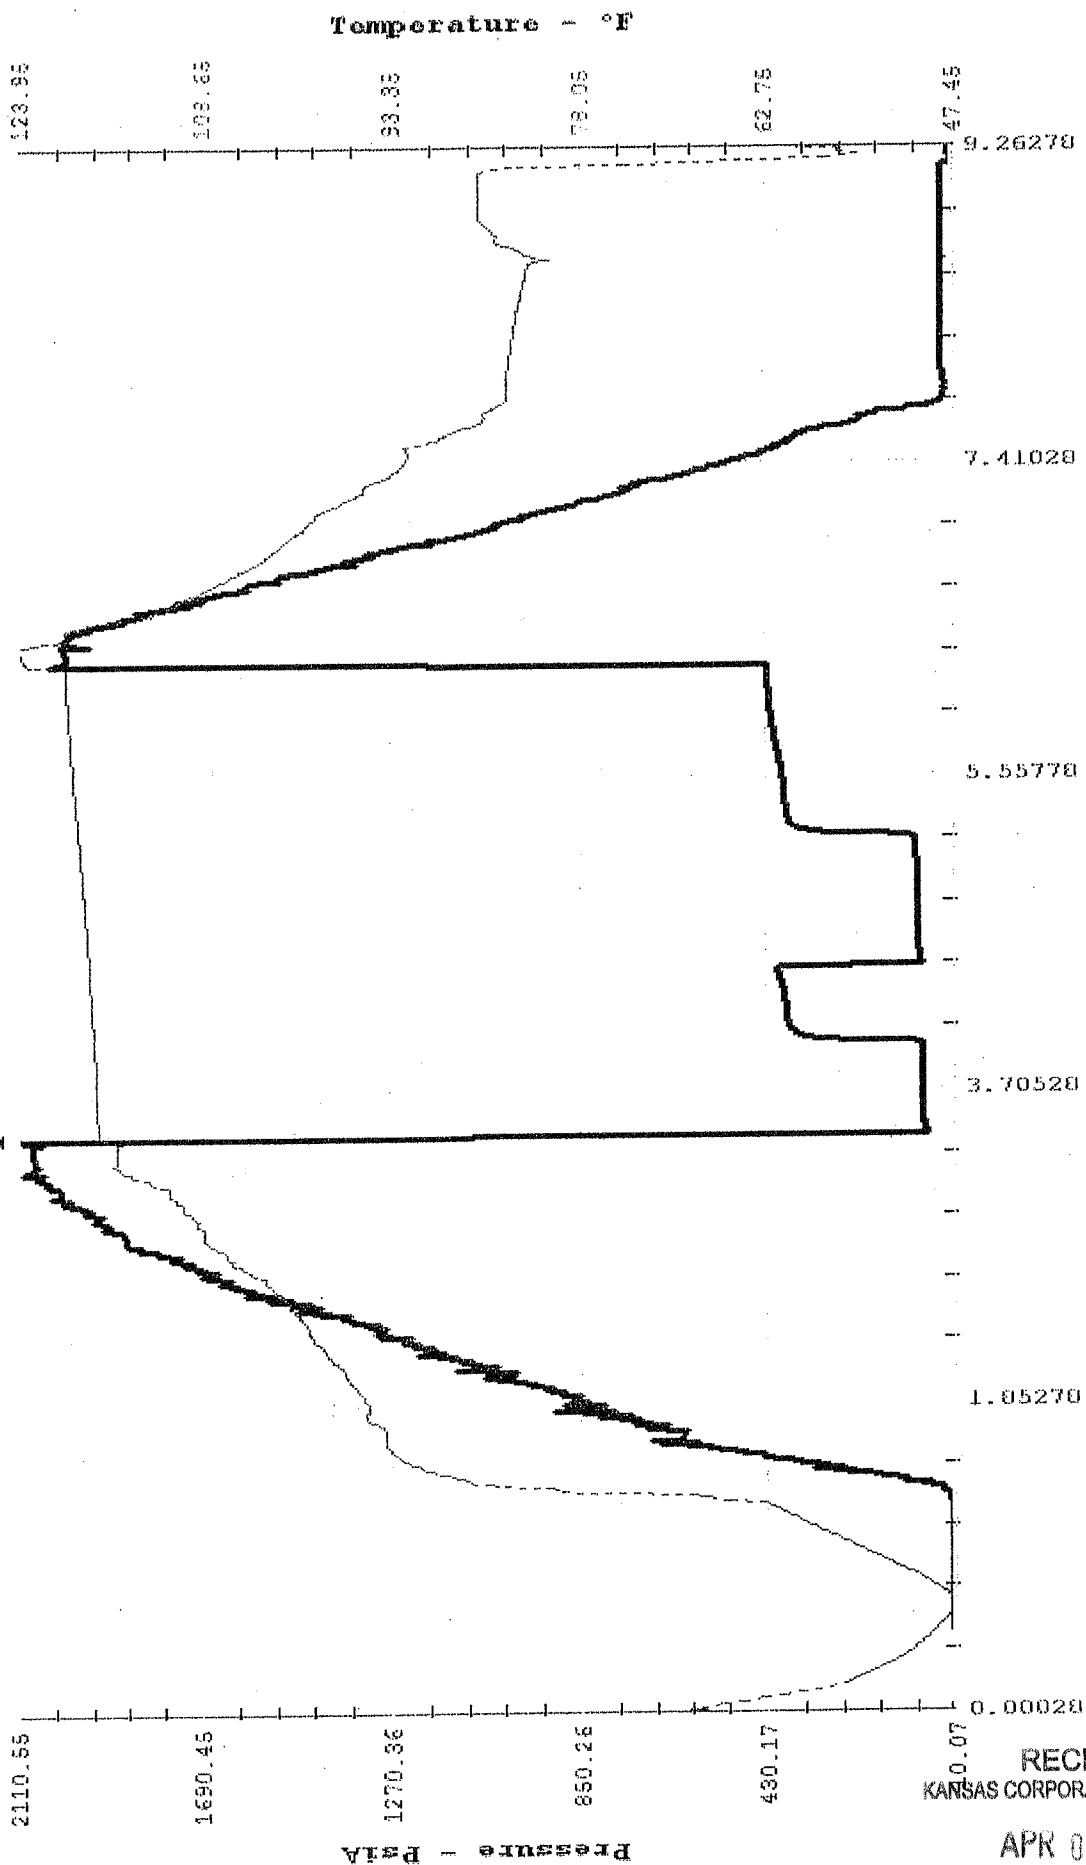

Elapsed Time - Hrs

5-16-06

35-18-28W

SHAPLAND LIVING TRUST

SEDONA OIL & GAS CORP

RECEIVED
KANSAS CORPORATION COMMISSION

APR 9 2007

CONSERVATION DIVISION
WICHITA, KS
