

Date 6-27-64

Ticket No. 4060

Company Hinkle Oil Co. Contractor Graves Drlg. CO.

Well No. A 3 Lease Disque County Rice Sec. Rg. Tw.

Test No. 1 Size Hole 7 7/8 Tool Joint 4 1/2

Anchor Length 70' Depth Well 3270'

Interval Tested From 3200' To 3270'

Size Choke 5/8 Tool Open 60 min.

IBHP Shut in time 30 min. FBHP Shut in time 30 min.

Blow Strong thruout test

Recovery 960' Muddy salt water

Remarks Temp 112

Approved Miller Tester Williams

Sun OILWELL CEMENTING, INC.
POST OFFICE BOX 89
HAYS, KANSAS

4060

A. Initial Hyd. Pressure	1811#
B. Final Hyd. Pressure	
C. Initial BHP	1021#
D. Initial Flow Pressure	91#
E. Final Flow Pressure	500#
F. Final BHP	977#

Date 6-28-64

Ticket No. 4061

Company Hinkle Oil Co. Contractor Graves Drlg. Co.

Well No. A3 Lease Disque County Rice Sec. Rg. Tw.

Test No. 2 Size Hole 7 7/8 Tool Joint 4 1/2

Anchor Length 4' Depth Well 3280'

Interval Tested From 3276' To 3280'

Size Choke 5/8 Tool Open 60 min.

IBHP Shut in time 30 min. FBHP Shut in time 30 min.


Blow Very strong 30 min decreasing to fair

Recovery 1750' Gas in pipe 1330' Clean gassy oil 120' Muddy oil

Remarks Temp 113

Approved Miller Tester Williams

Sun OILWELL CEMENTING, INC.
POST OFFICE BOX 89
HAYS, KANSAS

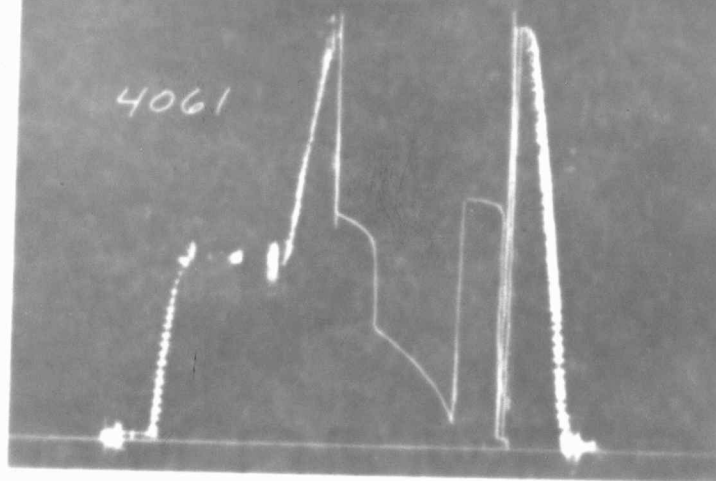

A. Initial Hyd. Pressure	1820#
B. Final Hyd. Pressure	
C. Initial BHP	1064#
D. Initial Flow Pressure	66#
E. Final Flow Pressure	500#
F. Final BHP	968#
