

Date 2-2-64

Ticket No. 3774

Company Hinkle Oil Co. Contractor Graves Drlg Co.

Well No. 1 Lease Disque County Rice Sec. 1 Rg. 8 Tw. 19

Test No. 1 Size Hole 7 7/8 Tool Joint 4 1/2

Anchor Length 42' Depth Well 3188'

Interval Tested From 3146' To 3188'

Size Choke 5/8 Tool Open 30 min.

IBHP Shut in time 30 min. FBHP Shut in time 30 min.

Blow Weak blow for 5 min. flushed tool in 20 min good surge

Recovery 4' Drlg. mud with few spk. oil


Remarks \_\_\_\_\_

Approved Howell Tester Branham

*Sun* OILWELL CEMENTING, INC.

POST OFFICE BOX 89  
HAYS, KANSAS

3774

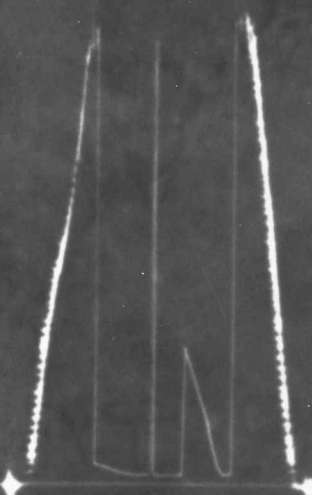

|                          |       |
|--------------------------|-------|
| A. Initial Hyd. Pressure | 1817# |
| B. Final Hyd. Pressure   |       |
| C. Initial BHP           | 529#  |
| D. Initial Flow Pressure | 38#   |
| E. Final Flow Pressure   | 38#   |
| F. Final BHP             | 76#   |

Date 2-2-64

Ticket No. 3775

Company Hinkle Oil Co. Contractor Graves Drlg Co.

Well No. 1 Lease Disque County Rice Sec. 1 Rg. 8 Tw. 19

Test No. 2 Size Hole 7 7/8 Tool Joint 4 1/2

Anchor Length 5' Depth Well 3255'

Interval Tested From 3250' To 3255'

Size Choke 5/8 Tool Open 40 min.


IBHP Shut in time 30 min. FBHP Shut in time 30 min.

Blow Weak blow for 5 min. flushed tool 30 min. good surge

Recovery 10' Drlg. mud No show of oil

Remarks \_\_\_\_\_

Approved Howell Tester Branham

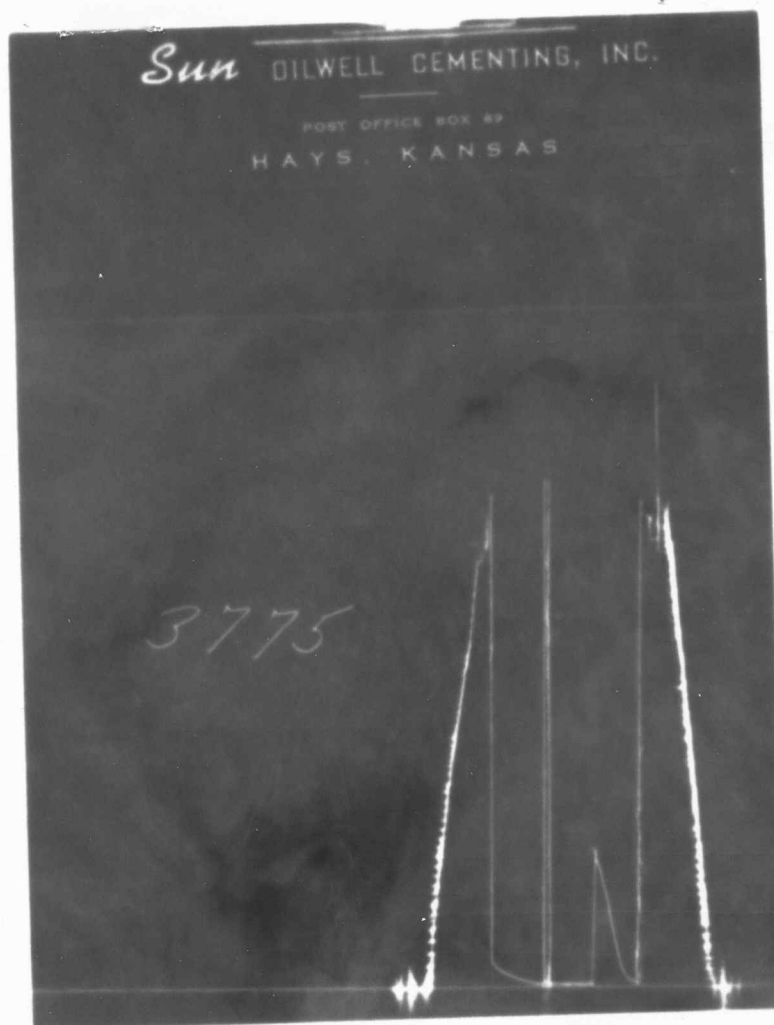

|                          |       |
|--------------------------|-------|
| A. Initial Hyd. Pressure | 1927# |
| B. Final Hyd. Pressure   |       |
| C. Initial BHP           | 536#  |
| D. Initial Flow Pressure | 15#   |
| E. Final Flow Pressure   | 15#   |
| F. Final BHP             | 76#   |

Date 2-3-64

Ticket No. 3776

Company Hinkle Oil Co. Contractor Graves Drlg. Co.

Well No. 1 Lease Disque County Rice Sec. 1 Rg. 8 Tw. 19

Test No. 3 Size Hole 7 7/8 Tool Joint 4 1/2

Anchor Length 5' Depth Well 3260'

Interval Tested From 3255' To 3260'

Size Choke 5/8 Tool Open 90 min.

IBHP Shut in time 30 min. FBHP Shut in time 30 min.

Blow Weak increase to fair in 15 min. Fair increase to strong thruout test

Recovery 425' Gas in pipe 165' Gascut muddy oil

Remarks \_\_\_\_\_

Approved Howell Tester Branham

Sun OILWELL CEMENTING, INC.

POST OFFICE BOX 88

HAYS, KANSAS

3776

|                          |       |
|--------------------------|-------|
| A. Initial Hyd. Pressure | 1895# |
| B. Final Hyd. Pressure   | 1887# |
| C. Initial BHP           | 1027# |
| D. Initial Flow Pressure | 22#   |
| E. Final Flow Pressure   | 53#   |
| F. Final BHP             | 989#  |
