

SUPERIOR TESTERS, INC.

433 SOUTH WESTVIEW, DERBY, KANSAS

Date 11/28/74 Ticket No. 3354 Elevation 2323 KB

Total Depth 4300 Tested From 4272 To 4300 Formation Tested Fert Scott

Blow Fair blow through out test

Mud Wt. 9.8 Viscosity 42 Bottom Hole Temp 118

Size Bottom Choke 1/2" Size Top Choke 1/2"

Size Drill Pipe 4 1/8" PH Size Hole 7 7/8" Length Air Chamber - Ft.

Tool Open 45 Hr 45 Min Initial Shut in Time 45 Min Tool Open 45 Hr 45 Min Final Shut in Time 45 Min

Recovery <u>330' of muddy water with a few spots of oil, 120' of salt water</u>	Office Corrected Pressure Reading
	Initial Shut in Pressure <u>1310</u> Lbs
	Initial Flow Pressure <u>105</u> Lbs
	Final Flow Pressure <u>232</u> Lbs
	Final Shut in Pressure <u>1289</u> Lbs
	Initial Hydrostatic Pressure <u>2289</u> Lbs
	Final Hydrostatic Pressure <u>2267</u> Lbs

Remarks Tore up one button

Witnessed By Gene Falkowski


Tool Operator R. E. Budig

Location SW, SE 9-19S-24W Name of Lease Davidson Well No. 1 Test No. 1 F & M Oil Company, Inc. Company
 County Ness State Kansas

3354

3186

D. 25. 41

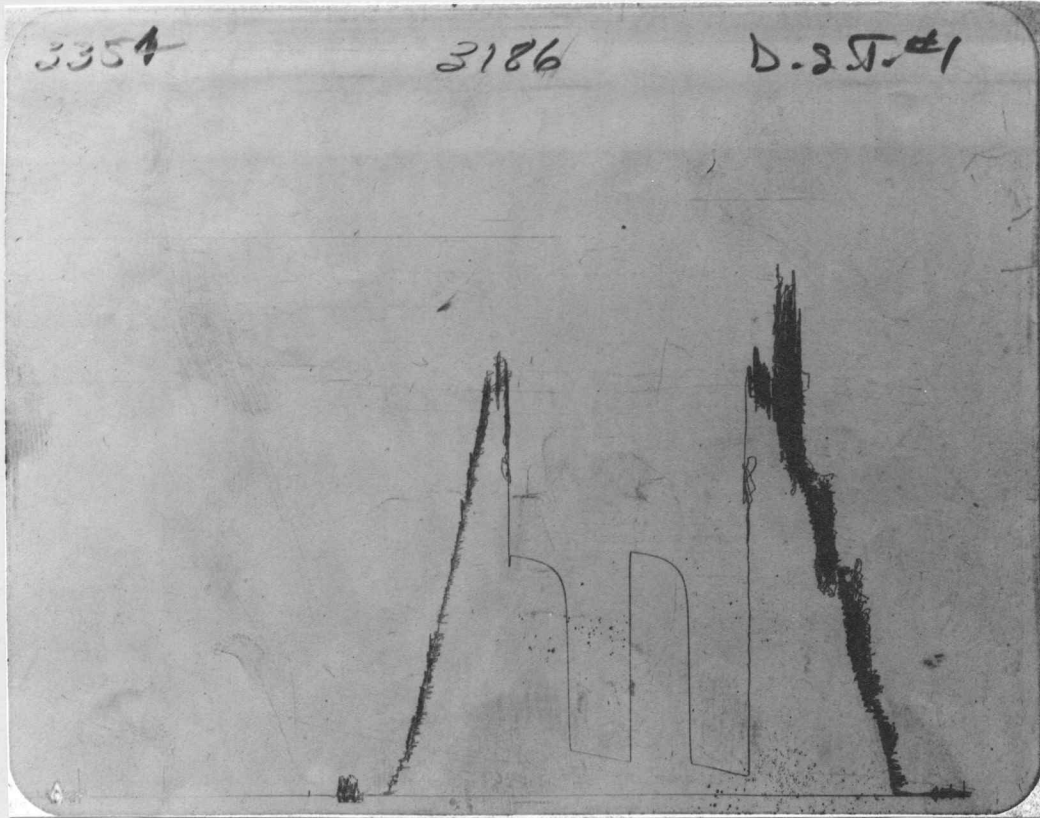

SUPERIOR TESTERS, INC.

433 SOUTH WESTVIEW, DERBY, KANSAS

Date 11/29/74 Ticket No. 3355 Elevation 2323 KB

Total Depth 4375 Tested From 4348 To 4375 Formation Tested Mississippi

Blow Weak blow for 5 minutes

Mud Wt. 9.8 Viscosity 42 Bottom Hole Temp 118

Size Bottom Choke 1/2" Size Top Choke 1/2"

Size Drill Pipe 4 1/8" FH Size Hole 7 7/8" Length Air Chamber - Ft.

Tool Open Hr 15 Min Initial Shut in Time 15 Min Tool Open Hr 15 Min Final Shut in Time 15 Min

Recovery <u>1' of mud</u>	Office Corrected Pressure Reading
	Initial Shut in Pressure <u>72</u> Lbs
	Initial Flow Pressure <u>64</u> Lbs
	Final Flow Pressure <u>64</u> Lbs
	Final Shut in Pressure <u>64</u> Lbs
	Initial Hydrostatic Pressure <u>2322</u> Lbs
	Final Hydrostatic Pressure <u>2304</u> Lbs

Remarks _____

Witnessed By Gene Falkowski


Tool Operator R. E. Budig

Location SW, SE 9-19S-24W Name of Lease Devison Well No. 1 County Ness Test No. 2 State Kansas F & W Oil Company, Inc. Company

3355

3875

D.S.T. #2

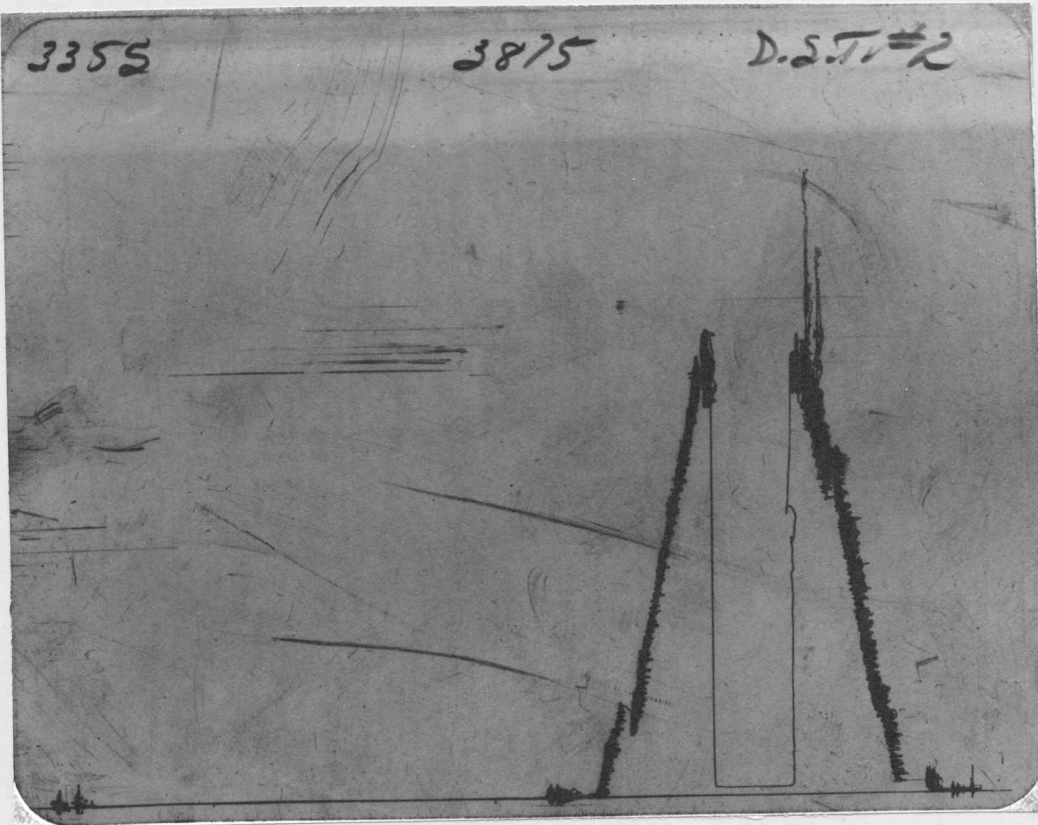

SUPERIOR TESTERS, INC.

433 SOUTH WESTVIEW, DERBY, KANSAS

Date 11/30/74 Ticket No. 3356 Elevation 2323 KB

Total Depth 4380 Tested From 4374 To 4380 . Formation Tested Mississippi

Blow Weak blow for 25 minutes

Mud Wt. 9.8 Viscosity 47 Bottom Hole Temp 118

Size Bottom Choke 1/2" Size Top Choke 1/2"

Size Drill Pipe 4 1/8" FH Size Hole 7 7/8" Length Air Chamber - Ft.

Tool Open 30 Hr 30 Min Initial Shut in Time 30 Min Tool Open 30 Hr 30 Min Final Shut in Time 30 Min

Recovery <u>30' watery mud, 60' of mud</u>	Office Corrected Pressure Reading
	Initial Shut in Pressure <u>800</u> Lbs
	Initial Flow Pressure <u>40</u> Lbs
	Final Flow Pressure <u>48</u> Lbs
	Final Shut in Pressure <u>-</u> Lbs
	Initial Hydrostatic Pressure <u>2332</u> Lbs
	Final Hydrostatic Pressure <u>2307</u> Lbs

Remarks Slid tool to bottom, tore up one packer

Witnessed By Hartman

Tool Operator R. E. Budig

Location SW, SEC 9-19S-24W

County Ness

State Kansas

Name of Lease DAVISON

Well No. 1 Test No. 3

Company F & M Oil Company, Inc.

