

15-009-24929

30-20s-11w


SUPERIOR TESTERS ENTERPRISES INC.

1(800)792-6902

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530

Temperature / Pressure Data

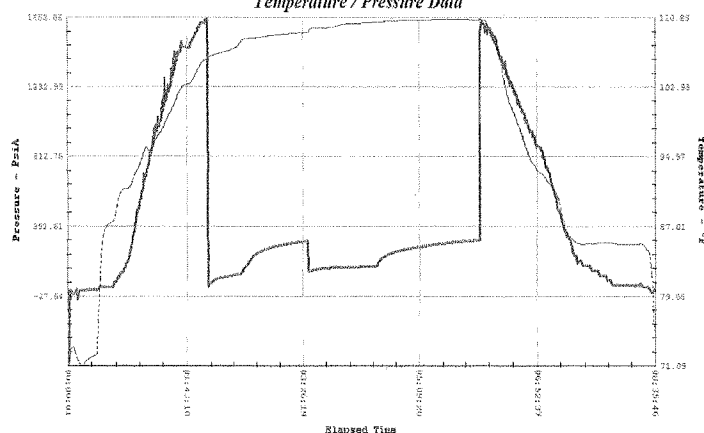

1	Initial Hydrostatic Pressure	1653
2	Initial Flow Pressure	26
3	Final Initial Flow Pressure	105
4	Initial Shut-In Pressure	304
5	Initial Final Flow Pressure	119
6	Final Flow Pressure	152
7	Final Shut-In Pressure	307
8	Final Hydrostatic Pressure	1582

Maximum Temperature 110

GENERAL INFORMATION

COMPANY NAMESHELBEY RESOURCES LLC

TEST DATE4/24/06

SECTION-TOWN-RANGE30-20-11W

STATEKANSAS

COUNTYBARTON

ELEVATION GROUND LEVEL1509

COMPANY REPRESENTATIVECLAYTON CAMMOZZ

LEASE AND WELL NUMBER SOEKEN 1-30

FORMATION TESTED ARBUCKLE

DRILL STEM TEST NUMBER 1

REPORT NUMBER 14257

ELEVATION KELLY BUSHINGS 1518

TESTING ENGINEER JARED SCHECK

TOOL SETTING INFORMATION

TEST INTERVAL (From) 3348

TEST INTERVAL (to) 3380

ANCHOR LENGTH 32

TOTAL DEPTH (ft) 3380

TOP PACKER DEPTH 3343

BOTTOM PACKER DEPTH 3348

NUMBER OF PACKERS 2

PACKER SIZE 6 3/4

HOLE SIZE 7 7/8

FLOW TIMES

TOOL OPEN (from) 11:26A

TOOL OPEN (to) 11:56A

DURATION (min.) 30

TOOL OPEN (from) 12:56

TOOL OPEN (to) 1:56

DURATION (min.) 60

TOOL CLOSED (from) 11:56

INITIAL SHUT-IN TOOL CLOSED (to) 12:56

DURATION (min.) 60

TOOL CLOSED (from) 1:56

TOOL CLOSED (to) 3:26P

DURATION (min.) 90

INITIAL FLOW

FAIR BLOW BUILT TO BOTTOM OF BUCKET IN 15 MIN

FINAL FLOW

FAIR BLOW BUILT TO BOTTOM OF BUCKET IN 35 MIN

FEET OF Recovery	RECOVERY DESCRIPTION	% GAS	% OIL	% MUD	% WATER
1) 60	SLIGHTLEY GASEY OIL CUT MUD	20	10	70	
2) 60	SLIGHLEY OILLEY CUT MUD	5	15	80	
3) 60	WATER CUT MUD			50	50
4) 60	WATER CUT MUD			40	60
5)					
6)					

RECEIVED

JAN 03 2016

KCC WICHITA
