

SUPERIOR TESTERS ENTERPRISES INC.

Great Bend, Kansas


CHART DATA

(316) 792-6902

15-185-23103

State KANSAS
 County STAFFORD
 Field

Test Date June 12, 2000
 Sec Town Range 12-21S-11W
 Report Number 11223

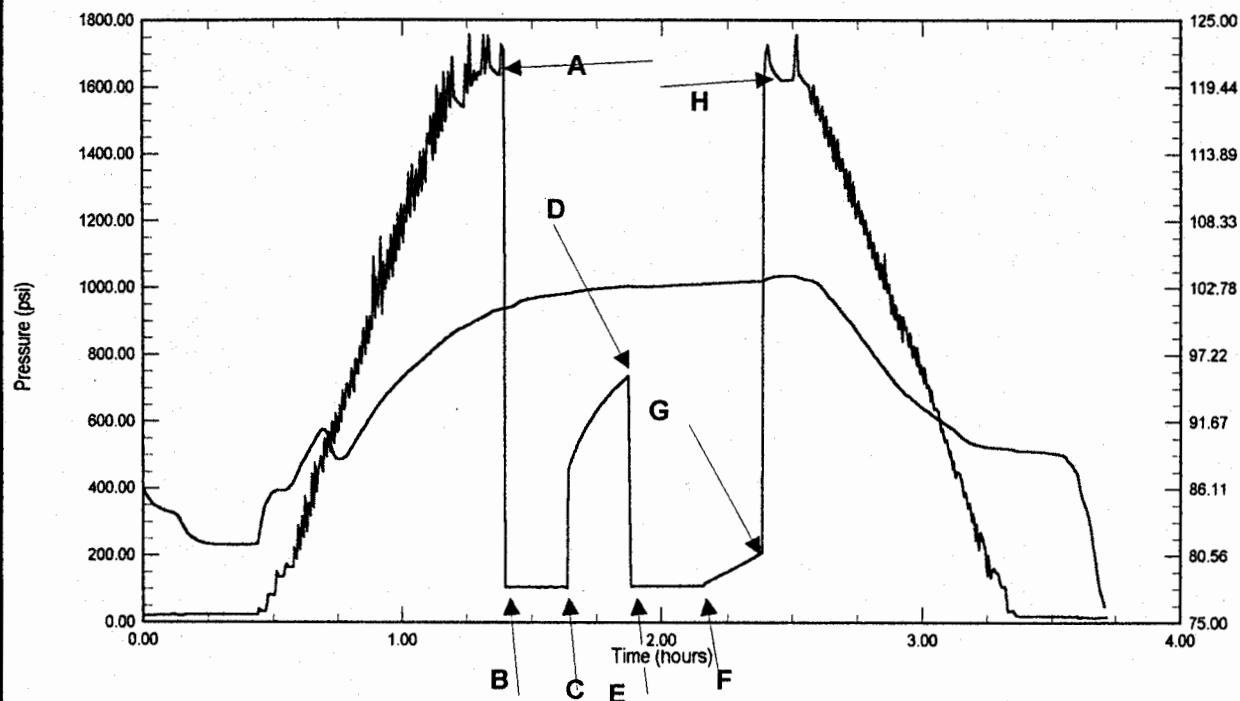

Field Reading

(A)	Initial Hydrostatic Pressure	1642
(B)	Initial Flow Pressure	107
(C)	Final Initial Flow Pressure	107
(D)	Initial Shut-In Pressure	736
(E)	Initial Final Flow Pressure	107
(F)	Final Flow Pressure	110
(G)	Final Shut-In Pressure	204
(H)	Final Hydrostatic Pressure	1620

RECEIVED
 STATE CORPORATION COMMISSION

APR - 4 2001

CONSERVATION DIVISION
 Wichita, Kansas

ELECTRONIC RECORDER DEPTH 3313 FT, RECORDER NUMBER 78225

Company: F.G.HOLL COMPANY L.L.C. Lease & Well No. SESSLER TRUST #1 Test # 1 Date: 6-12-2000
 SEC.12 TWP. 21S RGE.11W

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (316)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G.HOLL COMPANY L.L.C.	LEASE AND WELL NUMBER	SESSLER TRUST #1
TEST DATE	6/12/00	FORMATION TESTED	KANSAS CITY
SECTION-TOWN-RANGE	12-21S-11W	DRILL STEM TEST NUMBER	1
STATE	KANSAS	REPORT NUMBER	11223
COUNTY	STAFFORD	ELEVATION KELLY BUSHINGS	1760
ELEVATION GROUND LEVEL	1751	TESTING ENGINEER	GENE BUDIG
COMPANY REPRESENTATIVE	FRANK GREENBAUM		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	3265	TOP PACKER DEPTH	3260
TEST INTERVAL (to)	3320	BOTTOM PACKER DEPTH	3265
ANCHOR LENGTH	55	NUMBER OF PACKERS	2
TOTAL DEPTH (ft)	3320	PACKER SIZE	6 3/4
		HOLE SIZE	7 7/8

FLOW TIMES

INITIAL OPEN

TOOL OPEN (from) **12:45**
TOOL OPEN (to) **1:00**
DURATION (min.) **15**

INITIAL SHUT-IN

TOOL CLOSED (from) **1:00**
TOOL CLOSED (to) **1:15**
DURATION (min.) **15**

FINAL OPEN

TOOL OPEN (from) **1:15**
TOOL OPEN (to) **1:30**
DURATION (min.) **15**

FINAL SHUT-IN

TOOL CLOSED (from) **1:30**
TOOL CLOSED (to) **1:45**
DURATION (min.) **15**

PRESSURE READINGS

INITIAL HYDROSTATIC **1642**
INITIAL FLOW **107**
FINAL INITIAL FLOW **107**
INITIAL SHUT-IN **736**
INITIAL FINAL FLOW **107**
FINAL FLOW **110**
FINAL SHUT-IN **204**
FINAL HYDROSTATIC **1620**

MAXIMUM TEMPERATURE **104**

TOP RECORDER DEPTH **3313**
RECORDER NUMBER **78225**
BOTTOM RECORDER DEPTH **3317**
RECORDER NUMBER **13189**

INITIAL BLOW

WEAK BLOW FOR 7 MINUTES AND DIED

FINAL BLOW

NO BLOW

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOKWALL	NO
		SAMPLER	NO

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 6-12-2000 Location Shirley 1/4-1/4-1/4 1221-11W Elevation 1760 K.B. County Shelford
Company E.C. Hall Company L.L.C. Number of Copies 5

Charts Mailed to 6427 East Terrace P.O. Box 780167 Wichita Kansas 67228-0167

Drilling Contractor Strelise Drilling Rig #4

Length Drill Pipe 300' I.D. Drill Pipe 2.80 Tool Joint Size 4 1/2" X H.

Length Weight Pipe none I.D. Weight Pipe none Tool Joint Size none

Length Drill Collars 240 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2" X H.

Top Packer Depth 3260 Bottom Packer Depth 3265 Number of Packers 2 Packer Size 6 3/4"

TESTED FROM 3265 TO 3320 ANCHOR LENGTH 55 TOTAL DEPTH 3320 Hole Size 7 7/8

LEASE & WELL NO. Sessler Trust #1 FORMATION TESTED Kansas City TEST NO. 1

Mud Weight 9.3 Viscosity 40 Water Loss 10% Chlorides - Pits 5000 D.S.T.

Maximum Temp. 104 °F Initial Hydrostatic Pressure (A) 1642 P.S.I. Final Hydrostatic Pressure (H) 1630 P.S.I.

Tool Open I.F.P. from 12:45 a.m. to 1:00 a.m. 15 min

Tool Closed I.C.I.P. from 1:00 a.m. to 1:15 a.m. 15 min

Tool Open F.F.P. from 1:15 a.m. to 1:30 a.m. 15 min

Tool Closed F.C.I.P. from 1:30 a.m. to 1:45 a.m. 15 min

Initial Blow WORK blow for 7 minutes & DISC

Final Blow NO blow

Total Feet Recovered 65 Gravity of Oil Correc

65 Feet of Drilling Mud % Gas % Oil % Mud % Wa

Feet of % Gas % Oil % Mud % Wa

Feet of % Gas % Oil % Mud % Wa

Feet of % Gas % Oil % Mud % Wa

Feet of % Gas % Oil % Mud % Wa

Feet of % Gas % Oil % Mud % Wa

Feet of % Gas % Oil % Mud % Wa

Feet of % Gas % Oil % Mud % Wa

Feet of % Gas % Oil % Mud % Wa

Feet of % Gas % Oil % Mud % Wa

Remarks Slide tool 10-12 feet to bottom tool was plugged during the

1st flow & 1st shut-in

Extra Equipment - Jars none Safety Joint 403 Extra Packer none Straddle none Hook Wall none

Top Recorder No. 78225 Clock No. Electronic Depth 3313 Cir. Sub none Sampler none

Bottom Recorder No. 13185 Clock No. 47441 Depth 3317 Insurance none

Price of Job

Tool Operator Don Bulky

Approved By

No 11223

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to property or personnel of the one for whom a test is made, or for any loss suffered sustained, directly or indirectly, through the use of its equipment, or its statements opinion concerning the results of any test. Tools lost or damaged in the hole shall paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

Great Bend, Kansas


CHART DATA

(316) 792-6902

State KANSAS
County STAFFORD
Field

Test Date June 12, 2000
Sec Town Range 12-21S-11W
Report Number 11224

Company: F.G.HOLL COMPANY L.L.C. Lease & Well No. SESSLER TRUST #1 Test # 2 Date: 6-12-2000
SEC. 12 TWP. 21S RGE. 11W

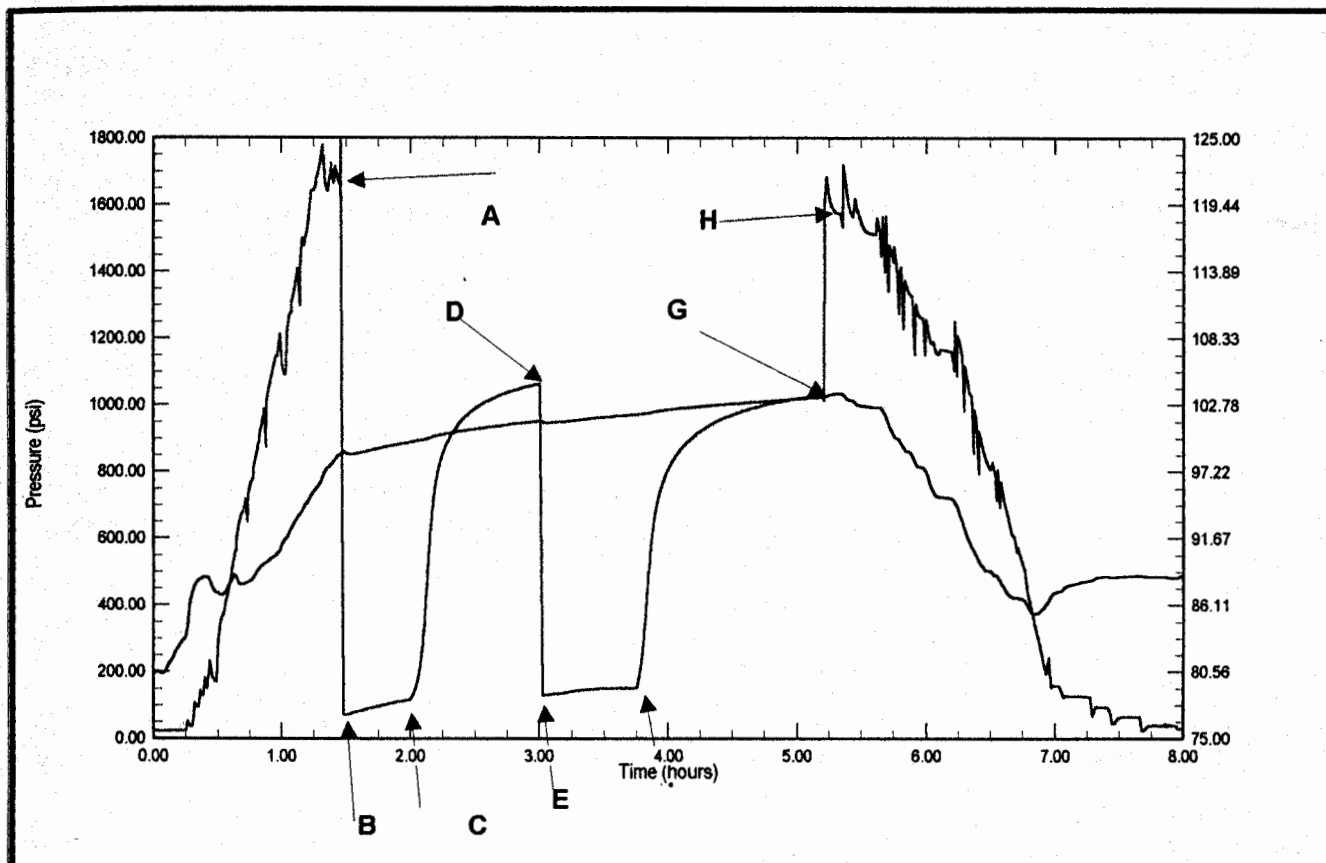

Field Reading

(A)	Initial Hydrostatic Pressure	1682
(B)	Initial Flow Pressure	72
(C)	Final Initial Flow Pressure	116
(D)	Initial Shut-In Pressure	1063
(E)	Initial Final Flow Pressure	131
(F)	Final Flow Pressure	160
(G)	Final Shut-In Pressure	1031
(H)	Final Hydrostatic Pressure	1573

ELECTRONIC RECORDER DEPTH 3357 FT, RECORDER NUMBER 78225

SUPERIOR TESTERS ENTERPRISES INC.

DRILL STEM TEST REPORT

GREAT BEND, KANSAS 67530 (316)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G.HOLL COMPANY L.L.C.	LEASE AND WELL NUMBER	SESSLER TRUST #1
TEST DATE	6/12/00	FORMATION TESTED	VIOLA
SECTION-TOWN-RANGE	12-21S-11W	DRILL STEM TEST NUMBER	2
STATE	KANSAS	REPORT NUMBER	11224
COUNTY	STAFFORD	ELEVATION KELLY BUSHINGS	1752
ELEVATION GROUND LEVEL	1743	TESTING ENGINEER	GENE BUDIG
COMPANY REPRESENTATIVE	FRANK GREENBAUM		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	3320	TOP PACKER DEPTH	3315
TEST INTERVAL (to)	3360	BOTTOM PACKER DEPTH	3320
ANCHOR LENGTH	40	NUMBER OF PACKERS	2
TOTAL DEPTH (ft)	3360	PACKER SIZE	6 3/4
		HOLE SIZE	7 7/8

FLOW TIMES

INITIAL OPEN

TOOL OPEN (from)

TOOL OPEN (to)

DURATION (min.)

INITIAL SHUT-IN

TOOL CLOSED (from)

TOOL CLOSED (to)

DURATION (min.)

FINAL OPEN

TOOL OPEN (from)

TOOL OPEN (to)

DURATION (min.)

FINAL SHUT-IN

TOOL CLOSED (from)

TOOL CLOSED (to)

DURATION (min.)

PRESSURE READINGS

INITIAL HYDROSTATIC

INITIAL FLOW

FINAL INITIAL FLOW

INITIAL SHUT-IN

INITIAL FINAL FLOW

FINAL FLOW

FINAL SHUT-IN

FINAL HYDROSTATIC

MAXIMUM TEMPERATURE

TOP RECORDER DEPTH

RECORDER NUMBER

BOTTOM RECORDER DEPTH

RECORDER NUMBER

INITIAL BLOW

WEAK BLOW THROUGH OUT

FINAL BLOW

WEAK BLOW THROUGH OUT

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOKWALL	NO
		SAMPLER	NO

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 6-12-2000 Location SW-1/4-21-11 Elevation 1752 K.B. County Stallard

Company F.G. Hall Company L.L.C. Number of Copies 5

Charts Mailed to 6427 East Kellogg P.O. Box 780167 Wichita Kansas 67228-0167

Drilling Contractor Steelers Drilling Co. Inc.

Length Drill Pipe 3059 I.D. Drill Pipe 3.80 Tool Joint Size 4 1/2" X 11

Length Weight Pipe None I.D. Weight Pipe None Tool Joint Size None

Length Drill Collars 240 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2" X 11

Top Packer Depth 3315 Bottom Packer Depth 3320 Number of Packers 2 Packer Size 6 3/4"

TESTED FROM 3320 TO 3360 ANCHOR LENGTH 40 TOTAL DEPTH 3360 Hole Size 7 7/8"

LEASE & WELL NO. Jessie Trust #1 FORMATION TESTED Viola TEST NO. 2

Mud Weight 9.4 Viscosity 49 Water Loss 19.4 Chlorides - Pits 8200 D.S.T.

Maximum Temp. 103 °F Initial Hydrostatic Pressure (A) 1682 P.S.I. Final Hydrostatic Pressure (H) 1573 P.S.I.

Tool Open I.F.P. from 11:45 m to 12:15 m 30 min

Tool Closed I.C.I.P. from 12:15 m to 1:15 m 60 min

Tool Open F.F.P. from 1:15 m to 2:00 m 45 min

Tool Closed F.C.I.P. from 2:00 m to 3:30 m 90 min

Initial Blow WEAK blow through out

Final Blow WEAK blow through out

Total Feet Recovered 250

Gravity of Oil _____ Corrected _____

200 Feet of Gas in the Pipe % Gas _____ % Oil _____ % Mud _____ % Water _____

200 Feet of VERY Gassy muddy oil 70% Gas 10% Oil 20% Mud 0% Water

60 Feet of VERY Heavy oil cut mud 0% Gas 40% Oil 60% Mud 0% Water

60 Feet of Heavy oil & Gas cut mud 10% Gas 25% Oil 65% Mud 0% Water

60 Feet of VERY Gassy muddy oil 80% Gas 8% Oil 12% Mud 0% Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Feet of _____ % Gas _____ % Oil _____ % Mud _____ % Water

Remarks _____

Extra Equipment - Jars None Safety Joint 405 Extra Packer None Straddle None Hook Wall None

Top Recorder No. 78225 Clock No. Electronic Depth 3354 Cir. Sub None Sampler None

Bottom Recorder No. 13185 Clock No. 47441 Depth 3357 Insurance None

Price of Job _____

Tool Operator Steve Bady

Approved By _____

No 11224

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.

Great Bend, Kansas


CHART DATA

(316) 792-6902

State KANSAS
County STAFFORD
Field

Test Date June 12, 2000
Sec Town Range 12-21S-11W
Report Number

Company: F.G.HOLL COMPANY L.L.C. Lease & Well No. SESSLER TRUST #1 Test # 3 Date: 6-132000
SEC. 12 TWP. 21S RGE. 11W

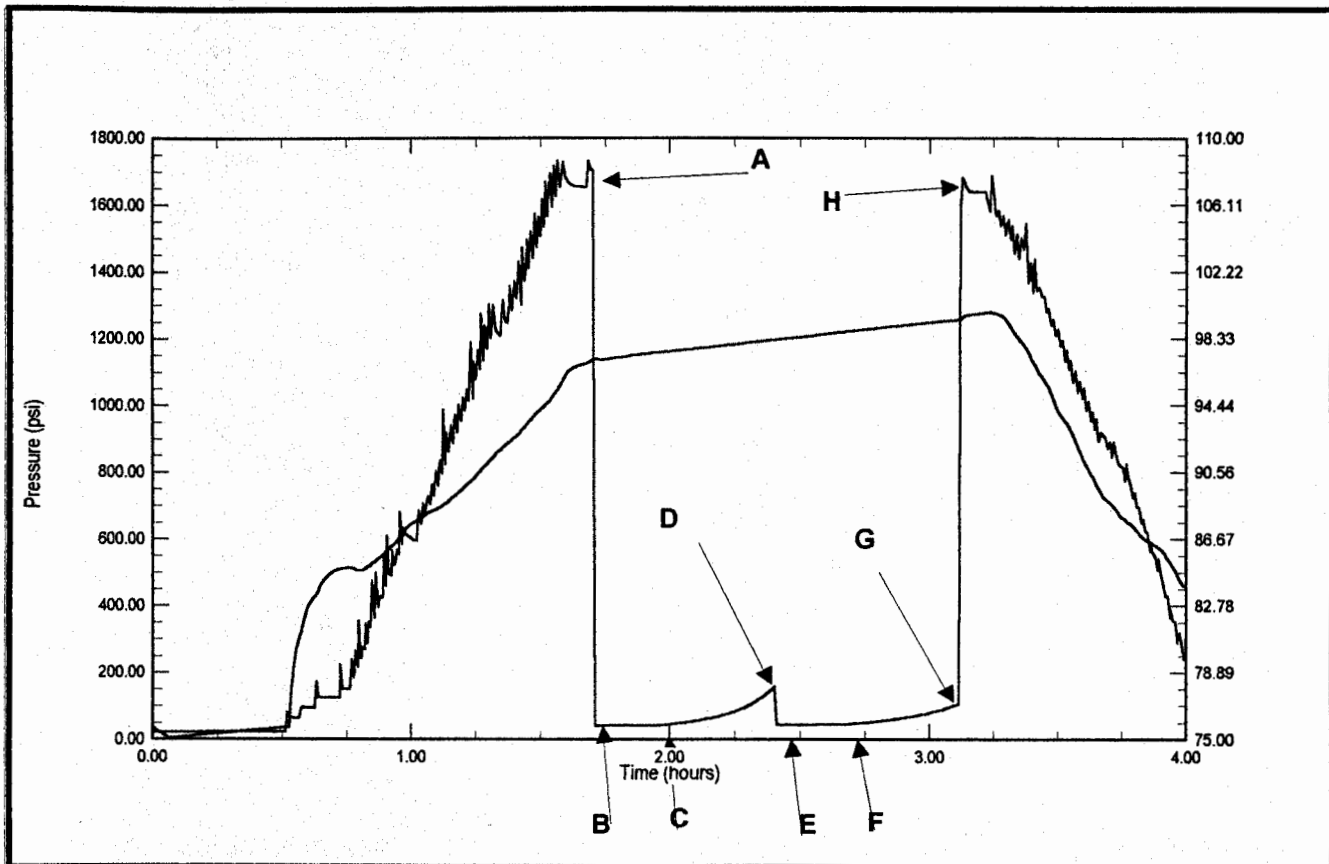

Field Reading

(A)	Initial Hydrostatic Pressure	1653
(B)	Initial Flow Pressure	40
(C)	Final Initial Flow Pressure	43
(D)	Initial Shut-In Pressure	152
(E)	Initial Final Flow Pressure	44
(F)	Final Flow Pressure	44
(G)	Final Shut-In Pressure	104
(H)	Final Hydrostatic Pressure	1640

ELECTRONIC RECORDER DEPTH 3393 FT, RECORDER NUMBER 78225

Superior Testers Enterprises, Inc.

R.R. 3, Box 295B, Great Bend, Kansas 67530

(316) 792-6902

Date 6-13-2000 Location SW 1/4 - 4W - 212-215-11W Elevation 1760 HL County Stafford

Company F.C. Hall Company L.L.C. Number of Copies 2

Charts Mailed to 6427 East Kellogg P.O. Box 780167 Wichita, Kansas 67278-0167

Drilling Contractor Steelman Drilling Rig #4

Length Drill Pipe 3115 I.D. Drill Pipe 3.80 Tool Joint Size 4 1/2" X.H.

Length Weight Pipe None I.D. Weight Pipe None Tool Joint Size None

Length Drill Collars 240 I.D. Drill Collars 2.25 Tool Joint Size 4 1/2" X.H.

Top Packer Depth 3371 Bottom Packer Depth 3376 Number of Packers 2 Packer Size 6 3/4"

TESTED FROM 3376 TO 3400 ANCHOR LENGTH 24 TOTAL DEPTH 3400 Hole Size 7 7/8"

LEASE & WELL NO. Sessler Trust #1 FORMATION TESTED Simpson Sand TEST NO. 2

Mud Weight 9.4 Viscosity 49 Water Loss 10.4 Chlorides - Pits 8200 D.S.T.

Maximum Temp. 100 °F Initial Hydrostatic Pressure (A) 1653 P.S.I. Final Hydrostatic Pressure (H) 1640 P.S.I.

Tool Open I.F.P. from 7:30 A.m to 7:45 A.m 15 min

Tool Closed I.C.I.P. from 7:45 A.m to 8:15 A.m 30 min

Tool Open F.F.P. from 8:15 A.m to 8:30 A.m 15 min

Tool Closed F.C.I.P. from 8:30 A.m to 9:00 A.m 30 min

Initial Blow Very weak surface blow for 8 minutes & Died

Final Blow No blow

Total Feet Recovered 10 Gravity of Oil Corrected

10 Feet of Drilling mud % Gas % Oil % Mud % Water

Feet of % Gas % Oil % Mud % Water

Feet of % Gas % Oil % Mud % Water

Feet of % Gas % Oil % Mud % Water

Feet of % Gas % Oil % Mud % Water

Feet of % Gas % Oil % Mud % Water

Feet of % Gas % Oil % Mud % Water

Feet of % Gas % Oil % Mud % Water

Feet of % Gas % Oil % Mud % Water

Feet of % Gas % Oil % Mud % Water

Remarks

Extra Equipment - Jars None Safety Joint Yes Extra Packer None Straddle None Hook Wall None

Top Recorder No. Electronica Clock No. 78225 Depth 3392 Cir. Sub None Sampler None

Bottom Recorder No. 13185 Clock No. 47441 Depth 3397 Insurance None

Price of Job

Tool Operator Steve Bushy

Approved By

No 13901

Superior Testers Enterprises, Inc. shall not be liable for damage of any kind to the property or personnel of the one for whom a test is made, or for any loss suffered or sustained, directly or indirectly, through the use of its equipment, or its statements or opinion concerning the results of any test. Tools lost or damaged in the hole shall be paid for at cost by the party for whom the test is made.

SUPERIOR TESTERS ENTERPRISES INC.**DRILL STEM TEST REPORT**

GREAT BEND .KANSAS 67530 (316)792-6902

GENERAL INFORMATION

COMPANY NAME	F.G.HOLL COMPANY L.L.C.	LEASE AND WELL NUMBER	SESSLER TRUST #1
TEST DATE	6/12/00	FORMATION TESTED	SIMPSON SAND
SECTION-TOWN-RANGE	12-21S-11W	DRILL STEM TEST NUMBER	3
STATE	KANSAS	REPORT NUMBER	
COUNTY	STAFFORD	ELEVATION KELLY BUSHINGS	1752
ELEVATION GROUND LEVEL	1743	TESTING ENGINEER	GENE BUDIG
COMPANY REPRESENTATIVE	FRANK GRENBAUM		

TOOL SETTING INFORMATION

TEST INTERVAL (From)	3376	TOP PACKER DEPTH	3371
TEST INTERVAL (to)	3400	BOTTOM PACKER DEPTH	3376
ANCHOR LENGTH	24	NUMBER OF PACKERS	2
TOTAL DEPTH (ft)	3400	PACKER SIZE	6 3/4
		HOLE SIZE	7 7/8

FLOW TIMES

INITIAL OPEN

TOOL OPEN (from) 7:30

TOOL OPEN (to) 7:45

DURATION (min.) 15

INITIAL SHUT-IN

TOOL CLOSED (from) 7:45

TOOL CLOSED (to) 8:15

DURATION (min.) 30

FINAL OPEN

TOOL OPEN (from) 8:15

TOOL OPEN (to) 8:30

DURATION (min.) 15

FINAL SHUT-IN

TOOL CLOSED (from) 8:30

TOOL CLOSED (to) 10:00

DURATION (min.) 30

PRESSURE READINGS

INITIAL HYDROSTATIC 1653

INITIAL FLOW 40

FINAL INITIAL FLOW 43

INITIAL SHUT-IN 152

INITIAL FINAL FLOW 44

FINAL FLOW 44

FINAL SHUT-IN 104

FINAL HYDROSTATIC 1640

MAXIMUM TEMPERATURE 100

TOP RECORDER DEPTH 3393

RECORDER NUMBER 78225

BOTTOM RECORDER DEPTH 3397

RECORDER NUMBER 13189

INITIAL BLOW

VERY WEAK SURFACE BLOW FOR 8 MINUTES AND DIED

FINAL BLOW

NO BLOW

EXTRA EQUIPMENT

JARS	NO	EXTRA PACKER (3RD)	NO
SAFETY JOINT	YES	EXTRA PACKER (4TH)	NO
ELECTRONIC RECORDER	YES	STRADDLE	NO
CIRCULATING SUB	NO	HOOKWALL	NO
		SAMPLER	NO
