

SHAWVER-ARMOUR TESTING

817 CENTRAL BUILDING

Date Jan 15-66 Ticket No. 126 Elevation 1295 KB

Total Depth 3740' Tested From 3735' To 3740' Formation Tested Mississipp

Blow Strong intermitting blow throughout test

Mud Wt. 9 8/ Viscosity 38 Bottom Hole Temp.

Size Bottom Choke 1/2 Size Top Choke 1/2

Size Drill Pipe 4 1/2 Size Hole 7 7/8 Length Air Chamber Ft.

Initial Shut in Time 30 Min Tool Open 1 Hr - Min Final Shut in Time 30 Min

Recovery 60' light oil cut mud
60' Heavy oil cut mud

Office Corrected Pressure Reading

Initial Shut in Pressure 1296 Lbs

Initial Flow Pressure 22 Lbs

Final Flow Pressure 26 Lbs

Final Shut in Pressure 1176 Lbs

Initial Hydrostatic Pressure 1916 Lbs

Final Hydrostatic Pressure 1834 Lbs

Remarks

Witnessed By Fred Stump

Tool Operator L J Casebolt

Location SW NE SW

County Sumner

State Kansas

Name of Lease


Well No. # 1

Test No. # 1

Company

Beardmore Drilling Co

Notes Unit 3-1 BATES

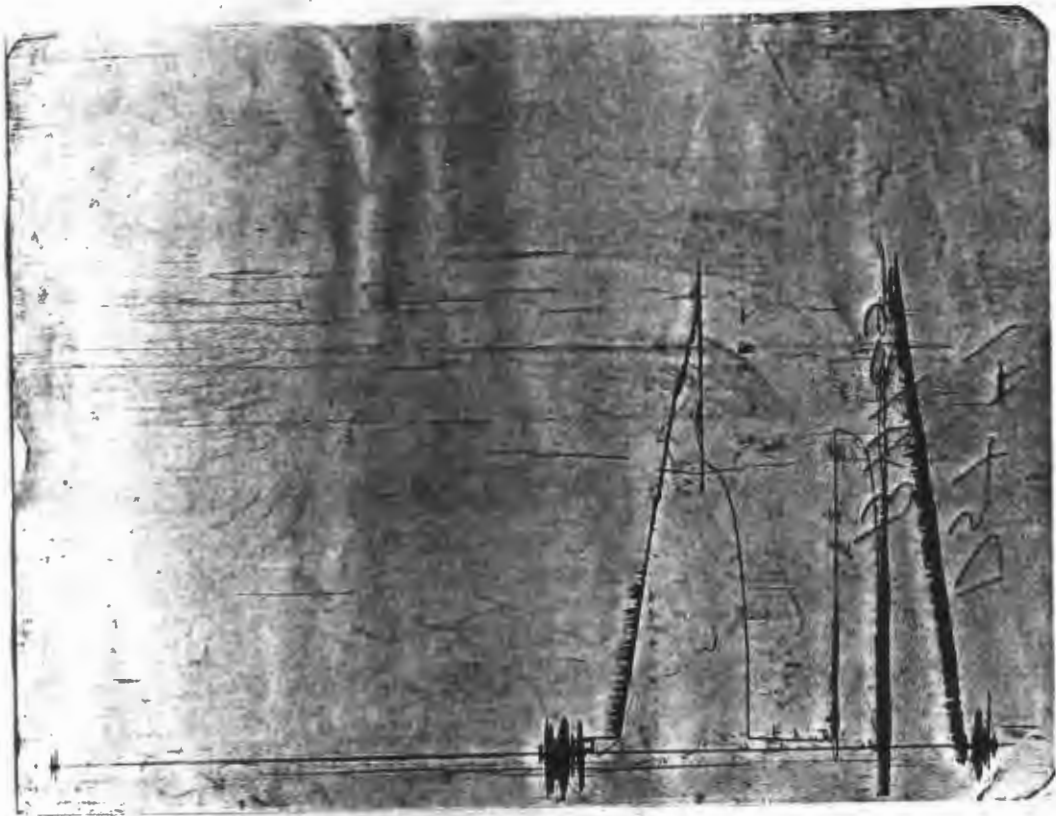

SHAWVER-ARMOUR TESTING

817 CENTRAL BUILDING

Date Jan 16, 1966 Ticket No. 127 Elevation 1295 KB
 Total Depth 3743 Tested From 3736 To 3743 Formation Tested Mississippi
 Blow Strong Blow throughout test
 Mud Wt. 9 8/ Viscosity 39 Bottom Hole Temp _____
 Size Bottom Choke 1/2 Size Top Choke 1/2
 Size Drill Pipe 4 1/2 Size Hole 7 7/8 Length Air Chamber _____ Ft.
 Initial Shut in Time 30 Min Tool Open 1 Hr - Min Final Shut in Time 30 Min

Recovery 80' Light oil cut mud
120' Heavy oil cut mud

Office Corrected Pressure Reading

Initial Shut in Pressure 1192 Lbs
 Initial Flow Pressure 26 Lbs
 Final Flow Pressure 72 Lbs
 Final Shut in Pressure 1032 Lbs
 Initial Hydrostatic Pressure 1874 Lbs
 Final Hydrostatic Pressure 1834 Lbs

Remarks _____

Witnessed By Fred Stump
 Tool Operator L. J. Casebolt

Location SW NE SW

County Sumner

State Kansas

Betty Unit 2-1 BATES

Name of Lease

#1 Well No.

#2 Test No.

Beardmore Drilling Co.
 Company

