


30-305-12W



DRILL STEM TEST REPORT

Prepared For: **Roberts Resources Inc.**

520 S. Holland STE. 207
Wichita KS 67209

ATTN: Kent Roberts

30 30 12 Barber KS

33-30-12W

Rule Ranch #1-33

Start Date: 2008.08.24 @ 00:43:25

End Date: 2008.08.24 @ 09:44:25

Job Ticket #: 32673 DST #: 1

Trilobite Testing, Inc

PO Box 1733 Hays, KS 67601

ph: 785-625-4778 fax: 785-625-5620

Roberts Resources Inc.


Rule Ranch #1-33

30 30 12 Barber KS

DST # 1

Tarkio Sands

2008.08.24



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Roberts Resources Inc.

520 S. Holland STE. 207
Wichita KS 67209

ATTN: Kent Roberts

Rule Ranch #1-33

30 30 12 Barber KS

Job Ticket: 32673

DST#: 1

Test Start: 2008.08.24 @ 00:43:25

GENERAL INFORMATION:

Formation: **Tarkio Sands**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 03:44:25

Time Test Ended: 09:44:25

Test Type: Conventional Bottom Hole

Tester: Kevin Taylor

Unit No: 32

Interval: 2831.00 ft (KB) To 2846.00 ft (KB) (TVD)

Total Depth: 2846.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1694.00 ft (KB)

1683.00 ft (CF)

KB to GR/CF: 11.00 ft

Serial #: 8360 Outside

Press@RunDepth: 18.89 psig @ 2832.00 ft (KB)

Start Date: 2008.08.24

End Date:

2008.08.24

Start Time: 00:43:27

End Time:

09:44:25

Capacity: 7000.00 psig

Last Calib.: 2008.08.24

Time On Btm: 2008.08.24 @ 03:43:55


Time Off Btm: 2008.08.24 @ 08:16:55

TEST COMMENT: IF Weak Blow BOB 30 Min

ISI No Blow

FF Strong Blow BOB Immediately GTS 45 Min See Gas Flow Report.

FSI Bled Off Of 15 Min No Blow

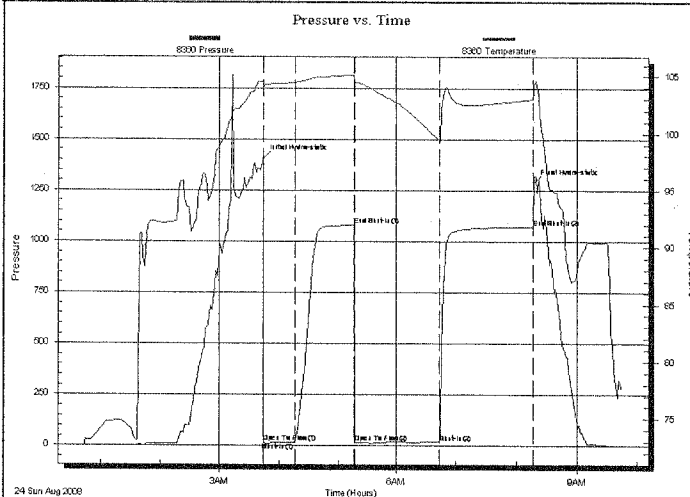

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1402.58	104.56	Initial Hydro-static
1	16.62	104.06	Open To Flow (1)
32	16.36	104.44	Shut-In(1)
93	1078.83	105.13	End Shut-In(1)
94	18.34	104.63	Open To Flow (2)
180	18.89	99.35	Shut-In(2)
273	1072.18	103.00	End Shut-In(2)
273	1287.52	103.78	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
5.00	Mud	0.04

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
First Gas Rate	0.13	1.00	5.76
Last Gas Rate	0.13	3.00	6.51
Max. Gas Rate	0.13	3.00	6.51



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TOOL DIAGRAM

Roberts Resources Inc.

Rule Ranch #1-33

520 S. Holland STE. 207
Wichita KS 67209

30 30 12 Barber KS

Job Ticket: 32673

DST#: 1

ATTN: Kent Roberts

Test Start: 2008.08.24 @ 00:43:25

Tool Information


Drill Pipe:	Length: 2634.00 ft	Diameter: 3.88 inches	Volume: 38.52 bbl	Tool Weight:	2100.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer:	30000.00 lb
Drill Collar:	Length: 182.00 ft	Diameter: 2.74 inches	Volume: 1.33 bbl	Weight to Pull Loose:	lb
		Total Volume:	39.85 bbl	Tool Chased	0.00 ft
Drill Pipe Above KB:	13.00 ft			String Weight: Initial	48000.00 lb
Depth to Top Packer:	2831.00 ft			Final	lb
Depth to Bottom Packer:	ft				
Interval between Packers:	15.00 ft				
Tool Length:	43.00 ft				
Number of Packers:	2	Diameter:	6.75 inches		

Tool Comments:

Tool Description

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	1.00			2804.00	
Shut In Tool	5.00			2809.00	
Hydraulic tool	5.00			2814.00	
Jars	5.00			2819.00	
Safety Joint	2.00			2821.00	
Packer	5.00			2826.00	28.00 Bottom Of Top Packer
Packer	5.00			2831.00	
Stubb	1.00			2832.00	
Recorder	0.00	8360	Outside	2832.00	
Recorder	0.00	6755	Inside	2832.00	
Perforations	11.00			2843.00	
Bullnose	3.00			2846.00	15.00 Bottom Packers & Anchor

Total Tool Length: 43.00



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

FLUID SUMMARY

Roberts Resources Inc.

Rule Ranch #1-33

520 S. Holland STE 207
Wichita KS 67209

30 30 12 Barber KS

Job Ticket: 32673

DST#: 1

ATTN: Kent Roberts

Test Start: 2008.08.24 @ 00:43:25

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 43.00 sec/qt

Water Loss: 9.57 in³

Resistivity: ohm.m

Salinity: 6000.00 ppm

Filter Cake: 0.02 inches

Cushion Type:

Cushion Length:

Cushion Volume:

Gas Cushion Type:

Gas Cushion Pressure:

ft

bbl

psig

Oil API:

Water Salinity:

deg API

ppm

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
5.00	Mud	0.036

Total Length: 5.00 ft

Total Volume: 0.036 bbl

Num Fluid Samples: 1


Num Gas Bombs: 1


Serial #: KT#1

Laboratory Name: Caraway

Laboratory Location: Liberal, KS

Recovery Comments:

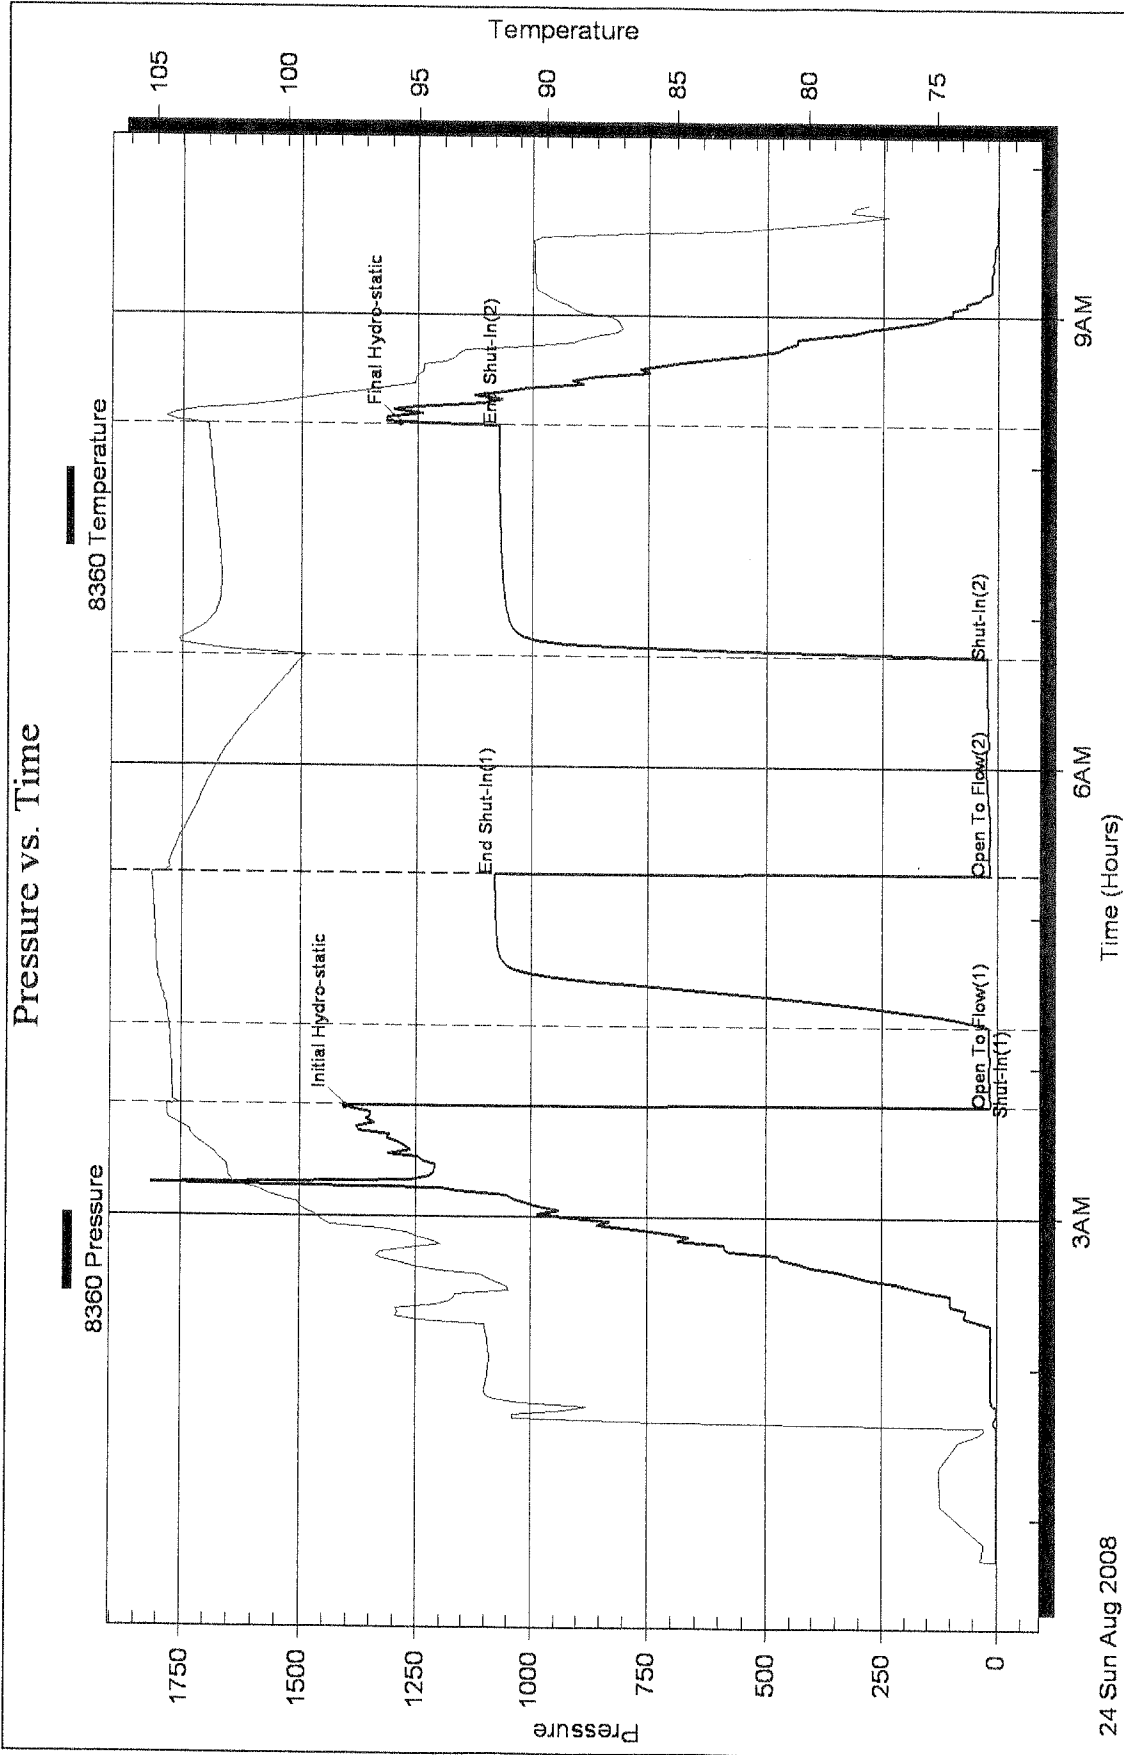



DRILL STEM TEST REPORT

Prepared For: **Roberts Resources Inc.**

520 S. Holland STE. 207
Wichita KS 67209

ATTN: Kent Roberts

30 30 12 Barber KS


Rule Ranch #1-33

Start Date: 2008.08.25 @ 17:04:11

End Date: 2008.08.25 @ 23:57:11

Job Ticket #: 32674 DST #: 2

Trilobite Testing, Inc
PO Box 1733 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Roberts Resources Inc.

520 S. Holland STE. 207
Wichita KS 67209

ATTN: Kent Roberts

Rule Ranch #1-33

30 30 12 Barber KS

Job Ticket: 32674

DST#: 2

Test Start: 2008.08.25 @ 17:04:11

GENERAL INFORMATION:

Formation: **Lower Douglas Sand**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 19:19:11

Time Test Ended: 23:57:11

Test Type: Conventional Bottom Hole

Tester: Kevin Taylor

Unit No: 32

Interval: **3600.00 ft (KB) To 3640.00 ft (KB) (TVD)**

Total Depth: 3640.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1694.00 ft (KB)

1683.00 ft (CF)

KB to GR/CF: 11.00 ft

Serial #: 8360 Outside

Press@RunDepth: 46.09 psig @ 3601.00 ft (KB)

Start Date: 2008.08.25

End Date: 2008.08.25

Capacity: 7000.00 psig

Last Calib.: 2008.08.26

Start Time: 17:04:13


End Time: 23:57:11

Time On Btm: 2008.08.25 @ 19:19:11

Time Off Btm: 2008.08.25 @ 21:56:41

TEST COMMENT: IF Strong Blow BOB 90 Sec
ISI Bleed Off For 2 Min. No Blow.
FF Strong Blow BOB Immediately G.T.S. 25 Min TSTM
FSI Bleed Off 10 Min No Blow

Pressure vs. Time

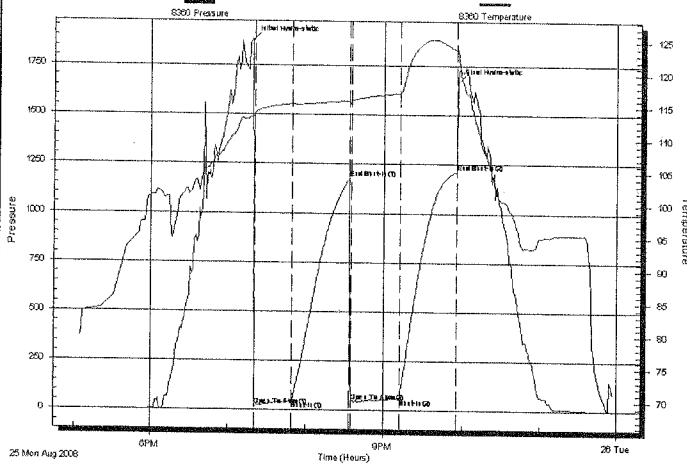

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1876.81	113.39	Initial Hydro-static
2	22.65	113.94	Open To Flow (1)
30	46.09	115.47	Shut-In (1)
75	1179.80	115.96	End Shut-In (1)
76	46.94	115.91	Open To Flow (2)
113	62.78	117.14	Shut-In (2)
157	1212.82	123.64	End Shut-In (2)
158	1665.77	123.87	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
60.00	SOWGCM 5%G 3%W 92%M	0.44
80.00	Mud	0.72

Gas Rates

	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

TOOL DIAGRAM

Roberts Resources Inc.

Rule Ranch #1-33

520 S. Holland STE. 207
Wichita KS 67209

30 30 12 Barber KS

Job Ticket: 32674

DST#: 2

ATTN: Kent Roberts

Test Start: 2008.08.25 @ 17:04:11

Tool Information

Drill Pipe:	Length: 3474.00 ft	Diameter: 3.88 inches	Volume: 50.80 bbl	Tool Weight: 2100.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 30000.00 lb
Drill Collar:	Length: 121.00 ft	Diameter: 2.74 inches	Volume: 0.88 bbl	Weight to Pull Loose: 60000.00 lb
			<u>Total Volume: 51.68 bbl</u>	Tool Chased 0.00 ft
Drill Pipe Above KB:	23.00 ft			String Weight: Initial 52000.00 lb
Depth to Top Packer:	3600.00 ft			Final 56000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	40.00 ft			
Tool Length:	68.00 ft			
Number of Packers:	2	Diameter: 6.75 inches		

Tool Comments:

Tool Description

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	1.00			3573.00	
Shut In Tool	5.00			3578.00	
Hydraulic tool	5.00			3583.00	
Jars	5.00			3588.00	
Safety Joint	2.00			3590.00	
Packer	5.00			3595.00	28.00 Bottom Of Top Packer
Packer	5.00			3600.00	
Stubb	1.00			3601.00	
Recorder	0.00	8360	Outside	3601.00	
Recorder	0.00	6755	Inside	3601.00	
Perforations	36.00			3637.00	
Bullnose	3.00			3640.00	40.00 Bottom Packers & Anchor

Total Tool Length: 68.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Roberts Resources Inc.

Rule Ranch #1-33

520 S. Holland STE. 207
Wichita KS 67209

30 30 12 Barber KS

Job Ticket: 32674

DST#: 2

ATTN: Kent Roberts

Test Start: 2008.08.25 @ 17:04:11

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 44.00 sec/qt

Water Loss: 10.37 in³

Resistivity: ohm.m

Salinity: 11000.00 ppm

Filter Cake: 0.02 inches

Cushion Type:

Cushion Length:

Cushion Volume:

Gas Cushion Type:

Gas Cushion Pressure:

ft
bbl

psig

Oil API:

Water Salinity:

deg API

ppm

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
60.00	SOWGCM 5%G 3%W 92%M	0.438
80.00	Mud	0.723

Total Length: 140.00 ft

Total Volume: 1.161 bbl

Num Fluid Samples: 1


Num Gas Bombs: 1


Serial #: KT#1

Laboratory Name: Caraway

Laboratory Location: Hugoton, KS

Recovery Comments:

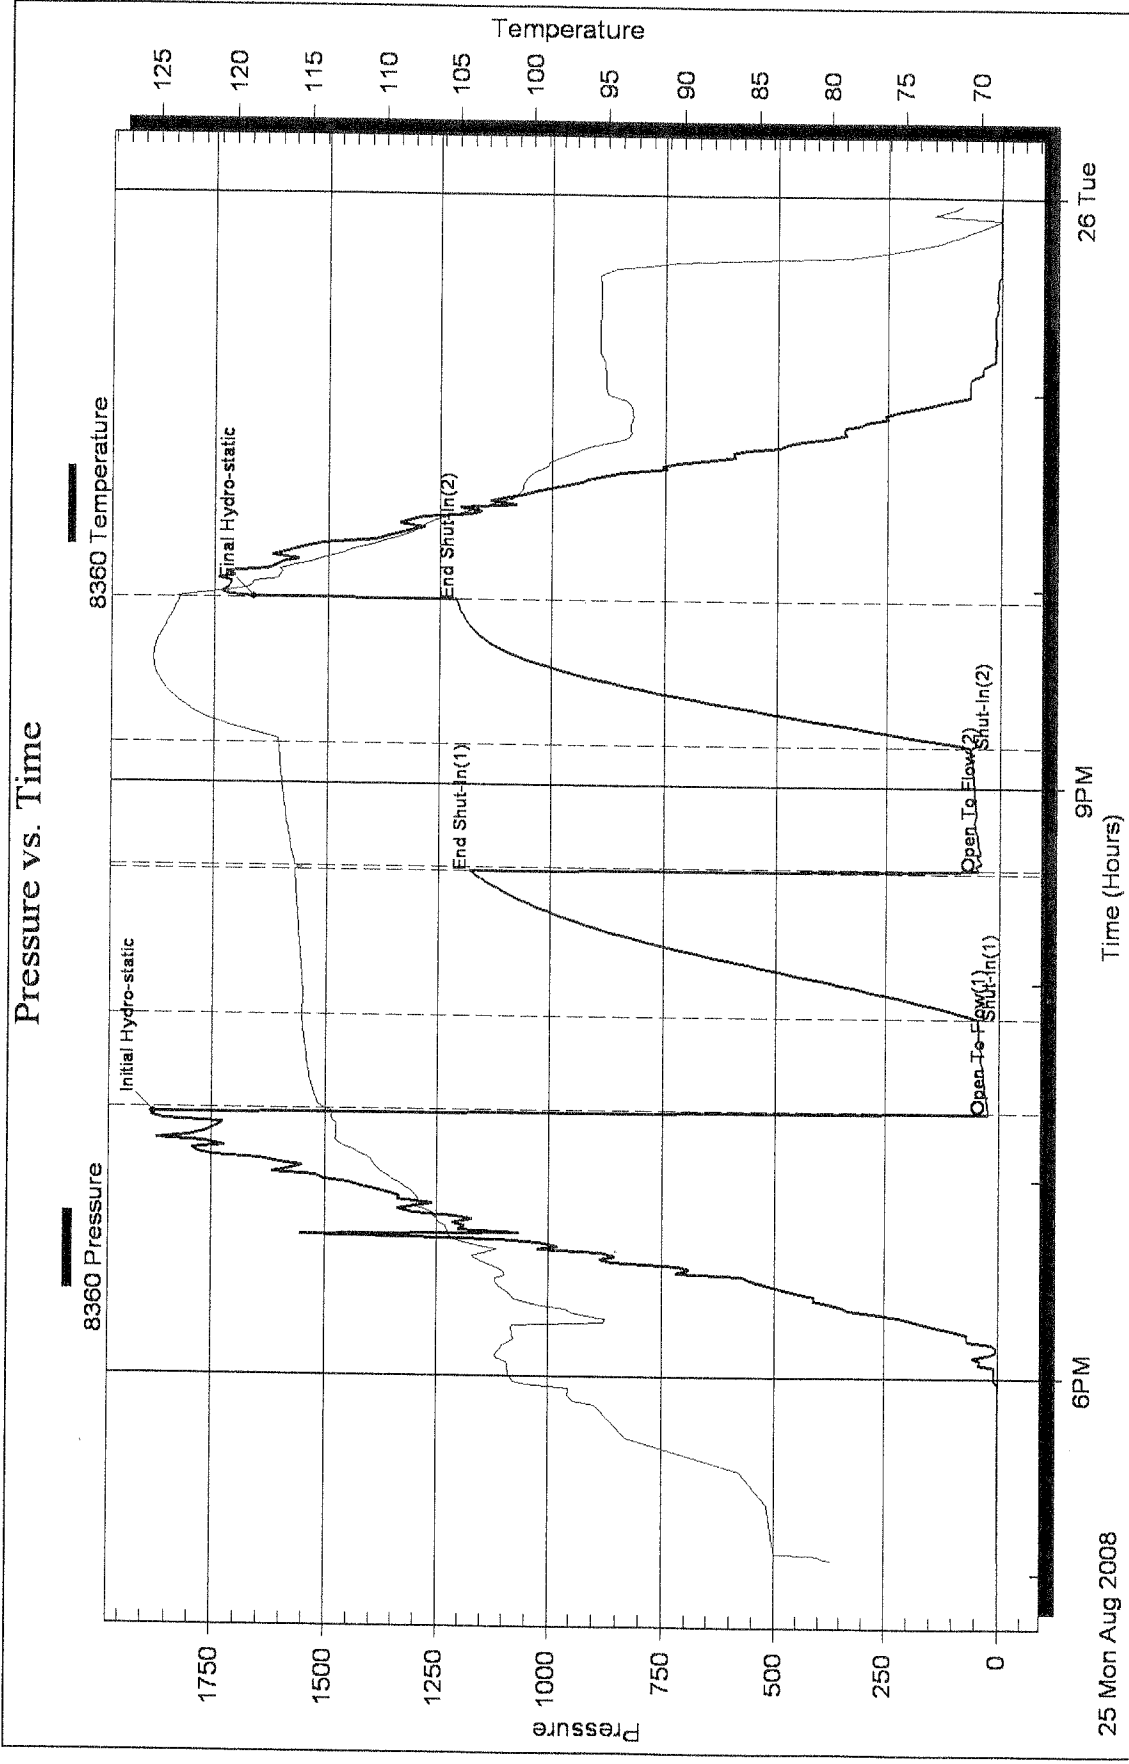



DRILL STEM TEST REPORT

Prepared For: **Roberts Resources Inc.**

520 S. Holland STE. 207
Wichita KS 67209

ATTN: Kent Roberts

30 30 12 Barber KS


Rule Ranch #1-33

Start Date: 2008.08.26 @ 14:07:31

End Date: 2008.08.26 @ 20:55:01

Job Ticket #: 32675 DST #: 3

Trilobite Testing, Inc
PO Box 1733 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Roberts Resources Inc.

520 S. Holland STE. 207
Wichita KS 67209

ATTN: Kent Roberts

Rule Ranch #1-33

30 30 12 Barber KS

Job Ticket: 32675

DST#: 3

Test Start: 2008.08.26 @ 14:07:31

GENERAL INFORMATION:

Formation: **LKC "D"**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 15:58:31

Time Test Ended: 20:55:01

Test Type: Conventional Bottom Hole

Tester: Kevin Taylor

Unit No: 32

Interval: **3840.00 ft (KB) To 3866.00 ft (KB) (TVD)**

Total Depth: 3866.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1694.00 ft (KB)

1683.00 ft (CF)

KB to GR/CF: 11.00 ft

Serial #: 8360

Outside

Press@RunDepth: 288.23 psig @ 3841.00 ft (KB)

Start Date: 2008.08.26

End Date:

2008.08.26

Start Time: 14:07:33

End Time:

20:55:01


Capacity: 7000.00 psig

Last Calib.: 2008.08.26

Time On Btm: 2008.08.26 @ 15:58:01

Time Off Btm: 2008.08.26 @ 19:01:31

TEST COMMENT: IF Fair Blow BOB 11 Min
ISI Bleed Off For 10 Min. No Blow
FF Weak Blow BOB 30 Min
FSI Bled Off For 10 Min No Blow

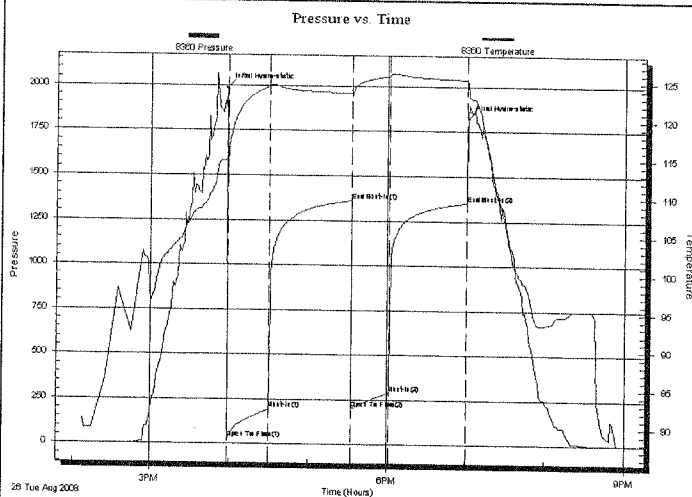

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	1987.22	114.88	Initial Hydro-static
1	27.82	113.91	Open To Flow (1)
32	193.63	124.39	Shut-In (1)
94	1359.70	123.62	End Shut-In (1)
95	200.76	123.14	Open To Flow (2)
123	288.23	125.82	Shut-In (2)
183	1350.65	125.40	End Shut-In (2)
184	1821.33	125.19	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
60.00	MCSW 40%W 60%M	0.44
420.00	CSW	5.25

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
----------------	-----------------	------------------



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

TOOL DIAGRAM

Roberts Resources Inc.

Rule Ranch #1-33

520 S. Holland STE. 207
Wichita KS 67209

30 30 12 Barber KS

Job Ticket: 32675

DST#: 3

ATTN: Kent Roberts

Test Start: 2008.08.26 @ 14:07:31

Tool Information

Drill Pipe:	Length: 3658.00 ft	Diameter: 3.88 inches	Volume: 53.50 bbl	Tool Weight: 2100.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 30000.00 lb
Drill Collar:	Length: 182.00 ft	Diameter: 2.74 inches	Volume: 1.33 bbl	Weight to Pull Loose: lb
		Total Volume: 54.83 bbl		Tool Chased 0.00 ft
Drill Pipe Above KB:	28.00 ft			String Weight: Initial 57000.00 lb
Depth to Top Packer:	3840.00 ft			Final lb
Depth to Bottom Packer:	ft			
Interval between Packers:	26.00 ft			
Tool Length:	54.00 ft			
Number of Packers:	2	Diameter: 6.75 inches		

Tool Comments:

Tool Description

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	1.00			3813.00	
Shut In Tool	5.00			3818.00	
Hydraulic tool	5.00			3823.00	
Jars	5.00			3828.00	
Safety Joint	2.00			3830.00	
Packer	5.00			3835.00	28.00 Bottom Of Top Packer
Packer	5.00			3840.00	
Stubb	1.00			3841.00	
Recorder	0.00	8360	Outside	3841.00	
Recorder	0.00	6755	Inside	3841.00	
Perforations	22.00			3863.00	
Bullnose	3.00			3866.00	26.00 Bottom Packers & Anchor

Total Tool Length: 54.00



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

FLUID SUMMARY

Roberts Resources Inc.

Rule Ranch #1-33

520 S. Holland STE. 207
Wichita KS 67209

30 30 12 Barber KS

Job Ticket: 32675

DST#: 3

ATTN: Kent Roberts

Test Start: 2008.08.26 @ 14:07:31

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 57.00 sec/qt

Water Loss: 9.58 in³

Resistivity: ohm.m

Salinity: 7500.00 ppm

Filter Cake: 0.02 inches

Cushion Type:

Cushion Length:

Cushion Volume:

Gas Cushion Type:

Gas Cushion Pressure:

ft
bbl

psig

Oil API:

deg API

Water Salinity: 40000 ppm

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
60.00	MCSW 40%W 60%M	0.438
420.00	CSW	5.248

Total Length: 480.00 ft

Total Volume: 5.686 bbl

Num Fluid Samples: 0


Num Gas Bombs: 0


Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

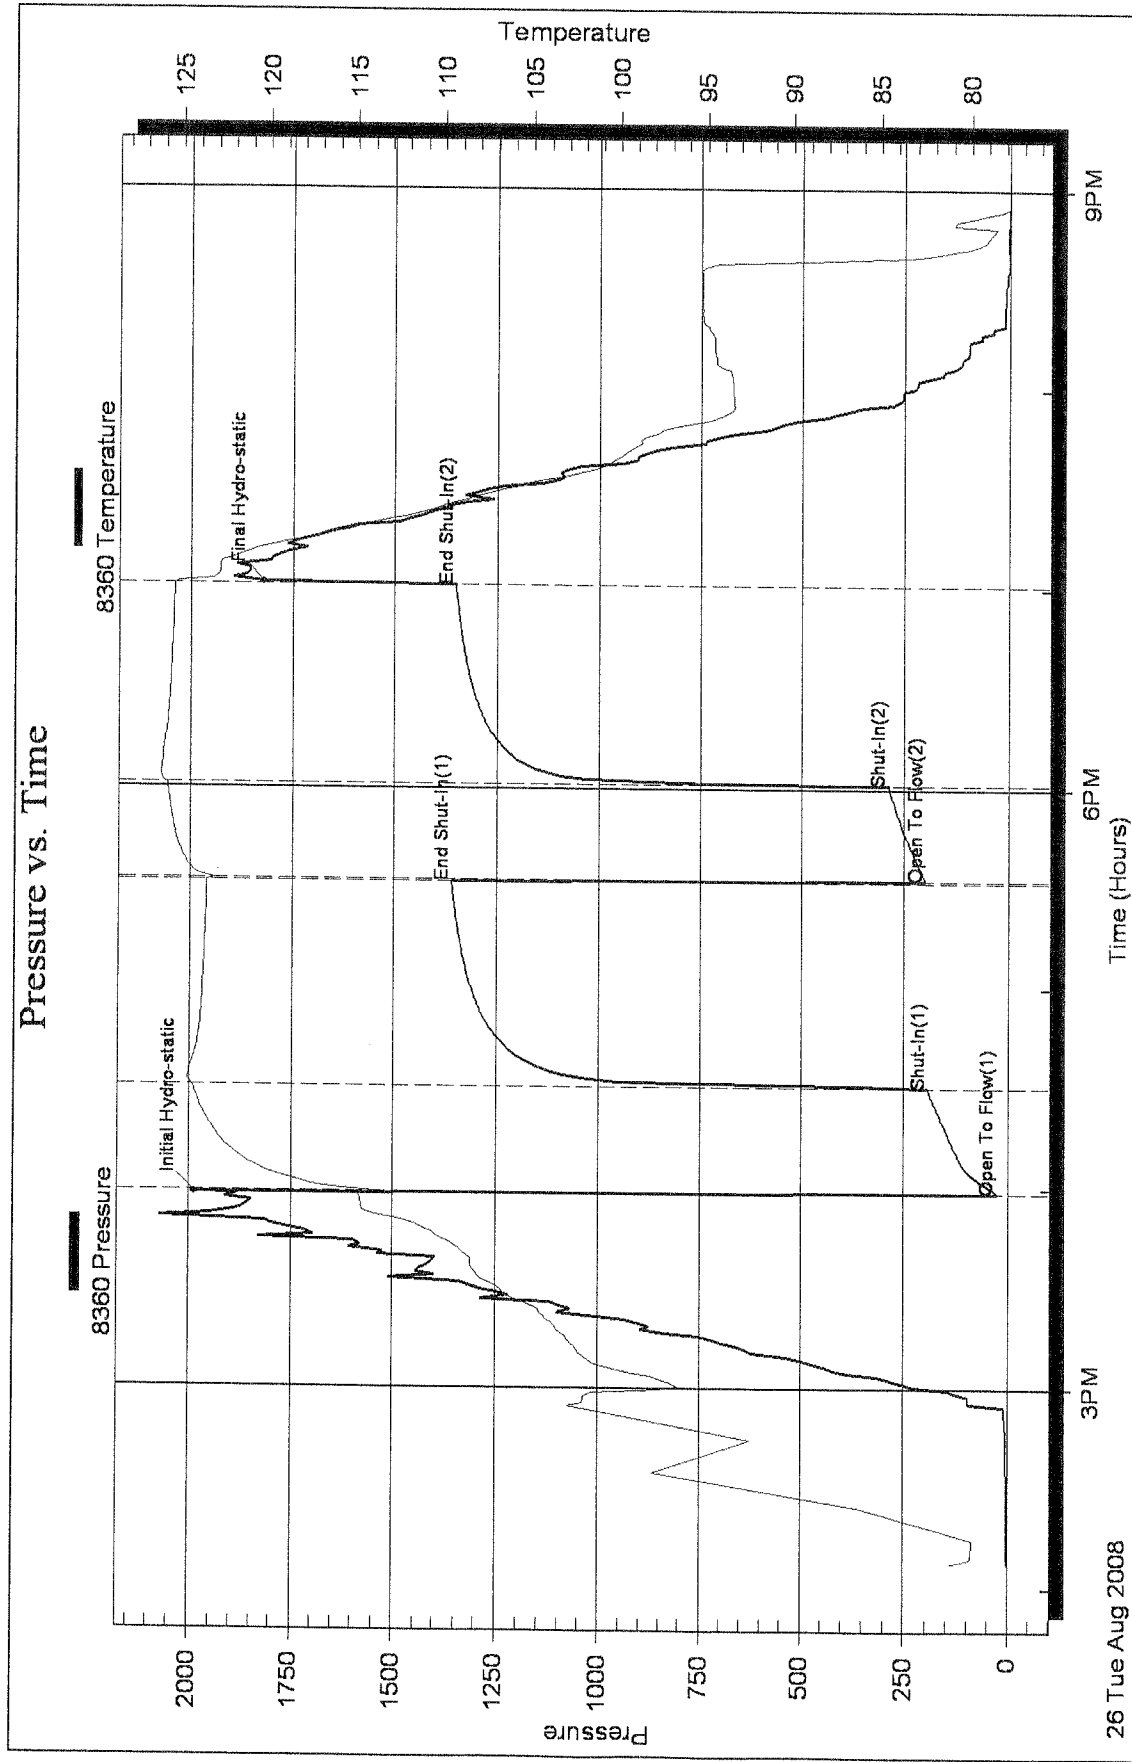



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

Prepared For: **Roberts Resources Inc.**

520 S. Holland STE. 207
Wichita KS 67209

ATTN: Kent Roberts

30 30 12 Barber KS


Rule Ranch #1-33

Start Date: 2008.08.27 @ 13:55:42

End Date: 2008.08.27 @ 20:31:12

Job Ticket #: 32501 DST #: 4

Trilobite Testing, Inc
PO Box 1733 Hays, KS 67601
ph: 785-625-4778 fax: 785-625-5620



**TRILOBITE
TESTING, INC.**

DRILL STEM TEST REPORT

Roberts Resources Inc.

520 S. Holland STE. 207
Wichita KS 67209

ATTN: Kent Roberts

Rule Ranch #1-33

30 30 12 Barber KS

Job Ticket: 32501

DST#: 4

Test Start: 2008.08.27 @ 13:55:42

GENERAL INFORMATION:

Formation: **Hertha**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 15:43:42

Time Test Ended: 20:31:12

Test Type: Conventional Bottom Hole

Tester: Kevin Taylor

Unit No: 32

Interval: 4115.00 ft (KB) To 4147.00 ft (KB) (TVD)

Total Depth: 4147.00 ft (KB) (TVD)

Hole Diameter: 7.88 inches Hole Condition: Fair

Reference Elevations: 1694.00 ft (KB)

1683.00 ft (CF)

KB to GR/CF: 11.00 ft

Serial #: 6755 Inside

Press@RunDepth: 33.07 psig @ 4116.00 ft (KB)

Start Date: 2008.08.27

End Date:

2008.08.27

Start Time: 13:55:44

End Time:

20:31:12

Capacity: 7000.00 psig


Last Calib.: 2008.08.27

Time On Btm: 2008.08.27 @ 15:42:42

Time Off Btm: 2008.08.27 @ 18:48:42

TEST COMMENT: IF Weak Blow BOB 30 Min
ISI No Blow
FFP Strong Blow BOB in 2Min.
FSI Dead

Pressure vs. Time

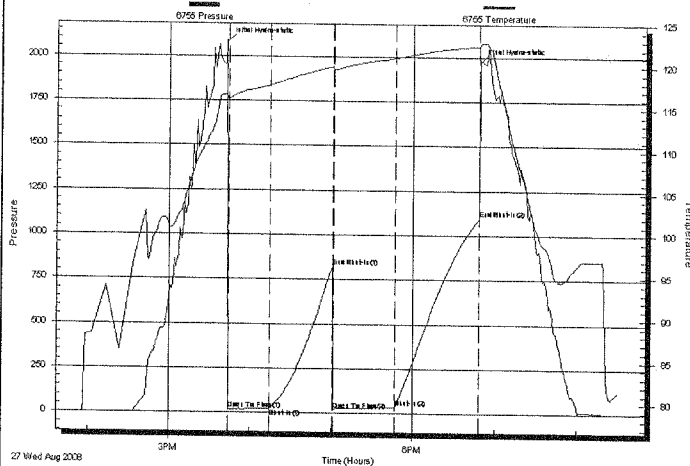

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	2080.74	116.64	Initial Hydro-static
1	15.30	115.94	Open To Flow (1)
32	22.97	117.76	Shut-In (1)
78	822.90	119.98	End Shut-In (1)
79	15.82	119.61	Open To Flow (2)
124	33.07	121.00	Shut-In (2)
186	1097.33	122.45	End Shut-In (2)
186	1973.57	122.76	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
15.00	Mud W/Oil Scum on Top	0.11
0.00	525' Gas In Pipe	0.00

Gas Rates

	Choke (Inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

TOOL DIAGRAM

Roberts Resources Inc.

Rule Ranch #1-33

520 S. Holland STE. 207
Wichita KS 67209

30 30 12 Barber KS

Job Ticket: 32501

DST#: 4

ATTN: Kent Roberts

Test Start: 2008.08.27 @ 13:55:42


Tool Information

Drill Pipe:	Length: 3937.00 ft	Diameter: 3.88 inches	Volume: 57.58 bbl	Tool Weight: 2100.00 lb
Heavy Wt. Pipe:	Length: 0.00 ft	Diameter: 0.00 inches	Volume: 0.00 bbl	Weight set on Packer: 30000.00 lb
Drill Collar:	Length: 182.00 ft	Diameter: 2.74 inches	Volume: 1.33 bbl	Weight to Pull Loose: 62000.00 lb
		Total Volume: 58.91 bbl		Tool Chased 0.00 ft
Drill Pipe Above KB:	32.00 ft			String Weight: Initial 59000.00 lb
Depth to Top Packer:	4115.00 ft			Final 59000.00 lb
Depth to Bottom Packer:	ft			
Interval between Packers:	32.00 ft			
Tool Length:	60.00 ft			
Number of Packers:	2	Diameter: 6.75 inches		
Tool Comments:				

Tool Description

Tool Description	Length (ft)	Serial No.	Position	Depth (ft)	Accum. Lengths
Change Over Sub	1.00			4088.00	
Shut In Tool	5.00			4093.00	
Hydraulic tool	5.00			4098.00	
Jars	5.00			4103.00	
Safety Joint	2.00			4105.00	
Packer	5.00			4110.00	28.00 Bottom Of Top Packer
Packer	5.00			4115.00	
Stubb	1.00			4116.00	
Recorder	0.00	8360	Outside	4116.00	
Recorder	0.00	6755	Inside	4116.00	
Perforations	28.00			4144.00	
Bullnose	3.00			4147.00	32.00 Bottom Packers & Anchor

Total Tool Length: 60.00



TRILOBITE
TESTING, INC

DRILL STEM TEST REPORT

FLUID SUMMARY

Roberts Resources Inc.

Rule Ranch #1-33

520 S. Holland STE. 207
Wichita KS 67209

30 30 12 Barber KS

Job Ticket: 32501

DST#: 4

ATTN: Kent Roberts

Test Start: 2008.08.27 @ 13:55:42

Mud and Cushion Information

Mud Type: Gel Chem

Mud Weight: 9.00 lb/gal

Viscosity: 51.00 sec/qt

Water Loss: 10.38 in³

Resistivity: ohm.m

Salinity: 6000.00 ppm

Filter Cake: 0.02 inches

Cushion Type:

Cushion Length:

Cushion Volume:

Gas Cushion Type:

Gas Cushion Pressure:

ft

bbl

psig

Oil API:

Water Salinity:

deg API

ppm

Recovery Information

Recovery Table

Length ft	Description	Volume bbl
15.00	Mud W/Oil Scum on Top	0.109
0.00	525' Gas In Pipe	0.000

Total Length: 15.00 ft

Total Volume: 0.109 bbl

Num Fluid Samples: 0

Num Gas Bombs: 0

Serial #:

Laboratory Name:

Laboratory Location:

Recovery Comments:

