

TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

O'Brien Energy Resources

18 Congress ST. Suite 207
Portsmouth NH, 03801

ATTN: Roger Pearson

Rickers #2-17

12/33/29

Job Ticket: 27238

DST#: 1

Test Start: 2008.08.23 @ 06:50:00

GENERAL INFORMATION:

Formation: **Chester**

Deviated: No Whipstock: ft (KB)

Time Tool Opened: 10:28:00

Time Test Ended: 19:00:30

Test Type: Conventional Straddle

Tester: Mike Slomp

Unit No: 28

Interval: **6000.00 ft (KB) To 6128.00 ft (KB) (TVD)**

Total Depth: 6254.00 ft (KB) (TVD)

Hole Diameter: 7.78 inches Hole Condition: Fair

Reference Elevations: 2694.00 ft (KB)

2682.00 ft (CF)

KB to GR/CF: 12.00 ft

Serial #: 8321 Outside

Press@RunDepth: 60.02 psig @ 6135.00 ft (KB)

Start Date: 2008.08.23

End Date:

2008.08.23

Start Time: 06:50:01

End Time:

19:00:30

Capacity: 7000.00 psig

Last Calib.: 2008.08.23

Time On Btm: 2008.08.23 @ 10:24:30


Time Off Btm: 2008.08.23 @ 14:37:00

TEST COMMENT: IF-Weak blow 1/2 inch in 30 min

ISI-No blow back

FF-No blow in 30 min

FSI-No blow back

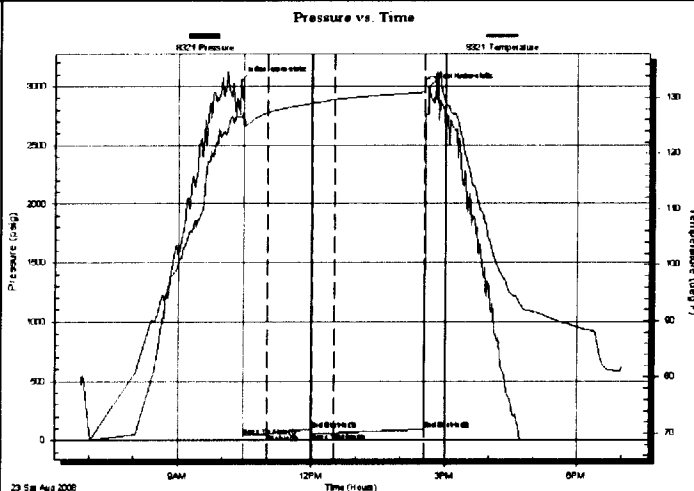

PRESSURE SUMMARY

Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
0	3045.31	126.62	Initial Hydro-static
4	38.56	127.34	Open To Flow (1)
36	52.29	127.37	Shut-In(1)
96	95.49	128.95	End Shut-In(1)
96	58.09	129.02	Open To Flow (2)
127	60.02	129.69	Shut-In(2)
248	92.18	130.98	End Shut-In(2)
253	2990.07	133.56	Final Hydro-static

Recovery

Length (ft)	Description	Volume (bbl)
5.00	mud 100%	0.02

Gas Rates


	Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
--	----------------	-----------------	------------------

RECEIVED
KANSAS CORPORATION COMMISSION

SEP 17 2008

CONSERVATION DIVISION

12-33-29W



TRILOBITE
TESTING, INC.

DRILL STEM TEST REPORT

O'Brien Energy Resources

18 Congress ST. Suite 207
Portsmouth NH, 03801

ATTN: Roger Pearson

Rickers #2-17

12/33/29

Job Ticket: 27238

DST#: 1

Test Start: 2008.08.23 @ 06:50:00

GENERAL INFORMATION:

Formation: **Chester**

Deviated: **No** Whipstock: **ft (KB)**

Time Tool Opened: 10:28:00

Time Test Ended: 19:00:30

Test Type: **Conventional Straddle**

Tester: **Mike Slomp**

Unit No: **28**

Interval: **6000.00 ft (KB) To 6128.00 ft (KB) (TVD)**

Total Depth: **6254.00 ft (KB) (TVD)**

Hole Diameter: **7.78 inches** Hole Condition: **Fair**

Reference Elevations: **2694.00 ft (KB)**

2682.00 ft (CF)

KB to GR/CF: **12.00 ft**

Serial #: 6752 Inside

Press@RunDepth: **psig @ 6007.00 ft (KB)**

Start Date: **2008.08.23**

End Date:

2008.08.23

Capacity: **7000.00 psig**

Last Calib.:

2008.08.23

Start Time: **06:45:01**

End Time:

18:59:45

Time On Btm:

Time Off Btm:


TEST COMMENT: IF-Weak blow 1/2 inch in 30 min

ISI-No blow back

FF-No blow in 30 min

FSI-No blow back

Pressure vs. Time

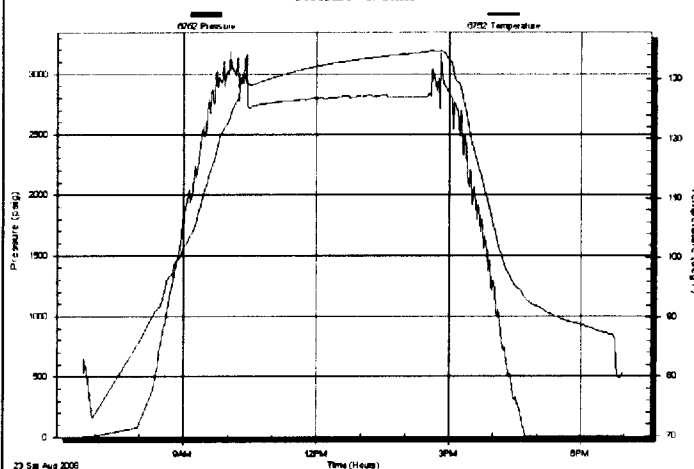

PRESSURE SUMMARY


Time (Min.)	Pressure (psig)	Temp (deg F)	Annotation
-------------	-----------------	--------------	------------

Recovery

Length (ft)	Description	Volume (bbl)
5.00	mud 100%	0.02

Gas Rates

Choke (inches)	Pressure (psig)	Gas Rate (Mcf/d)
----------------	-----------------	------------------

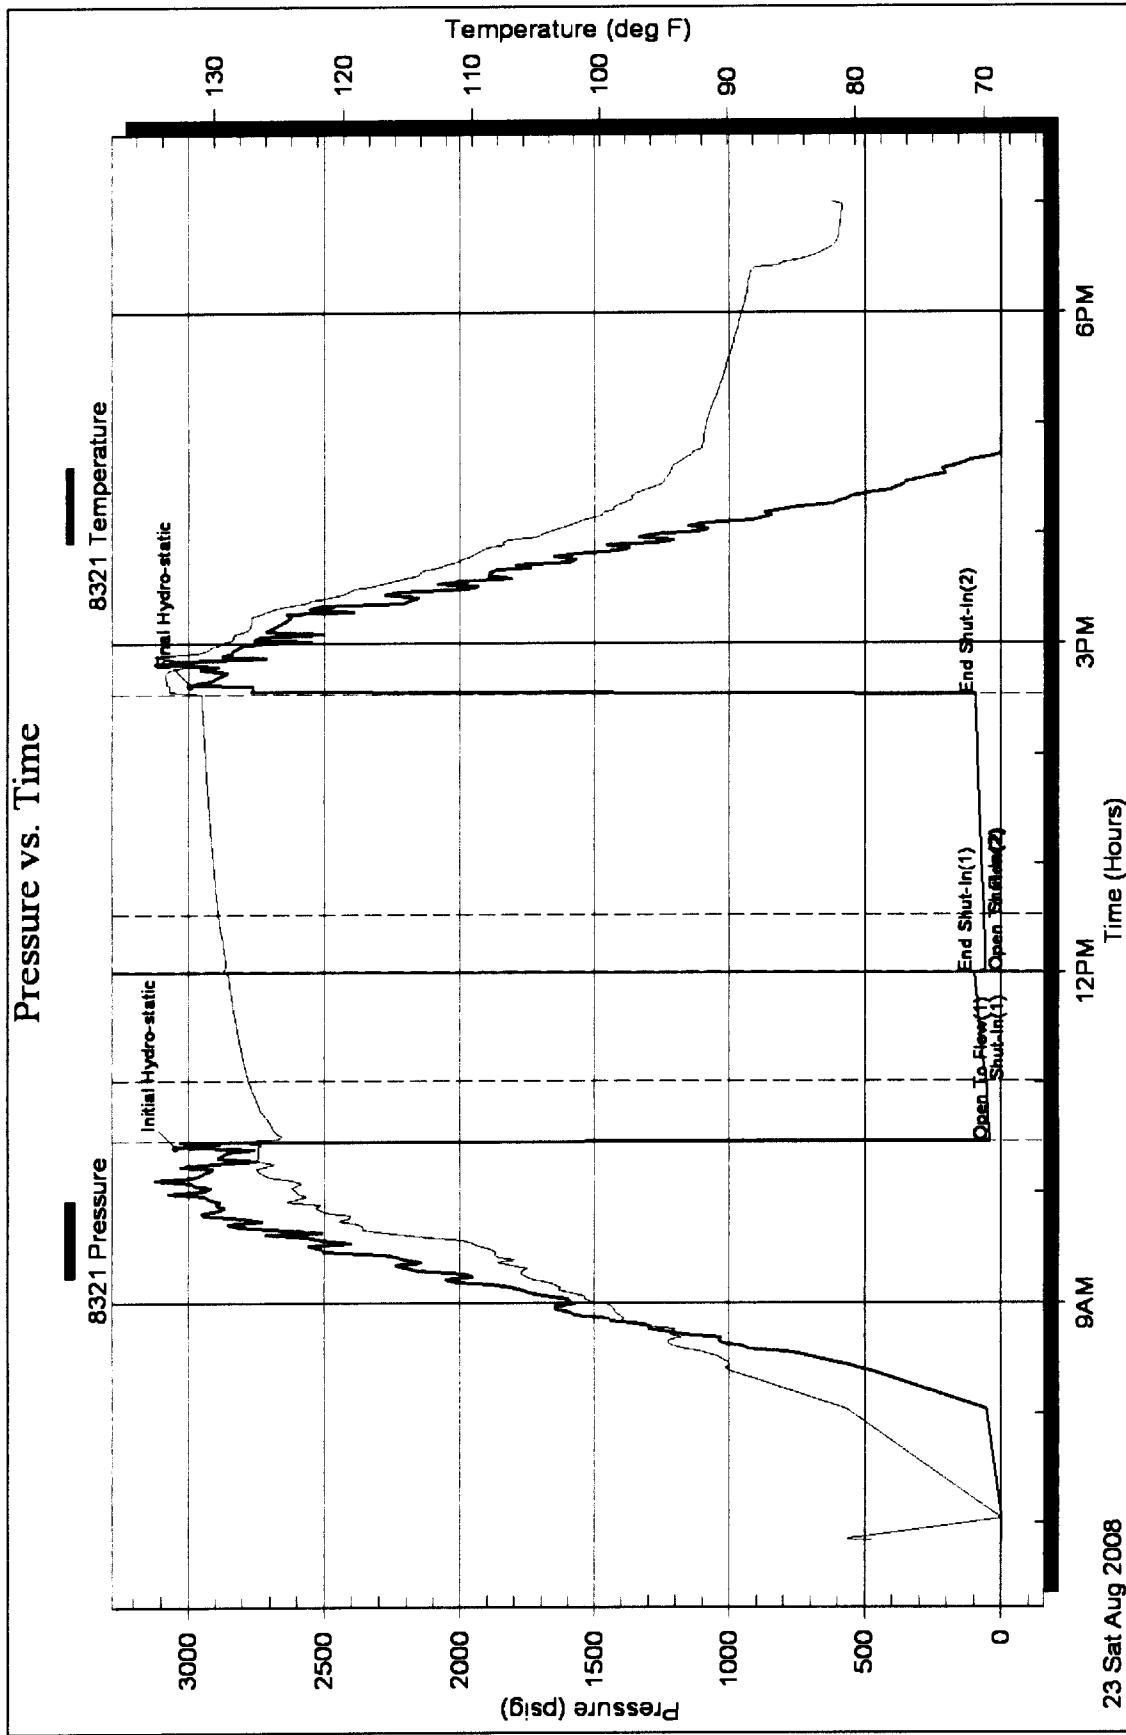

Serial #: 6752

Inside

OBrien Energy Resources

12/33/29

DST Test Number: 1

Pressure vs. Time

