

QUALITY OILWELL CEMENTING, INC.

Federal Tax I.D.# 20-2886107

Phone 785-483-2025

Home Office P.O. Box 32 Russell, KS 67665

No. 4294

Cell 785-324-1041

6-23-2010

Date	Sec. 34	Twp. 9	Range 24	County Graham	State Ks	On Location	Finish 8:15 PM
Lease Herman Trust		Well No. #4-34		Location Wakeeney, Ks N to Redline Rd, 6 1/2 W			
Contractor <u>Murfin Drilling Rig #16</u>				Owner <u>S/S</u>			
Type Job <u>Surface</u>				To Quality Oilwell Cementing, Inc. You are hereby requested to rent cementing equipment and furnish cementer and helper to assist owner or contractor to do work as listed.			
Hole Size <u>12 1/4"</u>		T.D. <u>220'</u>		Charge To <u>Phillips Exploration</u>			
Csg. <u>8 5/8" 23# New</u>		Depth <u>219'</u>		Street			
Tbg. Size		Depth		City			
Tool		Depth		State			
Cement Left in Csg. <u>15'</u>		Shoe Joint <u>15'</u>		The above was done to satisfaction and supervision of owner agent or contractor.			
Meas Line		Displace <u>13 BBLs</u>		Cement Amount Ordered <u>150 5x Common 3% CC 2% Gel</u>			

EQUIPMENT

Pumptrk <u>9</u>	No.	Cement Helper <u>Neale</u>	<u>3</u>	Common <u>150</u>
Bulktrk <u>8</u>	No.	Driver <u>Cisco</u>	<u>3</u>	Poz. Mix
Bulktrk pickup	No.	Driver <u>Pick</u>	<u>3</u>	Gel. <u>3</u>

JOB SERVICES & REMARKS

Remarks: <u>Cement did Circulate</u>	Hulls
Rat Hole	Salt
Mouse Hole	Flowseal
Centralizers	Kol-Seal
Baskets	Mud CLR 48
D/V or Port Collar	CFL-117 or CD110 CAF 38

Cement did Circulate
Used 8 5/8" Swedge

Sand	Handling <u>158</u>
Mileage	


FLOAT EQUIPMENT

Guide Shoe
Centralizer
Baskets
AFU Inserts
Float Shoe
Latch Down

Pumptrk Charge <u>Surface</u>
Mileage <u>38</u>

Tax
Discount
Total Charge

X Signature Aug [Signature]

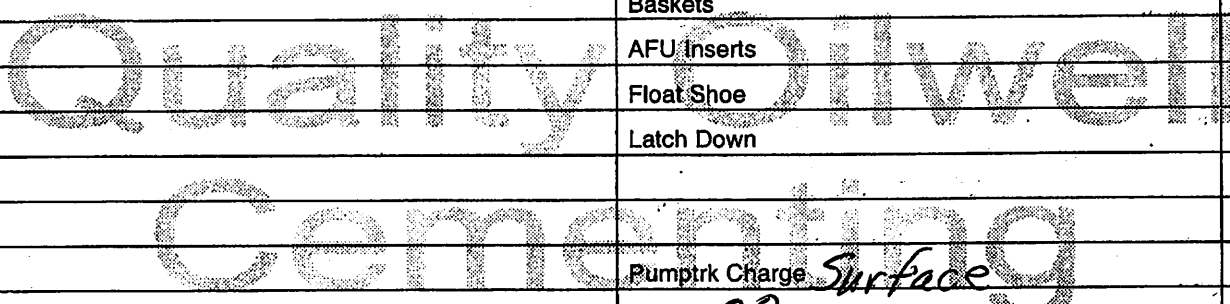

QUALITY OILWELL CEMENTING, INC.

Federal Tax I.D.# 20-2886107

Phone 785-483-2025
Cell 785-324-1041

Home Office P.O. Box 32 Russell, KS 67665

No. 4300

Date	6-28-2010	Sec.	34	Twp.	9	Range	24	County	Graham	State	Ks	On Location		Finish	1:00 AM
Lease	Hecman trust			Well No.	4-34			Location	Wakeeny, Ks N to Red line Rd, 62W						
Contractor	Mustin #16							Owner	5/5						
Type Job	Production (Top)							To Quality Oilwell Cementing, Inc. You are hereby requested to rent cementing equipment and furnish cementer and helper to assist owner or contractor to do work as listed.							
Hole Size	7 7/8"			T.D.	4150'			Charge To	Phillips exploration						
Csg.	5" 14# New			Depth	4147.18'			Street							
Tbg. Size				Depth				City	State						
Tool	DU Tool			Depth	2181'			The above was done to satisfaction and supervision of owner agent or contractor.							
Cement Left in Csg.	⓪			Shoe Joint				Cement Amount Ordered 400 sx QMDC 1/4 Flowseal							
Meas Line				Displace	53.25 BBLs										

EQUIPMENT

Pumptrk	5	No.	Cement Helper	Brandon	3	Common	400
Bulktrk	4	No.	Driver	Rocky	3	Poz. Mix	
Bulktrk pickup		No.	Driver	Rick	3	Gel.	

JOB SERVICES & REMARKS

Remarks:	30sx		Hulls
Rat Hole	30sx	30sx	Salt
Mouse Hole	15 sx		Flowseal 100
Centralizers			Kol-Seal
Baskets			Mud CLR 48 500 gal
D/V or Port Collar	2181'	48# JT.	CFL-117 or CD110 CAF 38

pipe on bottom, break Circulation pump 500 gal Mud Clear 48 pump 5 BBLs of water, plug Rat hole 30 sx, Mouse hole 15 sx Cement Casing with 355 sx Qm Dc, shut down wash up. Hook to casing and displaced with 53 1/2 BBLs of freshwater. Landel plug to 1200 #'s Released and held, 600 #/sq lift pressure

Cement did Circulate.

Handling	
Mileage	
FLOAT EQUIPMENT	
Guide Shoe	
Centralizer	
Baskets	
AFU Inserts	
Float Shoe	
Latch Down	

X Signature *Thull*

Pumptrk Charge		Tax	
Mileage		Discount	
		Total Charge	

QUALITY OILWELL CEMENTING, INC.

Federal Tax I.D.# 20-2886107

Phone 785-483-2025
Cell 785-324-1041

Home Office P.O. Box 32 Russell, KS 67665

No. 4299

Date	6-28-2010	Sec.	34	Twp.	9	Range	24	County	Graham	State	Ks	On Location		Finish	9:00 PM
Lease	Herman Trust			Well No.	4-34			Location	Wakeeny, Ks - N to Redline Rd, G&W						
Contractor	Murfin #16							Owner	5/5						
Type Job	Production			(Bottom)			To Quality Oilwell Cementing, Inc. You are hereby requested to rent cementing equipment and furnish cementer and helper to assist owner or contractor to do work as listed.								
Hole Size	7 7/8"			T.D.			4130								
Csg.	5 1/2" 14# New			Depth			4147.18								
Tbg. Size				Depth			Street								
Tool	DU Tool			Depth			2181'								
Cement Left in Csg.	16.94			Shoe Joint			16.94								
Meas Line				Displace			101 BBLs								
Cement Amount Ordered							165 5X Quality Pac C								

EQUIPMENT

Pumptrk	5	No.	Cement	Random	4	Common
Bulktrk	10	No.	Driver	Douglas	4	Poz. Mix
Bulktrk	up	No.	Driver	Rick	4	Gel.

JOB SERVICES & REMARKS

Remarks:	Hulls
Rat Hole	Will plug on top stage
Mouse Hole	See ticket #4380
Centralizers	3, 4, 5, 6, 7, 8, 10, 47
Baskets	13, 48
D/V or Port Collar	2181' DU Tool 48" JT
	pipe on bottom, break circulation, run 165 5X
	Quality Pac C, start down
	500 gal mud clear 48, pump 5 BBLs
	of freshwater, mix 165 5X Quality Pac C
	shut down Released plan washup
	and displaced with 914 BBLs of
	freshwater + 54 BBLs of mud.
	Land plug to 1250 #'s, Released and
	held. Drop the Dart, wait 10 min.
	and open tool, wash displacement
	tanks clear, and Circulate 2 hrs 1-
	With Rig pump.
	Lift PST 700#
	Bottom Stage
	Pumptrk Charge prod Long string
	Mileage 38

FLOAT EQUIPMENT

Guide Shoe	
Centralizer	8 - 5 1/2"
Baskets	2 - 5 1/2"
AFU Inserts	
Float Shoe	1 - 5 1/2"
Latch Down	
	DU Tool assy - 5 1/2"

X Signature *Paul R. Paulson*

Tax
Discount
Total Charge
