

Form	ACO1 - Well Completion
Operator	Triple Crown Operating LLC
Well Name	WONDERLAND 1-9
Doc ID	1415707

All Electric Logs Run

Dual Induction
Micro
Compensated Density
Sonic

Form	ACO1 - Well Completion
Operator	Triple Crown Operating LLC
Well Name	WONDERLAND 1-9
Doc ID	1415707

Casing

Purpose Of String	Size Hole Drilled	Size Casing Set	Weight	Setting Depth	Type Of Cement	Number of Sacks Used	Type and Percent Additives
Surface	12.25	8.625	23	218	Common	170	3% CC 2% Gel

Sean Deenihan
Petroleum Geologist

GEOLOGIST'S REPORT
DRILLING TIME AND SAMPLE LOG

COMPANY	Triple Crown Operating, LLC	ELEVATIONS
LEASE	Wonderland #1-9	KB 2245'
FIELD	Wildcat	DF
LOCATION	2513' FNL & 1750' F.W.L	GL 2240'
SEC	9 TWSP 20 S RGE 22 W	Measurements Are All From Kelly Bushing
COUNTY	Ness STATE Kansas	
CONTRACTOR	WW Drilling Rig #8	
SPUD	4/5/18 COMP 4/12/18	
RTD	4500 LTD 4503'	CASING
MUD UP	TYPE MUD Chemical	CONDUCTOR SURFACE 8-5/8" at 218'
SAMPLES SAVED FROM	3500' TO RTD	PRODUCTION None
DRILLING TIME KEPT FROM	3500' TO RTD	ELECTRICAL SURVEYS
SAMPLES EXAMINED FROM	3500' TO RTD	FLJ Wireline
GEOLOGICAL SUPERVISION FROM	3550'	CND/DIL, MIC/SON
REFERENCE WELL		
Formation	Sample Tops	E-log Tops
B/Amb/drite		1505' (-740)
Heebner Sh.		3726' (-1481)
Lansing		3772' (-1527)
BKC		4096' (-1851)
Ft Scott		4286' (-2041)
Cherokee Sh.		4310' (-2065)
Mississippi Por		4398' (-2153)


REMARKS Based on sample, log, and DST analysis, the Wonderland #1-9 was plugged and abandoned.

Respectfully Submitted,

Sean P. Deenihan

Printed by GEOstrip VC Striplog version 4.0.8.15 (www.grsi.ca)

TG, C1 - C5

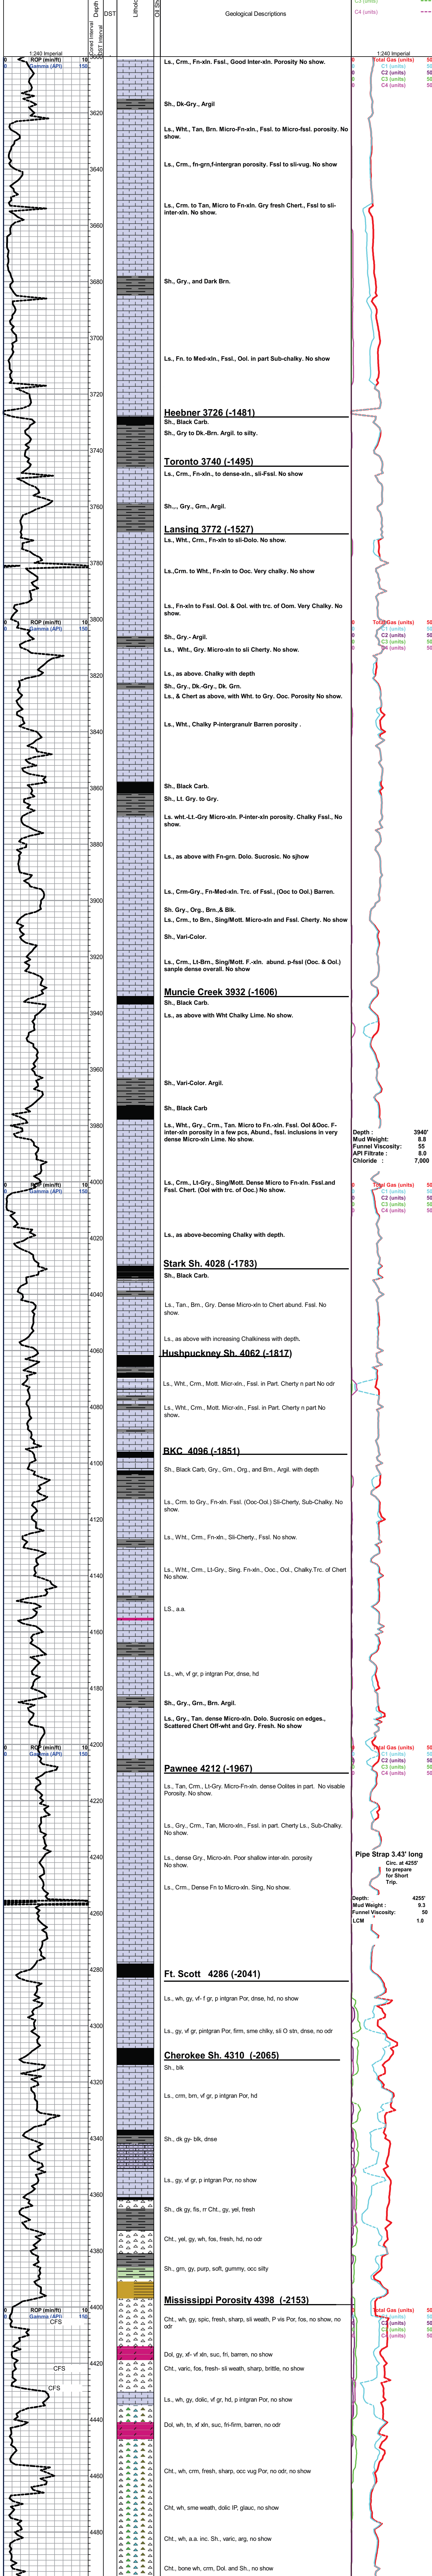

RTD: 4500'
LTD: 4503'

Triple Crown Operating, LLC
Wonderland #1-9
9 -20S-22W
Ness Co., KS

KB: 2245'

QUALITY OILWELL CEMENTING, INC.

Federal Tax I.D.# 20-2886107

Phone 785-483-2025
Cell 785-324-1041

Home Office P.O. Box 32 Russell, KS 67665

No. 688

Date	4-5-18	Sec.	9	Twp.	20	Range	22	County	Ness	State	Ks	On Location		Finish	11:00 PM
------	--------	------	---	------	----	-------	----	--------	------	-------	----	-------------	--	--------	----------

Lease	Wonderland	Well No.	1-9	Location	Bazine - 3w to AA Rd, 8S to 50 Rd,
-------	------------	----------	-----	----------	------------------------------------

Contractor	WW #8	Owner	1w, 1/2 S, E/Intro
Type Job	Surface	To Quality Oilwell Cementing, Inc. You are hereby requested to rent cementing equipment and furnish cementer and helper to assist owner or contractor to do work as listed.	

Hole Size	12 1/4"	T.D.	218'	Charge To	Triple Crown
Csg.	8 3/8"	Depth	218'	Street	

Tbg. Size		Depth		City		State	
-----------	--	-------	--	------	--	-------	--

Tool		Depth		The above was done to satisfaction and supervision of owner agent or contractor.		
------	--	-------	--	--	--	--

Cement Left in Csg.	15'	Shoe Joint	15'	Cement Amount Ordered	170 Q 86/20 3+2
---------------------	-----	------------	-----	-----------------------	----------------------------

Meas Line		Displace	12 3/4 BLS
-----------	--	----------	------------

EQUIPMENT

Pumptrk	16	No.	Cementer	Travis	Common	136
			Helper		Poz. Mix	34
Bulktrk	9	No.	Driver	Doug	Gel.	3
			Driver		Calcium	7
Bulktrk	pin.	No.	Driver	Rick		

JOB SERVICES & REMARKS

Remarks:	Cement did Circulate	Hulls	
Rat Hole		Salt	
Mouse Hole		Flowseal	
Centralizers		Kol-Seal	
Baskets		Mud CLR 48	
D/V or Port Collar		CFL-117 or CD110 CAF 38	
		Sand	
		Handling	180
		Mileage	

FLOAT EQUIPMENT

	Guide Shoe	
	Centralizer	
	Baskets	
	AFU Inserts	
	Float Shoe	
	Latch Down	
	Pumptrk Charge	Surface
	Mileage	25

X Signature	Scott L. Lano	Tax	
		Discount	
		Total Charge	

Federal Tax I.D.# 20-2886107

Phone 785-483-2025
Cell 785-324-1041

Home Office P.O. Box 32 Russell, KS 67665

No. 692

Date	4-12-18	Sec.	9	Twp.	20	Range	22	County	Ness	State	Ks	On Location		Finish	7:30 PM
								Location	Bazine - 3w to AARd, 85 to 50 Rd,						
Lease	Wonderland							Well No.	1-9		Owner	lw, 1/25, FLS			
Contractor	ww #8							To Quality Oilwell Cementing, Inc. You are hereby requested to rent cementing equipment and furnish cementer and helper to assist owner or contractor to do work as listed.							
Type Job	Plug							Charge To Triple Crown							
Hole Size	7 7/8"							T.D.	4500'		Street				
Csg.								Depth			City				
Tbg. Size	4 1/2" D.P.							Depth	1500'		State				
Tool								Depth			The above was done to satisfaction and supervision of owner agent or contractor.				
Cement Left in Csg.								Shoe Joint			Cement Amount Ordered 230 60/100 4% Gel 1/4# Flo-Seal				
Meas Line								Displace	H2O						
EQUIPMENT										Common 138					
Pumptrk	17	No.	Cementer	Craig					Poz. Mix 92						
Bulktrk	14	No.	Driver	Jordan					Gel. 9						
Bulktrk	p.u.	No.	Driver	Rick					Calcium						
JOB SERVICES & REMARKS										Hulls					
Remarks:	1500' - 50 SX									Salt					
Rat Hole	720' - 80 SX									Flowseal 60th					
Mouse Hole	270' - 50 SX									Kol-Seal					
Centralizers	60' - 20 SX									Mud CLR 48					
Baskets	Rathole w/ 30 SX									CFL-117 or CD110 CAF 38					
D/V or Port Collar	Cement did Circulate									Sand					
										Handling 239					
										Mileage					
										FLOAT EQUIPMENT					
										Guide Shoe					
										Centralizer					
										Baskets					
										AFU Inserts					
										Float Shoe					
										Latch Down					
										Pumptrk Charge plug					
										Mileage 25					
										Tax					
										Discount					
										Total Charge					
Signature															
