



Company: Jason Oil Company, LLC

Lease: Schoenberger #10-16

SEC: 10 TWN: 16S RNG: 14W
County: BARTON
State: Kansas
Drilling Contractor: WW Drilling, LLC - Rig 2
Elevation: 1928 EGL
Field Name: Nuss South
Pool: Infield
Job Number: 148

Operation:
Well Complete

DATE
April
24
2018

DST #2 **Formation: L/KC "H-K"** **Test Interval: 3270 - 3329'** **Total Depth: 3329'**

Time On: 04:14 04/24 Time Off: 09:35 04/24
Time On Bottom: 06:00 04/24 Time Off Bottom: 08:00 04/24

Electronic Volume Estimate:
42'


1st Open
Minutes: 30
Current Reading:
1.25" at 30 min
Max Reading: 1.25"

1st Close
Minutes: 30
Current Reading:
0" at 30 min
Max Reading: 0"

2nd Open
Minutes: 30
Current Reading:
.48" at 30 min
Max Reading: .48"

2nd Close
Minutes: 30
Current Reading:
0" at 30 min
Max Reading: 0"

Inside Recorder

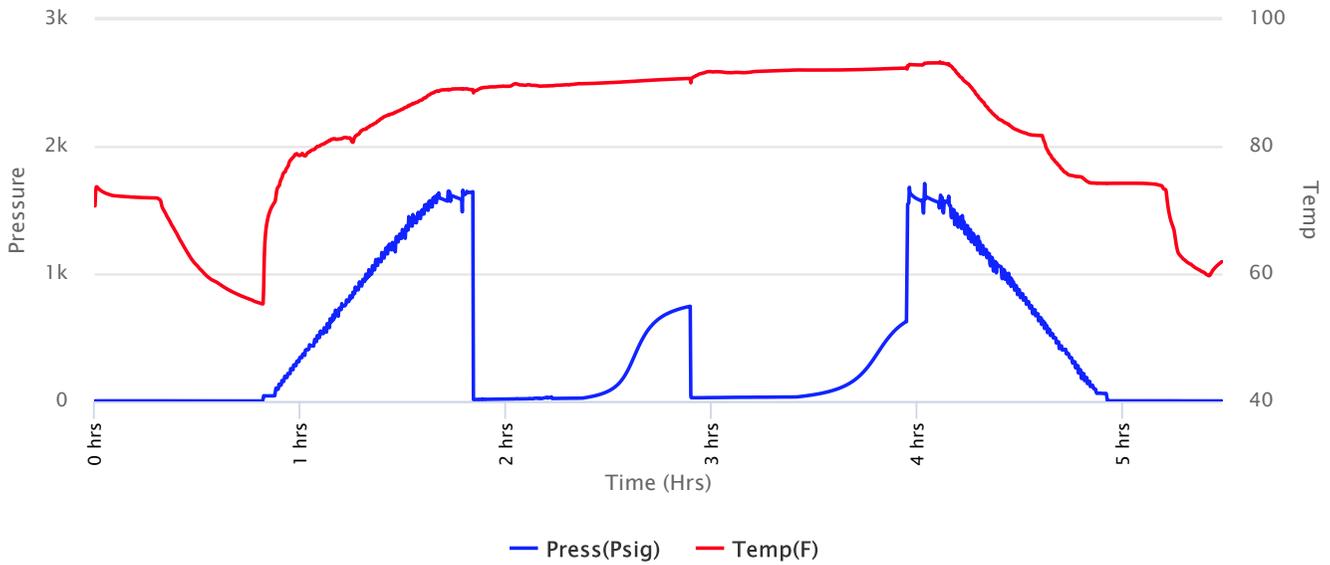



Company: Jason Oil Company, LLC

Lease: Schoenberger #10-16

SEC: 10 TWN: 16S RNG: 14W
County: BARTON
State: Kansas
Drilling Contractor: WW Drilling, LLC - Rig 2
Elevation: 1928 EGL
Field Name: Nuss South
Pool: Infield
Job Number: 148

Operation:
Well Complete

DATE
April
24
2018

DST #2 **Formation: L/KC "H-K"** **Test Interval: 3270 - 3329'** **Total Depth: 3329'**
Time On: 04:14 04/24 Time Off: 09:35 04/24
Time On Bottom: 06:00 04/24 Time Off Bottom: 08:00 04/24

Recovered


Foot	BBLs	Description of Fluid	Gas %	Oil %	Water %	Mud %
45	0.2214	SLOCM	0	2	0	98

Total Recovered: 45 ft
Total Barrels Recovered: 0.2214

Reversed Out
NO

Initial Hydrostatic Pressure	1591	PSI
Initial Flow	13 to 24	PSI
Initial Closed in Pressure	745	PSI
Final Flow Pressure	27 to 34	PSI
Final Closed in Pressure	623	PSI
Final Hydrostatic Pressure	1581	PSI
Temperature	93	°F
Pressure Change Initial Close / Final Close	16.3	%

Recovery at a glance

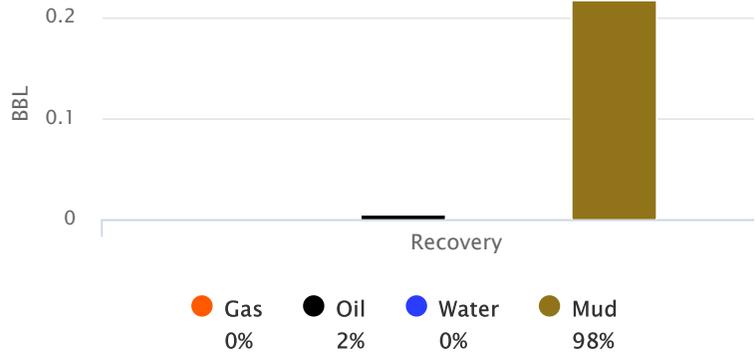



**Company: Jason Oil Company,
LLC**

Lease: Schoenberger #10-16

SEC: 10 TWN: 16S RNG: 14W
County: BARTON
State: Kansas
Drilling Contractor: WW Drilling, LLC -
Rig 2
Elevation: 1928 EGL
Field Name: Nuss South
Pool: Infield
Job Number: 148

Operation:
Well Complete

DATE
April
24
2018

DST #2	Formation: L/KC "H- K"	Test Interval: 3270 - 3329'	Total Depth: 3329'
	Time On: 04:14 04/24	Time Off: 09:35 04/24	
	Time On Bottom: 06:00 04/24	Time Off Bottom: 08:00 04/24	

BUCKET MEASUREMENT:

REMARKS:

Initial Flow: 1/4 in. blow building to 1 1/4 ins. in 30 mins.

Initial Shut-in: No blow back.

Final Flow: No blow building to 1/2 in. in 30 mins.

Final Shut-in: No blow back.

Tool Sample: 6% oil, 94% mud



Company: Jason Oil Company, LLC

Lease: Schoenberger #10-16

SEC: 10 TWN: 16S RNG: 14W
County: BARTON
State: Kansas
Drilling Contractor: WW Drilling, LLC - Rig 2
Elevation: 1928 EGL
Field Name: Nuss South
Pool: Infield
Job Number: 148

Operation:
Well Complete

DATE
April
24
2018

DST #2 **Formation: L/KC "H-K"** **Test Interval: 3270 - 3329'** **Total Depth: 3329'**
Time On: 04:14 04/24 Time Off: 09:35 04/24
Time On Bottom: 06:00 04/24 Time Off Bottom: 08:00 04/24

Down Hole Makeup

Heads Up: 31.19 FT	Packer 1: 3265 FT
Drill Pipe: 3157.03 FT <i>ID-3 1/2</i>	Packer 2: 3270 FT
Weight Pipe: FT <i>ID-2 7/8</i>	Top Recorder: 3257 FT
Collars: 119 FT <i>ID-2 1/4</i>	Bottom Recorder: 3308 FT
Test Tool: 26.16 FT <i>ID-3 1/2-FH</i>	Well Bore Size: 7 7/8
Total Anchor: 59	Surface Choke: 1"
<u>Anchor Makeup</u>	Bottom Choke: 5/8"
Packer Sub: 1 FT	
Perforations: (top): 3 FT <i>4 1/2-FH</i>	
Change Over: 1 FT	
Drill Pipe: (in anchor): 31.5 FT <i>ID-3 1/2</i>	
Change Over: .5 FT	
Perforations: (below): 22 FT <i>4 1/2-FH</i>	



**Company: Jason Oil Company,
LLC**

Lease: Schoenberger #10-16

SEC: 10 TWN: 16S RNG: 14W
County: BARTON
State: Kansas
Drilling Contractor: WW Drilling, LLC -
Rig 2
Elevation: 1928 EGL
Field Name: Nuss South
Pool: Infield
Job Number: 148

Operation:
Well Complete

DATE
April
24
2018

DST #2 **Formation: L/KC "H-
K"** **Test Interval: 3270 -
3329'** **Total Depth: 3329'**
Time On: 04:14 04/24 Time Off: 09:35 04/24
Time On Bottom: 06:00 04/24 Time Off Bottom: 08:00 04/24

Mud Properties

Mud Type: Chemical **Weight:** 8.8 **Viscosity:** 52 **Filtrate:** 8.0 **Chlorides:** 4,000 ppm
